




Pilgrim NDCAP Update




March 27, 2023

Draft Waterfall Chart


Pilgrim Decommissioning - Waterfall Chart

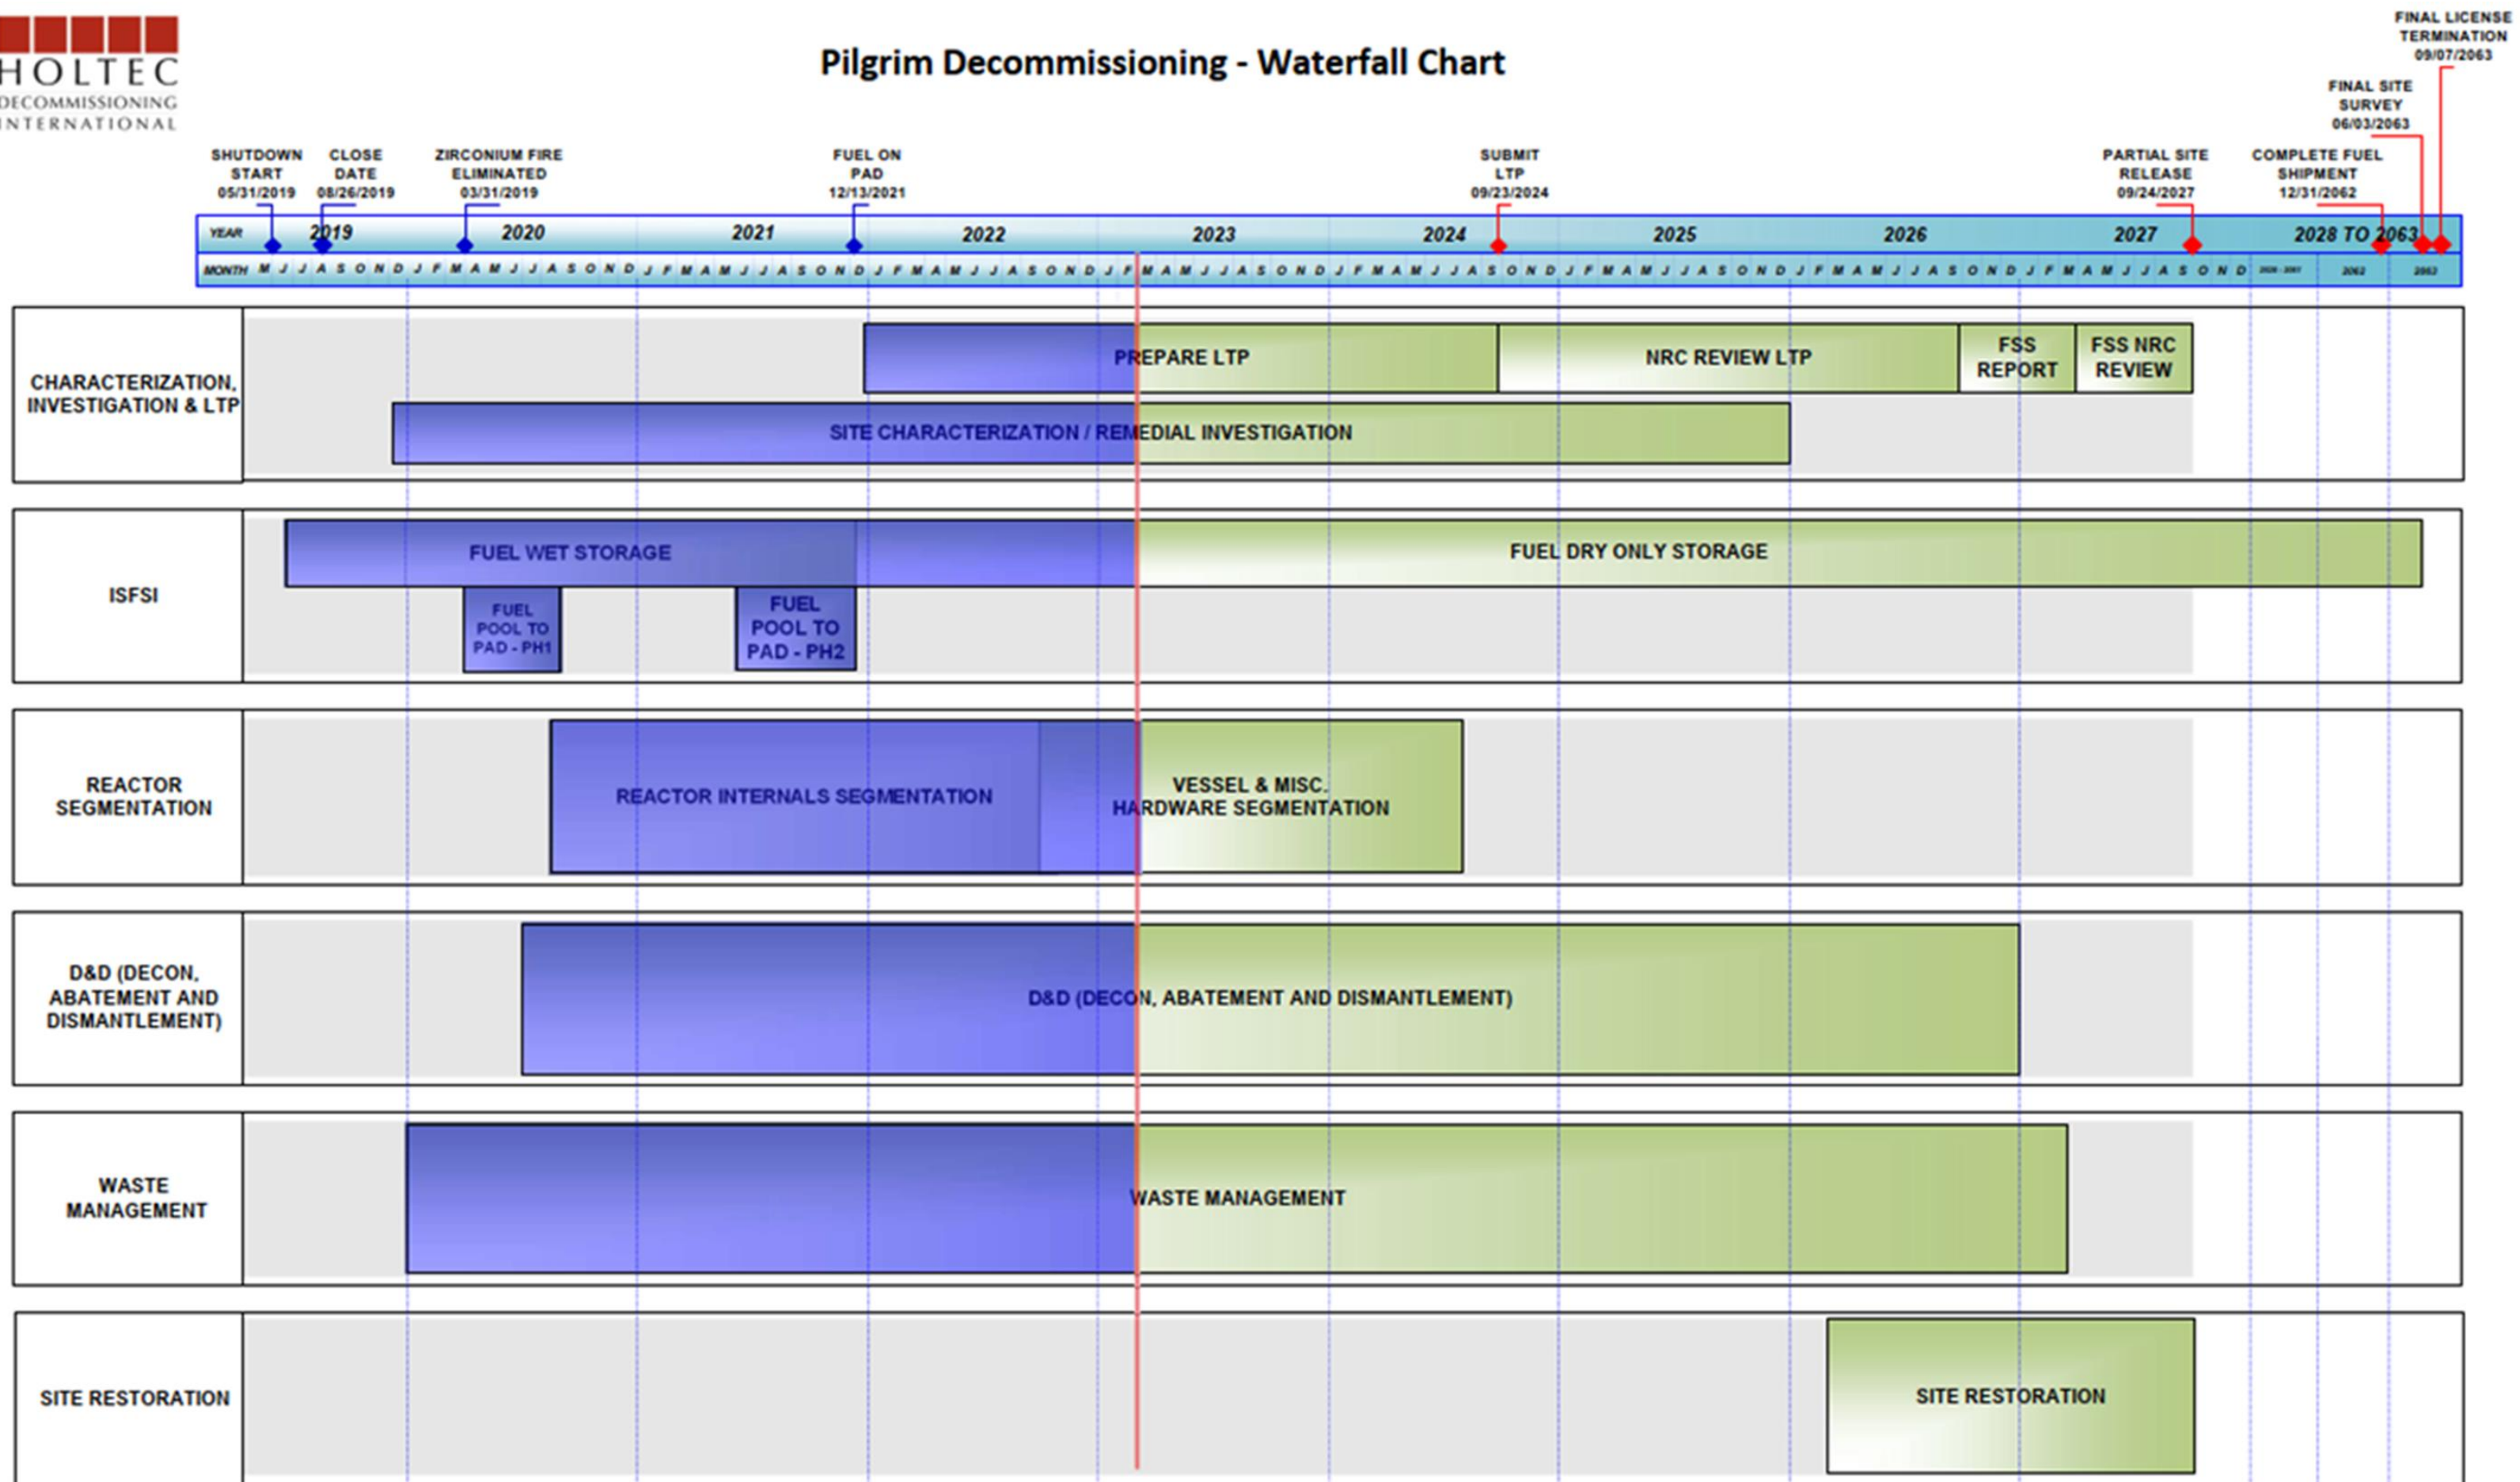

Demolition

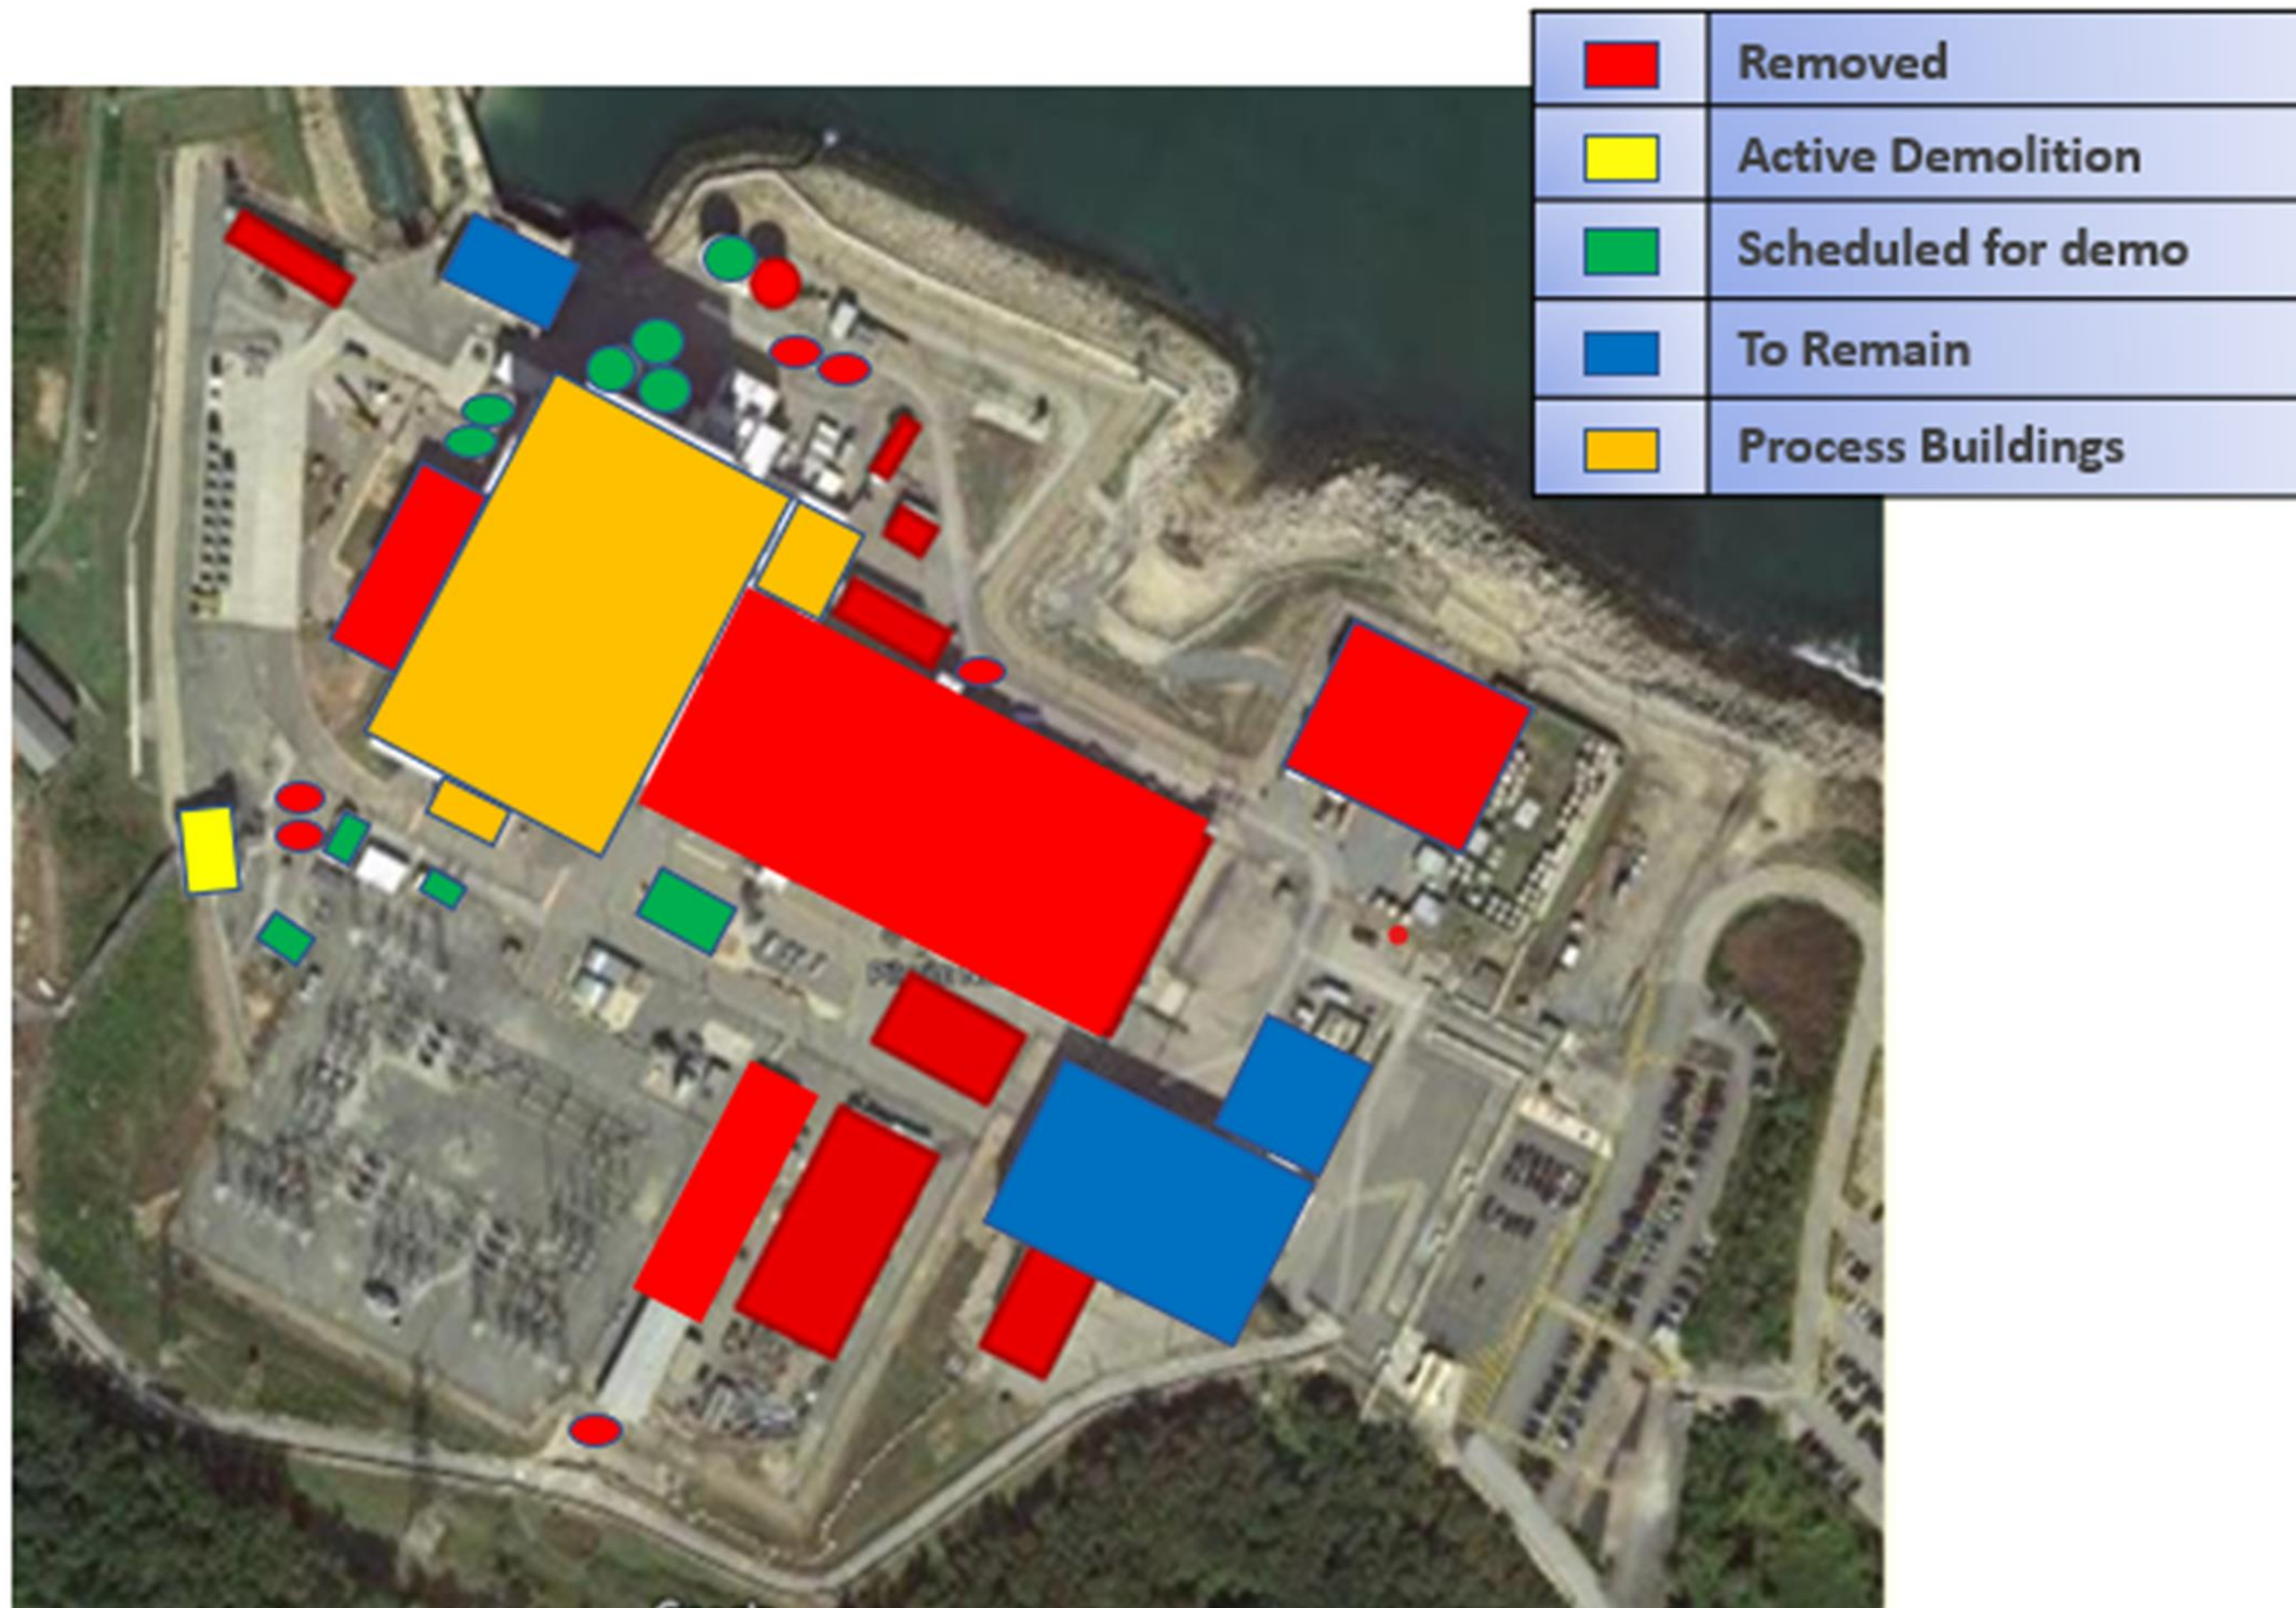

Demolition - Complete

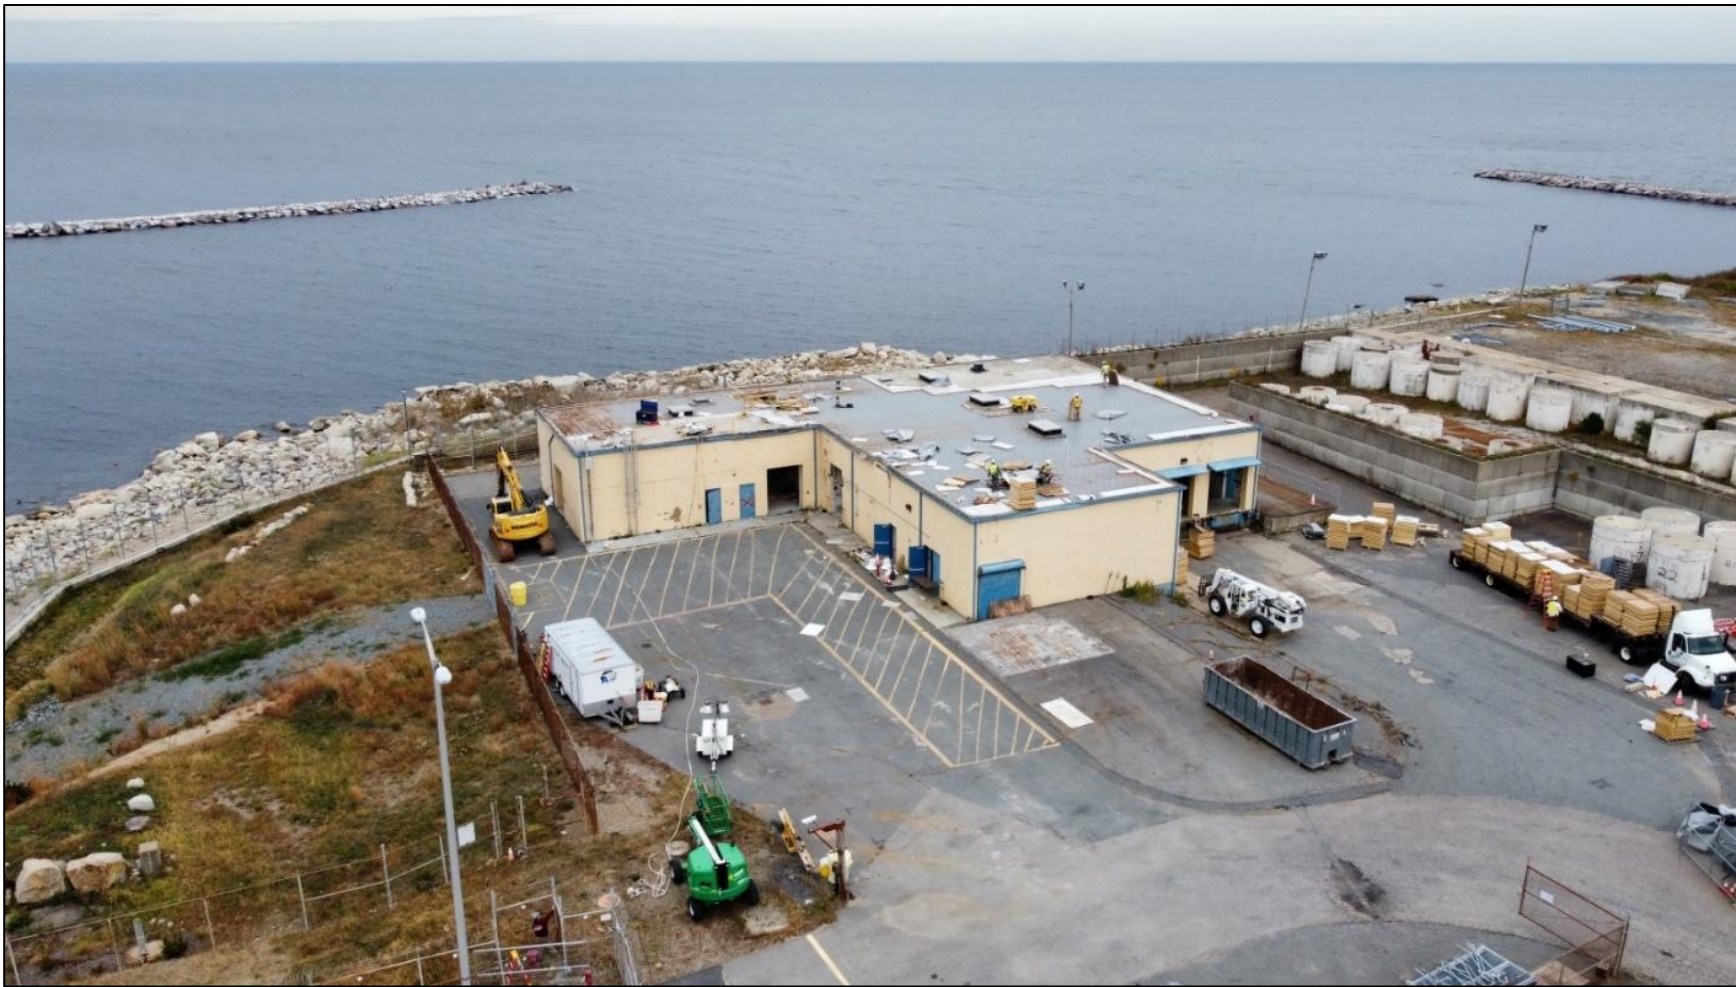


- Trash Compaction Facility- Demolition Clean-up Complete
- $\approx 14,000 \text{ ft}^3$ Removed and Disposed
- $\approx 22,000 \text{ ft}^3$ recycled (approx. 54%)
- $\approx 5,000 \text{ ft}^3$ radioactive waste

Demolition - Upcoming

TCF Adjacent Wall Structure

- Wall removal – Next Week
- OSSC Lid removal – Mid-April

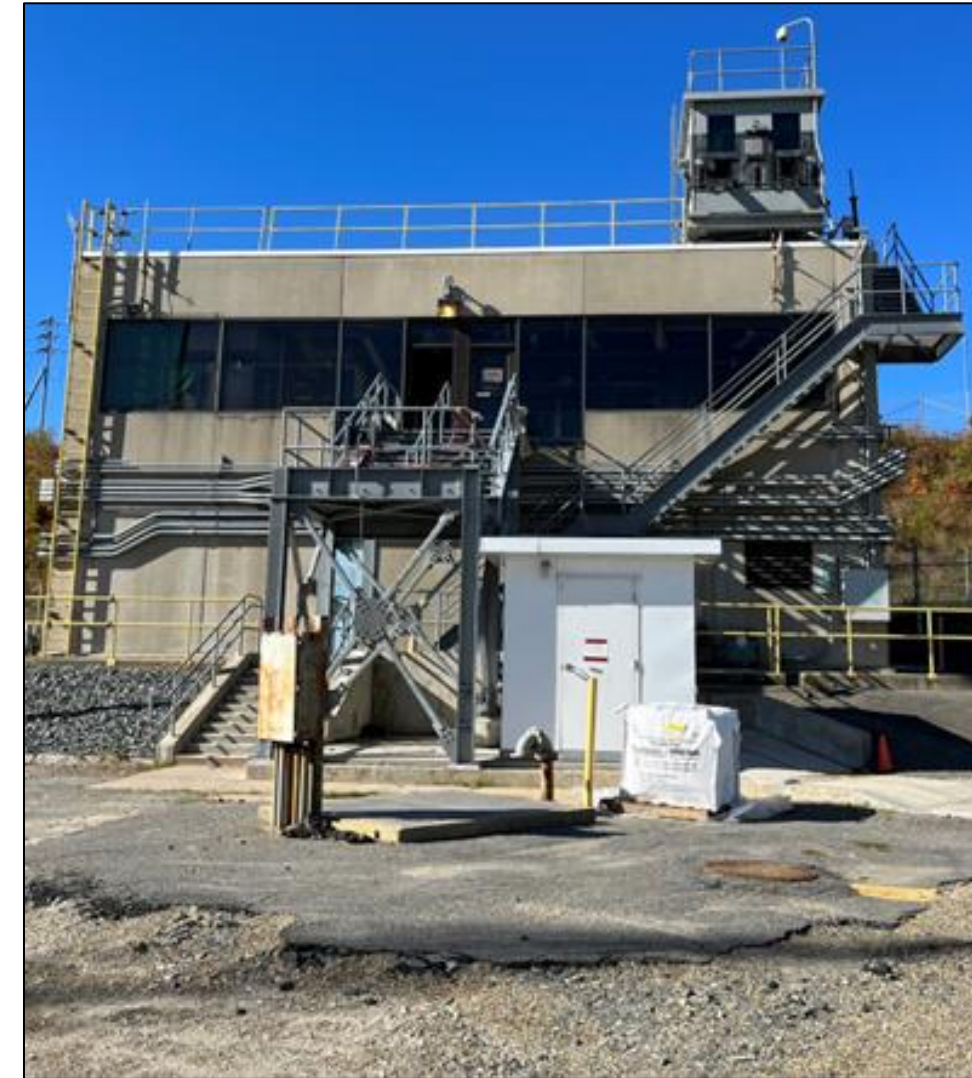

Old Main Gate

- Demolition - Mid-April Completion

SEP Diesel, Station Blackout Diesel Generator, Security Diesel, Central Alarm Station

- Demo to follow Old Main Gate



Reactor Internal Segmentation

- Control Rod Blades – Complete
- Fuel Support Castings – Complete
- Control Rod Guide Tubes – Complete

Upcoming in 2023

- Lower Core Plate Removal and Segmentation
- Shroud Ring Cut #3
- Segment Shroud Ring
- Jet Pumps



Waste Management


Radioactive Waste Shipments – Completed in 2023 Thru March 15th via Transload facility (Rail) and Highway shipments approximately 31,190 ft³ total



A "connestoga" conveyance and 20' seavans (2) on trailer



215 A Cask Shipment RVI and Filters

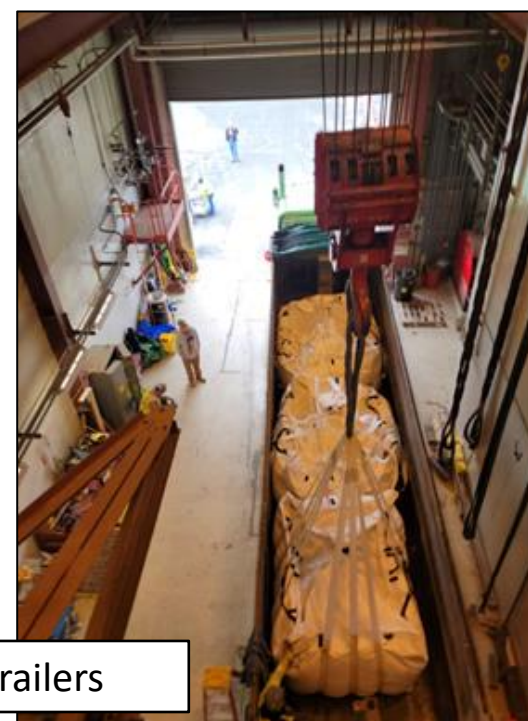

Load frames, lifts of bags from frames to transfer trailers



Regulatory Affairs

- Decommissioning Funding Annual Report Submittal –March 31
- Submit Permit Modification for EPA NPDES permit and State surface water discharge – March 31

Water Management

- Split Sampling with MassDEP and MDPH of Cavity / DSP, SFP, and Torus to occur in April, Town has been invited to observe
