

#### <u>AGENDA</u>

#### **Project Update**

- Project Schedule Update
- Early Package Workforce Report
- M/W/VBE Draft Resource List
- Ongoing Outreach
- Project Overview
- Questions
- Site Visit







# **Project Schedule**

Holyoke Soldiers' Home - Precon Milestone Schedule

- 1		_																												_	_	_				_	_
Tasks		┕					_																									丰			ears		
		L		202	2		⊥												2	023												23	2024	2025	2026	2027	2028
		L	Ü	ecem)	ber		┸		lanua	ry		F	ebrua	ary			Ν	larch		$\perp$		Apri	il			May				June							
									Weeks																												
		48	49	50	51	. 52	2	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17 :	18 1	9 2	20 2	21	22 2	23 24	25	L					
Current projection	Early Bid Package - Enabling Work			Г	Г							Τ													Τ						I	$\prod$					
Actual	Main Package Prequalification																														$oxed{oxed}$	$\prod$					
Actual	Main Package Bid Set Documents Complete																										Ι				$oxed{oxed}$						
Current projection	Main Package Bid Room Review and Finalization																										Ι				$oxed{L}$	$\prod$					
Current projection	Final Main Package Bid Package Issued to Bidders																														$oxed{oxed}$	$\prod$					
Current projection	Main Package Bidding Period																														$oxed{L}$						
Current projection	GMP Agreed																														$oxed{L}$						
Current projection	Final Documents																								Ι	Τ					$oxed{L}$						
Current projection	NTP for Main Package Construction Issued																														$oxed{oxed}$						
Current projection	Issue Subcontracts/Mobilize																																				
Current projection	Main Package Construction	Γ														T	T		T								Т										





### **Early Package – Work Force Report**

Holyoke Veterans' Home - Early Enabling Package [As of April 2023]

CURCONTRACTOR	TOTAL	MINORITY (1	5.3%)	<b>WOMEN</b> (6.9%)				
SUBCONTRACTOR	HOURS	HOURS	%	HOURS	%			
American Environmental, Inc.	600.00	96.00	16.00%	504.00	84.00%			
Atlantic Bridge & Engineering, Inc.	215.00	25.00	11.63%	-	0.00%			
B-G Mechanical Contractors, Inc.	846.00	-	0.00%	-	0.00%			
Carlysle Engineering, Inc.	123.00	-	0.00%	-	0.00%			
Collins Electric Co., Inc.	478.50	16.00	3.34%	8.00	1.67%			
Edward F. Corcoran Plumbing & Heating	146.00	-	0.00%	-	0.00%			
Insulation Contractor of New England LLC	113.00	-	0.00%	24.00	21.24%			
Northeast Painting Associates, Inc.	24.00	-	0.00%	24.00	100.00%			
Performance Testing and Balancing	-	-	0.00%	-	0.00%			
Power Line Contractors, Inc.	1,276.50	138.00	10.81%	-	0.00%			
Rockwell Roofing, Inc.	167.25	46.75	27.95%	-	0.00%			
Sweeney Drywall Finishes Corp	133.00	32.00	24.06%	-	0.00%			
T & M Equipment Corporation	248.50	40.50	16.30%	60.50	24.35%			
TOTALS TO DATE	4,370.75	394.25	9.02%	620.50	14.20%			

Apprentice & Veteran work force goals will start being tracked in the main package work.







#### M/W/VBE Draft Resource List

#### **Resource Categories**

- General Resources
- Mentoring
- Technical Assistance
- Financial Assistance
- Pairing Businesses with Workforce
- General Industry Resources





### **Ongoing Outreach**







# MBE/WBE Outreach Event

Join us to find out about construction projects and opportunities for subcontractors, vendors and suppliers to get involved on upcoming construction projects with the UMass Building Authority and Division of Capital Asset Management and Maintenance

Tuesday June 13,2023 1-4PM

Holyoke Community College 303 Homestead Ave, Holyoke, MA 01040







### **Project Overview**

#### **Existing Facilities**



#### New Veterans' Home



- 235 Long-term Care Beds; 230,000 GSF +/-
- Shared rooms, shared baths
- No Adult Day Health
- Under-utilized outpatient care
- 30 Bed Domiciliary Program

- 234 Long-term Care Beds; 350,000 GSF; 260 parking spaces
- · Mostly private beds with private baths
- Community spaces, nursing support, and kitchen in each floor
- Dedicated 32-bed memory-care floor
- 40-50 person Adult Day Health Program
- Upgraded clinical spaces for dental care
- Variety of outdoor spaces Dementia Garden, Barbeque Terrace, Memorial Garden








# **Project Overview**







### **Project Phasing – Sequences / Logistics**

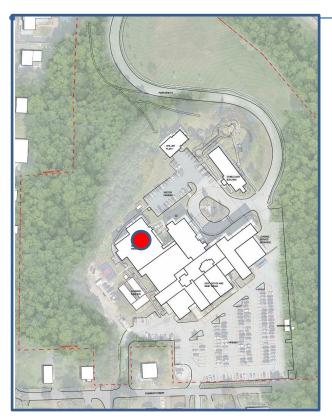





**Early Enabling - Temporary Chiller** 

Phase 1


Phase 2










### **Project Phasing - Sequences / Logistics**

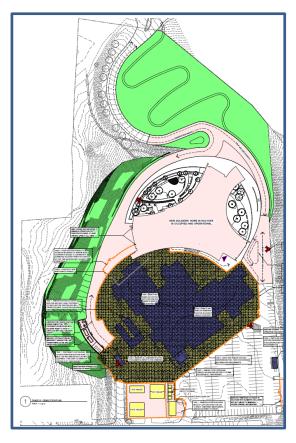



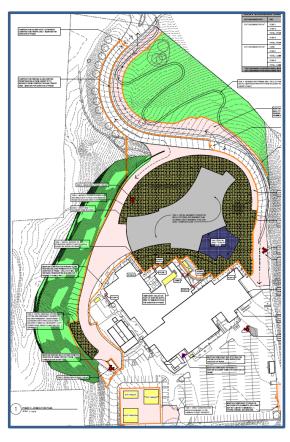

**Access Road** 

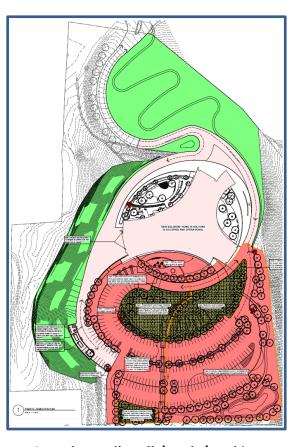

**Geo-Thermall Well / Park / Parking** 





# **QUESTIONS**





