

Massachusetts Department of Transportation

<MassDOT Project Info Number> <Short Project Description - City Names>

BL PDS Schedule Grouped by Area of Work



Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

◆

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023				2024				2025				2026				2027		
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1
HWY.200.020	32	Submit Functional Design Report	7/25/2024	7/25/2024																			
HWY.200.030	33	Review Functional Design Report	7/26/2024	10/23/2024																			
HWY.200.040	34	Approval of Functional Design Report	10/23/2024	10/23/2024																			
HWY.220	35	Design Justification Workbook (DJW)	12/9/2023	3/7/2024																			
HWY.220.010	36	Prepare Design Justification Workbook	12/9/2023	2/6/2024																			
HWY.220.020	37	Submit Design Justification Workbook	2/6/2024	2/6/2024																			
HWY.220.030	38	Review Design Justification Workbook	2/7/2024	3/7/2024																			
HWY.220.040	39	Complete Streets Engineer Concurrence	3/7/2024	3/7/2024																			
HWY.220.050	40	District Project Development Concurrence (DJW)	3/7/2024	3/7/2024																			
HWY.220.060	41	Approval of Design Justification Workbook by Chief Engineer	3/7/2024	3/7/2024																			
HWY.220.070	42	Submit DJW for Administrator/Secretary Review	2/6/2024	2/6/2024																			
HWY.220.080	43	Review of DJW by Administrator/Secretary	2/7/2024	3/7/2024																			
HWY.220.090	44	Approval of Design Justification Workbook by FHWA	3/7/2024	3/7/2024																			
HWY.220.100	45	Approval of Design Justification Workbook by	3/7/2024	3/7/2024																			
HWY.250	46	Pre-25% Design	4/4/2023	12/8/2023																			
HWY.250.010	47	Prepare and Submit Draft Project Scoping Checklist	4/4/2023	4/4/2023																			
HWY.250.020	48	Project Scoping Meeting	6/5/2023	6/5/2023																			
HWY.250.030	49	Prepare and Submit Final Project Scoping Checklist	6/6/2023	6/6/2023																			
HWY.250.040	50	Develop Reasonable Alternatives and Alternative Analysis	6/7/2023	7/6/2023																			
HWY.250.050	51	Prepare Pre-25% OTS Conceptual Design Package	7/7/2023	8/5/2023																			
HWY.250.060	52	Submit Pre-25% OTS Conceptual Design Package	10/5/2023	10/5/2023																			
HWY.250.070	53	Schedule Pre-25% OTS Review Meeting	10/6/2023	10/20/2023																			
HWY.250.080	54	Conduct Pre-25% OTS Review Meeting	10/23/2023	10/23/2023																			
HWY.250.090	55	Schedule Public Information Meeting	10/24/2023	12/7/2023																			

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

Massachusetts Department of Transportation

<MassDOT Project Info Number> <Short Project Description - City Names>

BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023				2024				2025				2026				2027		
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1
HWY.250.100	56	Conduct Public Information Meeting	12/8/2023	12/8/2023																			
HWY.275	57	Traffic and Safety	4/4/2023	8/7/2023																			
HWY.275.100	58	Intersection Control Evaluation (ICE)	4/4/2023	8/7/2023																			
HWY.275.100.44	59	Prepare ICE Stage 1	4/4/2023	4/5/2023																			
HWY.275.100.45	60	Submit ICE Stage 1	4/6/2023	4/6/2023																			
HWY.275.100.46	61	Review ICE Stage 1	4/7/2023	5/4/2023																			
HWY.275.100.47	62	Approve ICE Stage 1	5/5/2023	5/5/2023																			
HWY.275.100.48	63	Prepare ICE Stage 2	5/6/2023	6/4/2023																			
HWY.275.100.49	64	Submit ICE Stage 2	6/5/2023	6/5/2023																			
HWY.275.100.50	65	Review ICE Stage 2	6/6/2023	6/19/2023																			
HWY.275.100.51	66	Approve ICE Stage 2	6/20/2023	6/20/2023																			
HWY.275.100.52	67	Prepare ICE Stage 3	6/21/2023	7/20/2023																			
HWY.275.100.53	68	Submit ICE Stage 3	7/21/2023	7/21/2023																			
HWY.275.100.54	69	Review ICE Stage 3	7/22/2023	8/4/2023																			
HWY.275.100.55	70	Approve ICE Stage 3	8/7/2023	8/7/2023																			
HWY.275.200	71	Roadway Safety Audit (RSA)	4/4/2023	7/5/2023																			
HWY.275.200.56	72	Prepare RSA Background Materials	4/4/2023	6/2/2023																			
HWY.275.200.57	73	Conduct RSA	6/5/2023	6/5/2023																			
HWY.275.200.58	74	Prepare Draft RSA Report	6/6/2023	6/10/2023																			
HWY.275.200.59	75	Submit Draft RSA Report	6/12/2023	6/12/2023																			
HWY.275.200.60	76	Review Draft RSA Report	6/13/2023	6/17/2023																			
HWY.275.200.61	77	Prepare Final Draft RSA Report	6/18/2023	6/22/2023																			
HWY.275.200.62	78	Submit Final Draft RSA Report	6/23/2023	6/23/2023																			
HWY.275.200.63	79	Review Final Draft RSA Report	6/24/2023	6/28/2023																			
HWY.275.200.64	80	Revise and Resubmit Final RSA Report	6/29/2023	7/5/2023																			
HWY.300	81	25% Design Package	12/9/2023	11/23/2024																			
HWY.300.010	82	Prepare 25% Design Submission	12/9/2023	2/6/2024																			
HWY.300.020	83	Submit 25% Design Submission	7/25/2024	7/25/2024																			
HWY.300.030	84	Send to FHWA (if PODI)	7/25/2024	7/25/2024																			
HWY.300.040	85	Review 25% Design Submission	7/26/2024	10/23/2024																			
HWY.300.050	86	All Sections 25% Design Comments sent to DE	10/23/2024	10/23/2024																			

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

◆

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023				2024				2025				2026				2027		
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1
HWY.300.060	87	Prepare 25% Design Responses	10/24/2024	11/2/2024																			
HWY.300.070	88	Schedule Comment Resolution Meeting @25% (Full Team)	11/3/2024	11/23/2024																			
HWY.300.080	89	Comment Resolution Meeting @25% (Full Team)	11/23/2024	11/23/2024																			
HWY.302	90	Utility Coordination	11/4/2023	1/1/2024																			
HWY.302.010	91	Subsurface Utility Exploration	11/4/2023	11/18/2023																			
HWY.302.020	92	Schedule Utility Early Coordination Field Meeting	11/19/2023	12/2/2023																			
HWY.302.030	93	Utility Early Coordination Field Meetir	12/2/2023	12/2/2023																			
HWY.302.100	94	25% Third Party Utility Coordinatio	12/3/2023	1/1/2024																			
HWY.302.100.010	95	Prepare 25% Utility Plans	12/3/2023	1/1/2024																			
HWY.302.100.020	96	Submit 25% Utility Plans	1/1/2024	1/1/2024																			
HWY.352	97	Prepare for 25% Design Public Hearing	11/23/2024	12/4/2024																			
HWY.352.010	98	Submit DPH Request to District Project Development	11/23/2024	11/23/2024																			
HWY.352.020	99	Concurrence by District Project Deve	11/23/2024	11/23/2024																			
HWY.352.030	100	Prepare Hearing Notice	11/24/2024	11/30/2024																			
HWY.352.040	101	Submit Hearing Notice	11/30/2024	11/30/2024																			
HWY.352.050	102	Send DPH Request to Section Direct	12/1/2024	12/1/2024																			
HWY.352.060	103	Approval by Section Director	12/2/2024	12/4/2024																			
HWY.353	104	Conduct 25% Design Public Hearing	12/5/2024	2/14/2025																			
HWY.353.010	105	Schedule Public Hearing	12/5/2024	1/15/2025																			
HWY.353.020	106	Conduct Public Hearing	1/15/2025	1/15/2025																			
HWY.353.030	107	Respond to Comments (DPH)	1/16/2025	2/14/2025																			
HWY.375	108	25%/75% Design Package	12/9/2023	3/22/2024																			
HWY.375.010	109	Prepare 25%/75% Design Package	12/9/2023	2/6/2024																			
HWY.375.020	110	Submit 25%/75% Design Package	2/6/2024	2/6/2024																			
HWY.375.030	111	Review 25%/75% Design Package	2/7/2024	3/7/2024																			
HWY.375.040	112	All Sections 25%/75% Design Comments sent to DE	3/7/2024	3/7/2024																			
HWY.375.050	113	Prepare 25%/75% Design Responses	3/8/2024	3/17/2024																			

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

◆

Massachusetts Department of Transportation

<MassDOT Project Info Number> <Short Project Description - City Names>

BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023				2024				2025				2026				2027		
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1
HWY.375.060	114	Schedule Comment Resolution Meeting @25%/75% (Full Team)	3/18/2024	3/22/2024																			
HWY.375.070	115	Comment Resolution Meeting @25%/75% (Full Team)	3/22/2024	3/22/2024																			
HWY.400	116	75% Design Package	2/15/2025	6/24/2025																			
HWY.400.010	117	Prepare 75% Design Submission	2/15/2025	4/15/2025																			
HWY.400.020	118	Submit 75% Design Submission	4/15/2025	4/15/2025																			
HWY.400.030	119	Review 75% Design Submission	4/16/2025	5/15/2025																			
HWY.400.040	120	All Sections 75% Design Comments sent to DE	5/15/2025	5/15/2025																			
HWY.400.050	121	Prepare 75% Design Responses	5/16/2025	5/25/2025																			
HWY.400.060	122	Schedule Comment Resolution Meeting @75% (Full Team)	5/26/2025	5/30/2025																			
HWY.400.070	123	Comment Resolution Meeting @75% (Full Team)	6/24/2025	6/24/2025																			
HWY.400.100	124	75% Third Party Utility Coordination	2/15/2025	4/15/2025																			
HWY.400.100.010	125	Prepare 75% Utility Plans	2/15/2025	3/16/2025																			
HWY.400.100.020	126	Submit 75% Utility Plans	4/15/2025	4/15/2025																			
HWY.428	127	75% Contract Time Determination	3/17/2025	5/15/2025																			
HWY.428.010	128	Prepare 75% Contract Time Determination	3/17/2025	4/15/2025																			
HWY.428.020	129	Submit 75% Contract Time Determination	4/15/2025	4/15/2025																			
HWY.428.030	130	Review 75% Contract Time Determination	4/16/2025	5/15/2025																			
HWY.430	131	75%/100% Design Package	2/15/2025	5/30/2025																			
HWY.430.010	132	Prepare 75%/100% Design Package	2/15/2025	4/15/2025																			
HWY.430.020	133	Submit 75%/100% Design Package	4/15/2025	4/15/2025																			
HWY.430.030	134	Review 75%/100% Design Package	4/16/2025	5/15/2025																			
HWY.430.040	135	All Sections 75%/100% Design Comments sent to DE	5/15/2025	5/15/2025																			
HWY.430.050	136	Prepare 75%/100% Design Responses	5/16/2025	5/25/2025																			
HWY.430.060	137	Schedule Comment Resolution Meeting @75%/100% (Full Team)	5/26/2025	5/30/2025																			
HWY.430.070	138	Comment Resolution Meeting @75%/100% (Full Team)	5/30/2025	5/30/2025																			
HWY.450	139	100% Design Package	12/3/2023	12/3/2025																			

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

◆

Massachusetts Department of Transportation

<MassDOT Project Info Number> <Short Project Description - City Names>

BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023				2024				2025				2026				2027		
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1
HWY.450.010	140	Prepare 100% Design Submission	6/25/2025	8/23/2025																			
HWY.450.020	141	Submit 100% Design Submission	10/19/2025	10/19/2025																			
HWY.450.030	142	Review 100% Design Submission	10/20/2025	11/18/2025																			
HWY.450.040	143	All Sections 100% Design Comments sent to DE	11/18/2025	11/18/2025																			
HWY.450.050	144	Prepare 100% Design Responses	11/19/2025	11/28/2025																			
HWY.450.060	145	Schedule Comment Resolution Meeting @100% (Full Team)	11/29/2025	12/3/2025																			
HWY.450.070	146	Comment Resolution Meeting @100% (Full Team)	12/3/2025	12/3/2025																			
HWY.450.100	147	100% Third Party Utility Coordination	12/3/2023	7/24/2025																			
HWY.450.100.010	148	Prepare 100% Utility Plans	6/25/2025	7/24/2025																			
HWY.450.100.020	149	Submit 100% Utility Plans	7/24/2025	7/24/2025																			
HWY.450.100.030	150	Prepare Force Account Agreement	12/3/2023	3/1/2024																			
HWY.450.100.040	151	Prepare PUC Form	3/2/2024	3/31/2024																			
HWY.458	152	100% Contract Time Determination	7/25/2025	11/19/2025																			
HWY.458.010	153	Prepare 100% CTD utilizing PUC Form durations	7/25/2025	8/23/2025																			
HWY.458.020	154	Submit 100% Contract Time Determination	10/19/2025	10/19/2025																			
HWY.458.030	155	Review 100% Contract Time Determination	10/20/2025	11/18/2025																			
HWY.458.040	156	Request Construction Duration IOM from Area Engineer	11/19/2025	11/19/2025																			
HWY.470	157	100%/PSE Design Package	6/25/2025	10/7/2025																			
HWY.470.010	158	Prepare 100%/PSE Design Package	6/25/2025	8/23/2025																			
HWY.470.020	159	Submit 100%/PSE Design Package	8/23/2025	8/23/2025																			
HWY.470.030	160	Review 100%/PSE Design Package	8/24/2025	9/22/2025																			
HWY.470.040	161	All Sections 100%/PSE Design Comments sent to DE	9/22/2025	9/22/2025																			
HWY.470.050	162	Prepare 100%/PSE Design Responses	9/23/2025	10/2/2025																			
HWY.470.060	163	Schedule Comment Resolution Meeting @100%/PSE (Full Team)	10/3/2025	10/7/2025																			
HWY.470.070	164	Comment Resolution Meeting @100%/PSE (Full Team)	10/7/2025	10/7/2025																			

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

◆

Massachusetts Department of Transportation

<MassDOT Project Info Number> <Short Project Description - City Names>

BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023				2024				2025				2026				2027		
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1
HWY.800	165	PS&E Submittal	11/19/2025	9/18/2026													PS&E Submittal						
HWY.800.001	166	Request Federal Aid Number from F	11/19/2025	11/19/2025																			
HWY.800.002	167	FAPRO provides Federal Aid Numbe	11/20/2025	12/19/2025																			
HWY.800.010	168	Prepare PS&E Submission	12/5/2025	1/3/2026																			
HWY.800.020	169	Submit PS&E Submission	1/3/2026	1/3/2026																			
HWY.800.030	170	Review PS&E Submission	1/4/2026	1/18/2026																			
HWY.800.040	171	Send PS&E to FHWA (If Required)	1/5/2026	1/5/2026																			
HWY.800.050	172	FHWA Review PS&E Submission (If I	1/6/2026	2/4/2026																			
HWY.800.060	173	Approval of PS&E Submission	2/4/2026	2/4/2026																			
HWY.800.070	174	Prepare Advertising Documents for F	1/4/2026	1/14/2026																			
HWY.800.080	175	Review Advertising Documents by FA	9/8/2026	9/18/2026																			
HWY.800.090	176	Prepare Draft Contract Documents fo	2/5/2026	2/18/2026																			
HWY.800.100	177	Submit Draft Contract Documents to	2/25/2026	2/25/2026																			
HWY.800.110	178	Ready for Initial Review	2/26/2026	2/27/2026																			
HWY.800.120	179	Initial Review of Contract Documents	3/2/2026	3/11/2026																			
HWY.800.130	180	Prepare Bid Documents - Rev 1	3/12/2026	3/13/2026																			
HWY.800.140	181	Submit Bid Documents to Specs - Re	3/13/2026	3/13/2026																			
HWY.800.150	182	Ready For Final Review	3/16/2026	3/17/2026																			
HWY.800.160	183	Final Review of Bid Documents	3/18/2026	3/20/2026																			
HWY.800.170	184	Prepare CDSP Bid Package	3/23/2026	3/27/2026																			
HWY.800.180	185	Prepare Final Plans for Plans and Re	2/5/2026	2/18/2026																			
HWY.800.190	186	Submit Final Plans for Plans and Rec	2/19/2026	2/19/2026																			
HWY.800.200	187	Review Final Plans by Plans and Rec	2/20/2026	3/5/2026																			
HWY.800.210	188	Approve Final Plans by Plans and Re	3/5/2026	3/5/2026																			
HWY.807	189	PS&E Contract Time Determination	12/5/2025	2/6/2026													PS&E Contract Time Determination						
HWY.807.010	190	Prepare PS&E CTD utilizing PUC For	12/5/2025	12/19/2025																			
HWY.807.020	191	Submit PS&E CTD utilizing PUC Forr	12/22/2025	12/22/2025																			
HWY.807.030	192	Review PS&E CTD utilizing PUC For	1/4/2026	1/18/2026																			
HWY.807.040	193	Area Engineer Provides Construction Duration IOM to PM	1/19/2026	2/6/2026																			
BRD	194	Bridge Design	11/4/2023	12/4/2025					Bridge Design														
BRD.705	195	Preliminary Structures Report	1/13/2024	4/11/2024					Preliminary Structures Report														

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

◆

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023				2024				2025				2026				2027		
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1
BRD.705.010	196	Prepare Preliminary Structures Repoi	1/13/2024	3/12/2024																			
BRD.705.020	197	Submit Preliminary Structures Report	3/12/2024	3/12/2024																			
BRD.705.030	198	Review Preliminary Structures Repor	3/13/2024	4/11/2024																			
BRD.705.040	199	Send Preliminary Structures Report Comments to DE	4/11/2024	4/11/2024																			
BRD.705.050	200	Approval of Preliminary Structures Re	4/11/2024	4/11/2024																			
BRD.706	201	Bridge Type Selection Worksheet	4/12/2024	6/10/2024																			
BRD.706.010	202	Prepare Type Selection Worksheet	4/12/2024	5/11/2024																			
BRD.706.020	203	Submit Type Selection Worksheet	5/11/2024	5/11/2024																			
BRD.706.030	204	Review Type Selection Worksheet	5/12/2024	6/10/2024																			
BRD.706.040	205	Send Type Selection Worksheet Comments to DE	6/10/2024	6/10/2024																			
BRD.706.050	206	Approval of Type Selection Workshee	6/10/2024	6/10/2024																			
BRD.708	207	Preliminary Hydraulic Analysis and F	2/12/2024	12/24/2024																			
BRD.708.010	208	Prepare Preliminary Hydraulic Analys	2/12/2024	5/11/2024																			
BRD.708.020	209	Prepare Hydraulic Report	11/25/2024	12/24/2024																			
BRD.708.030	210	Send Hydraulic Report to DE	12/24/2024	12/24/2024																			
BRD.600	211	Geotechnical Design	11/4/2023	8/4/2024																			
BRD.600.010	212	Prepare Boring and Probe Layout Pla	11/4/2023	12/3/2023																			
BRD.600.020	213	Submit Boring and Probe Layout Plar	12/3/2023	12/3/2023																			
BRD.600.030	214	Review Boring and Probe Layout Plar	12/4/2023	12/13/2023																			
BRD.600.040	215	Perform Probes and Borings/Soil Samples for Hydraulics Analysis	12/14/2023	1/12/2024																			
BRD.600.050	216	Prepare and Submit Soil Sample Report for Hydraulics Analysis	1/13/2024	2/11/2024																			
BRD.600.060	217	Prepare Geotechnical Report	1/13/2024	3/12/2024																			
BRD.600.070	218	Submit Geotechnical Report	7/25/2024	7/25/2024																			
BRD.600.080	219	Review Geotechnical Report	7/26/2024	8/4/2024																			
BRD.600.090	220	Approval of Geotech Report	8/4/2024	8/4/2024																			
BRD.710	221	Bridge Sketch Plan Submittal	6/11/2024	11/24/2024																			
BRD.710.010	222	Prepare Bridge Sketch Plans	6/11/2024	7/25/2024																			

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

Massachusetts Department of Transportation

<MassDOT Project Info Number> <Short Project Description - City Names>

BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023				2024				2025				2026				2027			
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	
BRD.710.020	223	Submit Bridge Sketch Plans	7/25/2024	7/25/2024	◆ Submit Bridge Sketch Plans																			
BRD.710.030	224	Review Bridge Sketch Plans	7/26/2024	10/23/2024																				
BRD.710.040	225	Send Sketch Plan Comments to DE	10/23/2024	10/23/2024																				
BRD.710.050	226	Prepare Sketch Plan Design Respons	10/24/2024	11/2/2024																				
BRD.710.060	227	Comment Resolution Meeting @ Ske	11/24/2024	11/24/2024																				
BRD.710.070	228	Approval of Bridge Sketch Plans	11/24/2024	11/24/2024	◆ Approval of Bridge Sketch Plans																			
BRD.755	229	Bridge Submission-1st Structural	12/25/2024	6/25/2025	Bridge Submission-1st Structural																			
BRD.755.010	230	Prepare Bridge Submission-1st Struc	12/25/2024	2/22/2025																				
BRD.755.020	231	Submit Bridge Submission-1st Struct	4/15/2025	4/15/2025	◆ Submit Bridge Submission-1st Structural Plans																			
BRD.755.030	232	Review Bridge Submission-1st Struct	4/16/2025	6/14/2025																				
BRD.755.040	233	Send 1st Structural Comments to D E	6/14/2025	6/14/2025																				
BRD.755.050	234	Prepare 1st Structural Design Respo	6/15/2025	6/24/2025																				
BRD.755.060	235	Comment Resolution Meeting @ 1st	6/25/2025	6/25/2025																				
BRD.758	236	Bridge Submission-2nd Structural	6/26/2025	12/4/2025	Bridge Submission-2nd Structural																			
BRD.758.010	237	Prepare Bridge Submission-2nd Structural Plans	6/26/2025	8/9/2025																				
BRD.758.020	238	Submit Bridge Submission-2nd Struc	10/19/2025	10/19/2025	◆ Submit Bridge Submission-2nd Structural Plan																			
BRD.758.030	239	Review Bridge Submission-2nd Struc	10/20/2025	11/18/2025																				
BRD.758.040	240	Send 2nd Structural Review Commer	11/18/2025	11/18/2025																				
BRD.758.050	241	Prepare 2nd Structural Design Respc	11/19/2025	11/28/2025																				
BRD.758.060	242	Comment Resolution Meeting @ 2nd	12/4/2025	12/4/2025																				
ENV	243	Environmental	4/5/2023	8/15/2027	Environmental Review Checklist (ERC)																			
ENV.MS	244	Environmental Milestones	1/17/2026	8/15/2026											Environmental Milestones									
ENV.MS.010	245	Wetland Permits Filed	1/17/2026	1/17/2026											◆ Wetland Permits Filed									
ENV.MS.020	246	Issue Environmental Clearance	8/15/2026	8/15/2026											◆ Issue Environmental Clear									
ENV.150	247	Environmental Review Checklist (ERC)	4/5/2023	5/7/2023																				
ENV.150.010	248	Assign Environmental Analyst	4/5/2023	4/5/2023																				
ENV.150.020	249	Prepare Draft Environmental Review Checklist (ERC) (formerly EECC)	4/6/2023	5/5/2023																				
ENV.150.030	250	Prepare Final Environmental Review Checklist (ERC)	5/6/2023	5/6/2023																				
ENV.150.040	251	Prepare Response to ERC	5/7/2023	5/7/2023																				

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023				2024				2025				2026				2027		
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1
ENV.151	252	25% Environmental Coordination	6/6/2023	11/23/2024	25% Environmental Coordination																		
ENV.151.010	253	Perform 25% Environmental Coordination	6/6/2023	8/4/2023																			
ENV.151.020	254	Submit 25% Environmental Coordination	7/25/2024	7/25/2024																			
ENV.151.030	255	Review 25% Environmental Coordination	7/26/2024	8/24/2024																			
ENV.151.040	256	Approve 25% Environmental Coordination for DPH	11/23/2024	11/23/2024																			
ENV.152	257	Historic / Archeology (Section 106) Review	7/26/2024	10/23/2024																			
ENV.152.010	258	Conduct Historic Impact Analysis	7/26/2024	8/24/2024																			
ENV.152.020	259	No Effect Finding Determined	8/25/2024	9/23/2024																			
ENV.152.030	260	Submit No Effect Finding to Agency	9/23/2024	9/23/2024																			
ENV.152.040	261	Agency Review of No Effect Finding	9/24/2024	10/23/2024																			
ENV.152.050	262	Sec 106 Approve No Effect Finding	10/23/2024	10/23/2024																			
ENV.152.060	263	Section 106 Cleared	10/23/2024	10/23/2024																			
ENV.173	264	Section 4(f) De Minimis	7/26/2024	9/30/2024																			
ENV.173.010	265	Prepare 4(f) De Minimis	7/26/2024	8/24/2024																			
ENV.173.020	266	Publication of Legal Notice	8/25/2024	9/8/2024																			
ENV.173.021	267	Submit De Minimis	9/8/2024	9/8/2024																			
ENV.173.030	268	Official w/Jurisdiction App of De Minimis	9/9/2024	9/23/2024																			
ENV.173.040	269	FHWA Approval of De Minimis	9/24/2024	9/30/2024																			
ENV.173.050	270	Section 4F Cleared	9/30/2024	9/30/2024																			
ENV.190	271	Section 7 (Endangered Species Act)	11/24/2024	5/7/2025																			
ENV.190.010	272	Perform Section 7 Review	11/24/2024	1/22/2025																			
ENV.190.020	273	Submit Section 7	2/24/2025	2/24/2025																			
ENV.190.030	274	Review Section 7	2/25/2025	3/26/2025																			
ENV.190.040	275	Comments to PE/DE for Section 7	3/26/2025	3/26/2025																			
ENV.190.050	276	Review type-programatic or individual consultation for Section 7	3/27/2025	5/7/2025																			
ENV.190.060	277	Section 7 - NFMS Cleared	5/7/2025	5/7/2025																			
ENV.190.070	278	Section 7 - US Fish and Wildlife Service Cleared	5/7/2025	5/7/2025																			
ENV.188	279	Noise Study	2/15/2025	5/15/2025																			
ENV.188.010	280	Perform Noise Study	2/15/2025	4/15/2025																			

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task


Path Successor Milestone Task

◆

Massachusetts Department of Transportation

<MassDOT Project Info Number> <Short Project Description - City Names>

BL PDS Schedule Grouped by Area of Work

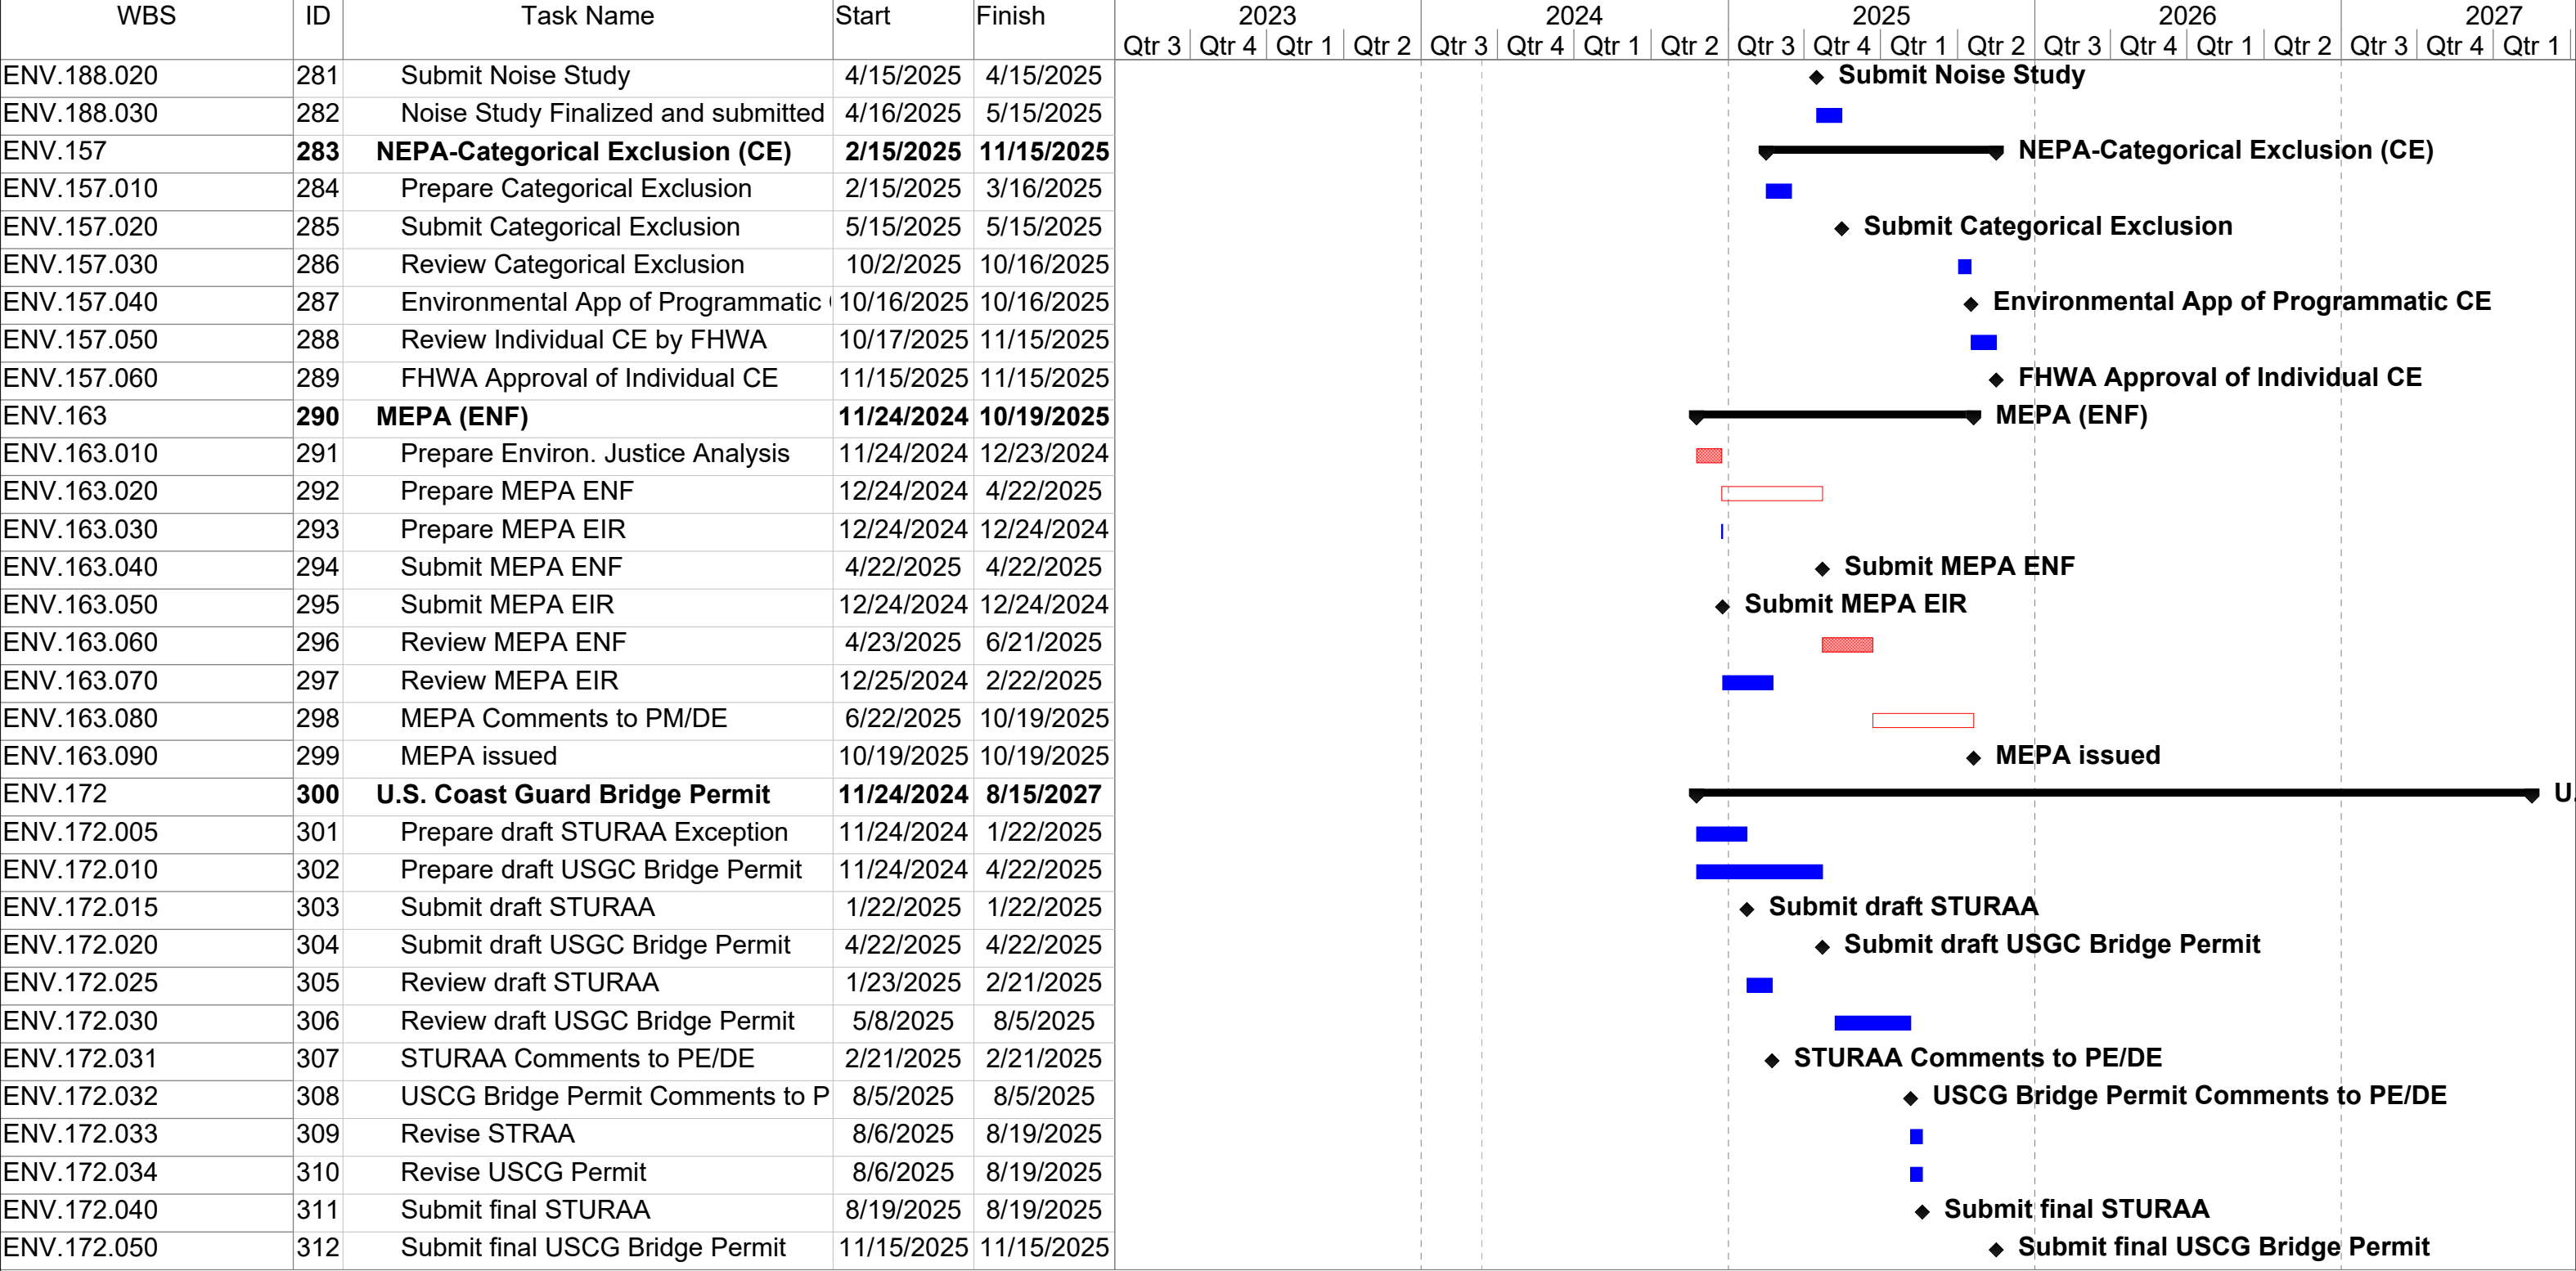

Task

Milestone

◆

Summary


Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work

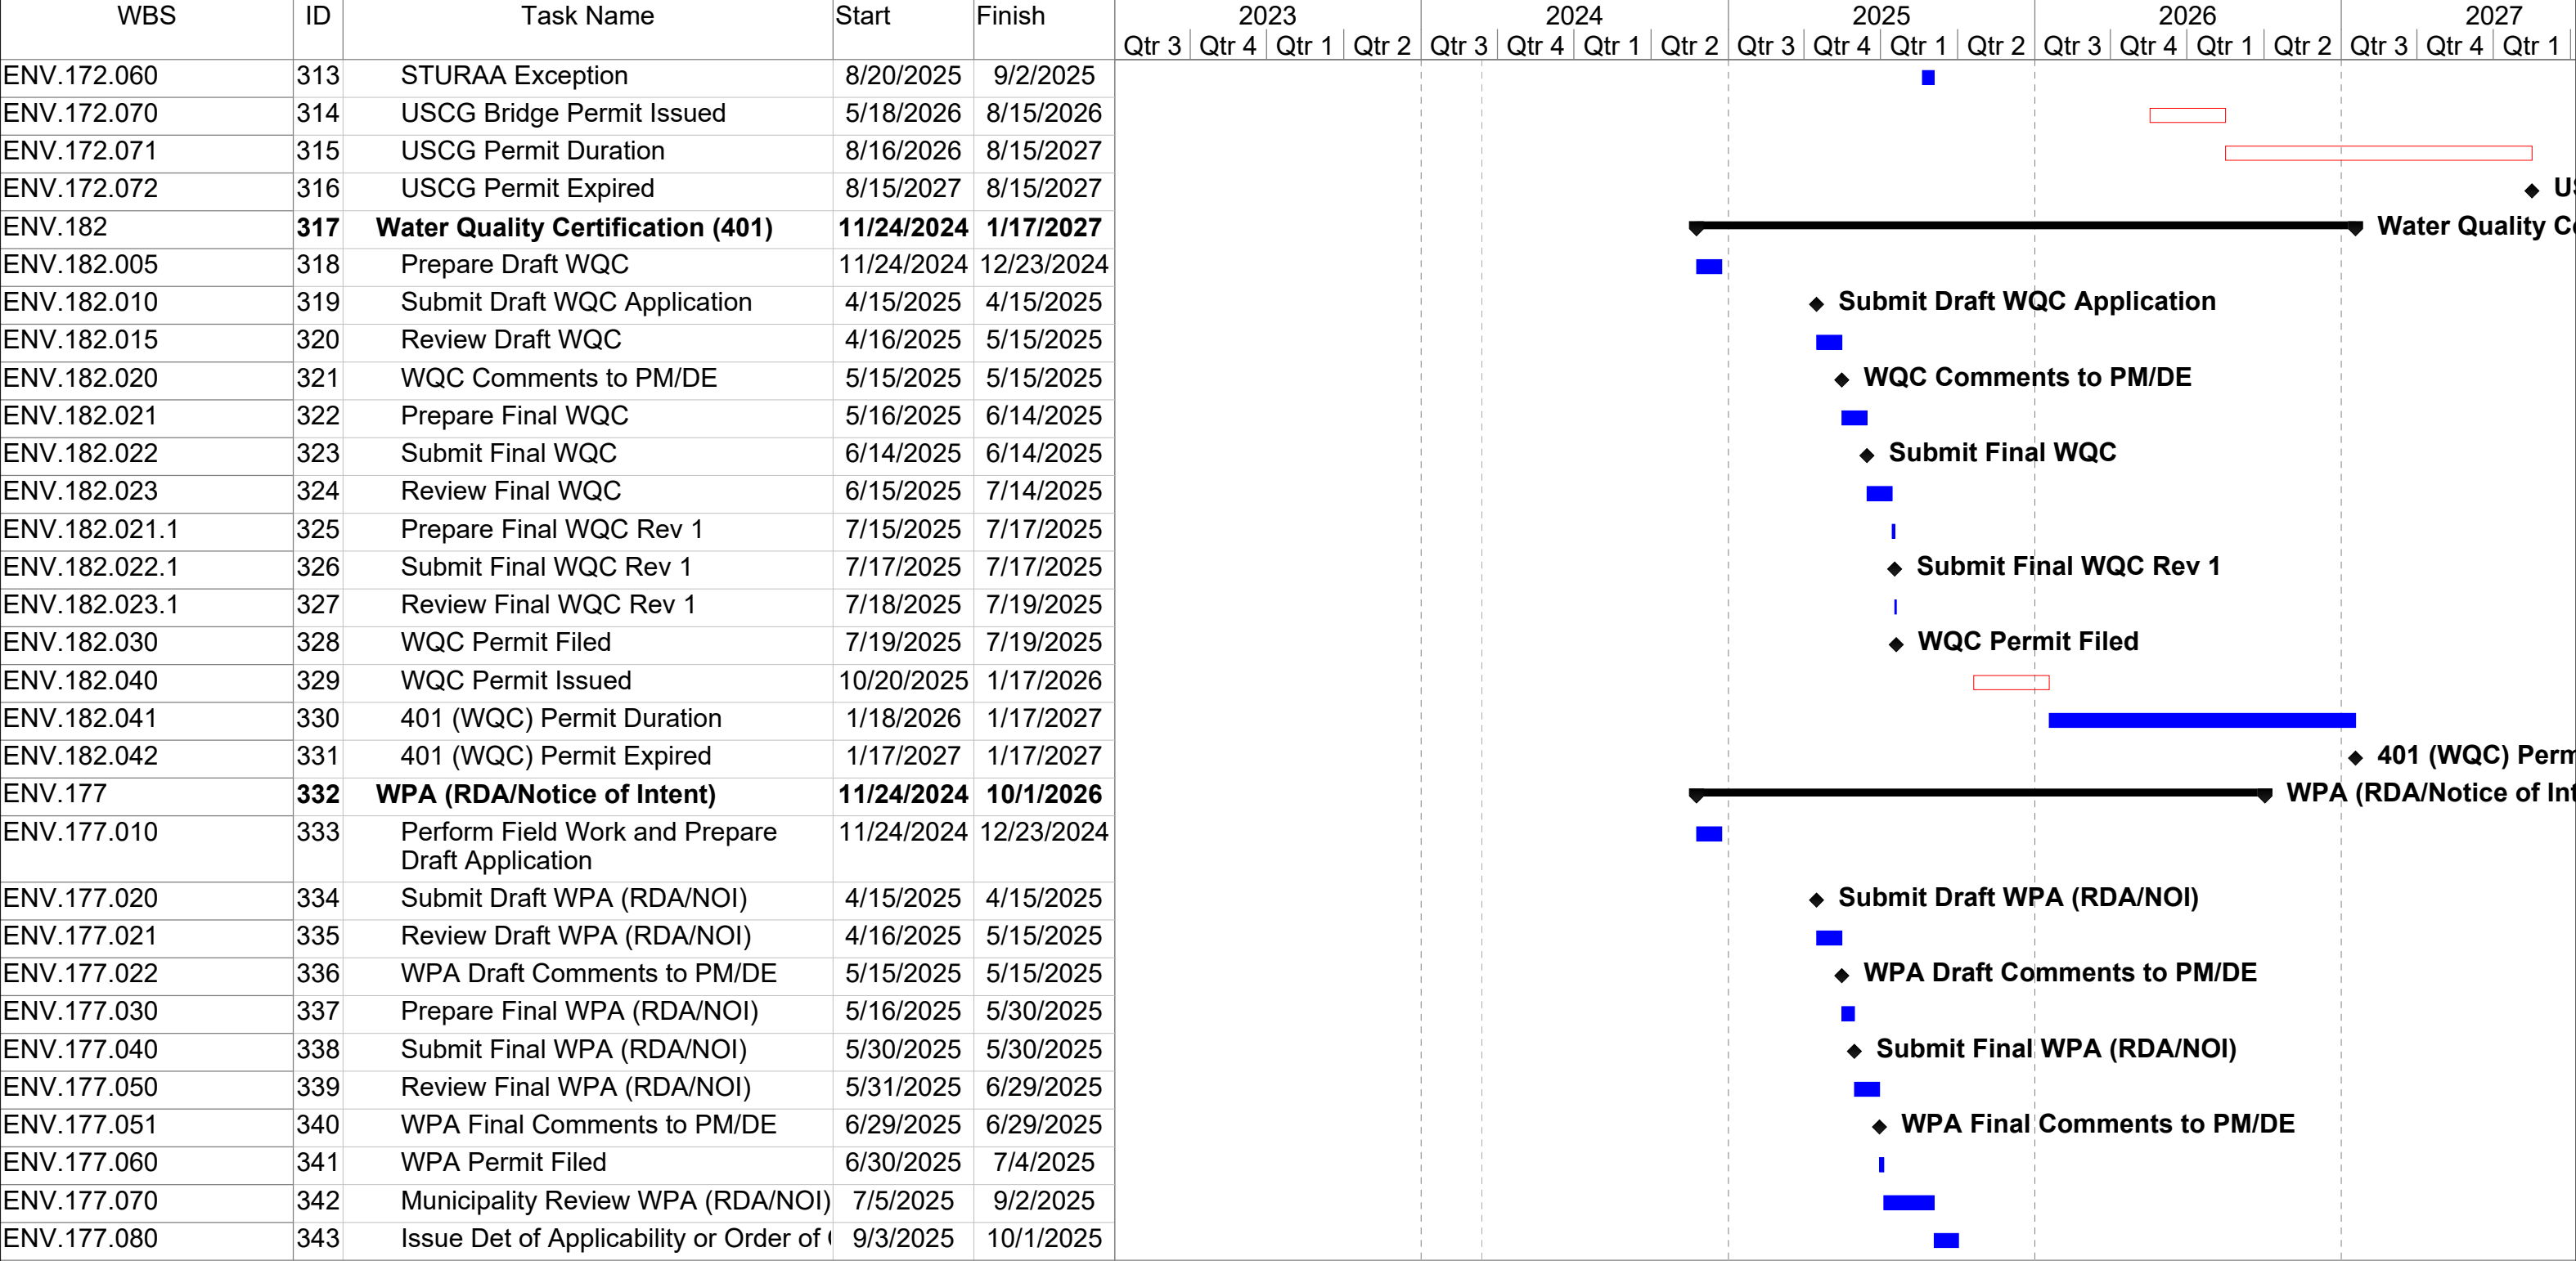

Task

Milestone

◆

Summary

Critical Path


Path Successor Normal Task

Path Successor Summary Task


Path Successor Milestone Task

◆

MassDOT
Massachusetts Department of Transportation
Highway Division

Task		Summary		Path Successor Normal Task		Path Successor Milestone Task	
Milestone		Critical Path		Path Successor Summary Task			

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work

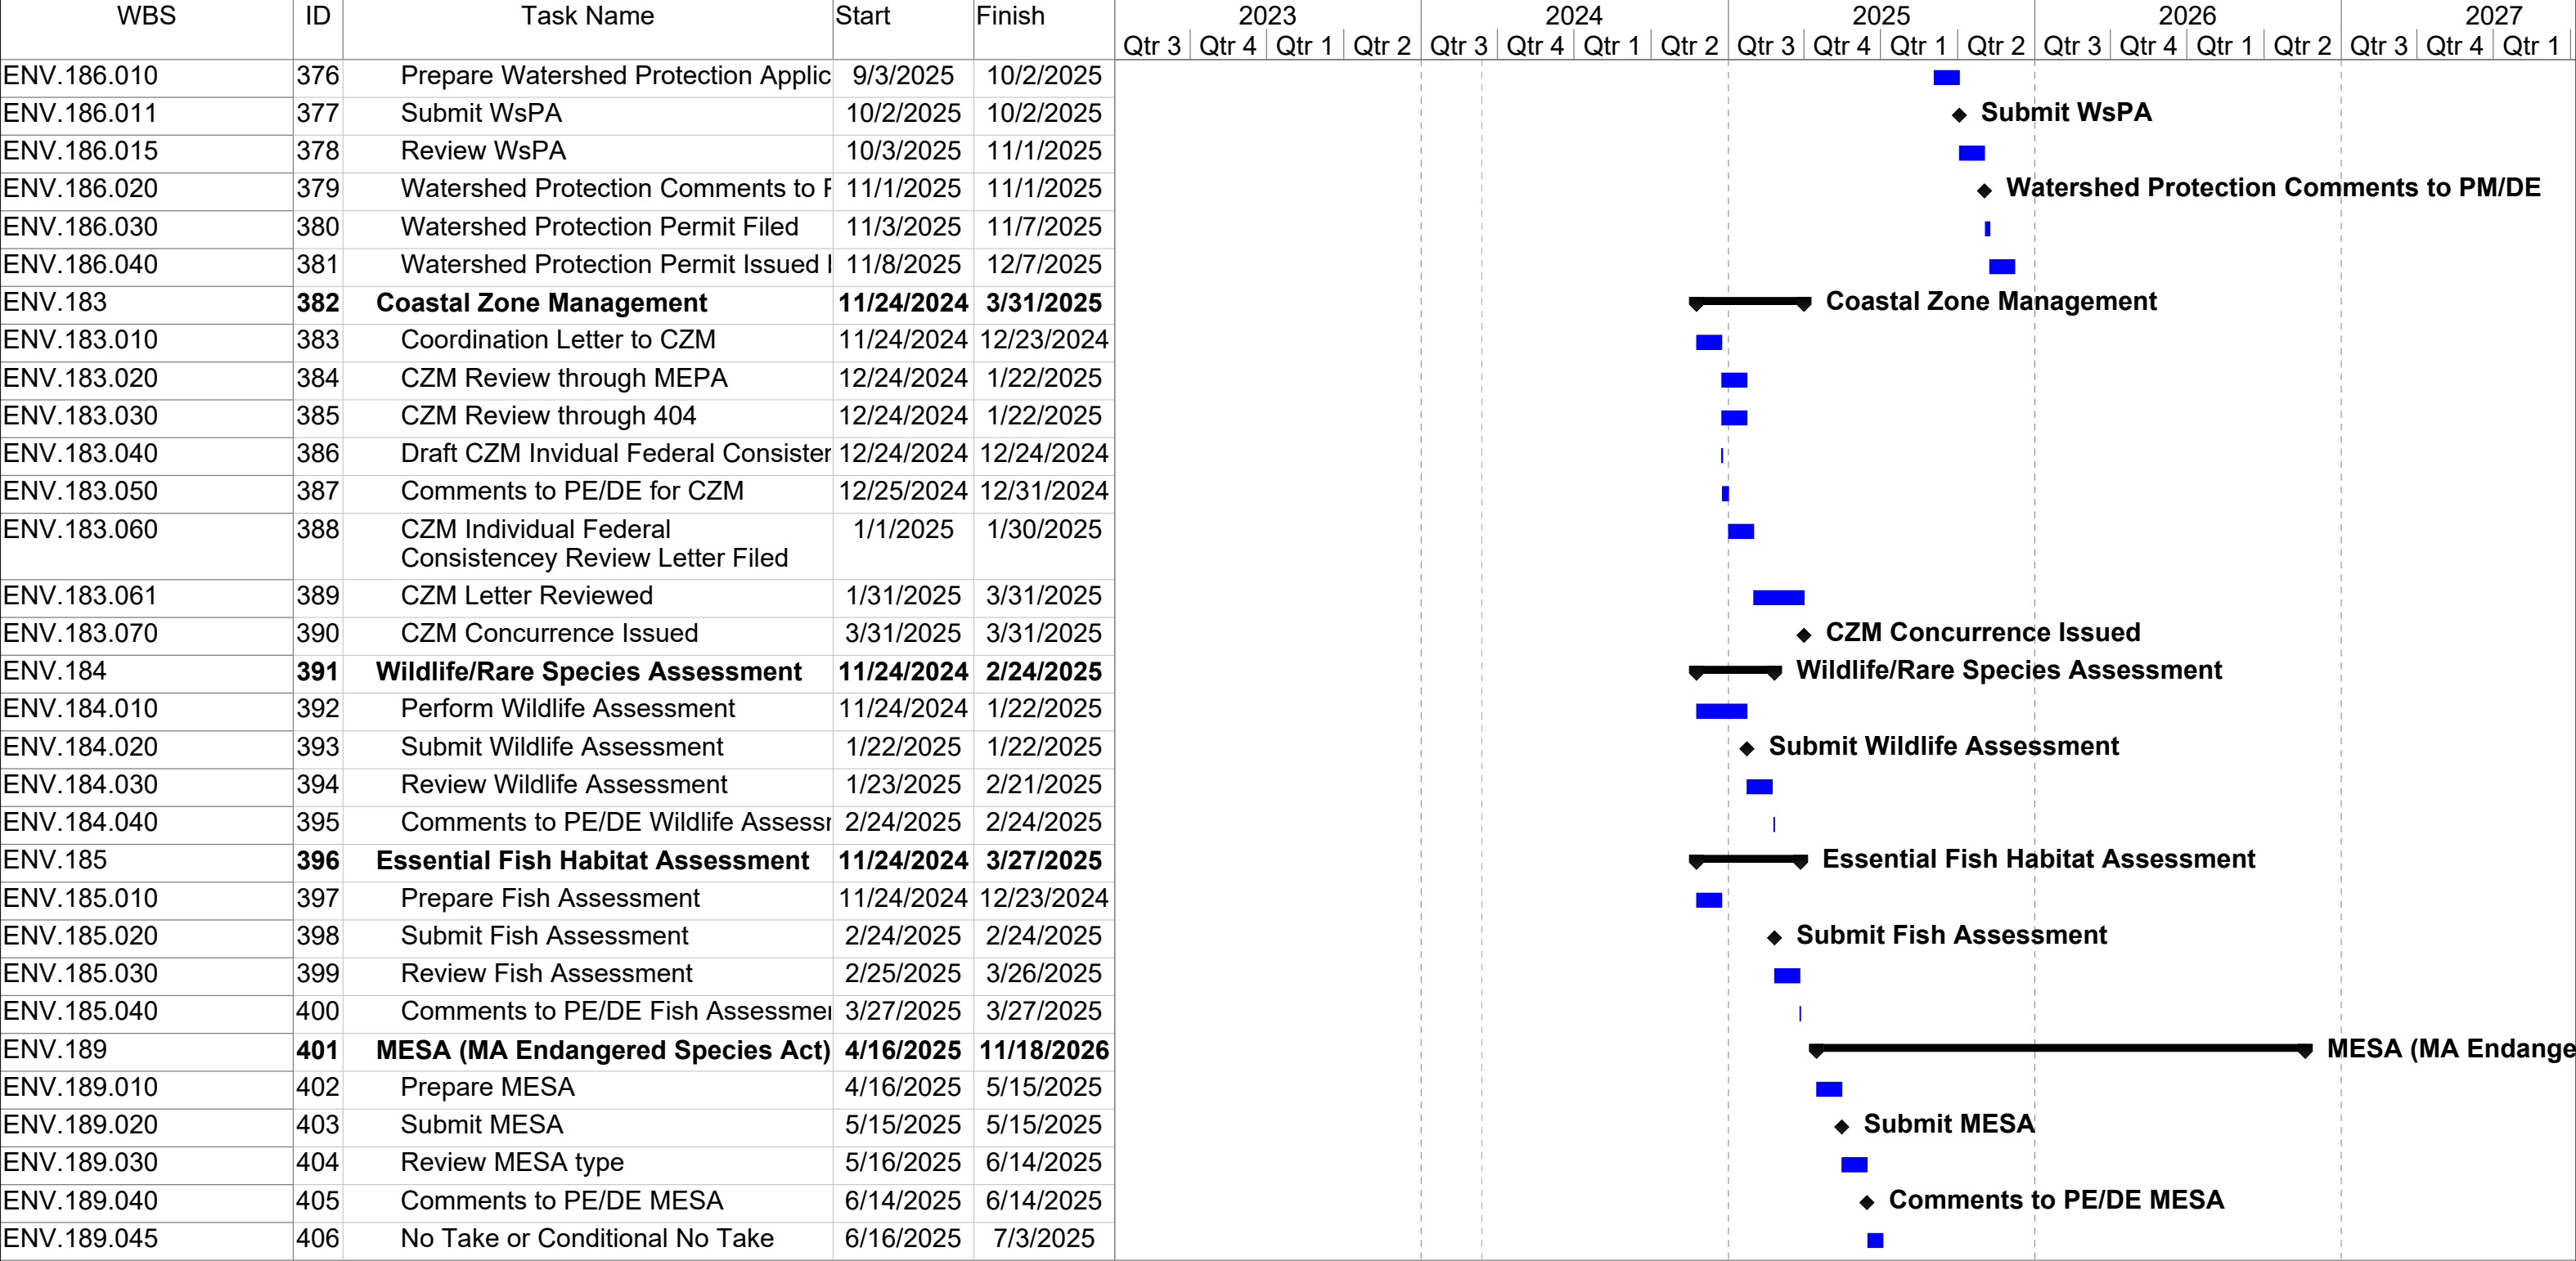

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task


Path Successor Milestone Task

◆

Massachusetts Department of Transportation

<MassDOT Project Info Number> <Short Project Description - City Names>

BL PDS Schedule Grouped by Area of Work

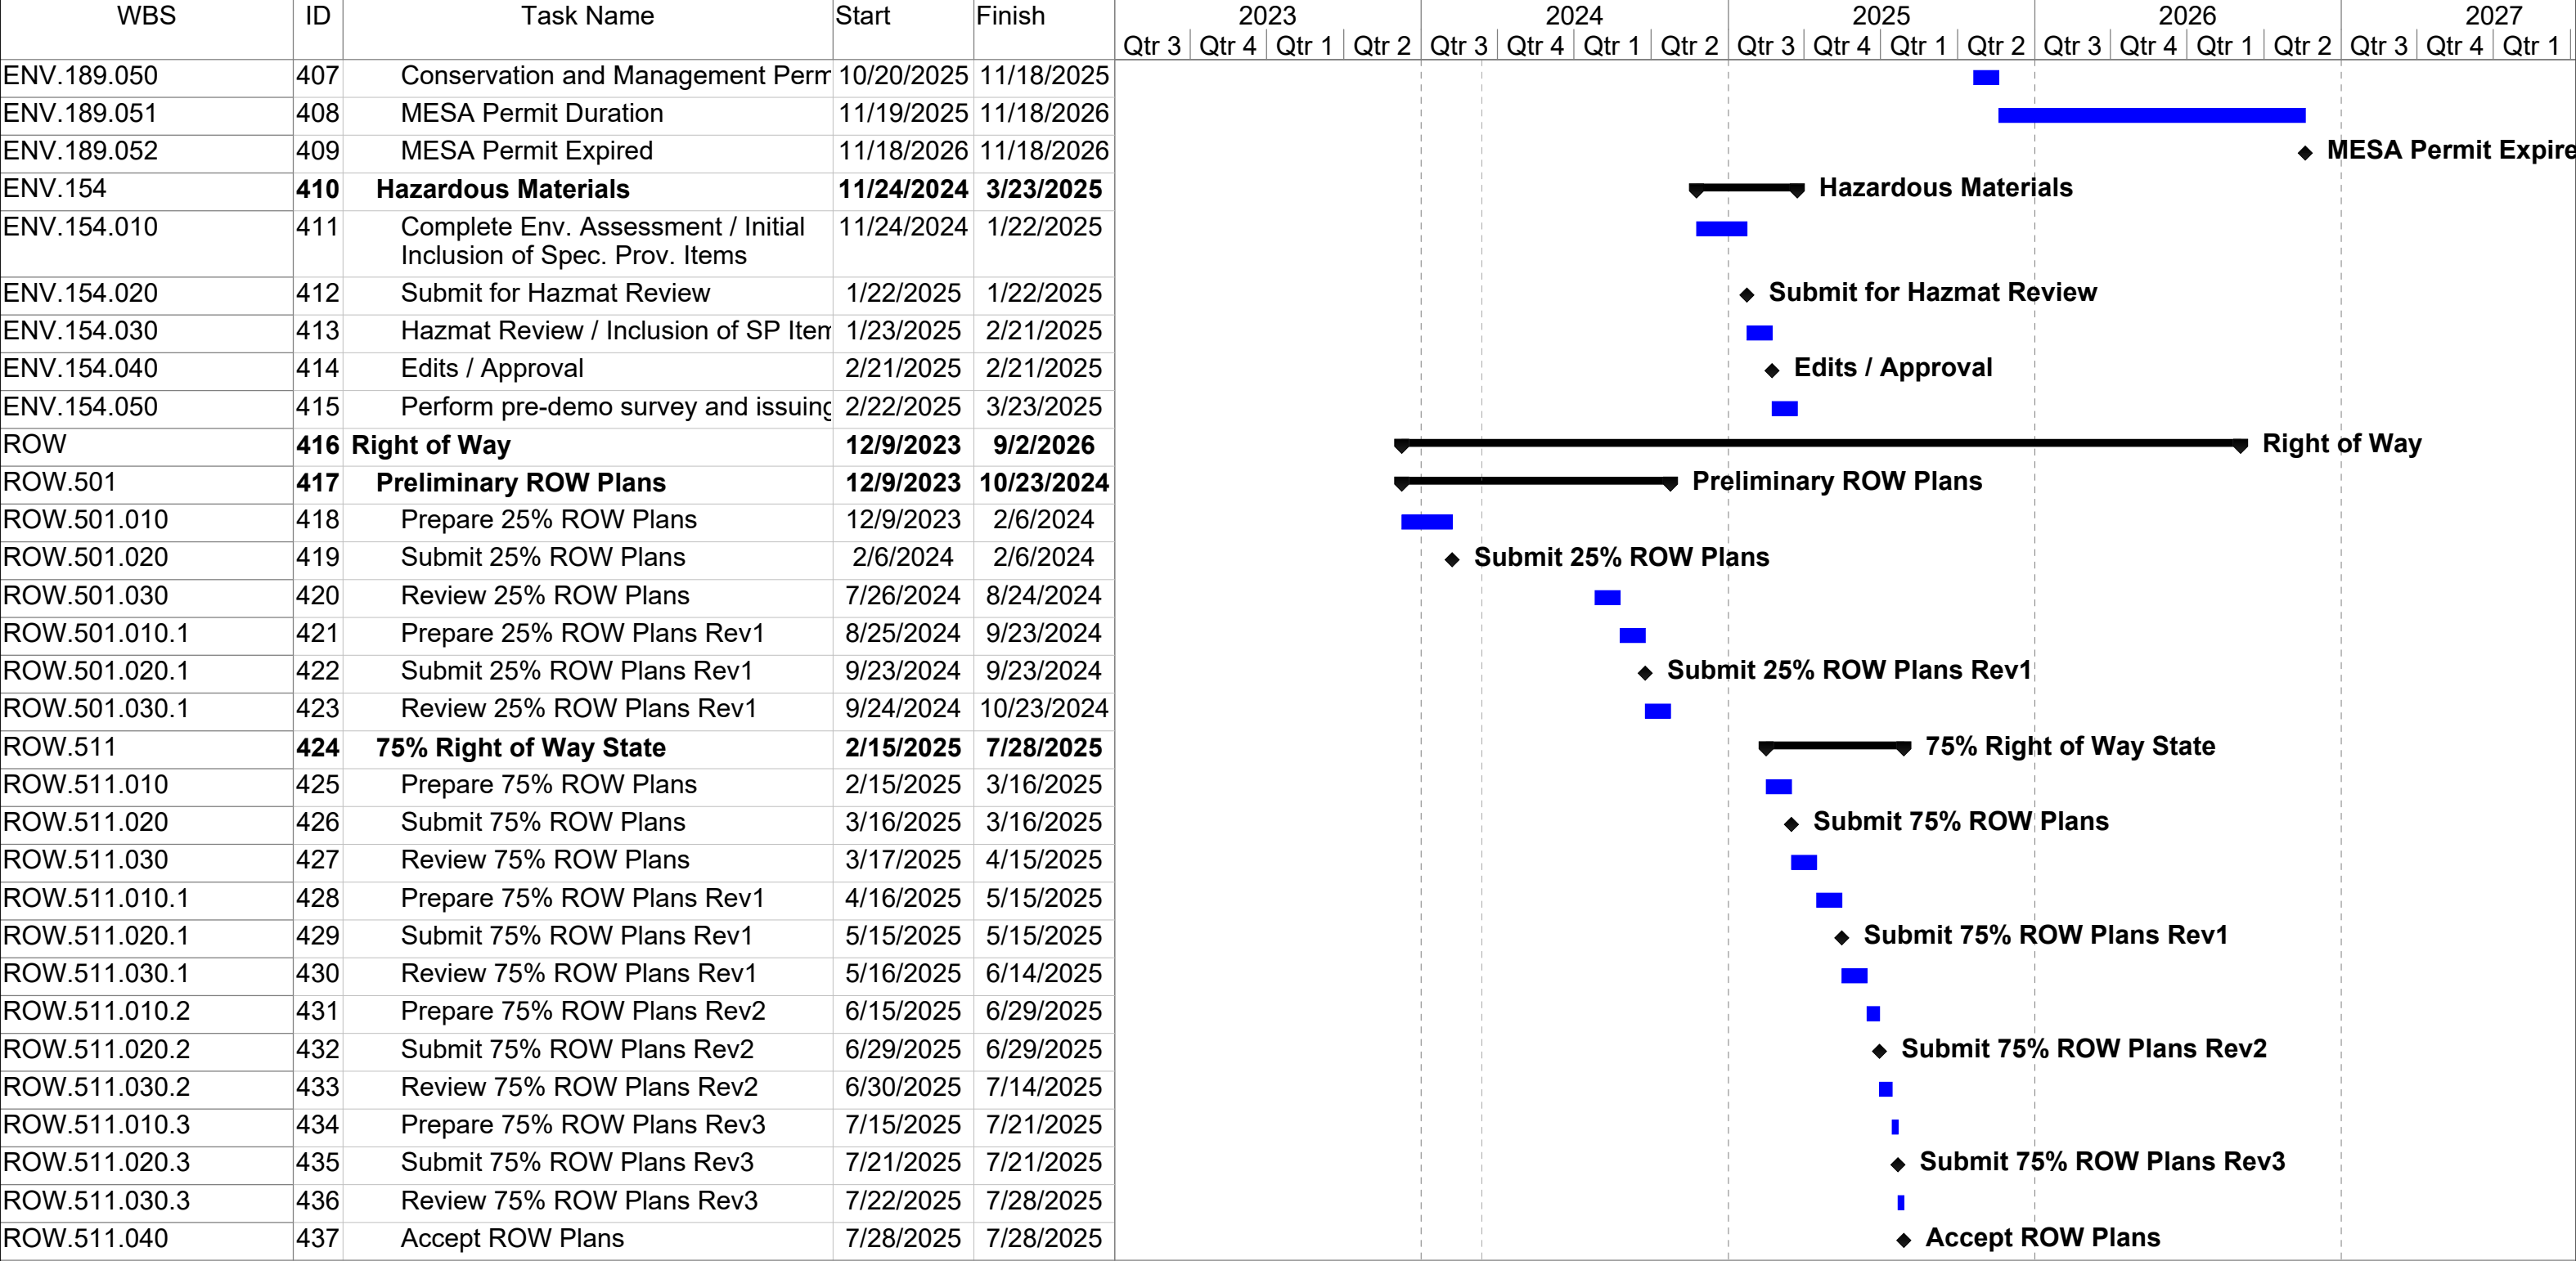

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

◆

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023				2024				2025				2026				2027			
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2
ROW.502	438	Acquisition Process - 100% through	7/26/2024	9/2/2026							◆ Acquisition Process - 100%													
ROW.502.01	439	State ROW Acquisition Process	7/26/2024	9/2/2026							◆ State ROW Acquisition P													
ROW.502.01.010	440	Perform Title Exams	7/29/2025	9/26/2025																				
ROW.502.01.020	441	Contact Property Owners	7/26/2024	8/14/2024																				
ROW.502.01.030	442	Property Interviews	9/27/2025	11/25/2025																				
ROW.502.01.040	443	Perform Appraisals	11/26/2025	2/23/2026																				
ROW.502.01.050	444	Prepare Draft Layout Taking Plans & Instrument (TPI)	7/29/2025	10/26/2025																				
ROW.502.01.060	445	Submit Draft Layout TPIs	10/26/2025	10/26/2025																				
ROW.502.01.070	446	Review Draft Layout TPIs	10/27/2025	12/10/2025																				
ROW.502.01.080	447	Approve Layout Taking Plans	12/10/2025	12/10/2025																				
ROW.502.01.090	448	Offer, Negotiations, Record & File	2/24/2026	4/29/2026																				
ROW.502.01.100	449	Payment; Issue ROW Certificate	4/30/2026	9/2/2026																				
ROW.502.03	450	Article 97 Proceedings	7/28/2025	7/28/2025																				
ROW.502.03.010	451	Article 97 Proceedings	7/28/2025	7/28/2025																				

Task

Milestone

◆

Summary

Critical Path

◆

Path Successor Normal Task

Path Successor Summary Task

◆

Path Successor Milestone Task
