

Agenda

Project Updates

- Project/Schedule Update
- Work in Progress
- Project MBE/WBE Participation Plan
- Project VBE Participation Plan

2

- Business Participation Payment Report
- Workforce Hours Report
- Ongoing Outreach
- Questions







Phase 1 Milestone Schedule

Scope	Planned
Temp Weather Tight (Level 2-5)	2/21/2025
Temp Weather Tight (Level 2 & Above)	6/24/2025
Permanent Power Available	9/11/2025
Building Weather Tight	3/20/2026
MDFs and IDFs Turned over to Owner	5/8/2026
Owner's Network Availability	7/8/2026
Complete Fire Alarm Testing	7/28/2026
Start FF&E	9/8/2026
Certificate of Occupancy	11/2/2026
Phase 1 Substantial Completion	11/9/2026







Work in Progress – Overall Site










Work in Progress – Roofing installation ongoing and AHU installed

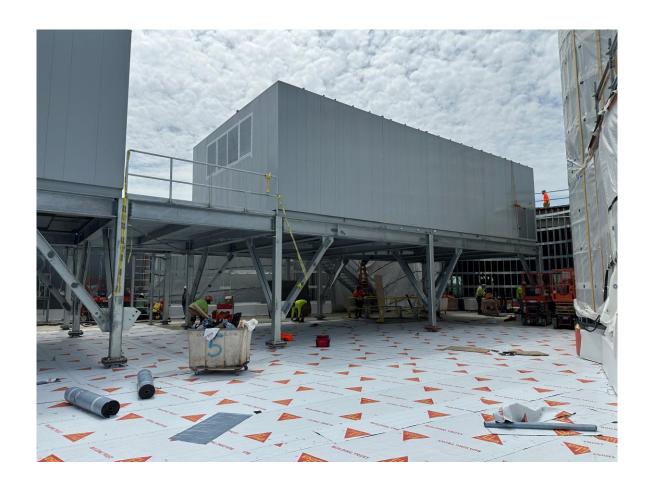








Work in Progress – Masonry installation continues

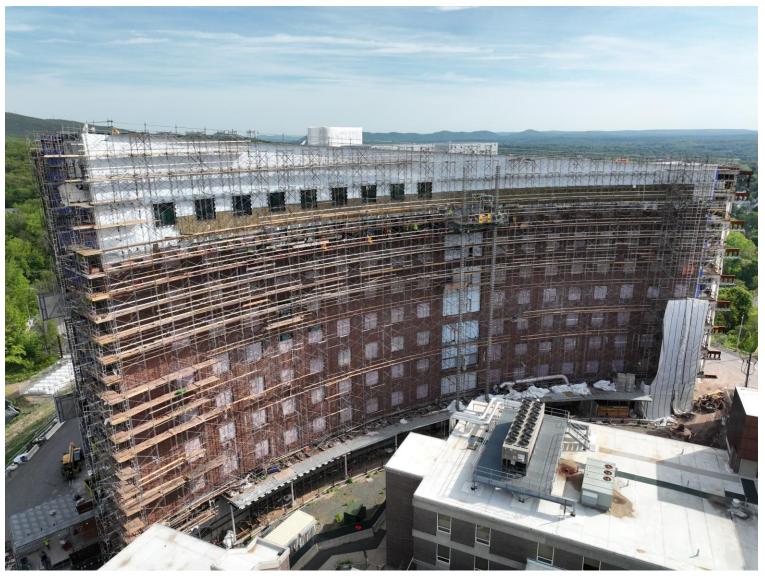







Work in Progress – Mockups review ongoing









Work in Progress – MEP Installation ongoing









8

Project MBE/WBE Participation Plan

Total GMP \$401,558,505

9

Contract Goals

MBE \$18,873,250

WBE \$30,920,005

MBE

4.7%

WBE

7.7%

Current Awards

MBE \$17,965,691

WBE \$32,045,461

MBE

4.5%

WBE

8.0%







Project VBE Participation Plan

Total GMP \$401,558,505

Contract Goals

VBE \$12,046,755

VBE

3.0%

Current Awards

VBE \$15,197,900

VBE

3.8%





MBE Participation – Paid through DCMS March Audit 2025

Bid Package Description	Prime / Filed Sub				Current Subcontract Value	MBE Paid to Date	Percent to Full Subcontract	Percent to Goal
Prime Contracts								
Demolition & Abatement - Dorm & Chiller	American Environmental, Inc.				\$ 610,776.00	\$ 601,298.20	98.4%	0.1%
Demolition & Abatement - Main	Not yet identified				\$ -	\$ -	0.0%	0.0%
Roofing and Flashing	Titan Roofing, Inc.				\$ 3,383,129.00	\$ 110,200.00	3.3%	0.0%
Tier Packages (Trade-Description)	Tier Subcontractor							
Concrete Prime - Tier 2 Installation of Reinforcing	Regis Steel Corp				\$ 1,215,000.00	\$ 889,586.35	73.2%	0.2%
Structural Steel - Tier 3 Welding	Trident Production Welding				\$ 850,000.00	\$ 808,421.36	95.1%	0.2%
Fireproofing Prime - Tier 2 Labor for Carpentry Fireproofing Support	Triple J Drywall & Carpentry, Inc.				\$ 90,000.00	\$ 90,000.00	100.0%	0.0%
Drywall Prime - Tier 2 Furnishing Labor For Taping/Carpentry Support	Scorpions Contracting, Inc.				\$ 23,650.00	\$ -	0.0%	0.0%
Drywall Prime - Tier 2 Furnishing Labor For Taping	American Finish Systems, Inc.				\$ 1,480,000.00	\$ -	0.0%	0.0%
Acoustical Tile Prime - Tier 2 Furnishing Labor For Carpentry Support	Triple J Drywall & Carpentry, Inc.				\$ 72,000.00	\$ •	0.0%	0.0%
Food Service Equipment Prime - Tier 2 Sheetmetal installation	Titan Roofing, Inc.				\$ 100,000.00	\$ -	0.0%	0.0%
Plumbing Prime - Tier 2 Furnish & Installation of Plumbing Insulation	Kim Industries, Inc.				\$ 1,116,000.00	\$ -	0.0%	0.0%
HVAC Prime - Tier 2 Material and Field Labor	Kim Industries, Inc.				\$ 3,975,000.00	\$ 85,500.00	2.2%	0.0%
Electrical Prime - Tier 2 Furnish & Install Systems	KB-Mac, Inc.				\$ 3,032,664.00	\$ 997,500.00	32.9%	0.2%
Earthwork Prime - Tier 2 Trucking of Materials To & From the Site	C&C Contractors, LLC				\$ 1,162,000.00	\$ 860,101.25	74.0%	0.2%
Earthwork Prime - Tier 2 Installation of Reinforcing	Regis Steel Corp				\$ 100,000.00	\$ 45,318.56	45.3%	0.0%
Earthwork Prime - Tier 2 Furnish & Install Asphalt Paving	Don Martin Corp				\$ 300,000.00	\$ 369,437.57	123.1%	0.1%
Material Only (Prime Trade-Description)	Material Supplier	Cı		Subcontraci /alue	15% of Subcontract dollar value for credit			
Ceramic Tile Prime - Tier 2 Furnishing Materials	ST Materials & Equipment, LLC	\$		150,000.00	\$ 22,500.00	\$ -	0.0%	0.0%
Plumbing Prime - Tier 2 Furnish Only Plumbing Materials	JHP Industrial Supply Company, Inc.	\$		986,483.00	\$ 147,972.45	\$ 61,251.17	41.4%	0.0%
HVAC Prime -Tier 2 Furnish Only HVAC Materials	Carl-Louis & Co., Inc.	\$		900,000.00	\$ 135,000.00	\$ 53,793.58	39.8%	0.0%
Electrical Prime - Tier 2 Furnish Low Voltage Materials	Certified Connections, Inc.	\$	1,	,000,000.00	\$ 150,000.00	\$ 7,223.58	4.8%	0.0%
		•					Percent to Full Subcontract	Percent to Projected Goal
					\$ 17,965,691.45	\$ 4,857,363.29	27.0%	1.2%





11 May 2025

Projected GOAL 4.5%

WBE Participation – Paid through DCMS March Audit 2025

Bid Package Description	Prime / Filed Sub		Current Subcontract Value	WBE Paid to Date	Percent to Full Subcontract	Percent to Goal
Prime Contracts						
Final Cleaning	Front Line, Inc.		\$ 701,550.00	-	0.0%	0.0%
Doors, Frames, and Hardware	Thompson Company, Inc.		\$ 5,631,924.00	248,772.04	4.4%	0.1%
Carpet	Ayotte & King for Tile, Inc.		\$ 103,478.00	55,801.10	53.9%	0.0%
Window Treatments	Contexture		\$ 2,470,093.00	251,462.48	10.2%	0.1%
Resilient Flooring	Ayotte & King for Tile, Inc.		\$ 3,575,000.00	\$ 41,572.00	1.2%	0.0%
Tier Packages (Trade-Description)	Tier Subcontractor					
Concrete Prime - Tier 2 Furnishing Reinforcing	Rebars & Mesh, Inc.		\$ 1,400,000.00	1,249,686.50	89.3%	0.3%
Steel Prime - Tier 3 Install Shear Connectors	Composite Co., Inc.		\$ 187,610.00	162,992.60	86.9%	0.0%
Millwork Prime - Tier 2 Installation of Millwork	J. Thibert Architectural Woodwork Installation		\$ 1,924,092.00	-	0.0%	0.0%
Millwork Prime - Tier 2 Labor for loading of materials and clean up	Front Line, Inc.		\$ 937,500.00	-	0.0%	0.0%
Drywall Prime - Tier 2 Labor For Carpentry Support	Adams and Ruxton Construction Company		\$ 725,000.00	\$ 44,559.68	6.1%	0.0%
Drywall Prime - Tier 2 Labor For Carpentry Support	Advanced Scaffold Services of N.E. LLC		\$ 39,250.00	\$ 13,680.00	34.9%	0.0%
Plumbing Prime - Tier 2 Furnish & Installation of Plumbing Materials	413 Plumbing & Heating, Inc.		\$ 1,620,000.00	\$ 497,929.11	30.7%	0.1%
HVAC Prime - Tier 2 Furnish & Installation of Sheetmetal Ductwork	L.K. Sheet Metal, Inc.		\$ 5,500,000.00	1,479,592.55	26.9%	0.4%
Electrical Prime - Tier 2 Furnish & Install Site Lighting	Chapman Construction Group, Inc.		\$ 1,308,394.00	-	0.0%	0.0%
Electrical Prime - Tier 2 Material and Install Gear and Lighting Package	Seaport Energy Co., Inc.		\$ 2,811,675.00	1,913,454.34	68.1%	0.5%
Earthwork Prime - Tier 2 Furnishing & Installing/ReloTemporary Site	Guardrail Solutions, LLC		\$ 494,875.00	290,615.92		0.1%
Fence					58.7%	0.176
Earthwork Prime - Tier 2 Silt Fence, jute mesh & temp seeding	CSL, Inc.		\$ 142,038.00		90.6%	0.0%
Landscaping Prime - Tier 2 Labor and site clean up	Front Line, Inc.		\$ 900,000.00	-	0.0%	0.0%
Material Only (Prime Trade-Description)	Material Supplier	Contract Value	15% of Subcontract dollar value for credit			
Masonry Prime - Tier 2 Furnish only masonry materials	Architectural Products, Inc.	\$ 195,607.00	\$ 29,341.05	12,676.03	43.2%	0.0%
Masonry Prime - Tier 2 Furnish only masonry materials	Della Supply, LLC	\$ 815,000.00	\$ 122,250.00	-	0.0%	#DIV/0!
Steel Prime - Tier 3 Furnish only of Safety Screening System	Essential Perimeter	\$ 1,972,250.00	\$ 295,837.50	310,426.65	104.9%	0.1%
Curtain Wall, Windows & Panels Prime -Tier 2 Furnish Louvers & Vents	Architectural Products, Inc.	\$ 3,907,941.00	\$ 586,191.15	492,273.99	84.0%	0.1%
Painting Prime -Tier 2 Furnish Only Painting Supplies	Heritage Construction & Supply	\$ 156,059.00	\$ 23,408.85	-	0.0%	0.0%
HVAC Prime - Tier 2 Furnish Only Controls Material	Northeast Controls Panel Fabrication. Inc.	\$ 600,000.00	\$ 90,000.00	7,500.00	8.3%	0.0%
					Percent to Full Subcontract	Percent to Projected Goal
COMMODODE WALCH			\$ 32,045,460.55	\$ 7,677,306.66	24.0%	1.9%





12 May 2025

Projected GOAL

8.0%

VBE Participation – Paid through DCMS March Audit 2025

Bid Package Description	Prime / Filed Sub	Current Subcontract Value	VBE Paid toDate	Percent to Full Subcontract	Percent to Goal
Management	Commodore Builders	\$ 12,000,000.00	\$ 5,754,938.37	48.0%	1.4%
Prime - Waterproofing and Dampproofing	Superior Caulking & Waterproofing Co., Inc.	\$ 3,188,000.00	\$ 932,102.00	29.2%	0.2%
				Percent to Full Subcontract	Percent to Projected Goal
		\$ 15,188,000.00	\$ 6,687,040.37	44.0%	1.7%
				Projected GOAL	3.8%





Workforce Participation - *Percentages as of 05-04-2025

Goal	All Workers	Minority 15.3%	Women 6.9%	Veterans 7%
Reported Hours	352,305.59	86,897.78	36,338.63	32,632.75
% percent	N/A	24.7%	10.3%	9.26%

Goal	Apprentice 20%	**Minority, Women, Veteran Apprentices 40% of Apprentice Hours
Reported Hours	69,915.00	44,290.25
% percent	19.8%	More than 40%

Goal – 40% of Apprentice Hours	Minority Apprentices	**Women Apprentices	• •	Minority & Women Apprentices
Reported Hours	26,630.00	20,968.25	3,173.00	7,365.50
% percent	38.1%	30.0%	4.5%	10.5%

^{**} Includes women who are also part of a minority group.







^{*} Percentages are based on hours reported in DCMS LCPtracker

Workforce Participation April 2025 (1 of 2)

				Apprentice (Goal 20%	Minority Go	oal 15.3%	Women 6.9		Veteran 7%	
Division	Description	Tier 1 Contractor	Total Hours	Hours	%	Hours	%	Hours	%	Hours	%
Division 01	Scaffolding	BrandSafway Services LLC, Inc.	1,335.00	523.00	39.2%	779.00	58.4%	180.00	13.5%	-	0%
Division 06	Rough Carpentry/Progress Cleaning	Charles Services & Equipment	1,945.00	600.00	30.8%	720.00	37.0%	176.00	9.0%	522.00	27%
Division 03	Cast-In-Place Concrete	Manafort-Precision, LLC	236.50	-	0.0%	62.00	26.2%	-	0.0%	-	0%
Division 03	Concrete Reinforcing	Regis Steel Corporation	32.00	-	0.0%	-	0.0%	16.00	50.0%	-	0%
Division 03	Cast-In-Place Concrete	Manafort + Tiers Aggregate:	268.50	0.00	0.0%	62.00	23.1%	16.00	6.0%	0.00	0%
Division 04	Masonry	Capasso Enterprises Inc.	2,552.50	221.00	8.7%	961.50	37.7%	109.50	4.3%	230.00	9%
Division 05	Structural Steel	Les Constructions Beauce Atlas, Inc.	-	-	0.0%	-	-	-	-	-	-
Division 05	Structural Steel	Prime Steel Erecting, Inc.	905.00	219.00	24.2%	-	0.0%	-	0.0%	107.00	12%
Division 05	Structural Steel	Composite Company, Inc.	1,021.00	136.00	13.3%	-	0.0%	-	0.0%	136.00	13%
Division 05	Structural Steel	Trident Production Welding, Inc.	62.00	-	0.0%	62.00	100.0%	-	0.0%	-	0%
Division 05	Structural Steel	Beauce + Tiers Aggregate:	1,988.00	355.00	17.9%	62.00	3.1%	0.00	0.0%	243.00	12%
Division 05	Misc. Metals	Quinn Brothers of essex, Inc.	104.00	-	0.0%	24.00	23.1%	-	0.0%	-	0%
Division 07	Fireproofing	H Carr & Sons, Inc	176.00	-	0.0%	80.00	0.45	-	-	-	-
Division 07	Waterproofing and Dampproofing	Superior Caulking & Waterproofing Co., Inc.	828.00	-	0.0%	217.00	26.2%	-	0.0%	-	0%
Division 07	Roofing and Flashing	Titan Roofing, Inc.	370.00	76.00	20.5%	355.50	96.1%	-	0.0%	-	0%
Division 08	Glass & Glazing	Chandler Architectural Products, Inc.	2,009.50	352.00	17.5%	599.50	29.8%	345.00	17.2%	596.00	30%
Division 09	Resinous Flooring	Allegheny Contract Flooring, Inc.	80.00	-	0.0%	32.00	40.0%	-	0.0%	-	0%
Division 09	Painting	John W. Egan Company Inc.	18.00	2.00	11.1%	-	0.0%	-	0.0%	-	0%
Division 09	Drywall	Professional Drywall Construction, Inc.	4,073.00	964.00	23.7%	1,948.00	47.8%	400.00	9.8%	299.00	7%
Division 09	Window Blocking/Clean Up	Adams & Ruxton Construction Co.	852.00	164.00	19.2%	371.50	43.6%	118.00	13.8%	142.00	17%
Division 09	Taping	American Finish Systems, Inc.	24.00	-	0.0%	24.00	100.0%	-	0.0%	-	0%
Division 09	Drywall	PDC + Tiers Aggregate:	4,949.00	1,128.00	22.8%	2,343.50	47.4%	863.00	17.4%	441.00	9%





Workforce Participation April 2025 (2 of 2)

				Apprentice (Goal 20%	Minority Go	oal 15.3%	Women 6.99		Veteran 7%	
Division	Description	Tier 1 Contractor	Total Hours	Hours	%	Hours	%	Hours	%	Hours	%
Division 11	Appliances/Food Service	Singer MA, LLC dba Singer Kittredge	2.00	-	0.0%	-	0.0%	-	0.0%	-	0%
Division 22	Plumbing	Arden Engineering Constructors, LLC	5,601.00	846.00	15.1%	418.50	7.5%	262.50	4.7%	89.00	2%
Division 22	Plumbing	M.J.Daly LLC	151.00	-	0.0%	151.00	100.0%	-	0.0%	-	0%
Division 22	Plumbing Insulation	Kim Industries Inc	455.00	-	0.0%	135.00	26.7%	-	0.0%	-	0%
Division 21	Fire Protection and Division 22 Plumbing	Arden + Tiers Aggregate:	5,752.00	846.00	14.7%	704.50	12.2%	262.50	4.6%	89.00	2%
Division 23	HVAC	Harry Grodsky & Co., Inc.	3,091.00	602.50	19.5%	358.50	11.6%	202.00	6.5%	191.50	6%
Division 23	HVAC Insulation	Kim Industries Inc	479.00	112.00	23.4%	144.00	30.1%	-	0.0%	-	0%
Division 23	HVAC Sheetmetal Work	LK Sheetmetal	2,956.50	1,014.00	34.3%	933.00	31.6%	724.50	24.5%	184.00	6%
Division 07	Firestopping	Barber Firestop Systems LLC	20.00	8.00	40.0%	-	0.0%	-	0.0%	-	0%
Division 23	HVAC	Automated Logic Contracting Services	17.00	-	0.0%	-	0.0%	-	0.0%	-	0%
Division 23	HVAC	William Roberts Electric Co., Inc	457.00	144.00	31.5%	144.00	31.5%	-	0.0%	-	0%
Division 23	HVAC	Grodsky + Tiers Aggregate:	7,020.50	1,880.50	26.8%	1,579.50	22.5%	926.50	13.2%	375.50	5%
Division 26	Electrical / Low Voltage	Collins Electric Co., Inc.	4,750.00	1,361.50	28.7%	1,047.00	22.0%	830.00	17.5%	762.00	16%
Division 31	Earthwork	Northern Construction Service, LLC	-	-	0.0%	-	0.0%	-	0.0%	-	0%
Division 31	Earthwork	Northern General Contractors, Inc.	-	-	0.0%	-	0.0%	-	0.0%	-	0%
Division 31	Earthwork	Northern + Tiers Aggregate:	0.00	0.00	#DIV/0!	0.00	#DIV/0!	0.00	#DIV/0!	0.00	#DIV/0!
Division 41	Cranes	Marr Crane & Rigging	500.00	-	0.0%	248.50	49.7%	231.50	46.3%	-	0%
			34,000.00	7,209.00	21.2%	9,783.50	28.8%	3,595.00	10.6%	3,122.50	9.2%





Workforce Participation as of 05/04/2025 (1 of 2)

									Women		Veteran (
				Total Hours	Apprentice (_		6.99	-	7%	
	Description Scaffolding	Tier 1 Contractor	Tier 2 or 3 Contractor	12,213.50	Hours 3,025.50	% 24.8%	Hours 5,632.50	% 46.1%	Hours 1,050.00	% 8.6%	Hours 312.50	% 3%
	•	BrandSafway Services LLC, Inc.			·		,					
	Rough Carpentry/Cleaning	Charles Services & Equipment		12,203.50	3,657.00	30.0%	5,276.00	43.2%	2,054.00	16.8%	1,875.50	15%
	Cast-In-Place Concrete	Manafort-Precision, LLC		33,670.00	4,508.50	13.4%	6,691.50	19.9%	2,340.00	6.9%	3,442.50	10%
	Concrete Reinforcing	Manafort-Precision, LLC	Regis Steel Corporation	9,067.00	1,509.00	16.6%	1,820.00	20.1%	1,945.00	21.5%	1,735.00	19%
	Cast-In-Place Concrete	Manafort-Precision, LLC + Tiers		42,737.00	6,017.50	14.1%	8,511.50	19.9%	4,285.00	10.0%	5,177.50	12%
Division 04	<u> </u>	Capasso Enterprises Inc.		8,432.50	753.50	8.9%	3,234.50	38.4%	335.00	4.0%	585.50	7%
	Structural Steel	Les Constructions Beauce Atlas, Inc.	McGregor Industries Inc	1,176.00	-	0.0%	328.00	27.9%	328.00	27.9%	-	0%
Division 05	Structural Steel	Les Constructions Beauce Atlas, Inc.	Prime Steel Erecting, Inc.	50,974.00	10,849.50	21.3%	10,603.00	20.8%	2,782.50	5.5%	6,355.00	12%
Division 41	Cranes	Les Constructions Beauce Atlas, Inc. / Prime Steel Erecting, Inc.	Morrow Equipment Company, LLC	4,302.50	1,143.00	26.6%	-	0.0%	2,021.50	47.0%	-	0%
Division 05	Structural Steel	Les Constructions Beauce Atlas, Inc. / Prime Steel Erecting, Inc.	Composite Company, Inc.	1,021.00	136.00	13.3%	-	0.0%	-	0.0%	136.00	13%
Division 05	Structural Steel	Les Constructions Beauce Atlas, Inc. / Prime Steel Erecting, Inc.	Trident Production Welding, Inc.	6,111.00	-	0.0%	5,580.00	91.3%	-	0.0%	-	0%
Division 05	Structural Steel	Les Constructions Beauce Atlas, Inc. + Tiers		63,584.50	12,128.50	19.1%	16,511.00	26.0%	5,132.00	8.1%	6,491.00	10%
Division 05	Misc. Metals	Quinn Brothers of essex, Inc.		269.00	0.00	0.0%	79.00	29.4%	55.00	20.4%	55.00	20.4%
Division 09	Acoustical Tile Ceilings	H Carr & Sons, Inc		3,991.00	89.00	2.2%	2,349.50	58.9%	-	0.0%	32.00	1%
Division 07	Fireproofing	H Carr & Sons, Inc	Triple J Drywall and Carpentry, Inc.	659.50	510.00	77.3%	-	0.0%	40.00	6.1%	-	0%
Division 07	Fireproofing and 09 ACT	H Carr & Sons, Inc + Tiers		4,650.50	599.00	12.9%	2,349.50	50.5%	40.00	0.9%	32.00	1%
Division 07	Waterproofing and Dampproofing	Superior Caulking & Waterproofing Co., Inc.		4,329.50	-	0.0%	1,036.50	23.9%	-	0.0%	-	0%
Division 07	Roofing and Flashing	Titan Roofing, Inc.		519.75	111.50	21.5%	486.50	93.6%	2.00	0.4%	-	0%
Division 08	Glass & Glazing	Chandler Architectural Products, Inc.		10,187.00	1,682.50	16.5%	2,177.00	21.4%	1,249.50	12.3%	2,913.50	29%
Division 09	Resinous Flooring	Allegheny Contract Flooring, Inc.		80.00	-	0.0%	32.00	40.0%	-	0.0%	-	0%
Division 09	Drywall	Professional Drywall Construction, Inc.		27,327.00	5,751.00	21.0%	9,882.00	36.2%	3,455.50	12.6%	2,771.50	10%
Division 09	Window Blocking/Clean Up	Professional Drywall Construction, Inc.	Adams & Ruxton Construction Co.	2,337.00	531.00	22.7%	1,046.50	44.8%	293.00	12.5%	488.50	21%
Division 09	Taping	Professional Drywall Construction, Inc.	Scorpions Contracting, Inc.	268.00	-	0.0%	224.00	83.6%	-	0.0%	-	0%
Division 09	Taping	Professional Drywall Construction, Inc.	American Finish Systems	281.00	-	0.0%	281.00	100.0%	-	0.0%	-	0%
Division 09	Taping	Professional Drywall Construction, Inc.	Connecticut Drywal Finishing	24.00	-	0.0%	-	0.0%	-	0.0%	-	0%
Division 01	Scaffolding	Professional Drywall Construction, Inc.	Advanced Scaffold Services of NE	82.00	-	0.0%	41.00	50.0%	-	0.0%	-	0%
Division 09	Drywall	Professional Drywall Construction, Inc. + Tiers	6	30,319.00	6,282.00	20.7%	11,474.50	37.8%	3,748.50	12.4%	3,260.00	11%





Workforce Participation as of 05/04/2025 (2 of 2)

					Apprentice (Goal 20%	Minority G	oal 15.3%			Veteran 7%	
Dissistant Dis	Hours	%										
Division 21	Fire Protection	Arden Engineering Constructors, LLC		-	-	0.0%	-	-	-	-	-	-
Division 22	Plumbing	Arden Engineering Constructors, LLC		31,200.00	6,582.00	21.1%	3,338.50	10.70%	1,425.50	4.57%	2,861.50	9.17%
Division 22	Plumbing	Arden Engineering Constructors, LLC	413 Plumbing & Heating Inc.	1,187.50	431.00	36.3%	114.00	9.6%	-	0.0%	32.00	3%
Division 22	Plumbing	Arden Engineering Constructors, LLC	M.J.Daly LLC	1,593.50	-	0.0%	1,585.50	99.5%	-	0.0%	-	0%
Division 22	Plumbing Insulation	Arden Engineering Constructors, LLC	Kim Industries Inc	534.00	-	0.0%	135.00	25.3%	-	0.0%	-	0%
		Arden Engineering Constructors, LLC + Tiers		34,515.00	7,013.00	20.3%	5,173.00	15.0%	1,425.50	4.1%	2,893.50	8%
Division 23	HVAC	Harry Grodsky & Co., Inc.		19,979.00	4,490.00	22.5%	3,495.00	17.5%	1,111.50	5.6%	1,307.50	7%
Division 23	HVAC Sheetmetal Work	Harry Grodsky & Co., Inc.	LK Sheetmetal	14,762.50	5,071.00	34.4%	5,246.00	35.5%	2,757.50	18.7%	508.00	3%
Division 23	HVAC Insulation	Harry Grodsky & Co., Inc.	Kim Industries Inc	904.00	112.00	12.4%	176.00	19.5%	-	0.0%	-	0%
Division 07	Firestopping	Harry Grodsky & Co., Inc.	Barber Firestop Systems LLC	20.00	8.00	40.0%	-	0.0%	-	0.0%	-	0%
Division 41	Cranes	Harry Grodsky & Co., Inc.	Central Mass Crane Service Inc.	24.00	-	0.0%	-	0.0%	-	0.0%	-	0%
Division 23	HVAC	Harry Grodsky & Co., Inc.	Automated Logic Contracting Services	110.00	-	0.0%	-	0.0%	-	0.0%	-	0%
Division 23	HVAC		William Roberts Electric Co., Inc	2,012.50	603.00	30.0%	570.00	28.3%	-	0.0%	-	0%
Division 23	HVAC	Harry Grodsky & Co., Inc. + Tiers		37,812.00	10,284.00	27.2%	9,487.00	25.1%	3,869.00	10.2%	1,815.50	5%
Division 26	Electrical / Low Voltage	Collins Electric Co., Inc. + Tiers		26,194.00	7,093.00	27.1%	3,662.00	14.0%	5,821.75	22.2%	3,338.25	13%
Division 31	Earthwork	Northern Construction Service, LLC		675.50	-	0.0%	-	0.0%	263.00	38.9%	3.50	1%
Division 31	Earthwork	Northern Construction Service, LLC	Northern General Contractors, Inc.	46,189.50	10,193.50	22.1%	8,692.00	18.8%	3,716.50	8.0%	3,008.00	7%
Division 31	Earthwork	Northern Construction Service, LLC	Northern Land Clearance LLC	332.50	-	0.0%	-	0.0%	-	0.0%	-	0%
Division 03	Concrete cutting	Northern Construction Service, LLC	Ace Concrete Cutting, LLC	4.00	-	0.0%	-	0.0%	-	0.0%	-	0%
Division 31	Erosion and sediment control	Northern Construction Service, LLC	CSL, Inc.	376.00	-	0.0%	108.00	28.7%	-	0.0%	-	0%
Division 01	Fence and gates	Northern Construction Service, LLC	Guardrail Solutions LLC	938.00	-	0.0%	332.50	35.4%	-	0.0%	47.50	5%
Division 31	Earthwork	Northern Construction Service, LLC	Keller North America	4,239.00	704.50	16.6%	179.00	4.2%	-	0.0%	281.00	7%
Division 32	Asphalt Paving	Northern Construction Service, LLC	Don Martin Corporation	95.00	-	0.0%	38.00	40.0%	-	0.0%	19.00	20%
Division 31	Geothermal	Northern Construction Service, LLC	Skillings & Sons, Inc.	2,206.25	-	0.0%	416.25	18.9%	-	0.0%	344.00	16%
Division 31	Geothermal	· ·	Ground Source Drilling LLC	136.00	-	0.0%	-	0.0%	-	0.0%	-	0%
Division 31	Geothermal	· ·	Wragg Well Company LLC	319.00	-	0.0%	-	0.0%	-	0.0%	-	0%
Division 31	Earthwork	Northern Construction Service, LLC + Tiers		55,510.75	10,898.00	19.6%	9,765.75	17.6%	3,979.50	7.2%	3,703.00	7%
Division 32	Landscaping	Brightview Landscape + Tiers		586.78	0.00	0.0%	0.00	0.0%	147.88	25.2%	0.00	0%
Division 41	Cranes	Marr Crane & Rigging		3,232.00	-	0.0%	1,283.50	39.7%	2,322.00	71.8%	-	0%
				352,305.59	69,915.00	19.8%	86,897.78	3 24.7%	36,338.63	10.3%	32,632.75	5 9.3%

18





Apprentice Workforce Participation as of 05/04/2025

Tier 1 Contractor															
Tier 2 Contrator	Annren	tice 20%	Goal		linority		,	Nomen		,	Veteran		Minority & Women		
Tier 3 Contrator	Hours	Count	%	Hours	Count	%	Hours	Count	%	Hours	Count	%	Hours	Count	%
Arden Engineering Constructors, LLC	6,582.00	14	21.1%	553	4	8.4%	921.00	2	14.0%	36.00	1	0.5%	0.00	0	0.0%
413 Plumbing & Heating Inc.	431.00	3	36.3%	0	0	0.0%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
B-G Mechanical Contractors, Inc.	303.00	1	30.0%	0.2	0	0.0%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
BrandSafway Services LLC, Inc.	3,025.50	3	24.8%	1767.5	2	58.4%	1,050.00	1	34.7%	0.00	0	0.0%	1,050.00	1	34.7%
Capasso Enterprises Inc.	753.50	2	8.9%	345	1	45.8%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
Chandler Architectural Products, Inc.	1,682.50	6	16.5%	387	1	23.0%	600.00	3	35.7%	800.00	1	47.5%	387.00	1	23.0%
Charles Services & Equipment	3,657.00	4	30.0%	2729	3	74.6%	1,486.00	2	40.6%	0.00	0	0.0%	1,486.00	2	40.6%
Collins Electric Co., Inc.	7,093.00	22	27.1%	1645	6	23.2%	3,849.25	4	54.3%	533.00	2	7.5%	0.00	0	0.0%
Edward F. Corcoran Plumbing & Heating	48.00	1	32.0%	0.2	0	0.0%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
H Carr & Sons, Inc	89.00	2	3.1%	0	0	0.0%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
Triple J Drywall and Carpentry, Inc.	510.00	1	77.3%	0	0	0.0%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
Harry Grodsky & Co., Inc.	4,490.00	5	22.5%	1639	1	36.5%	1,111.50	1	24.8%	0.00	0	0.0%	0.00	0	0.0%
Kim Industries Inc	112.00	2	12.4%	0	0	0.0%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
LK Sheetmetal	5,071.00	9	34.4%	1634	2	32.2%	1,838.00	3	36.2%	0.00	0	0.0%	0.00	0	0.0%
Todd Barber dba Barber Firestop Systems LLC	8.00	1	40.0%	0	0	0.0%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
William Roberts Electric Co., Inc	603.00	2	30.0%	570	1	94.5%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
John W. Egan Company Inc.	2.00	1	11.1%	0	0	0.0%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
es Constructions Beauce-Atlas, Inc.															
Prime Steel Erecting, Inc.	10,849.50	16	21.3%	2299.5	6	21.2%	1,239.50	3	11.4%	1,154.00	2	10.6%	277.50	1	2.6%
Composite Company, Inc.	136.00	1	13.3%	0	0	0.0%	-	0	0.0%	136.00	1	100.0%	0.00	0	0.0%
Morrow Equipment Company, LLC	1,143.00	2	26.6%	0	0	0.0%	1,112.00	1	97.3%	0.00	0	0.0%	0.00	0	0.0%
Manafort-Precision, LLC	4,508.50	8	13.5%	2265	3	50.2%	2,340.00	4	51.9%	78.00	1	1.7%	1,702.00	1	37.8%
Regis Steel Corporation	1,509.00	6	17.1%	631	2	41.8%	584.00	2	38.7%	436.00	1	28.9%	431.00	1	28.6%
Moran Sheet Metal, Inc.	7.00	1	54.0%	0.2	0	0.0%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
Northern General Contractors, Inc.	10,193.50	12	22.1%	7345.5	7	72.1%	2,870.00	3	28.2%	0.00	0	0.0%	1,315.00	1	12.9%
Keller North America	704.50	2	17.0%	0	0	0.0%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
Power Line Contractors, Inc.	10.00	1	1.0%	0.2	0	0.0%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
Professional Drywall Construction, Inc.	5,751.00	10	21.0%	2415	4	42.0%	1,674.00	2	29.1%	0.00	0	0.0%	424.00	1	7.4%
Adams & Ruxton Construction Company	531.00	3	22.7%	293	1	55.2%	293.00	1	55.2%	0.00	0	0.0%	293.00	1	55.2%
Titan Roofing, Inc.	111.50	2	21.5%	111.5	2	100.0%	-	0	0.0%	0.00	0	0.0%	0.00	0	0.0%
Total for Project (Chiller & Main):	69,915.00	143	19.8%	26,630	46	38.1%	20,968.25	32	30.0%	3,173.00	9	4.5%	7,365.50	10	10.5%







Outreach Events – Upcoming

Monthly: 8:00 A.M. – 9:00 A.M. Have questions about DCAMM Certification? Stop by and ask us.

5/21 Certification's May Zoom Meeting

6/18 Certification's June Zoom Meeting





MA Construction Opportunities Event

Join us to learn what you need to know to start bidding and working on public projects, and about upcoming opportunities for subcontractors, vendors, and suppliers to participate in construction projects on publicly owned buildings.

June 12, 2025, 1:00-2:30 P.M.

Published on 4/6/2025

https://www.eventbrite.com/e/1143295279959?aff=oddtdtcreator

October 8, 2025, 10:00-11:30 A.M.

Published on 6/8/2025

https://www.eventbrite.com/e/1143296333109?aff=oddtdtcreator





Questions





