

# Highway Administrator's Report

Jonathan Gulliver

May 14, 2018

# Mass Ave Bridge over Comm Ave



- SPS New England
- \$7.9M Project
- Accelerated Bridge Techniques (PBUs)
- Bridge Phase 36 hours ahead of schedule

# Spring Clean up

- MassDOT uses in-house forces as well as outside forces to remove litter in areas adjacent to MassDOT highways and roadways
- Some crews began in late March, all were active by the 3<sup>rd</sup> week of April.
- First we target known hot spots/major litter areas and then begin a linear (end to end) effort to clean the roadways. This is an ongoing, constant effort
- Annually, MassDOT picks up on average 90,000 bags of trash in addition to larger items like tires, TVs, microwaves, refrigerators.



# Personnel and Organizational Changes

- Appointed Two New DHDs
  - Barry Lorion, District 3
  - John McInerney, District 6
- New Prequal, Records and Procedures unit
- Owners Representative Program Revamp

# Longfellow Bridge Project



# Longfellow Bridge Project Status

- Major upcoming milestones
  1. *May 31, 2018* - All modes of traffic open in final alignment over Longfellow Bridge
  2. *August 31, 2018* - Substantial Completion of remaining non-roadway work.
  3. *December 31, 2018* - Final Completion
- White-Skanska-Consigli and MassDOT are in process of working out the details for a global agreement on all issues related to the Project.
- Final Contract Value approximately \$306.6 Mil


# Outbound Roadway, MBTA Fence, & Lighting



# Pedestrian Bridge (From Esplanade)



# Final Traffic Configuration

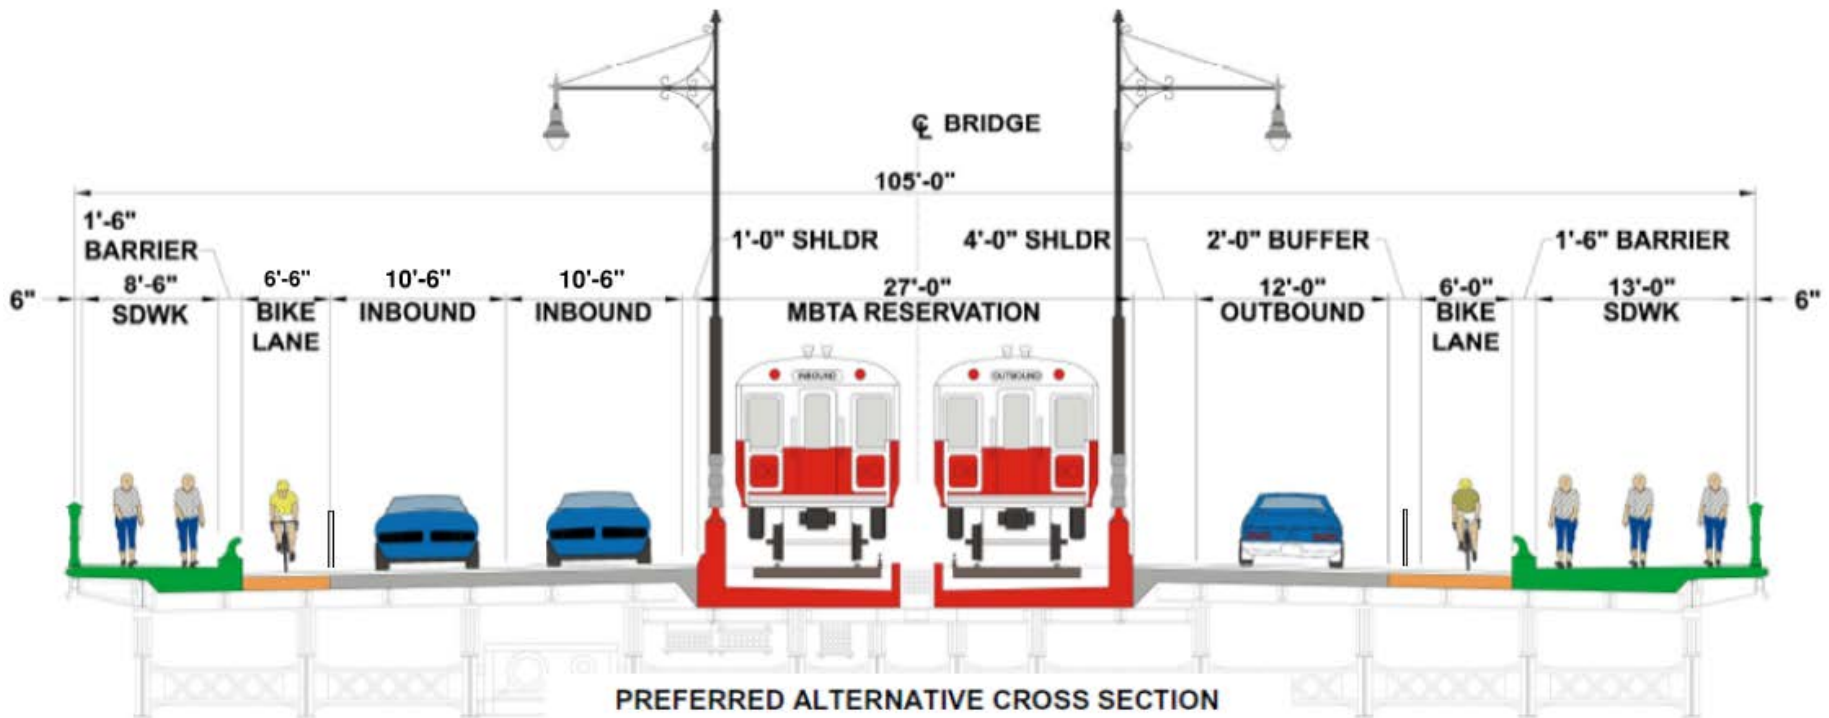

Milestone 3, Full Beneficial Use – May 31, 2018

# Final Traffic Configuration



Milestone 3, Full Beneficial Use – May 31, 2018
