
























































































































































EXHIBIT K
Project Plan





















ID	View	Roadmap	Artifact Type	Artifact Status	Task Name	Resource Names	Task Mod	Duration	Start	Finish	Predecessors	Mon Sep 1			Tue Sep 2			Wed Sep 3		
321		6.4 Policy & Procedures			Document Retroactive Coverage Process			5 days	Mon 9/29/14	Fri 10/3/14										
322		6.4 Policy & Procedures			Document System Access Process			12 days	Mon 9/29/14	Fri 10/10/14										
323		6.4 Policy & Procedures			Policy & Procedures Documents			33 days	Mon 9/15/14	Fri 10/17/14										
324		6.4 Policy & Procedures			Deliverable Development CCA			25 days	Mon 9/22/14	Thu 10/16/14										
325		6.4 Policy & Procedures			Document Customer Service P&Ps			10 days	Mon 9/22/14	Wed 10/1/14										
326		6.4 Policy & Procedures			Document ID Proofing P&Ps for Telephonic applica			5 days	Mon 9/22/14	Fri 9/26/14										
327		6.4 Policy & Procedures			Document ID Proofing P&Ps for Online application			3 days	Mon 9/29/14	Wed 10/1/14										
328		6.4 Policy & Procedures			Document Application Processing P&Ps			5 days	Mon 9/22/14	Fri 9/26/14										
329		6.4 Policy & Procedures			Document Paper Application P&Ps			17 days	Mon 9/22/14	Wed 10/8/14										
330		6.4 Policy & Procedures			Document Subsidized Paper Application P&Ps			5 days	Mon 9/22/14	Fri 9/26/14										
331		6.4 Policy & Procedures			Document Unsubsidized Paper Application P&Ps			3 days	Mon 9/29/14	Wed 10/1/14										
332		6.4 Policy & Procedures			Document Dental Paper Application P&Ps			3 days	Mon 10/6/14	Wed 10/8/14										
333		6.4 Policy & Procedures			Document Small Group Paper Application P&Ps			5 days	Mon 9/22/14	Fri 9/26/14										
334		6.4 Policy & Procedures			Document MWS P&Ps			5 days	Mon 9/22/14	Fri 9/26/14										
335		6.4 Policy & Procedures			Document Missing Critical Data (MCD) P&Ps			4 days	Mon 9/29/14	Thu 10/2/14										
336		6.4 Policy & Procedures			Document Eligibility Verifications P&Ps			3 days	Mon 9/29/14	Wed 10/1/14										
337		6.4 Policy & Procedures			Document Report-A-Change P&Ps			10 days	Thu 10/2/14	Sat 10/11/14										
338		6.4 Policy & Procedures			Document Report A Change - Closed Enrollment P&Ps			5 days	Thu 10/2/14	Mon 10/6/14										
339		6.4 Policy & Procedures			Document LEC/CE: Qualifying Event Verifications P&Ps			5 days	Thu 10/2/14	Mon 10/6/14										
340		6.4 Policy & Procedures			Document New Member Life Events - Closed Enrollment P&Ps			5 days	Tue 10/7/14	Sat 10/11/14										
341		6.4 Policy & Procedures			Document Premium Billing & Enrollment P&Ps			4 days	Mon 10/13/14	Thu 10/16/14										
342		6.4 Policy & Procedures			Document Appeals P&Ps			5 days	Tue 9/23/14	Sat 9/27/14										
343		6.4 Policy & Procedures			Deliverable Development MassHealth			32 days	Mon 9/15/14	Thu 10/16/14										
344		6.4 Policy & Procedures			Document Customer Service P&Ps			10 days	Mon 9/22/14	Wed 10/1/14										
345		6.4 Policy & Procedures			Document ID Proofing P&Ps for Telephonic applica			5 days	Mon 9/22/14	Fri 9/26/14										
346		6.4 Policy & Procedures			Document ID Proofing P&Ps for Online application			3 days	Mon 9/29/14	Wed 10/1/14										
347		6.4 Policy & Procedures			Document Application P&Psing P&Ps			5 days	Mon 9/22/14	Fri 9/26/14										
348		6.4 Policy & Procedures			Document Paper Application P&Ps			10 days	Mon 9/22/14	Wed 10/1/14										
349		6.4 Policy & Procedures			Document Subsidized Paper Application P&Ps			5 days	Mon 9/22/14	Fri 9/26/14										
350		6.4 Policy & Procedures			Document Unsubsidized Paper Application P&Ps			3 days	Mon 9/29/14	Wed 10/1/14										
351		6.4 Policy & Procedures			Document MWS P&Ps			5 days	Mon 9/22/14	Fri 9/26/14										
352		6.4 Policy & Procedures			Document Missing Critical Data (MCD) P&Ps			5 days	Mon 9/22/14	Fri 9/26/14										
353		6.4 Policy & Procedures			Document Eligibility Verifications P&Ps			5 days	Mon 9/22/14	Fri 9/26/14										
354		6.4 Policy & Procedures			Document Report-A-Change P&Ps			3 days	Mon 9/29/14	Wed 10/1/14										
355		6.4 Policy & Procedures			Document LEC/CE: Qualifying Event Verifications P&Ps			3 days	Mon 9/29/14	Wed 10/1/14										
356		6.4 Policy & Procedures			Document Operational Workarounds			32 days	Mon 9/15/14	Thu 10/16/14										
357		6.4 Policy & Procedures			Document Pregnancy End Date P&Ps			1 day	Mon 9/15/14	Mon 9/15/14										
358		6.4 Policy & Procedures			Document Born MassHealth Eligible P&Ps			1 day	Mon 9/15/14	Mon 9/15/14										
359		6.4 Policy & Procedures			Document Non-Custodial Parent P&Ps			1 day	Mon 9/15/14	Mon 9/15/14										
360		6.4 Policy & Procedures			Document Member Turning 65 P&Ps			15 days	Thu 10/2/14	Thu 10/16/14										
Project: MA_Integrated_Project_S Date: Tue 9/30/14		Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous												
		Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current												
		Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous												
		Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current												
		Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress												
Page 9																				


ID	View	Roadmap	Artifact Type	Artifact Status	Task Name	Resource Names	Task Mod	Duration	Start	Finish	Predecessors	Mon Sep 1			Tue Sep 2			Wed Sep 3		
681		5.1 Master Test Plan (Upda			Circulate Draft Sub Test Plan for internal review			5 days	Mon 9/15/14	Fri 9/19/14										
682		5.1 Master Test Plan (Upda			Update and Finalize Sub Test Plan for client review			5 days	Mon 9/15/14	Fri 9/19/14										
683		5.1 Master Test Plan (Upda			Functional: End to End Integrated			5 days	Mon 9/15/14	Fri 9/19/14										
684		5.1 Master Test Plan (Upda			Draft Sub Test Plan in Standard Template			5 days	Mon 9/15/14	Fri 9/19/14										
685		5.1 Master Test Plan (Upda			Optum hCentive Front End			5 days	Mon 9/15/14	Fri 9/19/14										
686		5.1 Master Test Plan (Upda			Dell Back End			5 days	Mon 9/15/14	Fri 9/19/14										
687		5.1 Master Test Plan (Upda			Full End to End			5 days	Mon 9/15/14	Fri 9/19/14										
688		5.1 Master Test Plan (Upda			Circulate Draft Sub Test Plan for internal review			5 days	Mon 9/15/14	Fri 9/19/14										
689		5.1 Master Test Plan (Upda			Update and Finalize Sub Test Plan for client review			5 days	Mon 9/15/14	Fri 9/19/14										
690		5.1 Master Test Plan (Upda			Functional: UDT			5 days	Mon 9/15/14	Fri 9/19/14										
691		5.1 Master Test Plan (Upda			Draft Sub Test Plan in Standard Template			5 days	Mon 9/15/14	Fri 9/19/14										
692		5.1 Master Test Plan (Upda			CCA			5 days	Mon 9/15/14	Fri 9/19/14										
693		5.1 Master Test Plan (Upda			MassHealth			5 days	Mon 9/15/14	Fri 9/19/14										
694		5.1 Master Test Plan (Upda			Carriers			5 days	Mon 9/15/14	Fri 9/19/14										
695		5.1 Master Test Plan (Upda			CSRs and Assisters			5 days	Mon 9/15/14	Fri 9/19/14										
696		5.1 Master Test Plan (Upda			Circulate Draft Sub Test Plan for internal review			5 days	Mon 9/15/14	Fri 9/19/14										
697		5.1 Master Test Plan (Upda			Update and Finalize Sub Test Plan for client review			5 days	Mon 9/15/14	Fri 9/19/14										
698		5.1 Master Test Plan (Upda			Other: BluePrint			5 days	Mon 9/15/14	Fri 9/19/14										
699		5.1 Master Test Plan (Upda			Draft Sub Test Plan in Standard Template			5 days	Mon 9/15/14	Fri 9/19/14										
700		5.1 Master Test Plan (Upda			Circulate Draft Sub Test Plan for internal review			5 days	Mon 9/15/14	Fri 9/19/14										
701		5.1 Master Test Plan (Upda			Update and Finalize Sub Test Plan for client review			5 days	Mon 9/15/14	Fri 9/19/14										
702		5.1 Master Test Plan (Upda			Other: ADA			5 days	Mon 9/15/14	Fri 9/19/14										
703		5.1 Master Test Plan (Upda			Draft Sub Test Plan in Standard Template			5 days	Mon 9/15/14	Fri 9/19/14										
704		5.1 Master Test Plan (Upda			Circulate Draft Sub Test Plan for internal review			5 days	Mon 9/15/14	Fri 9/19/14										
705		5.1 Master Test Plan (Upda			Update and Finalize Sub Test Plan for client review			5 days	Mon 9/15/14	Fri 9/19/14										
706		5.1 Master Test Plan (Upda			Other: Issuer			5 days	Mon 9/15/14	Fri 9/19/14										
707		5.1 Master Test Plan (Upda			Draft Sub Test Plan in Standard Template			5 days	Mon 9/15/14	Fri 9/19/14										
708		5.1 Master Test Plan (Upda			Circulate Draft Sub Test Plan for internal review			5 days	Mon 9/15/14	Fri 9/19/14										
709		5.1 Master Test Plan (Upda			Update and Finalize Sub Test Plan for client review			5 days	Mon 9/15/14	Fri 9/19/14										
710		5.1 Master Test Plan (Upda			Deliverable Submission and Approval			5 days	Mon 9/22/14	Fri 9/26/14										
711		5.1 Master Test Plan (Upda			Submit Master Test Plan (Upload to MassForge)			1 day	Mon 9/22/14	Mon 9/22/14										
712		5.1 Master Test Plan (Upda			Review Master Test Plan			1 day	Tue 9/23/14	Tue 9/23/14										
713		5.1 Master Test Plan (Upda			Revise Master Test Plan			1 day	Wed 9/24/14	Wed 9/24/14										
714		5.1 Master Test Plan (Upda			Finalize Master Test Plan			1 day	Thu 9/25/14	Thu 9/25/14										
715		5.1 Master Test Plan (Upda			Approve Master Test Plan			1 day	Fri 9/26/14	Fri 9/26/14										
716		5.1 Master Test Plan (Upda	Work Pr	In Progre	Testing Dashboard (Daily)			45 days	Mon 9/1/14	Wed 10/15/14		▶								
717		5.1 Master Test Plan (Upda			Draft Test Dashboard in standard template			45 days	Mon 9/1/14	Wed 10/15/14		▶								
718		5.1 Master Test Plan (Upda			Finalize Draft Test Dashboard			45 days	Mon 9/1/14	Wed 10/15/14		▶								
719		5.1 Master Test Plan (Upda			Distribute Test Dashboard and upload to project repository (M			45 days	Mon 9/1/14	Wed 10/15/14		▶								
720		5.1 Master Test Plan (Upda	Work Pr	In Progre	Defect Report (Weekly)			47 days	Mon 9/15/14	Fri 10/31/14										
Project: MA_Integrated_Project_S Date: Tue 9/30/14		Milestone			Summary: Previous			Placeholder Start: Current			Inactive Milestone: Previous									
		Task: Previous			Summary: Current			Placeholder Finish: Previous			Inactive Milestone: Current									
		Task: Current			Placeholder Duration: Previous			Placeholder Finish: Current			Inactive Summary: Previous									
		Milestone: Previous			Placeholder Duration: Current			Inactive Task: Previous			Inactive Summary: Current									
		Milestone: Current			Placeholder Start: Previous			Inactive Task: Current			Manual Progress									
Page 18																				


ID	View	Roadmap	Artifact Type	Artifact Status	Task Name	Resource Names	Task Mod	Duration	Start	Finish	Predecessors	Mon Sep 1	Tue Sep 2	Wed Sep 3
1520		1.1 Project Execution & Monitoring			Draft Configuration Management Plan			16 days	Mon 9/15/14	Tue 9/30/14				
1521		1.1 Project Execution & Monitoring			Draft Development Approach Plan			16 days	Mon 9/15/14	Tue 9/30/14				
1522		1.1 Project Execution & Monitoring			Draft Requirements Management Plan			16 days	Mon 9/15/14	Tue 9/30/14				
1523		1.1 Project Execution & Monitoring			Draft Records Management Plan			16 days	Mon 9/15/14	Tue 9/30/14				
1524		1.1 Project Execution & Monitoring			Draft Procurement Management Plan			16 days	Mon 9/15/14	Tue 9/30/14				
1525		1.1 Project Execution & Monitoring			Draft Sub-Contractor Management Plan			16 days	Mon 9/15/14	Tue 9/30/14				
1526		1.1 Project Execution & Monitoring			Draft Communications Matrix			16 days	Mon 9/15/14	Tue 9/30/14				
1527		1.1 Project Execution & Monitoring			Circulate Draft Project Management Plan for internal review			16 days	Mon 9/15/14	Tue 9/30/14				
1528		1.1 Project Execution & Monitoring			Update and Finalize Project Management Plan for client review			16 days	Mon 9/15/14	Tue 9/30/14				
1529		1.1 Project Execution & Monitoring			Deliverable Submission and Approval			17 days	Mon 9/15/14	Wed 10/1/14				
1530		1.1 Project Execution & Monitoring			Submit Project Management Plan (Upload to MassForge)			12 days	Mon 9/15/14	Fri 9/26/14				
1531		1.1 Project Execution & Monitoring			Review Project Management Plan			1 day	Sat 9/27/14	Sat 9/27/14	1530			
1532		1.1 Project Execution & Monitoring			Revise Project Management Plan			2 days	Sun 9/28/14	Mon 9/29/14	1531			
1533		1.1 Project Execution & Monitoring			Finalize Project Management Plan			1 day	Tue 9/30/14	Tue 9/30/14	1532			
1534		1.1 Project Execution & Monitoring			Approve Project Management Plan			1 day	Wed 10/1/14	Wed 10/1/14	1533			
1535		1.1 Project Execution & Monitoring	CMS Del In Progress		Communications Matrix			23 days	Mon 9/15/14	Tue 10/7/14				
1536		1.1 Project Execution & Monitoring			Deliverable Expectations Document (DED)			5 days	Mon 9/15/14	Fri 9/19/14				
1537		1.1 Project Execution & Monitoring			Confirm Acceptance Criteria, Timeline, Reviewers & Approvals			1 day	Mon 9/15/14	Mon 9/15/14				
1538		1.1 Project Execution & Monitoring			Create Deliverable Draft DED including Deliverable Table of Contents			1 day	Tue 9/16/14	Tue 9/16/14	1537			
1539		1.1 Project Execution & Monitoring			Send draft DED out for review			1 day	Wed 9/17/14	Wed 9/17/14	1538			
1540		1.1 Project Execution & Monitoring			Conduct meeting to review DED			1 day	Thu 9/18/14	Thu 9/18/14	1539			
1541		1.1 Project Execution & Monitoring			Update DED and upload to project repository (MassForge)			1 day	Fri 9/19/14	Fri 9/19/14	1540			
1542		1.1 Project Execution & Monitoring			Deliverable Development			15 days	Mon 9/15/14	Mon 9/29/14				
1543		1.1 Project Execution & Monitoring			Draft Communications Matrix in Standard Template			7 days	Mon 9/15/14	Sun 9/21/14				
1544		1.1 Project Execution & Monitoring			Circulate Draft Communications Matrix for internal review			7 days	Mon 9/22/14	Sun 9/28/14	1543			
1545		1.1 Project Execution & Monitoring			Update and Finalize Communications Matrix for client review			1 day	Mon 9/29/14	Mon 9/29/14	1544			
1546		1.1 Project Execution & Monitoring			Deliverable Submission and Approval			8 days	Tue 9/30/14	Tue 10/7/14	1542			
1547		1.1 Project Execution & Monitoring			Submit Communications Matrix (Upload to MassForge)			1 day	Tue 9/30/14	Tue 9/30/14				
1548		1.1 Project Execution & Monitoring			Review Communications Matrix			2 days	Wed 10/1/14	Thu 10/2/14	1547			
1549		1.1 Project Execution & Monitoring			Revise Communications Matrix									


ID	View	Roadmap	Artifact Type	Artifact Status	Task Name	Resource Names	Task Mod	Duration	Start	Finish	Predecessors	Mon Sep 1	Tue Sep 2	Wed Sep 3
1637		1.5 Demos			Demo FM functionality		 1 day	1 day	Wed 10/15/14	Wed 10/15/14				
1638		1.5 Demos			Demo hCentive 3.x functionality		 1 day	1 day	Thu 10/16/14	Thu 10/16/14	1637			





Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

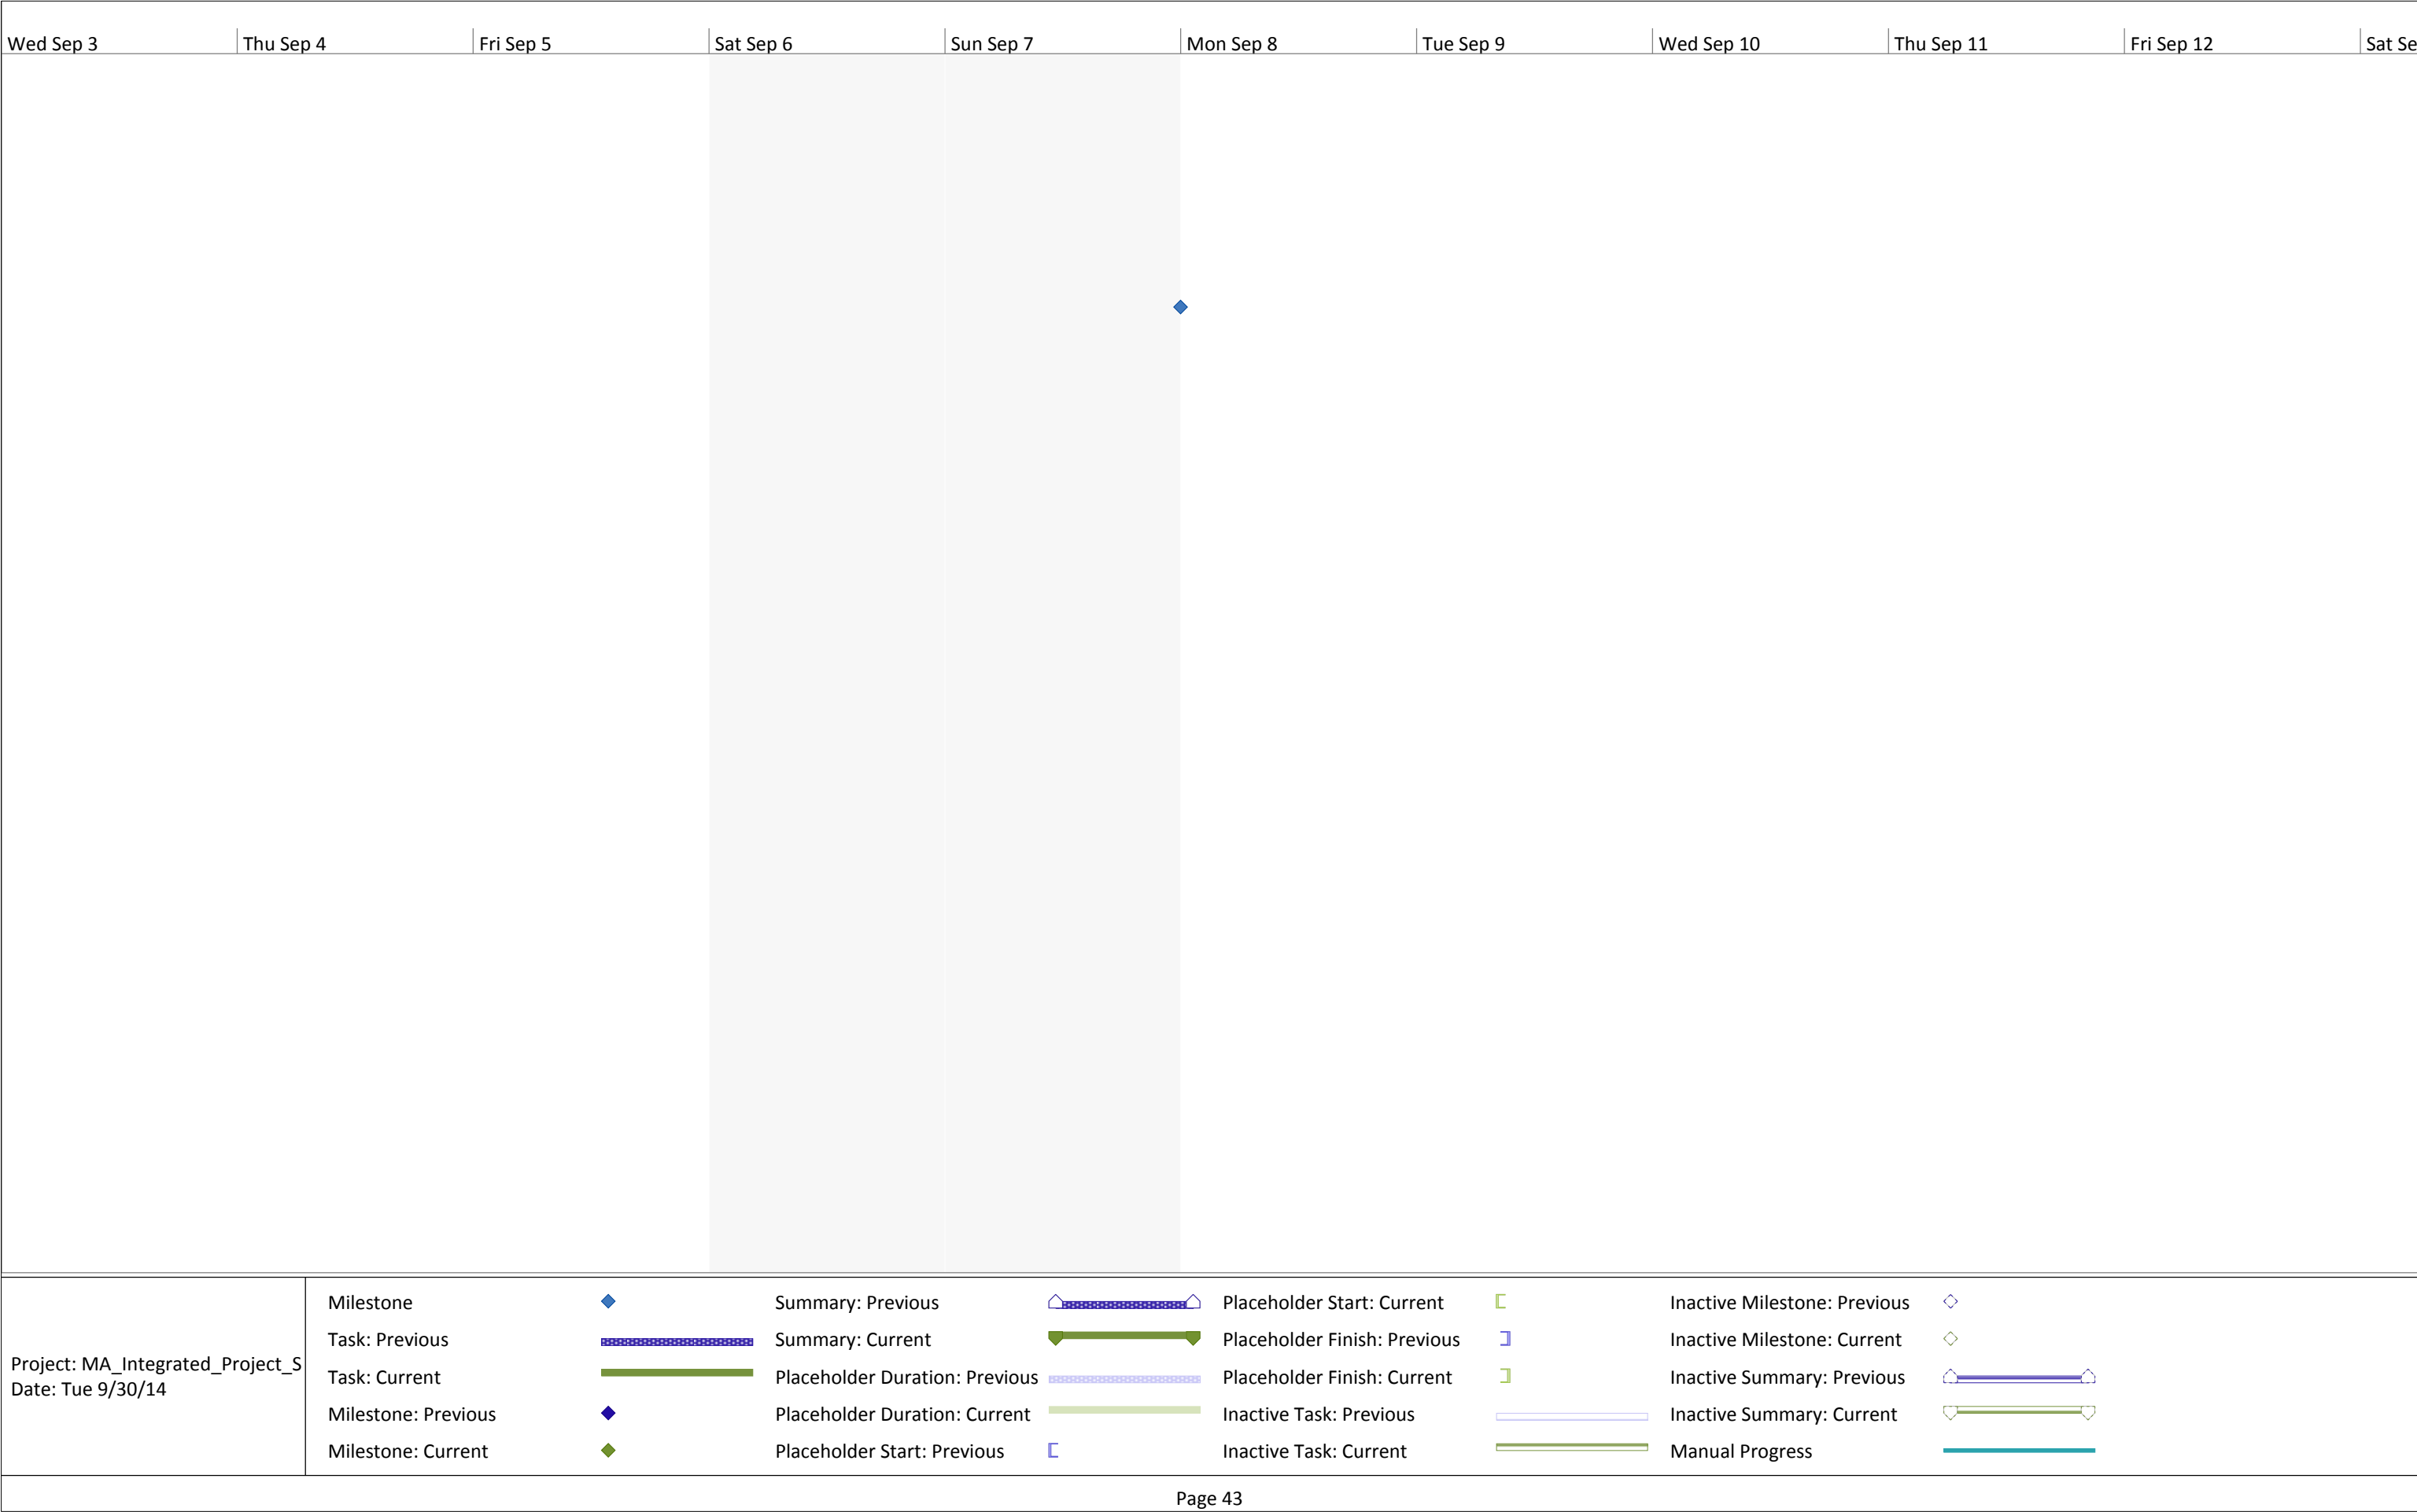







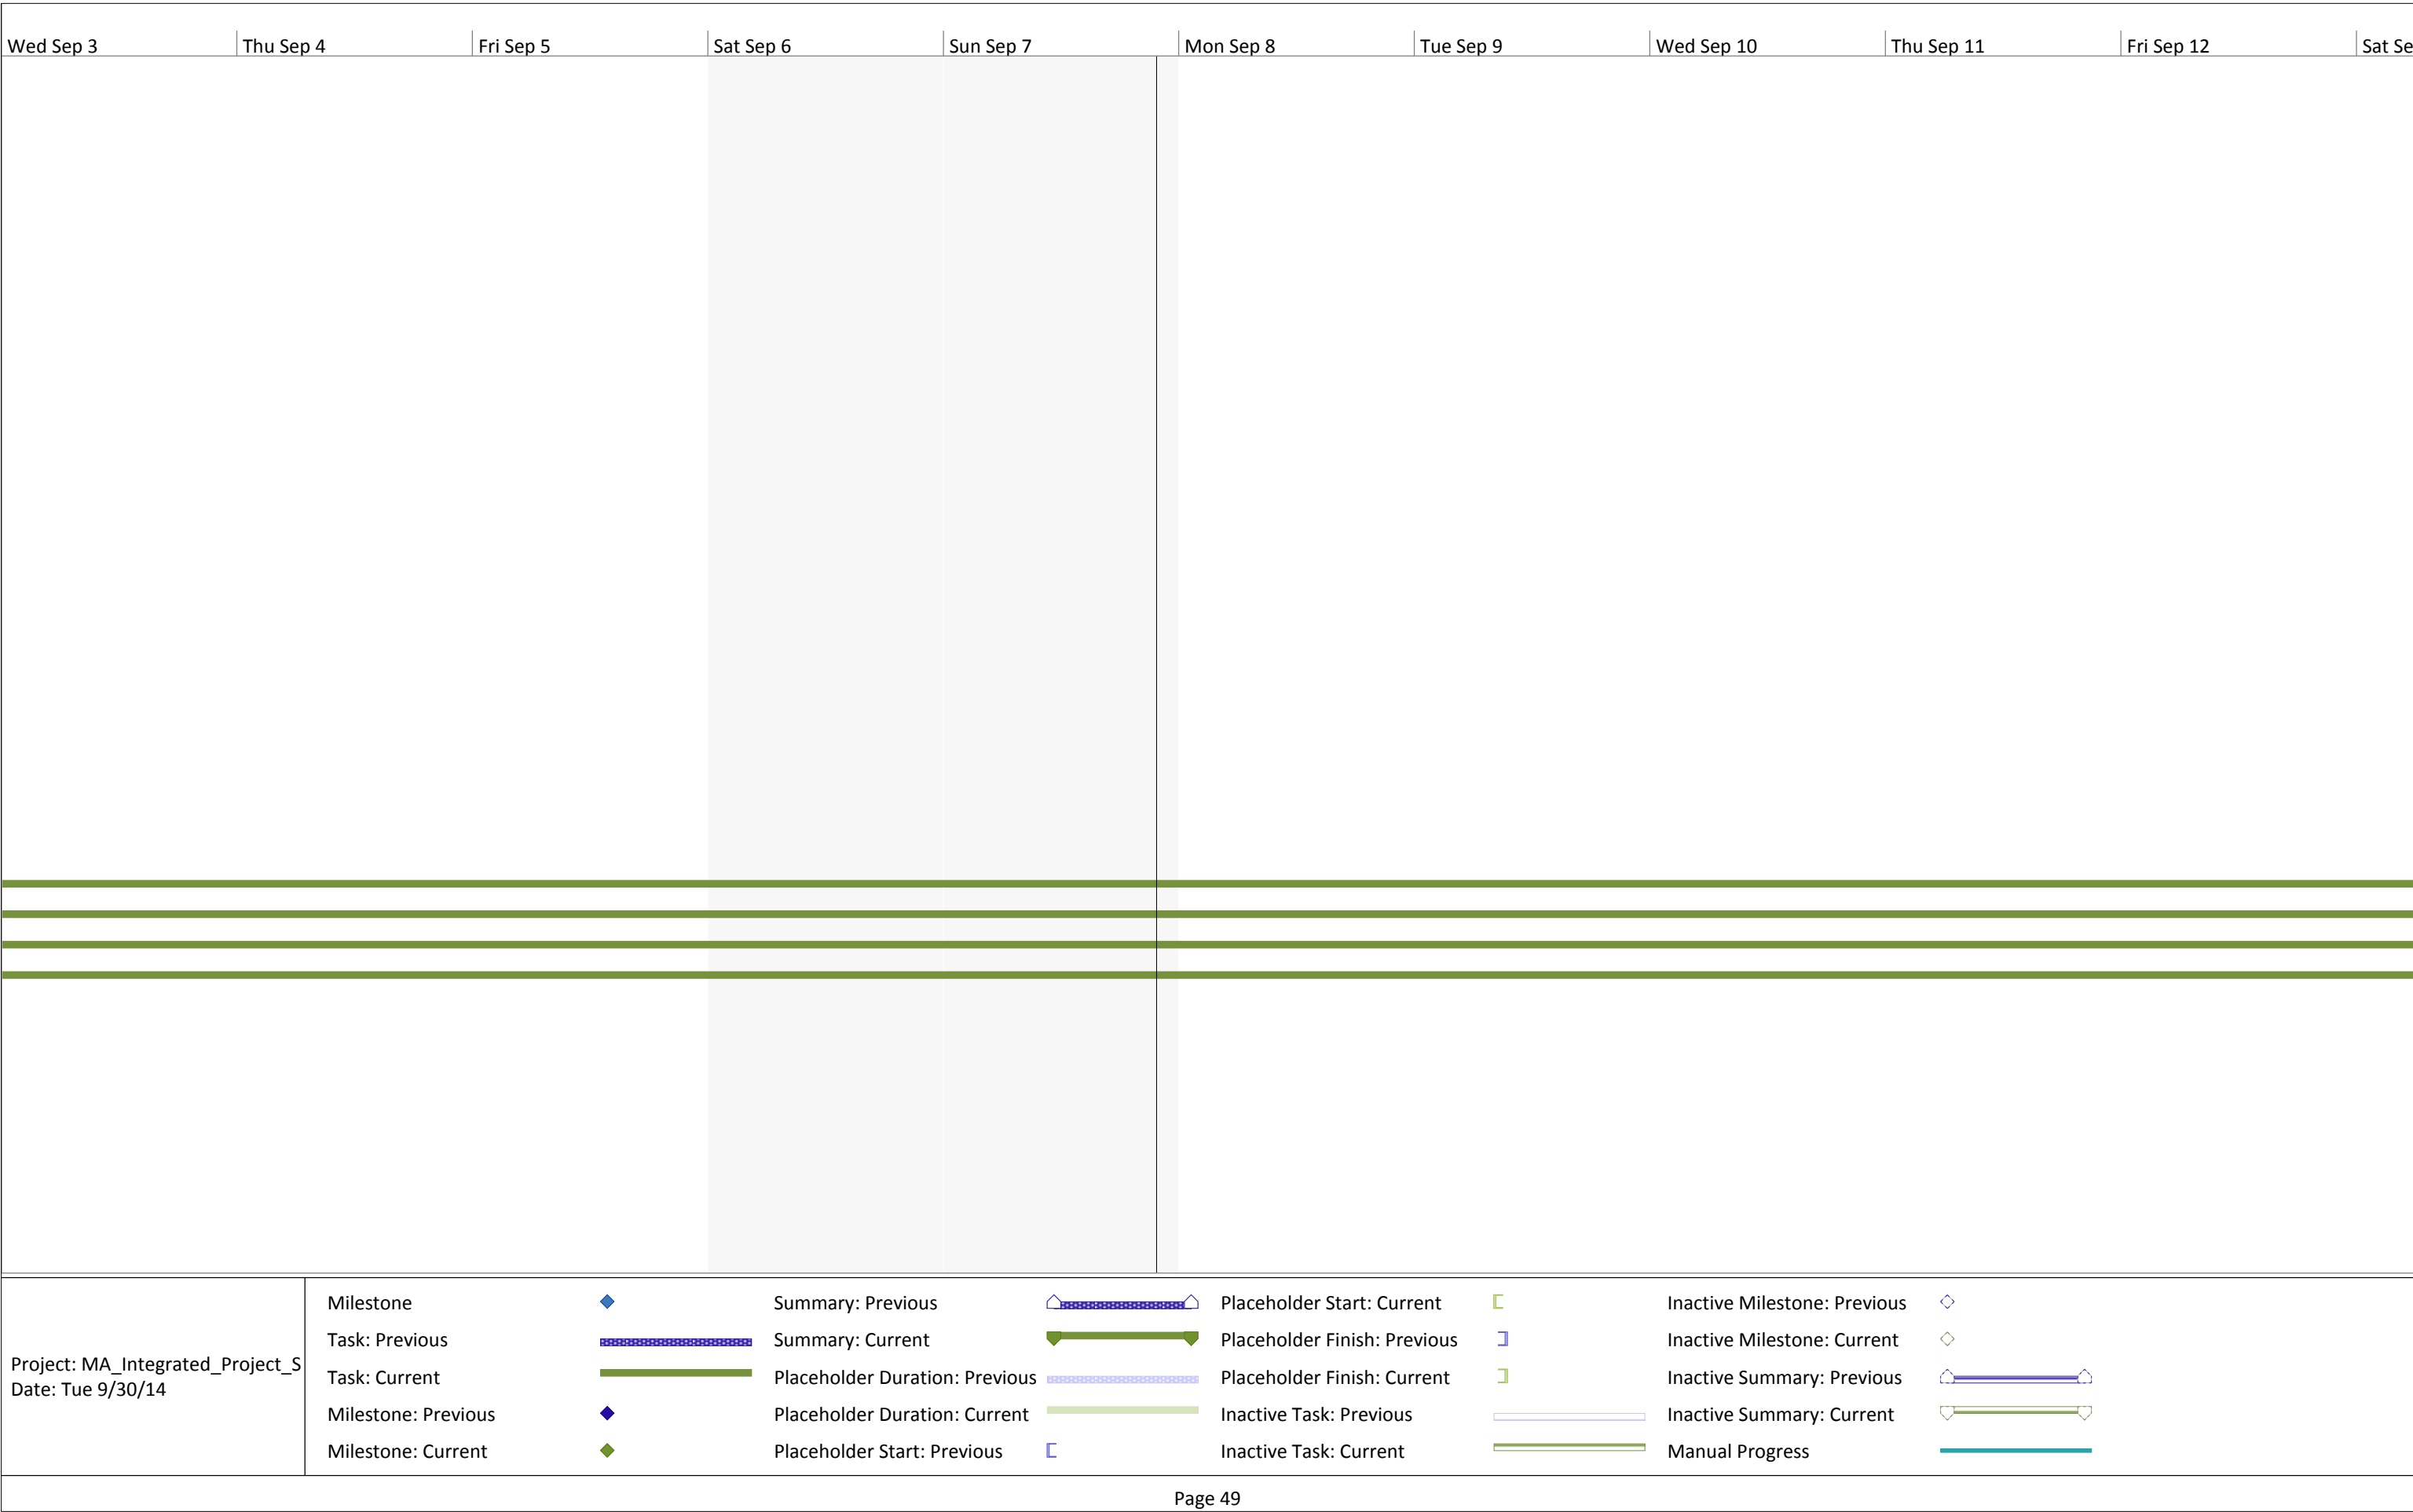





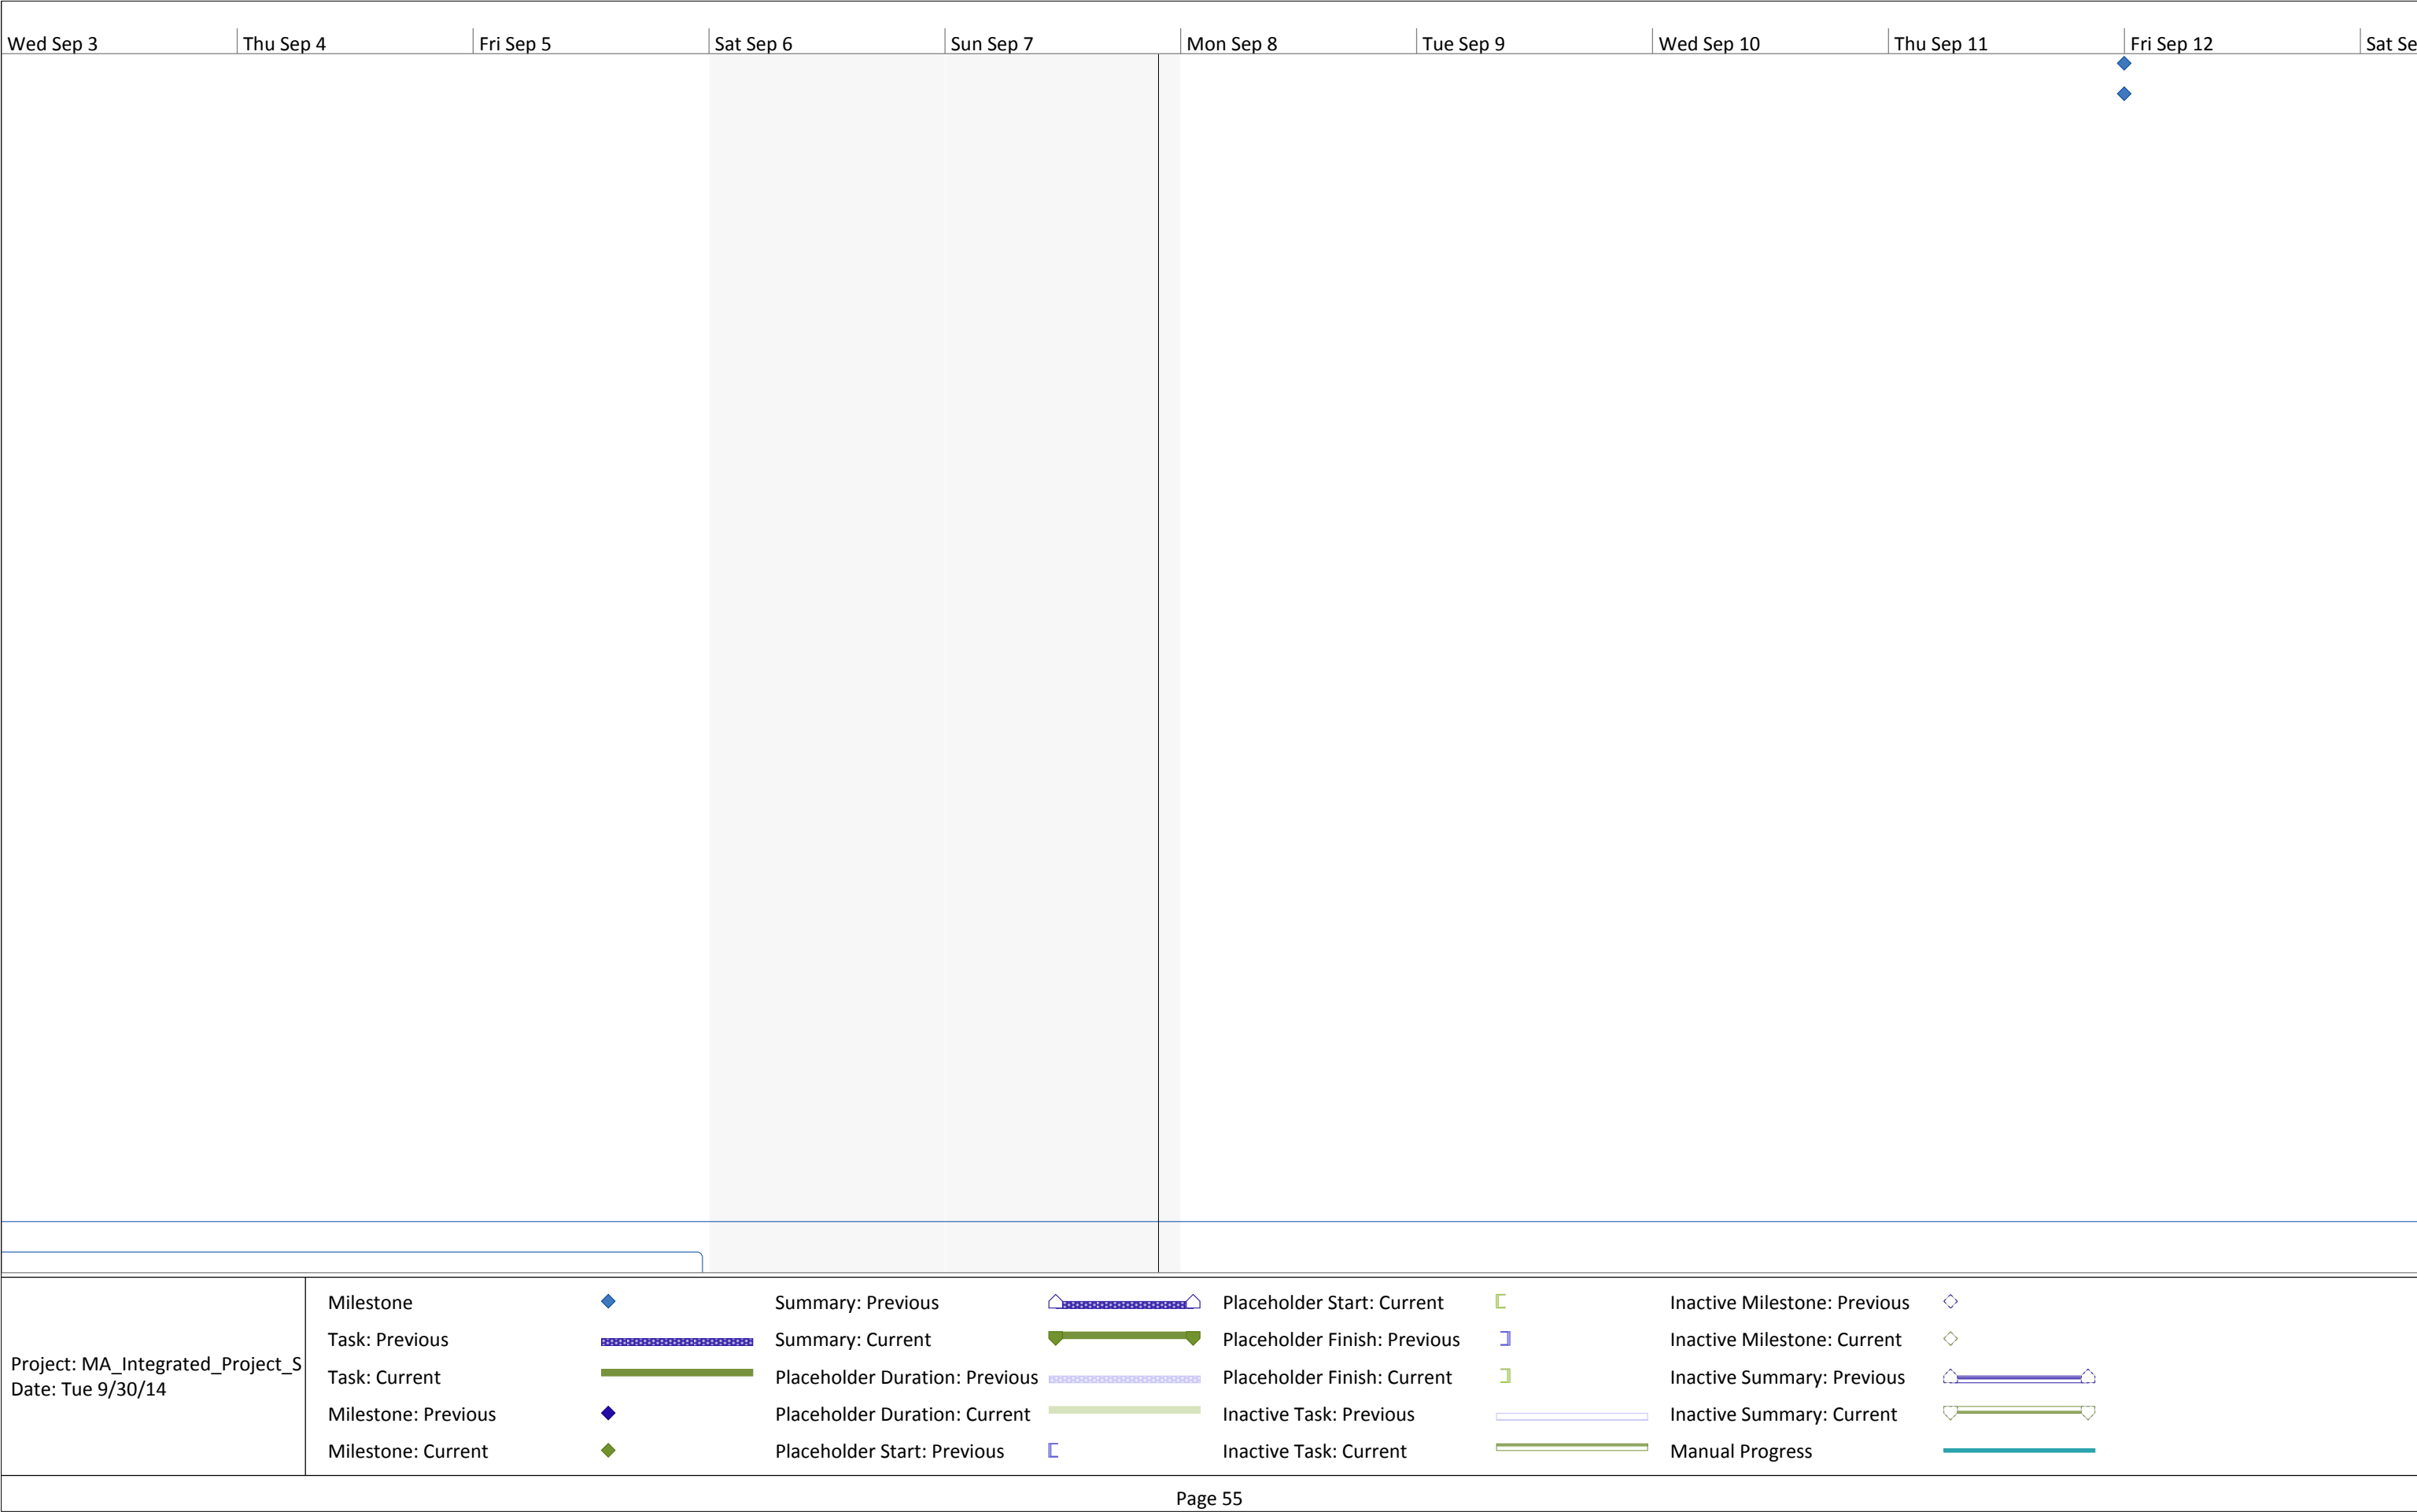



Page 55










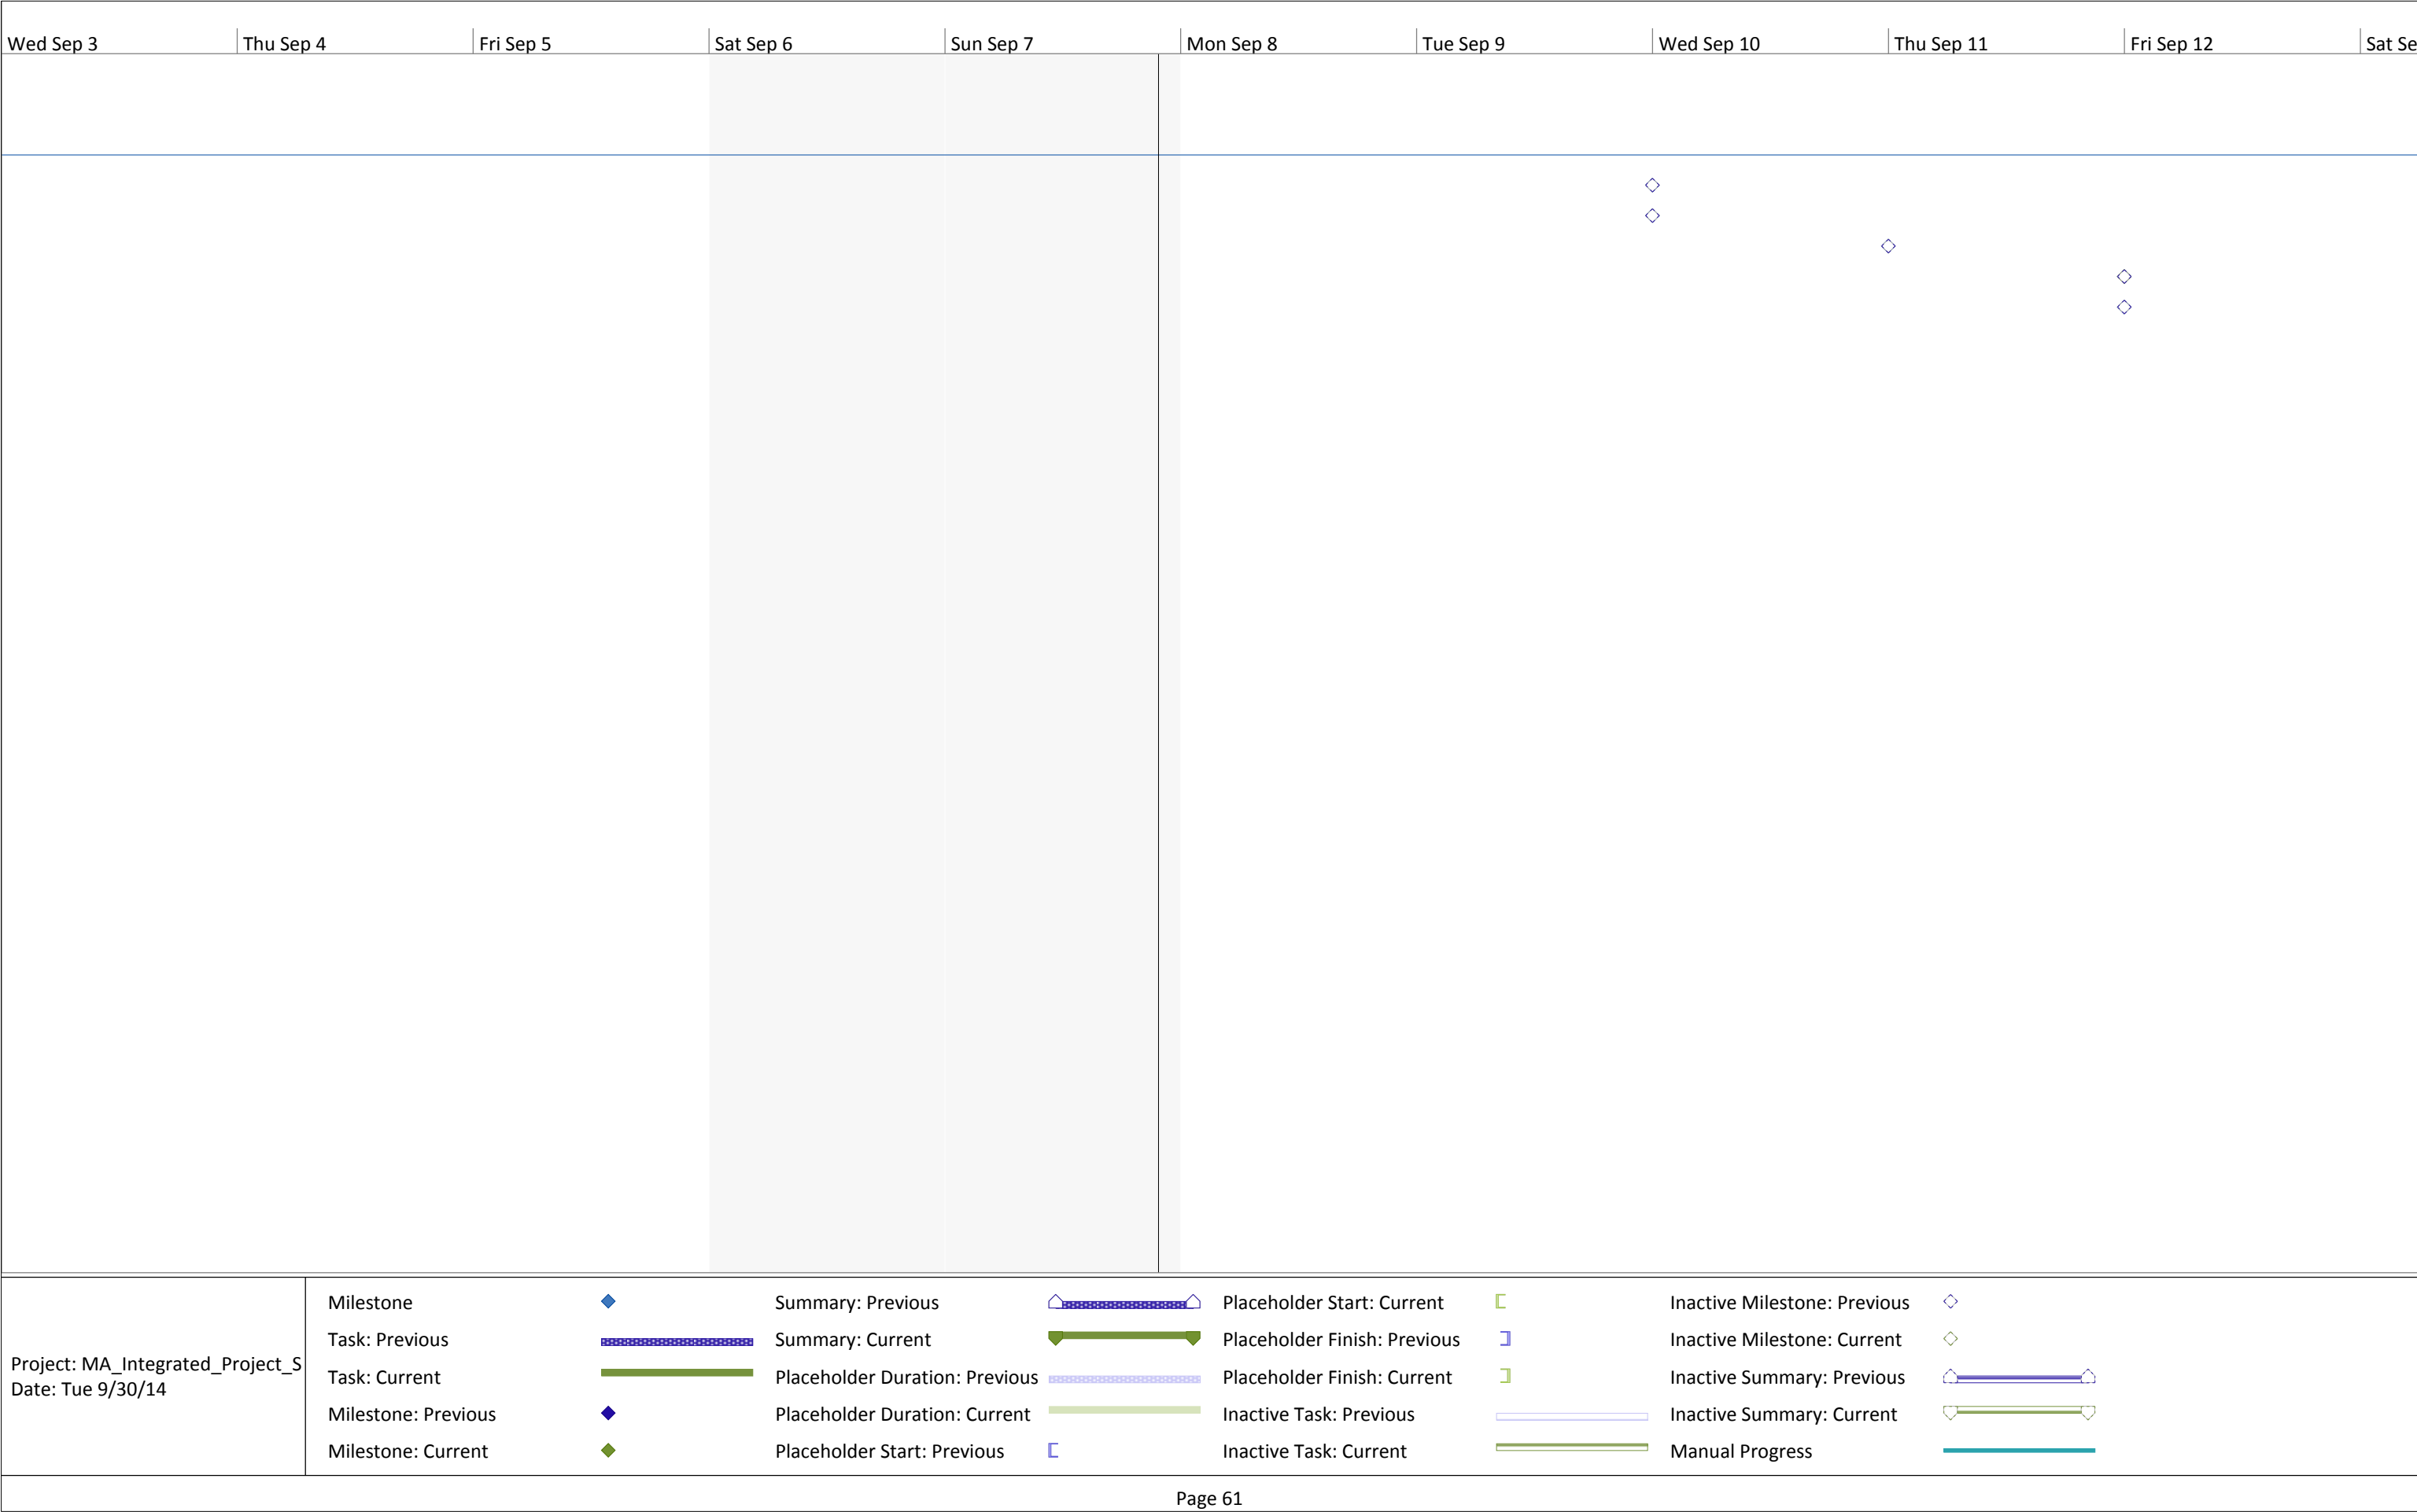





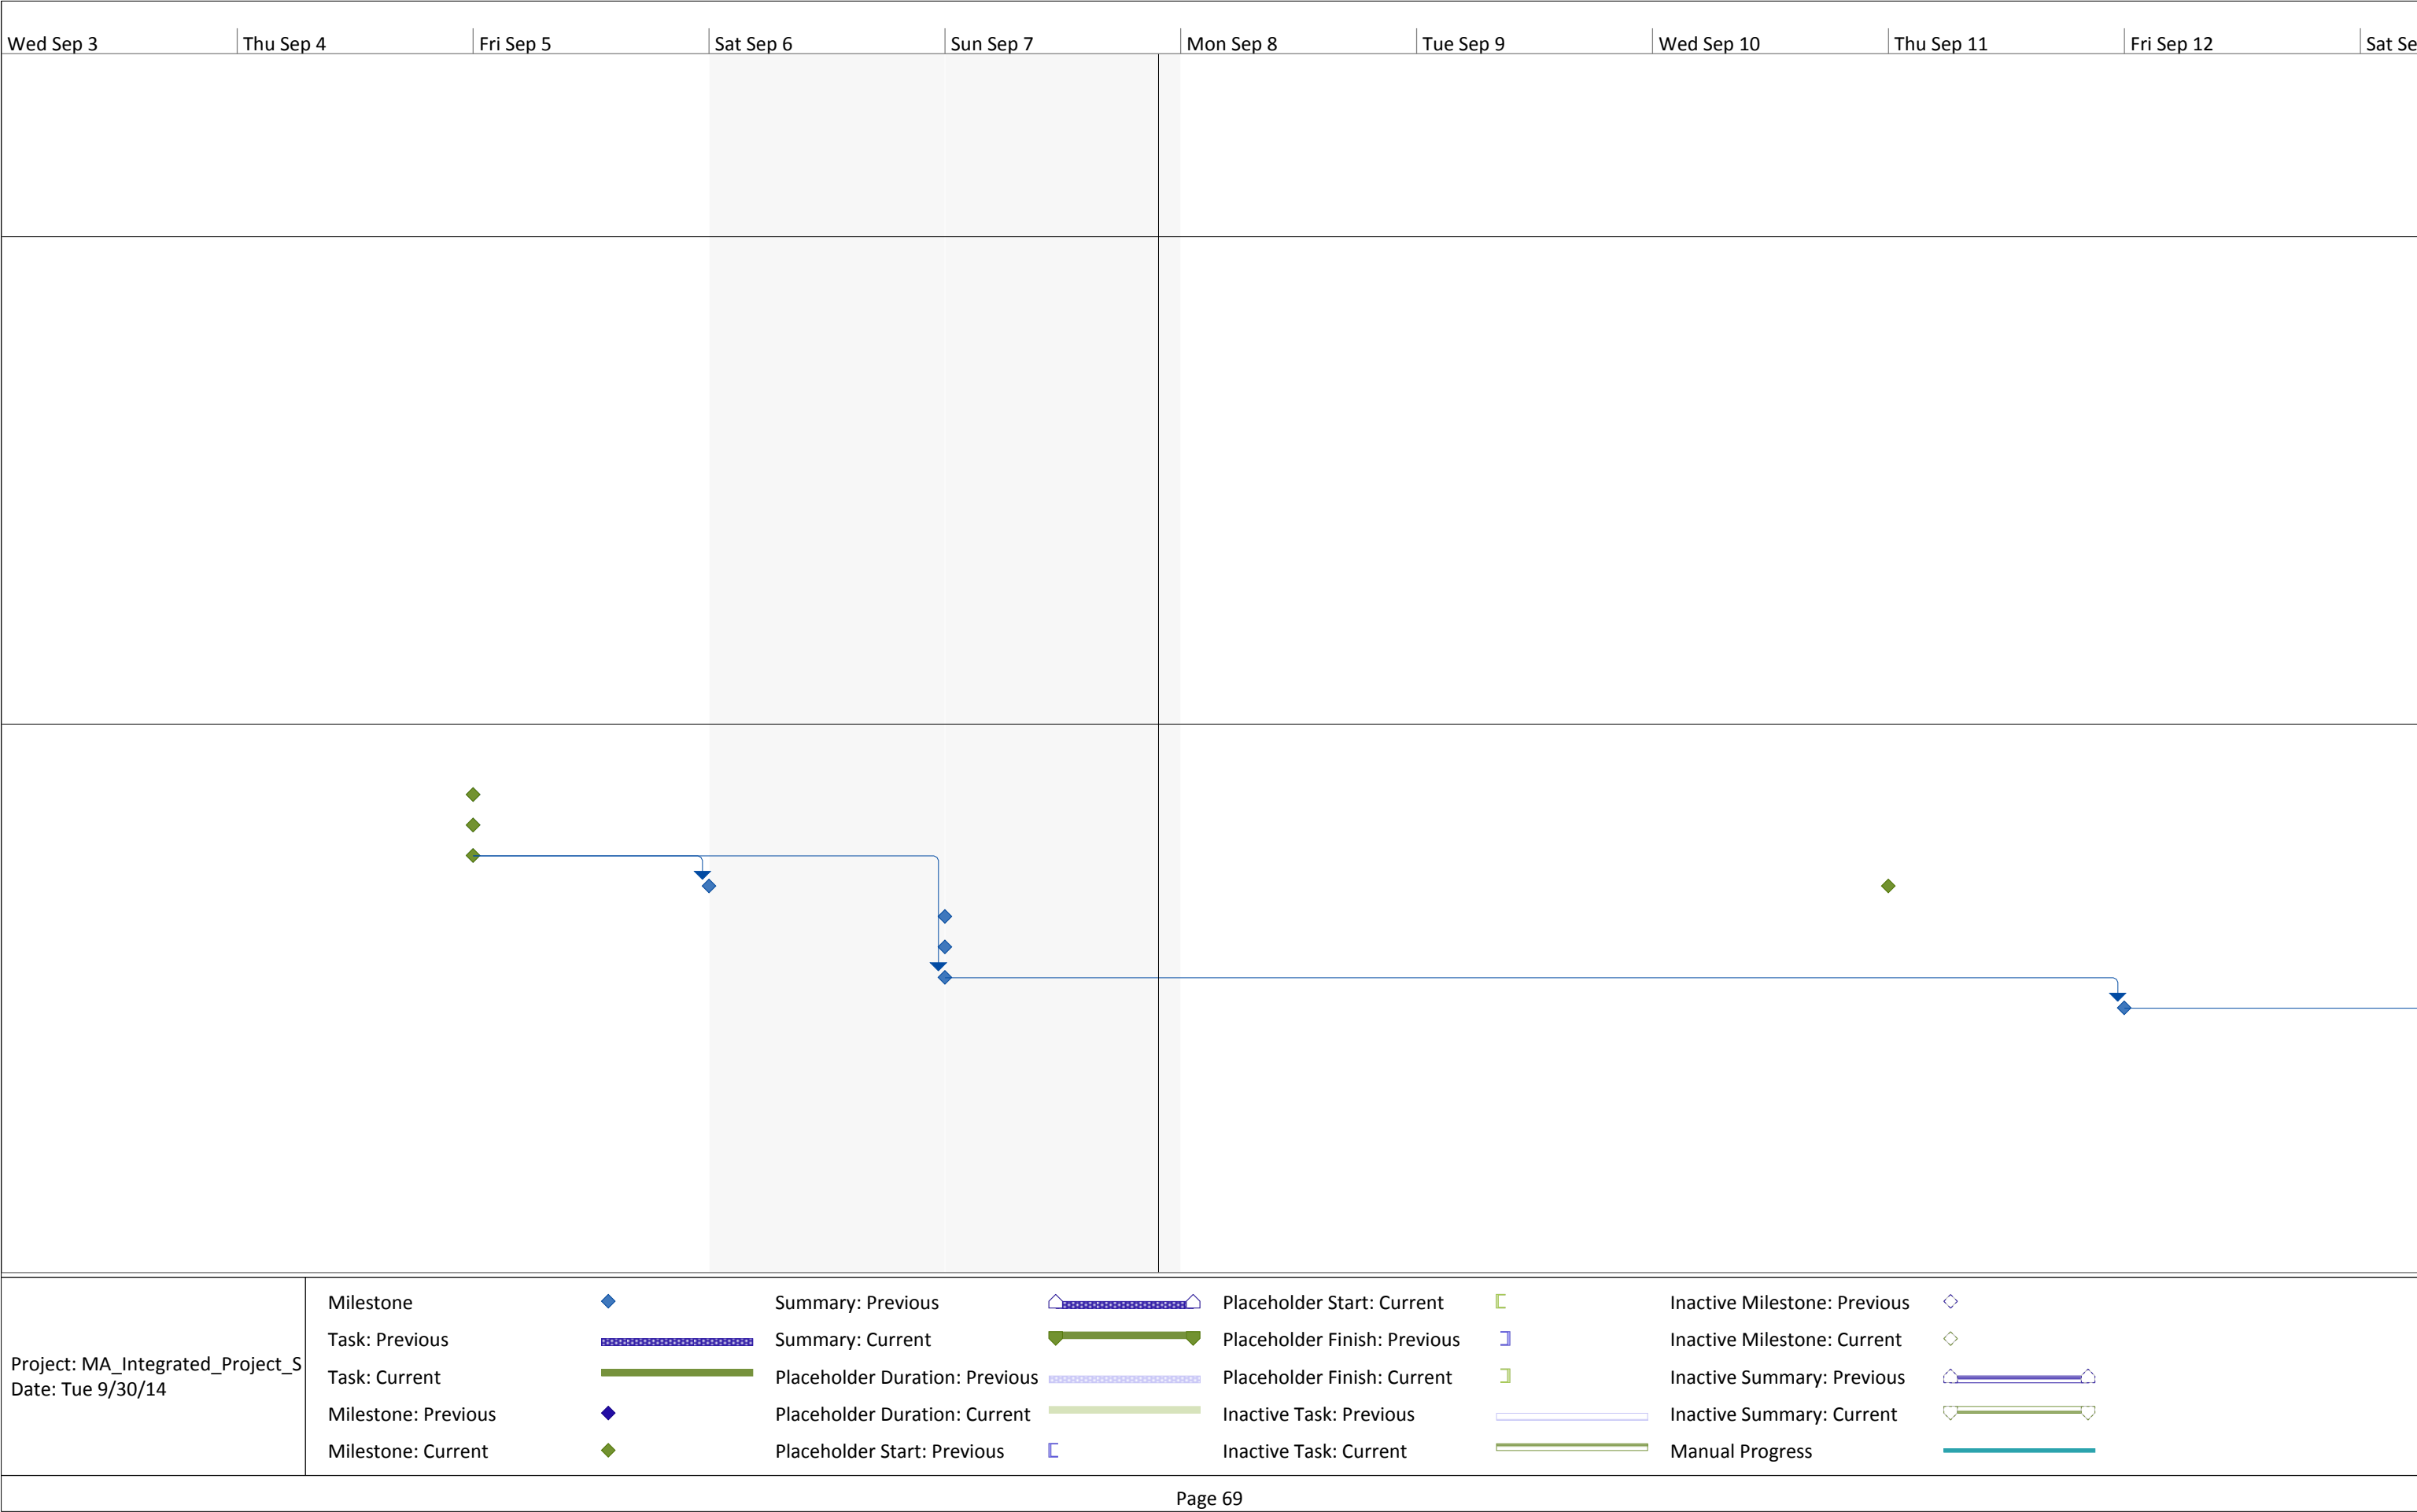




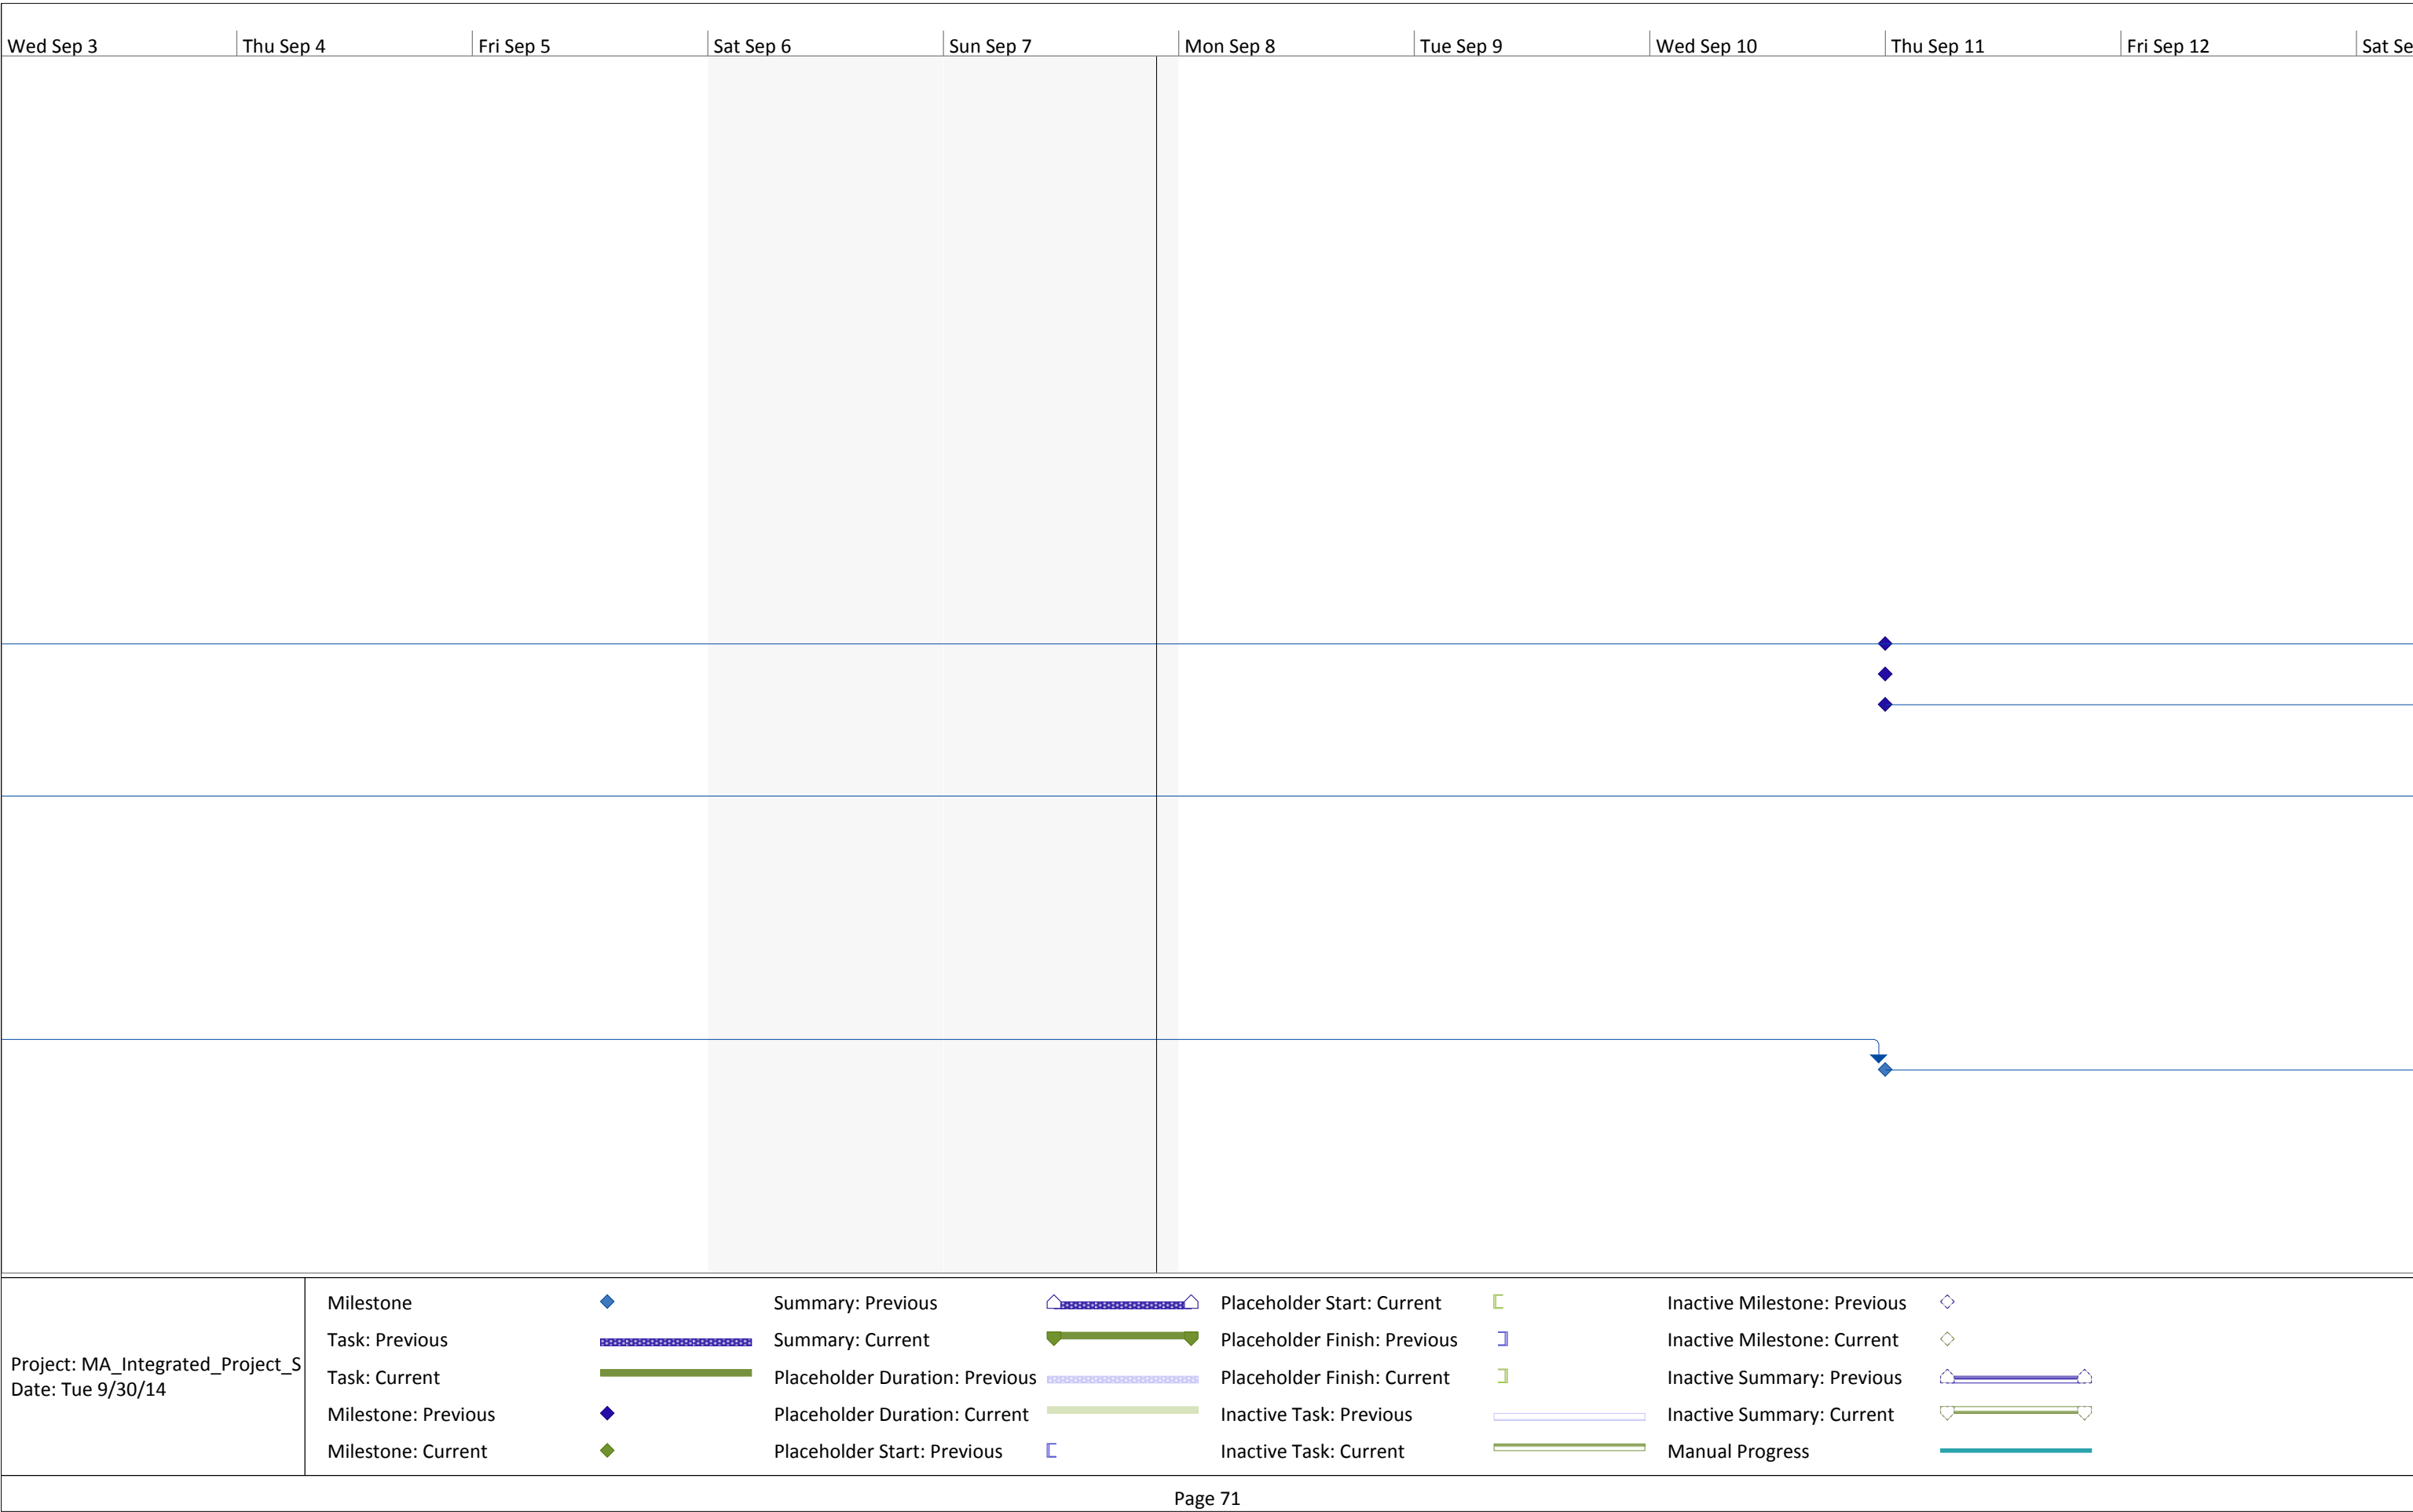







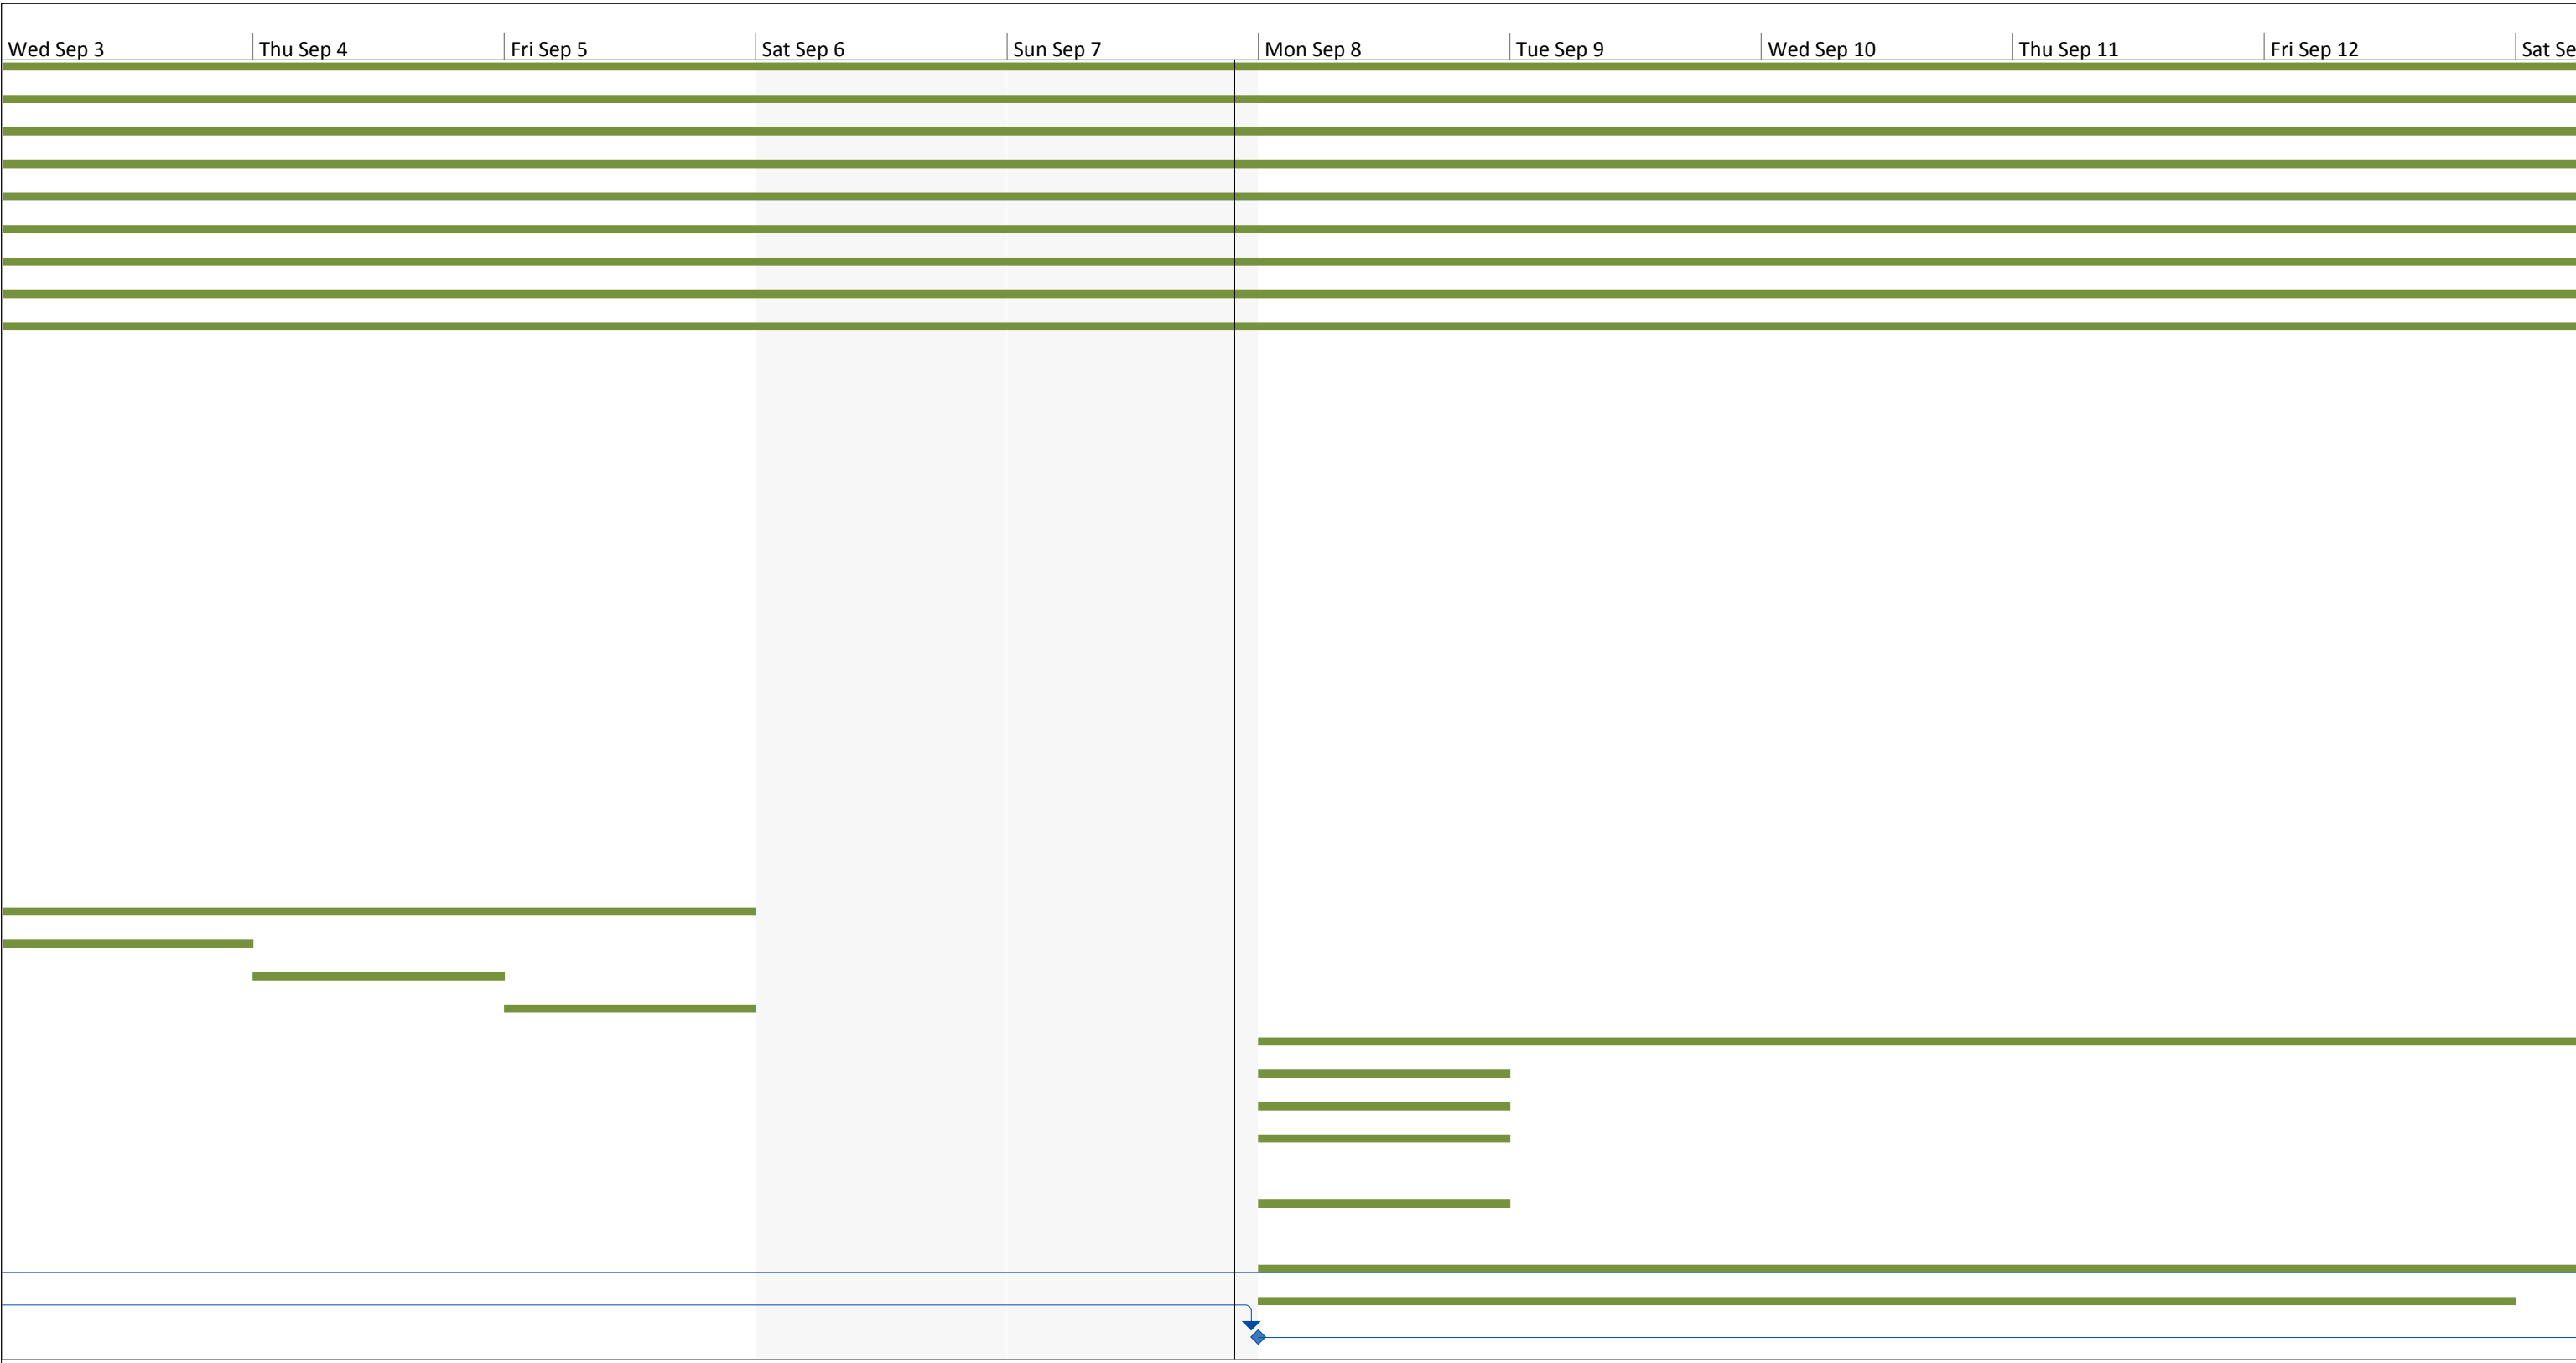




















[illegible]




Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

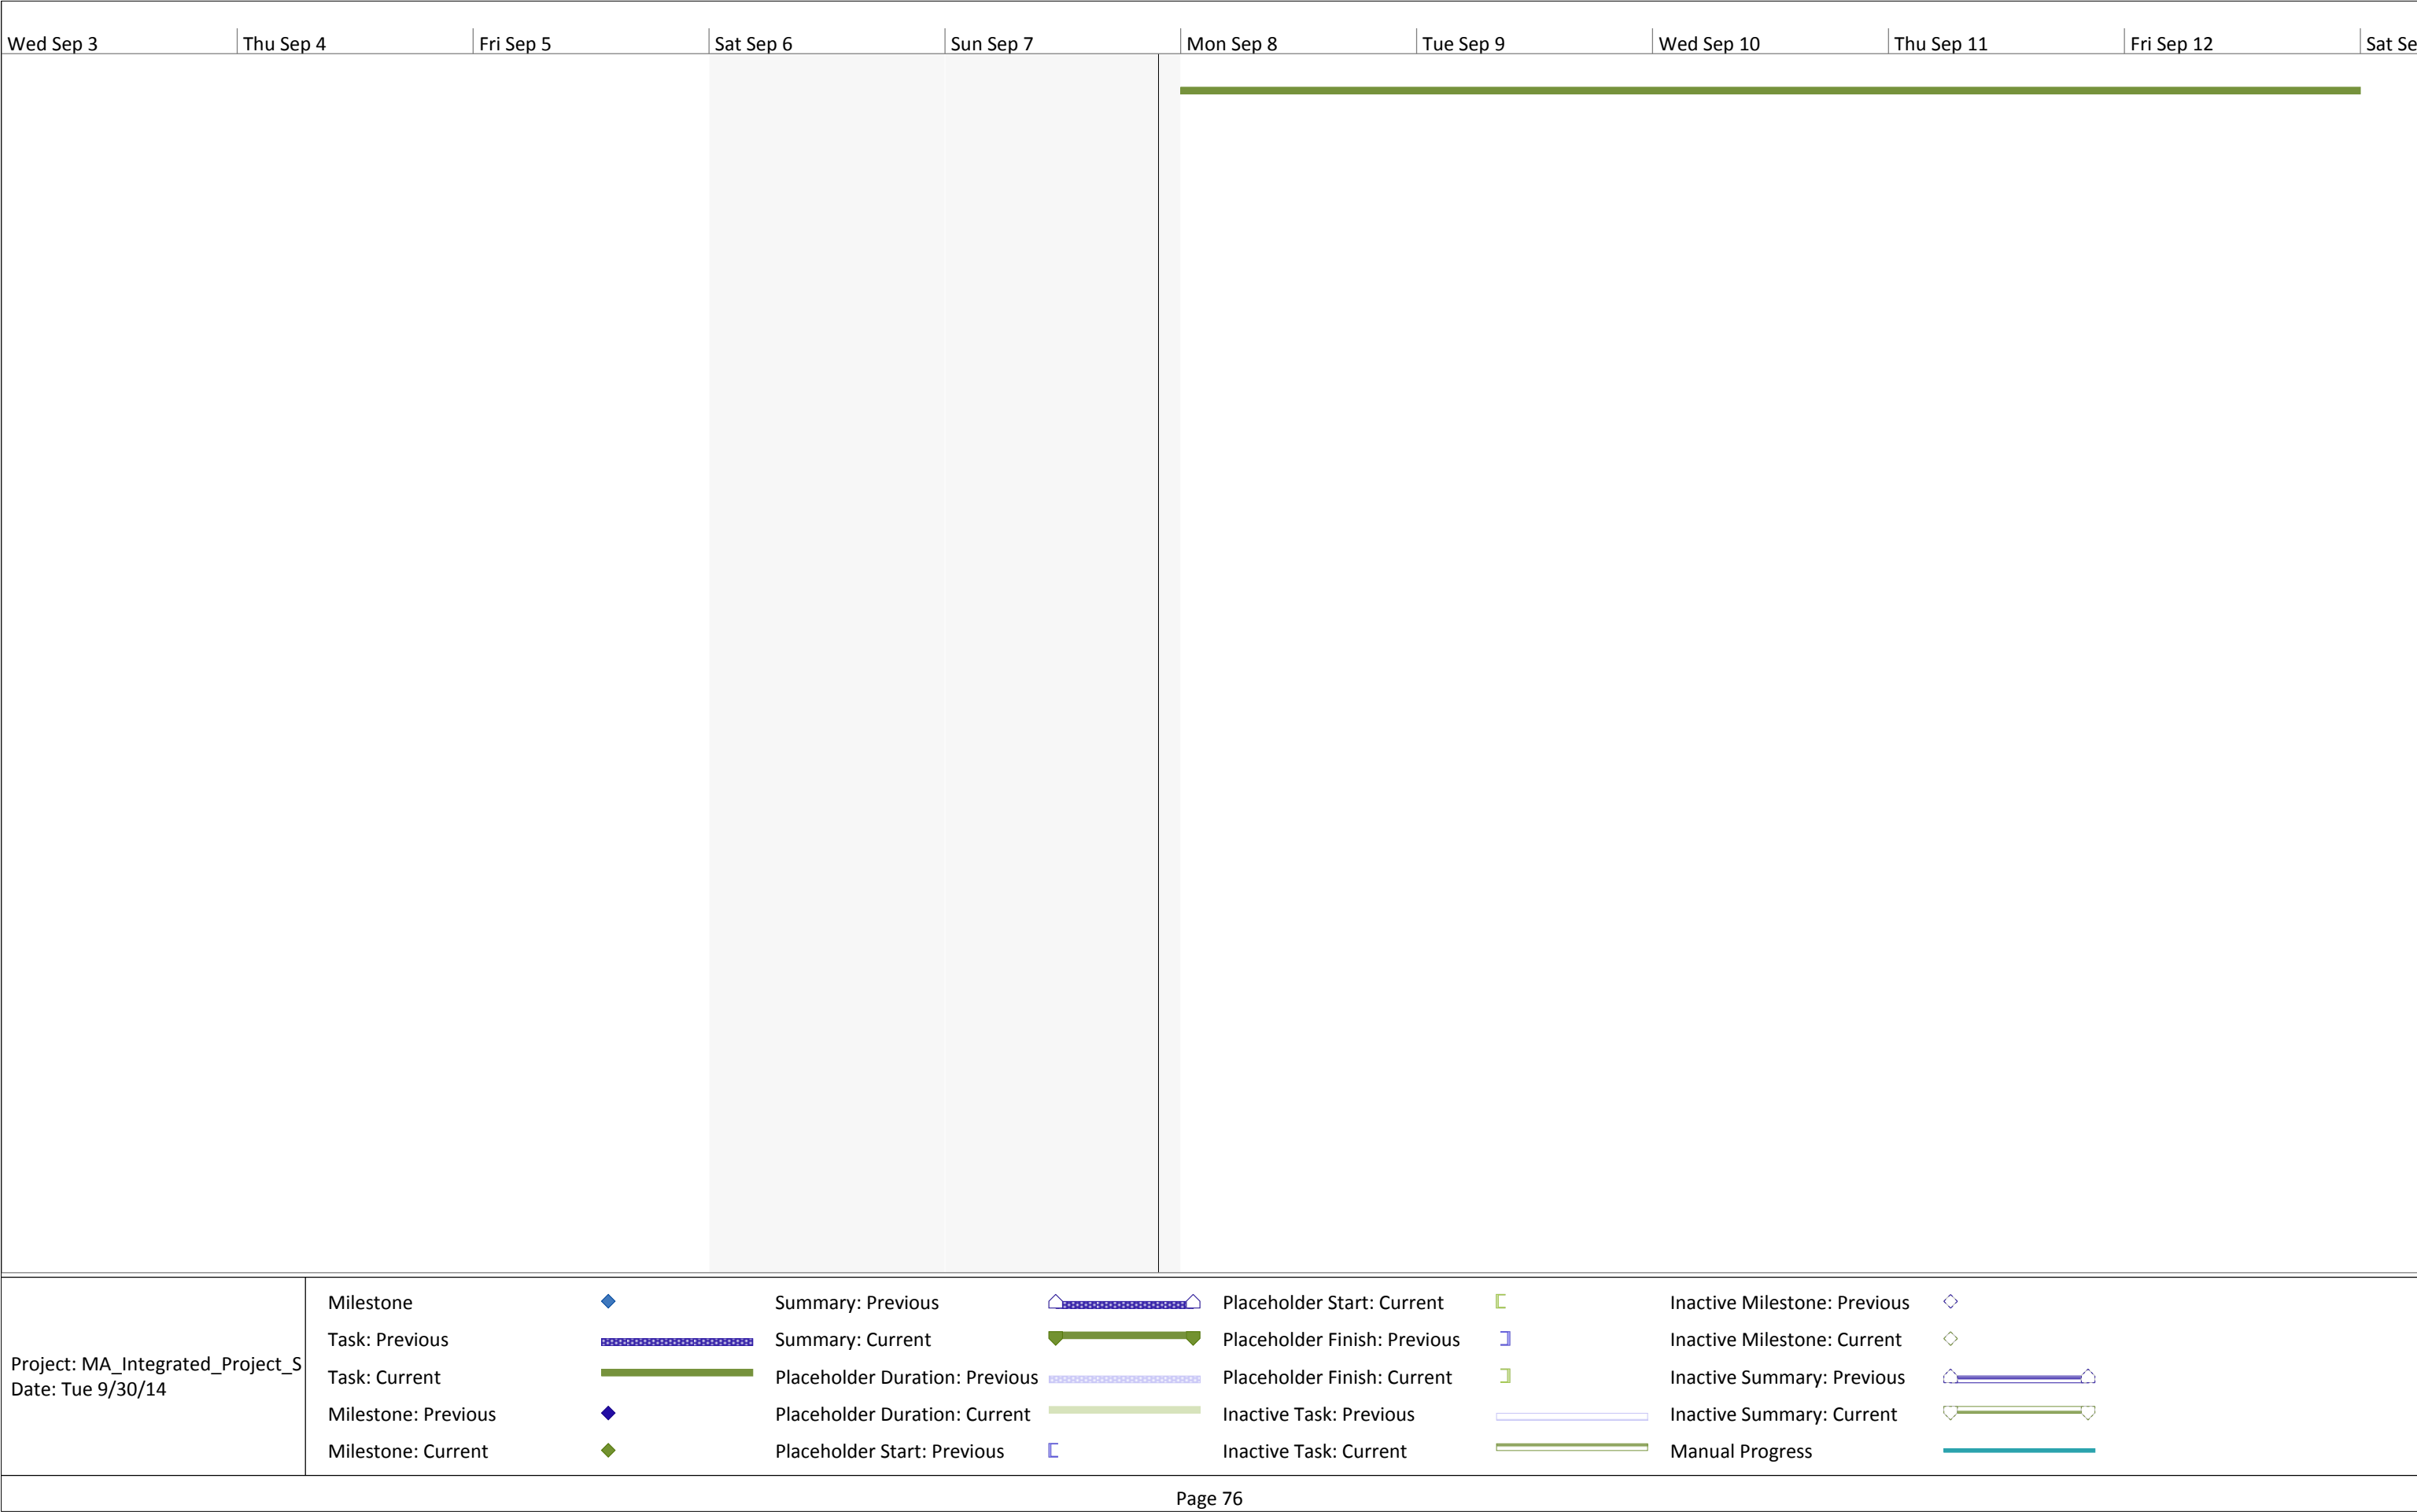




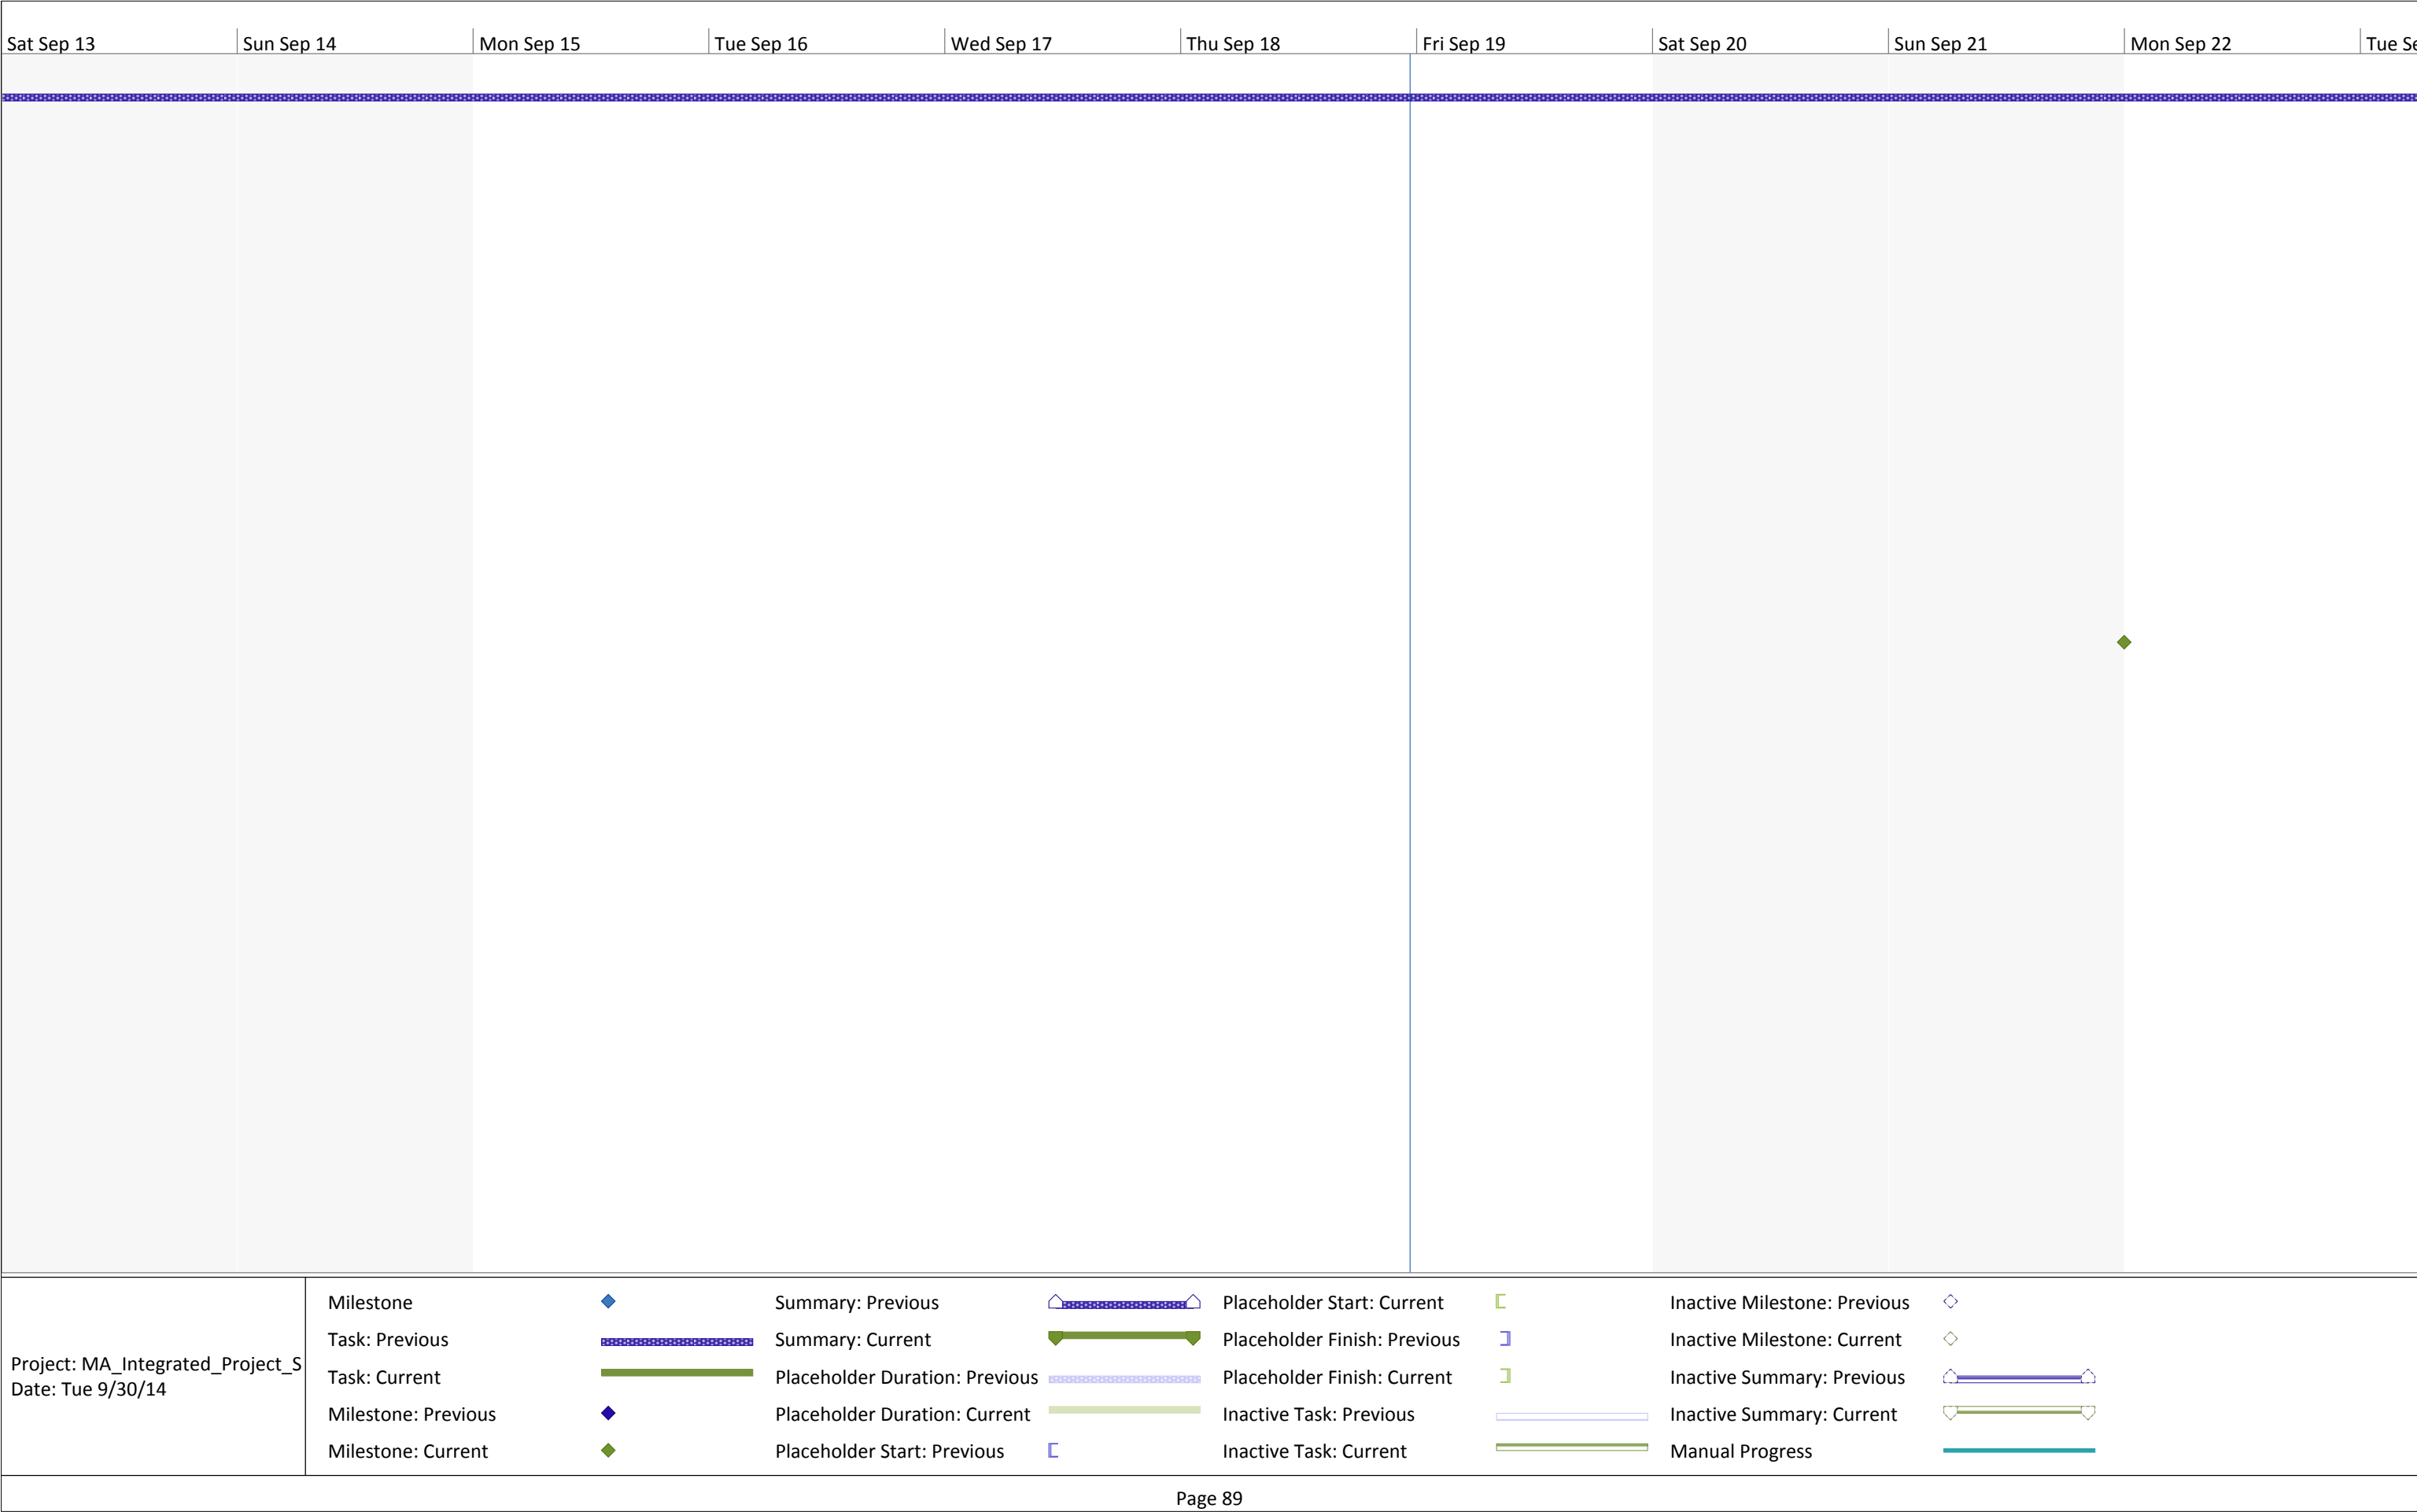


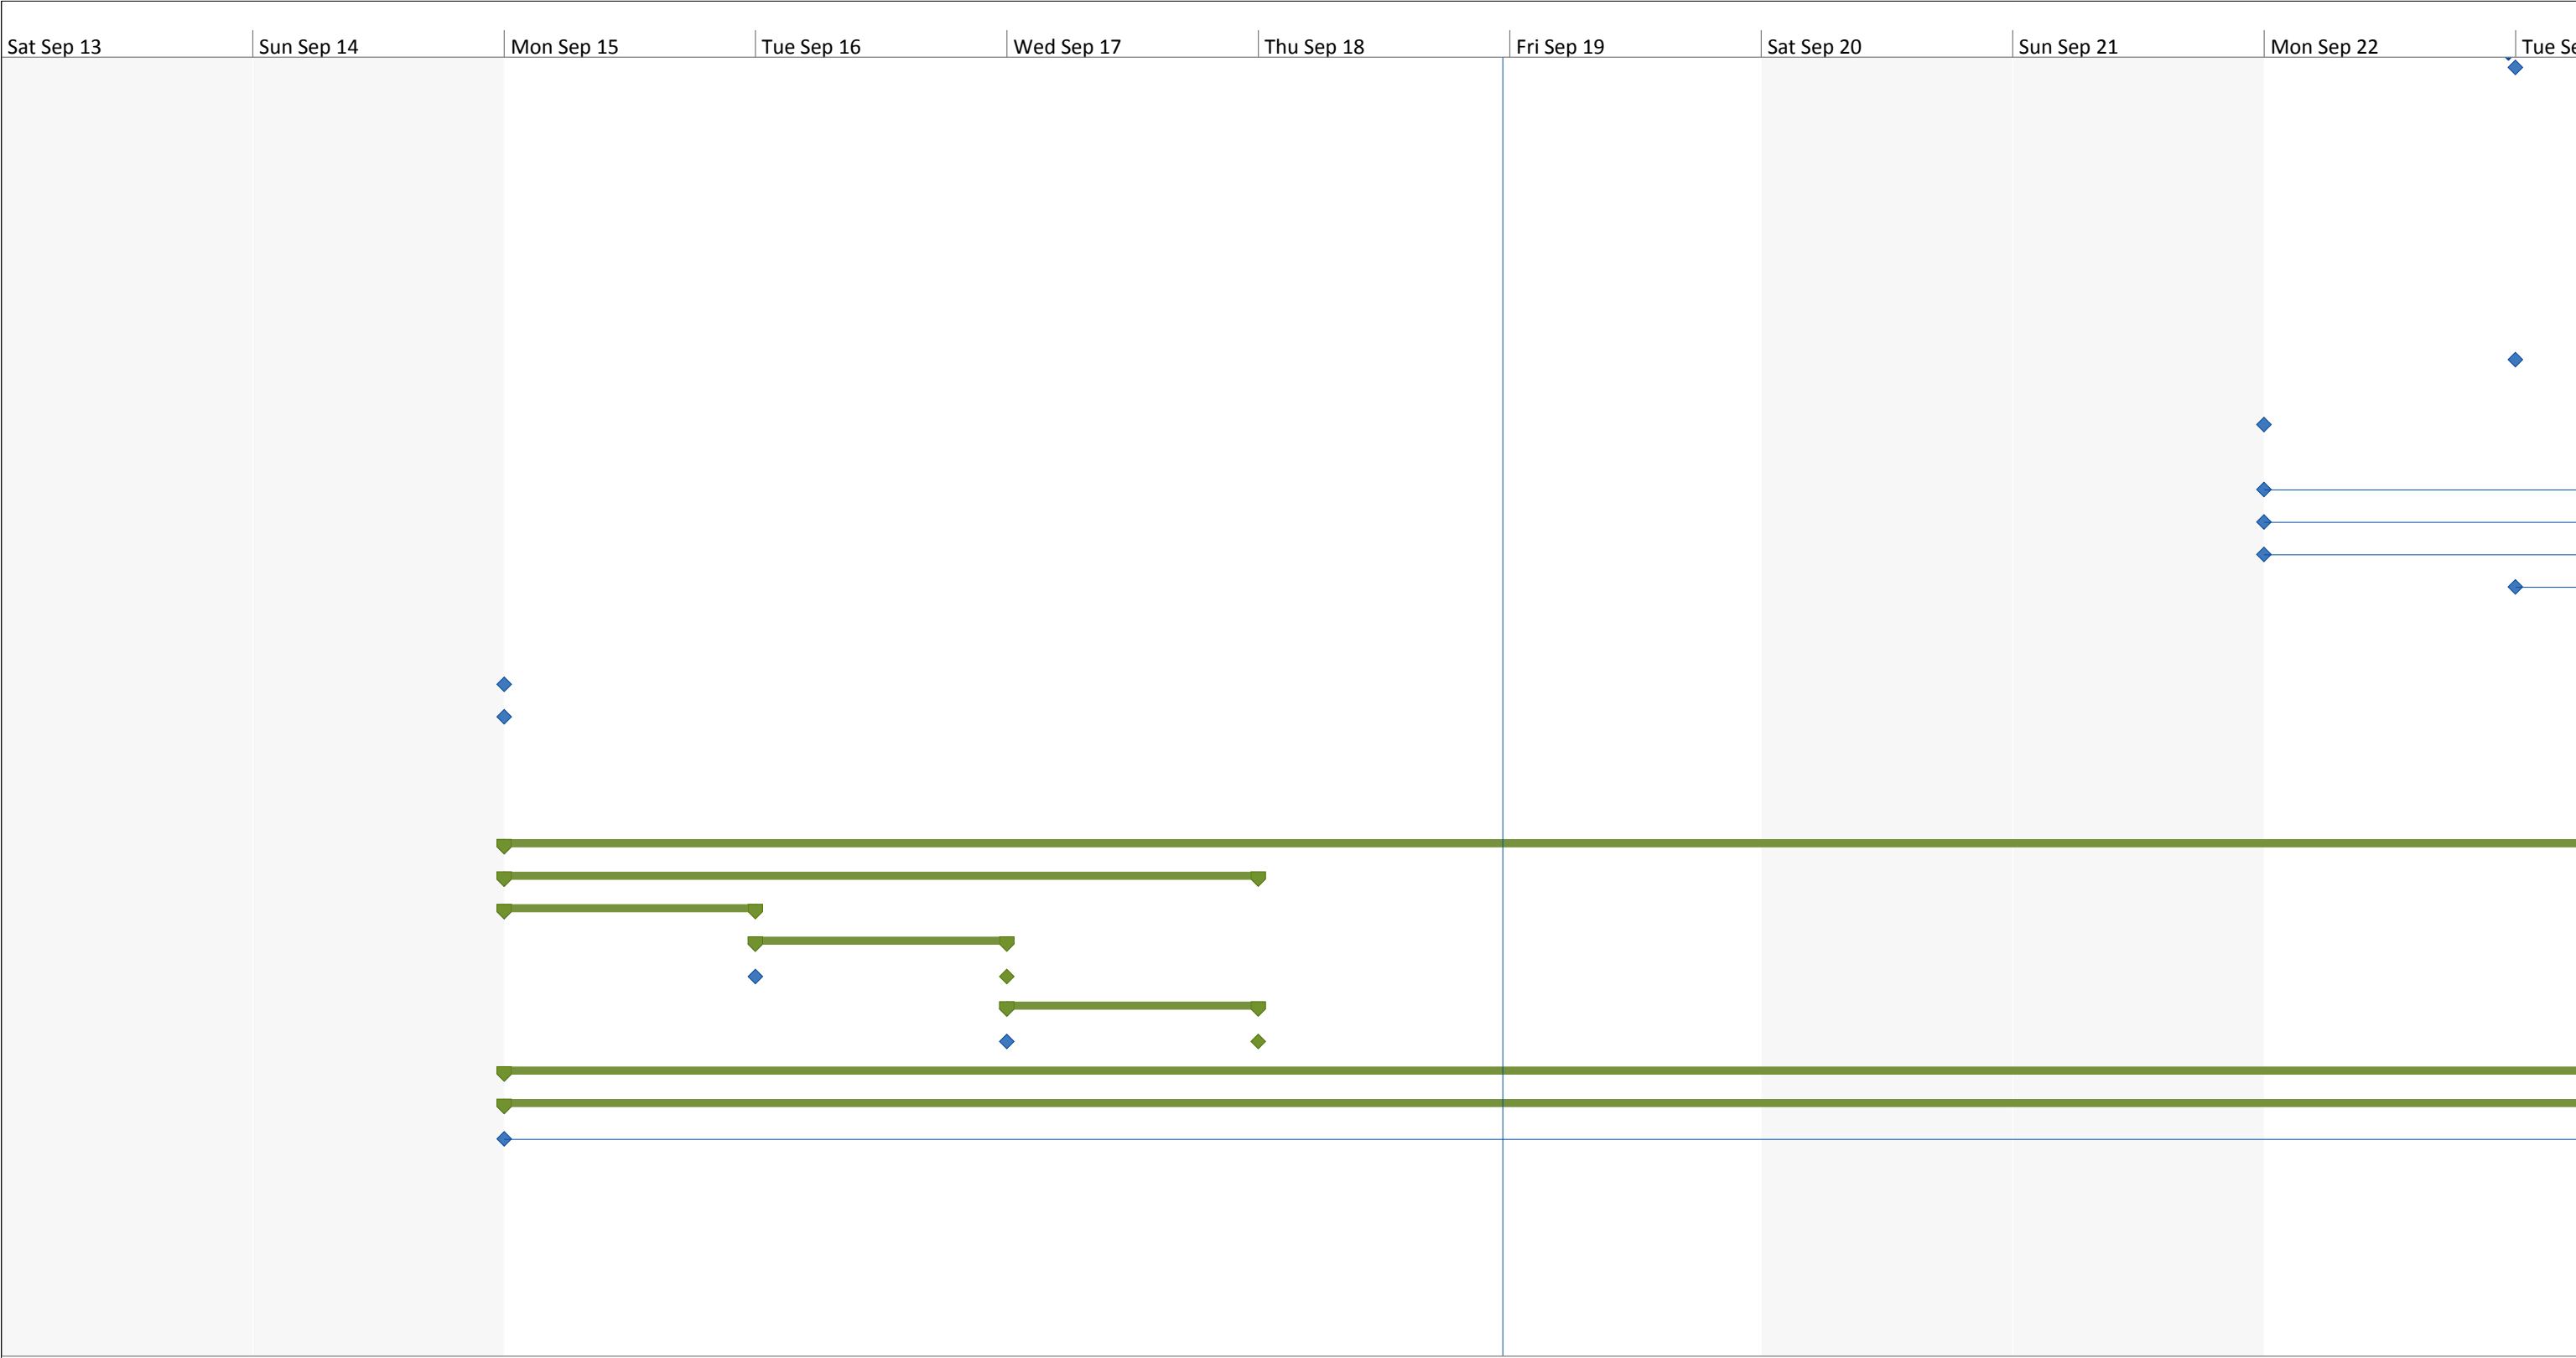


Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

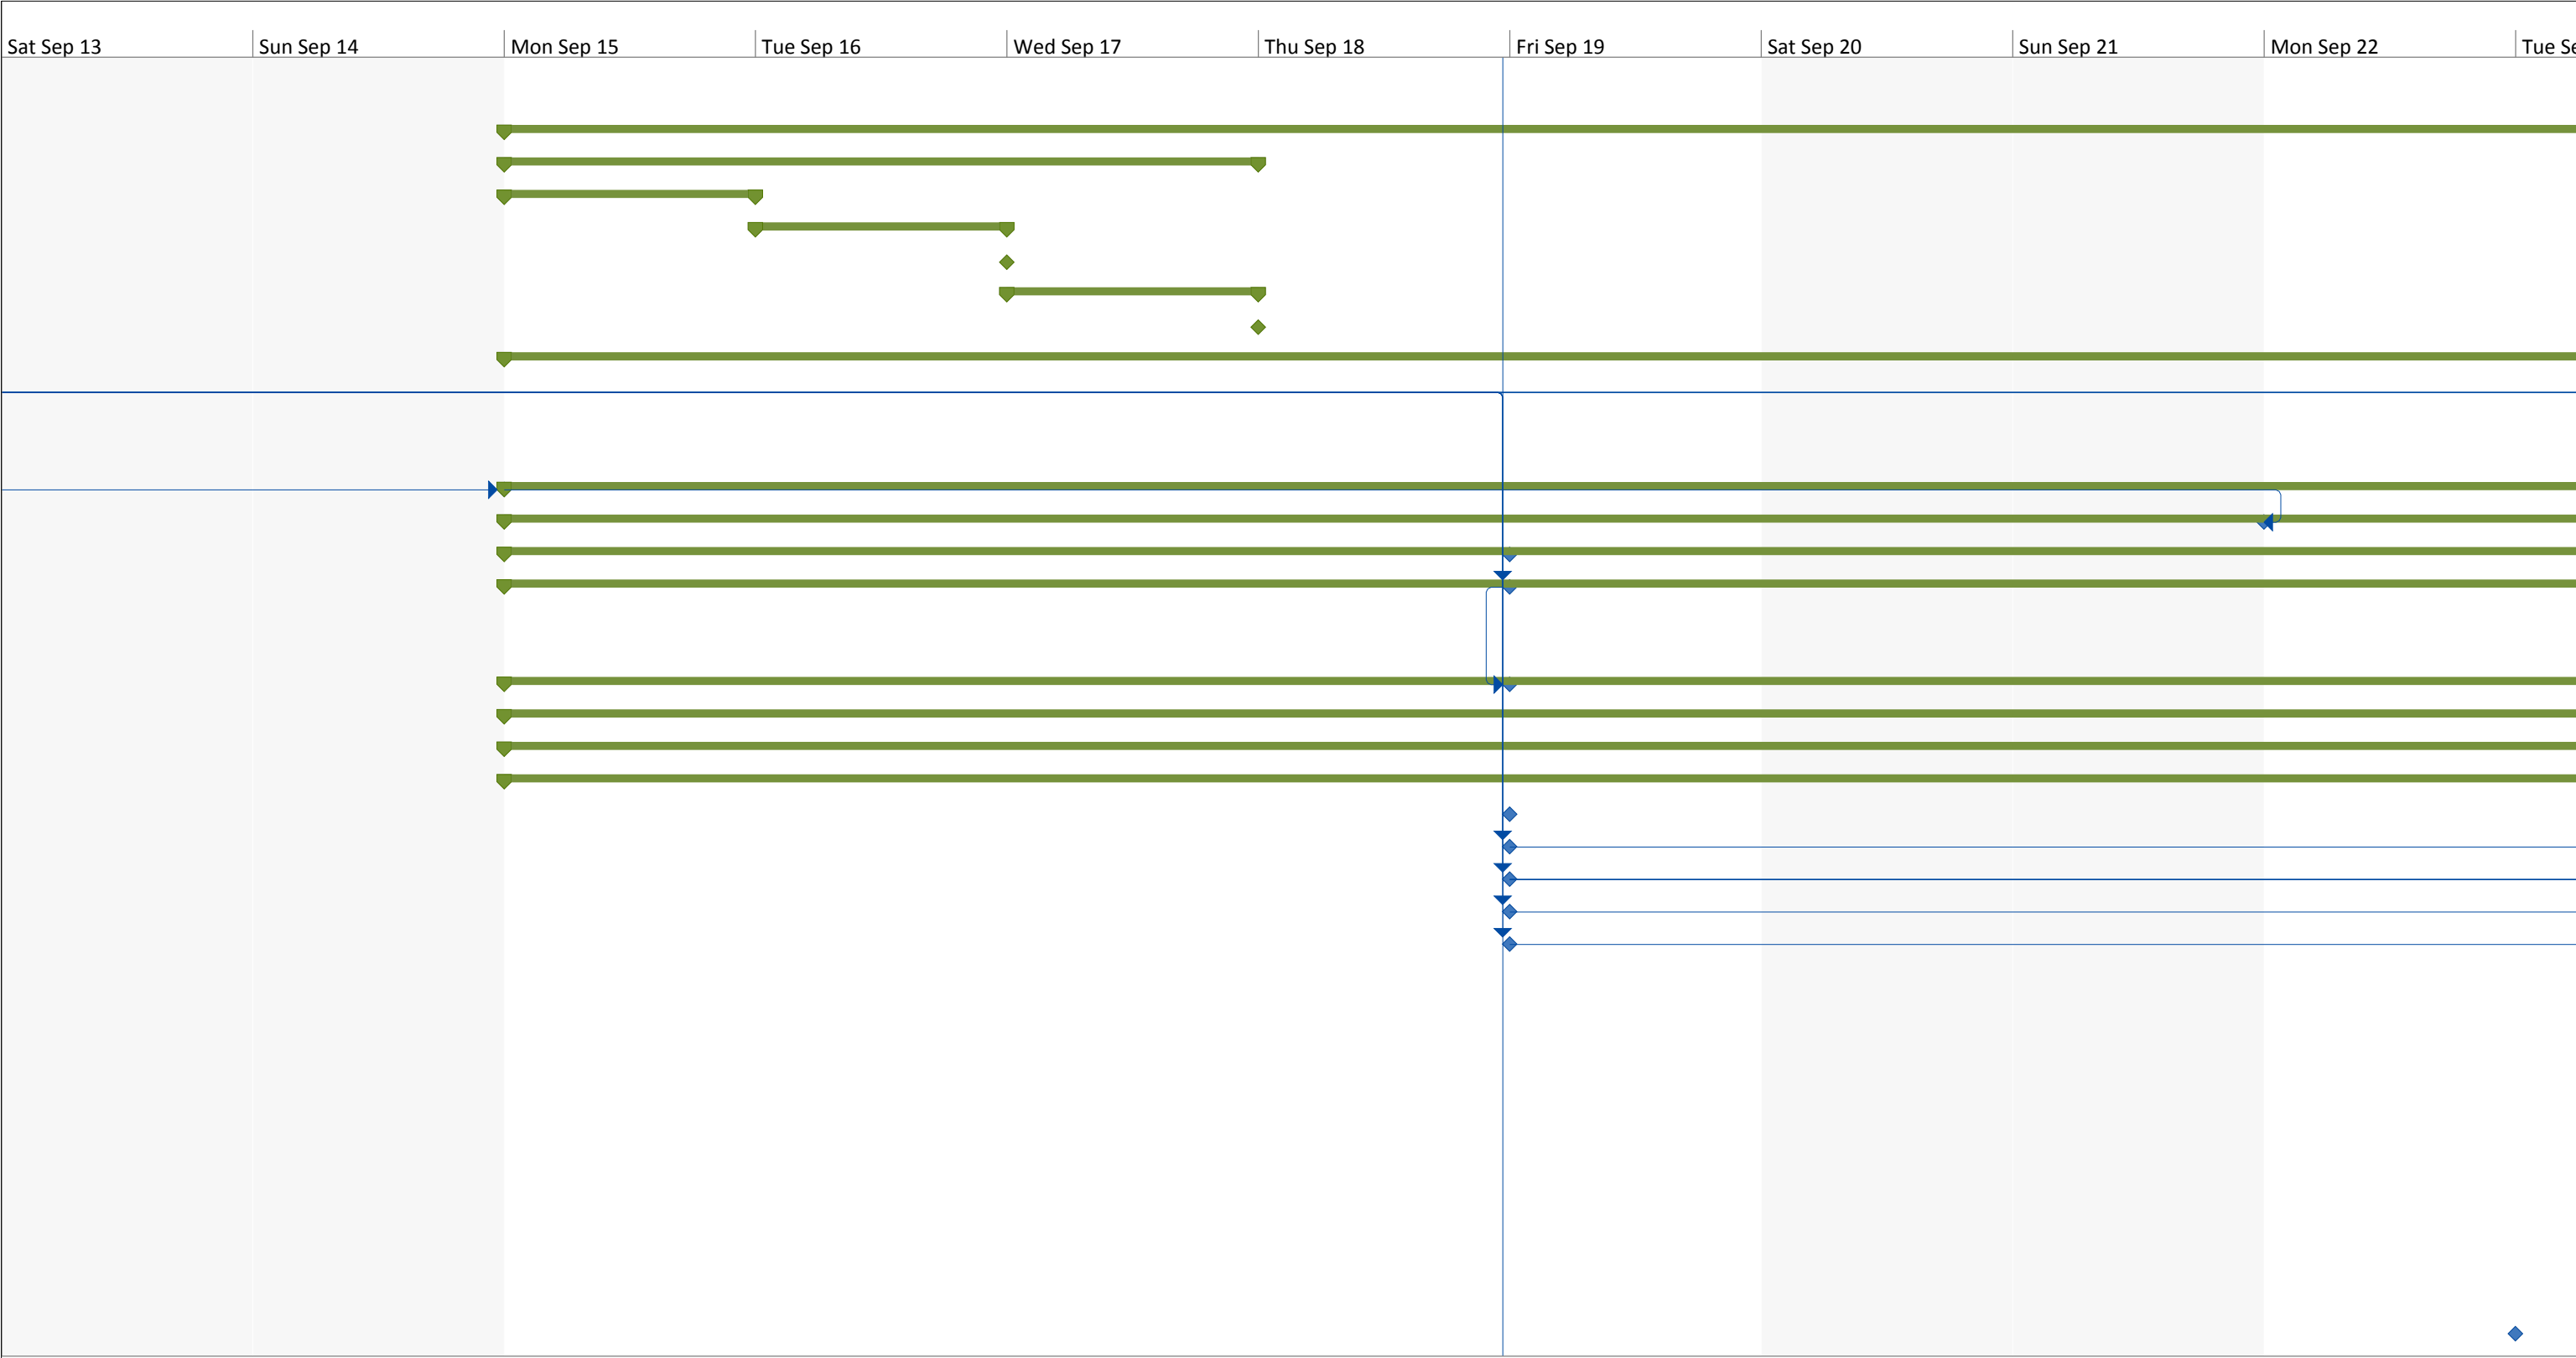


Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

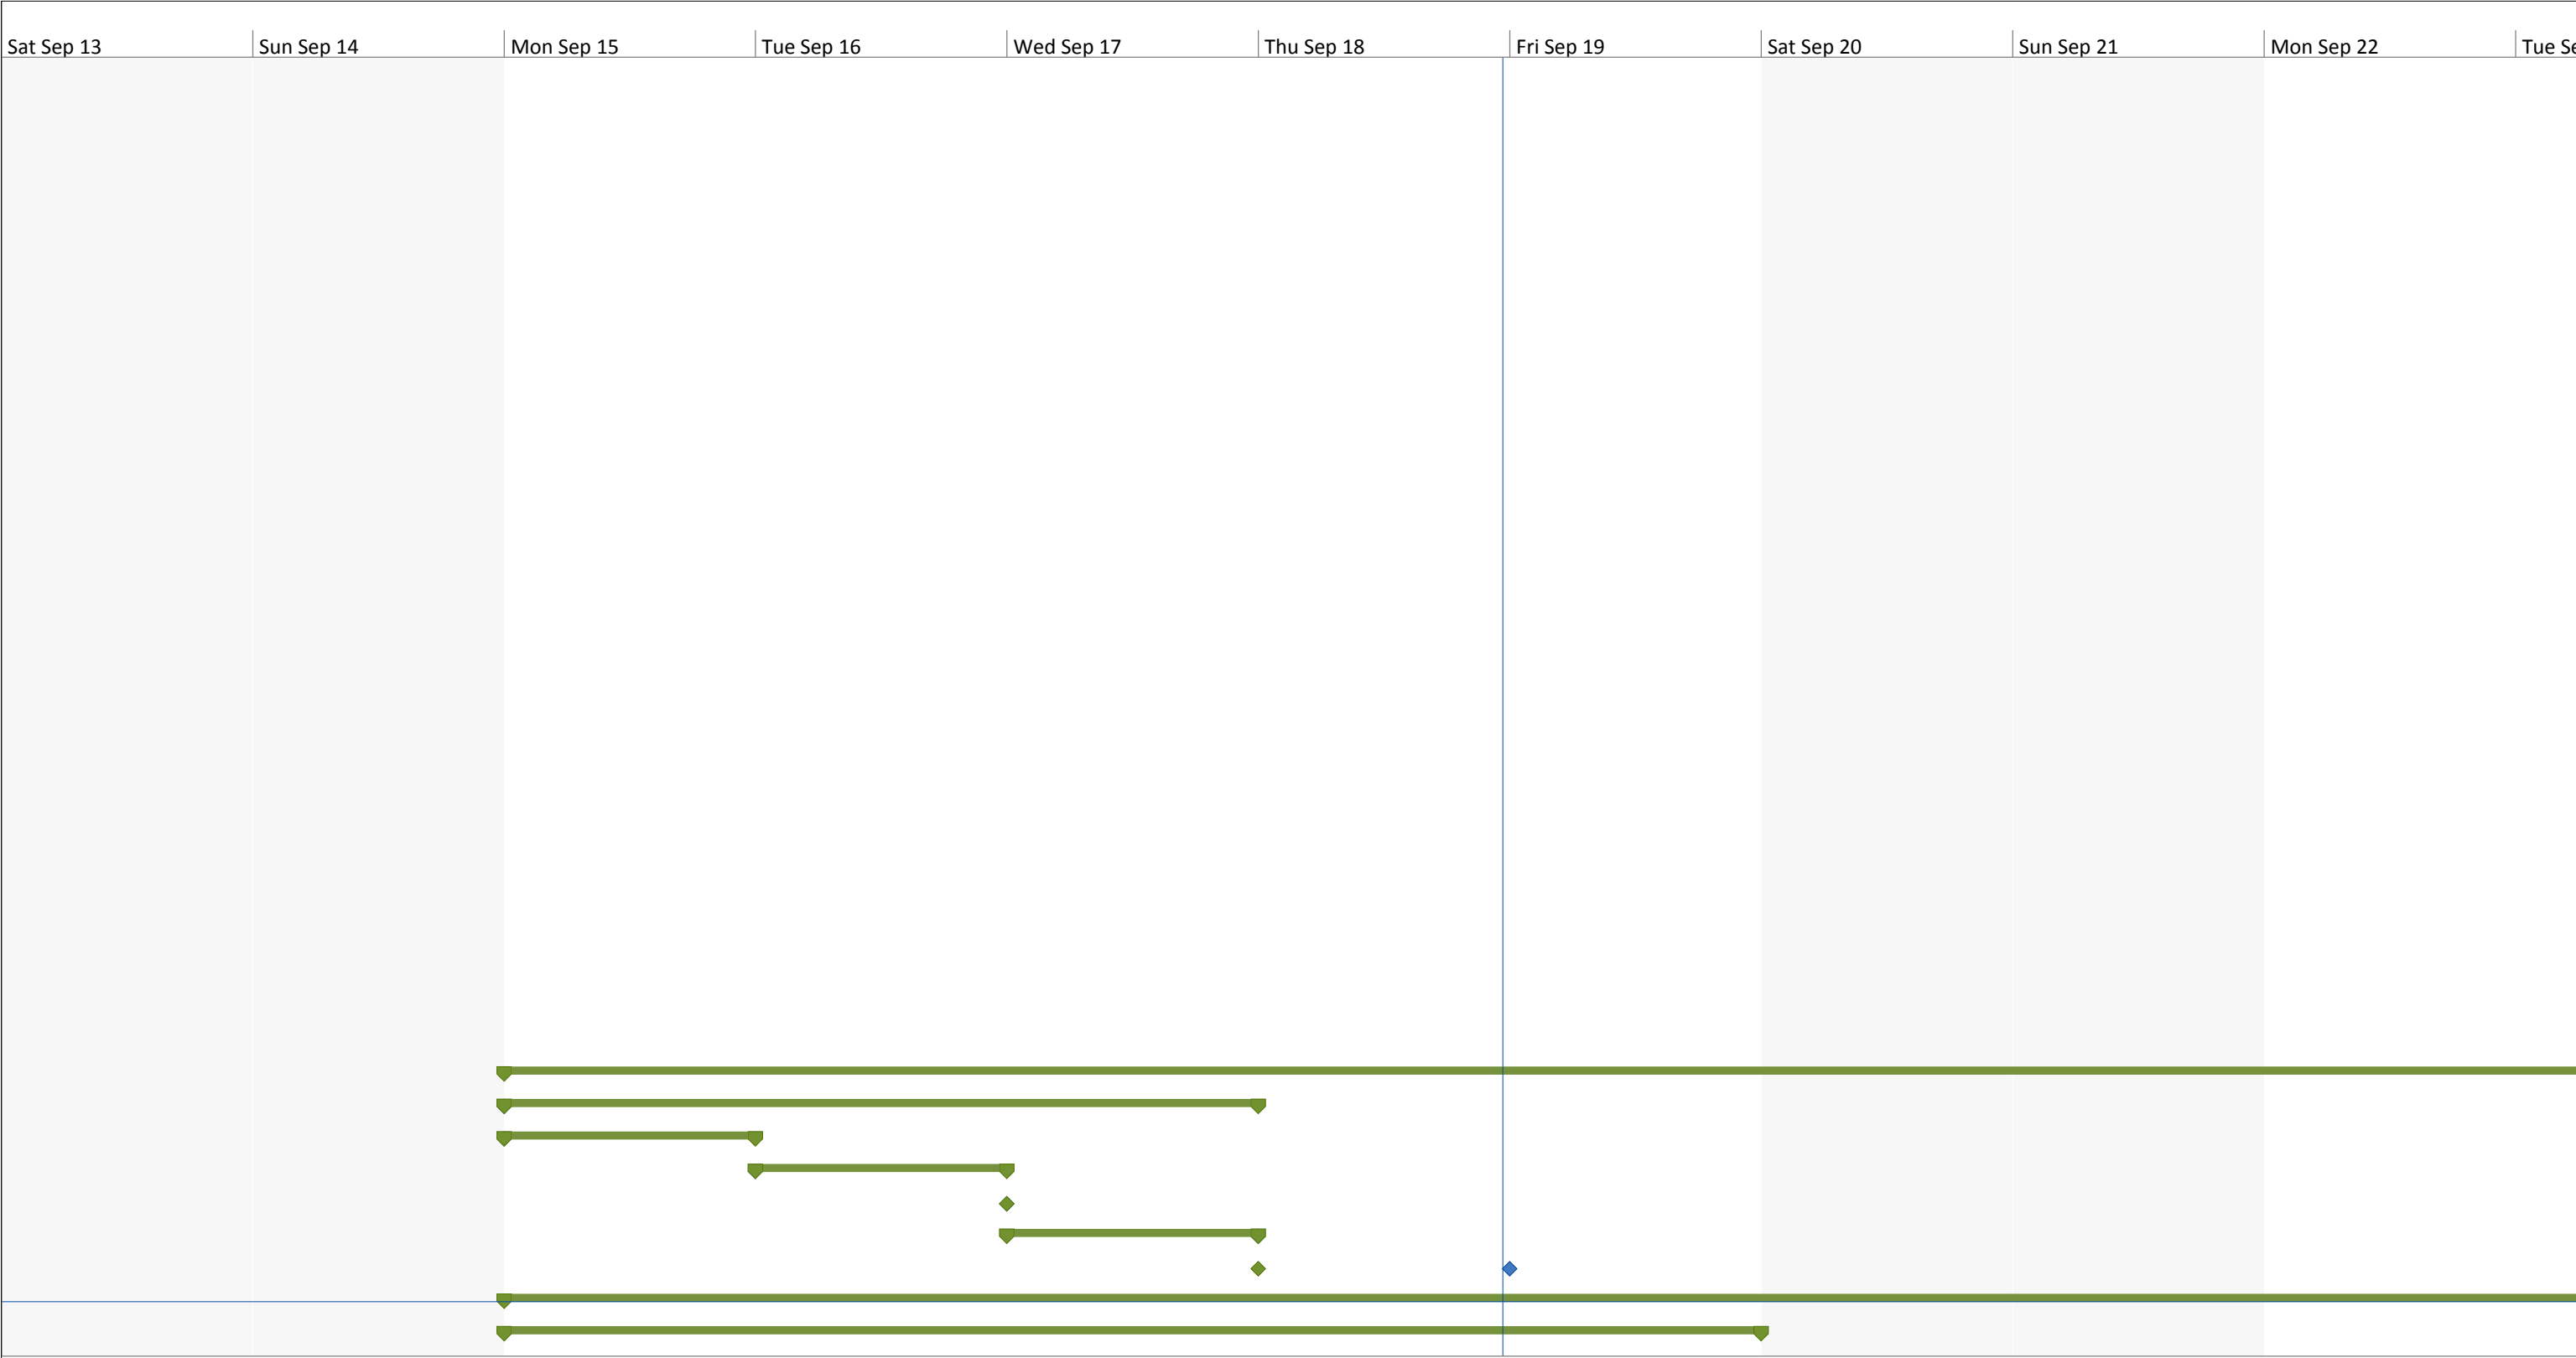


Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

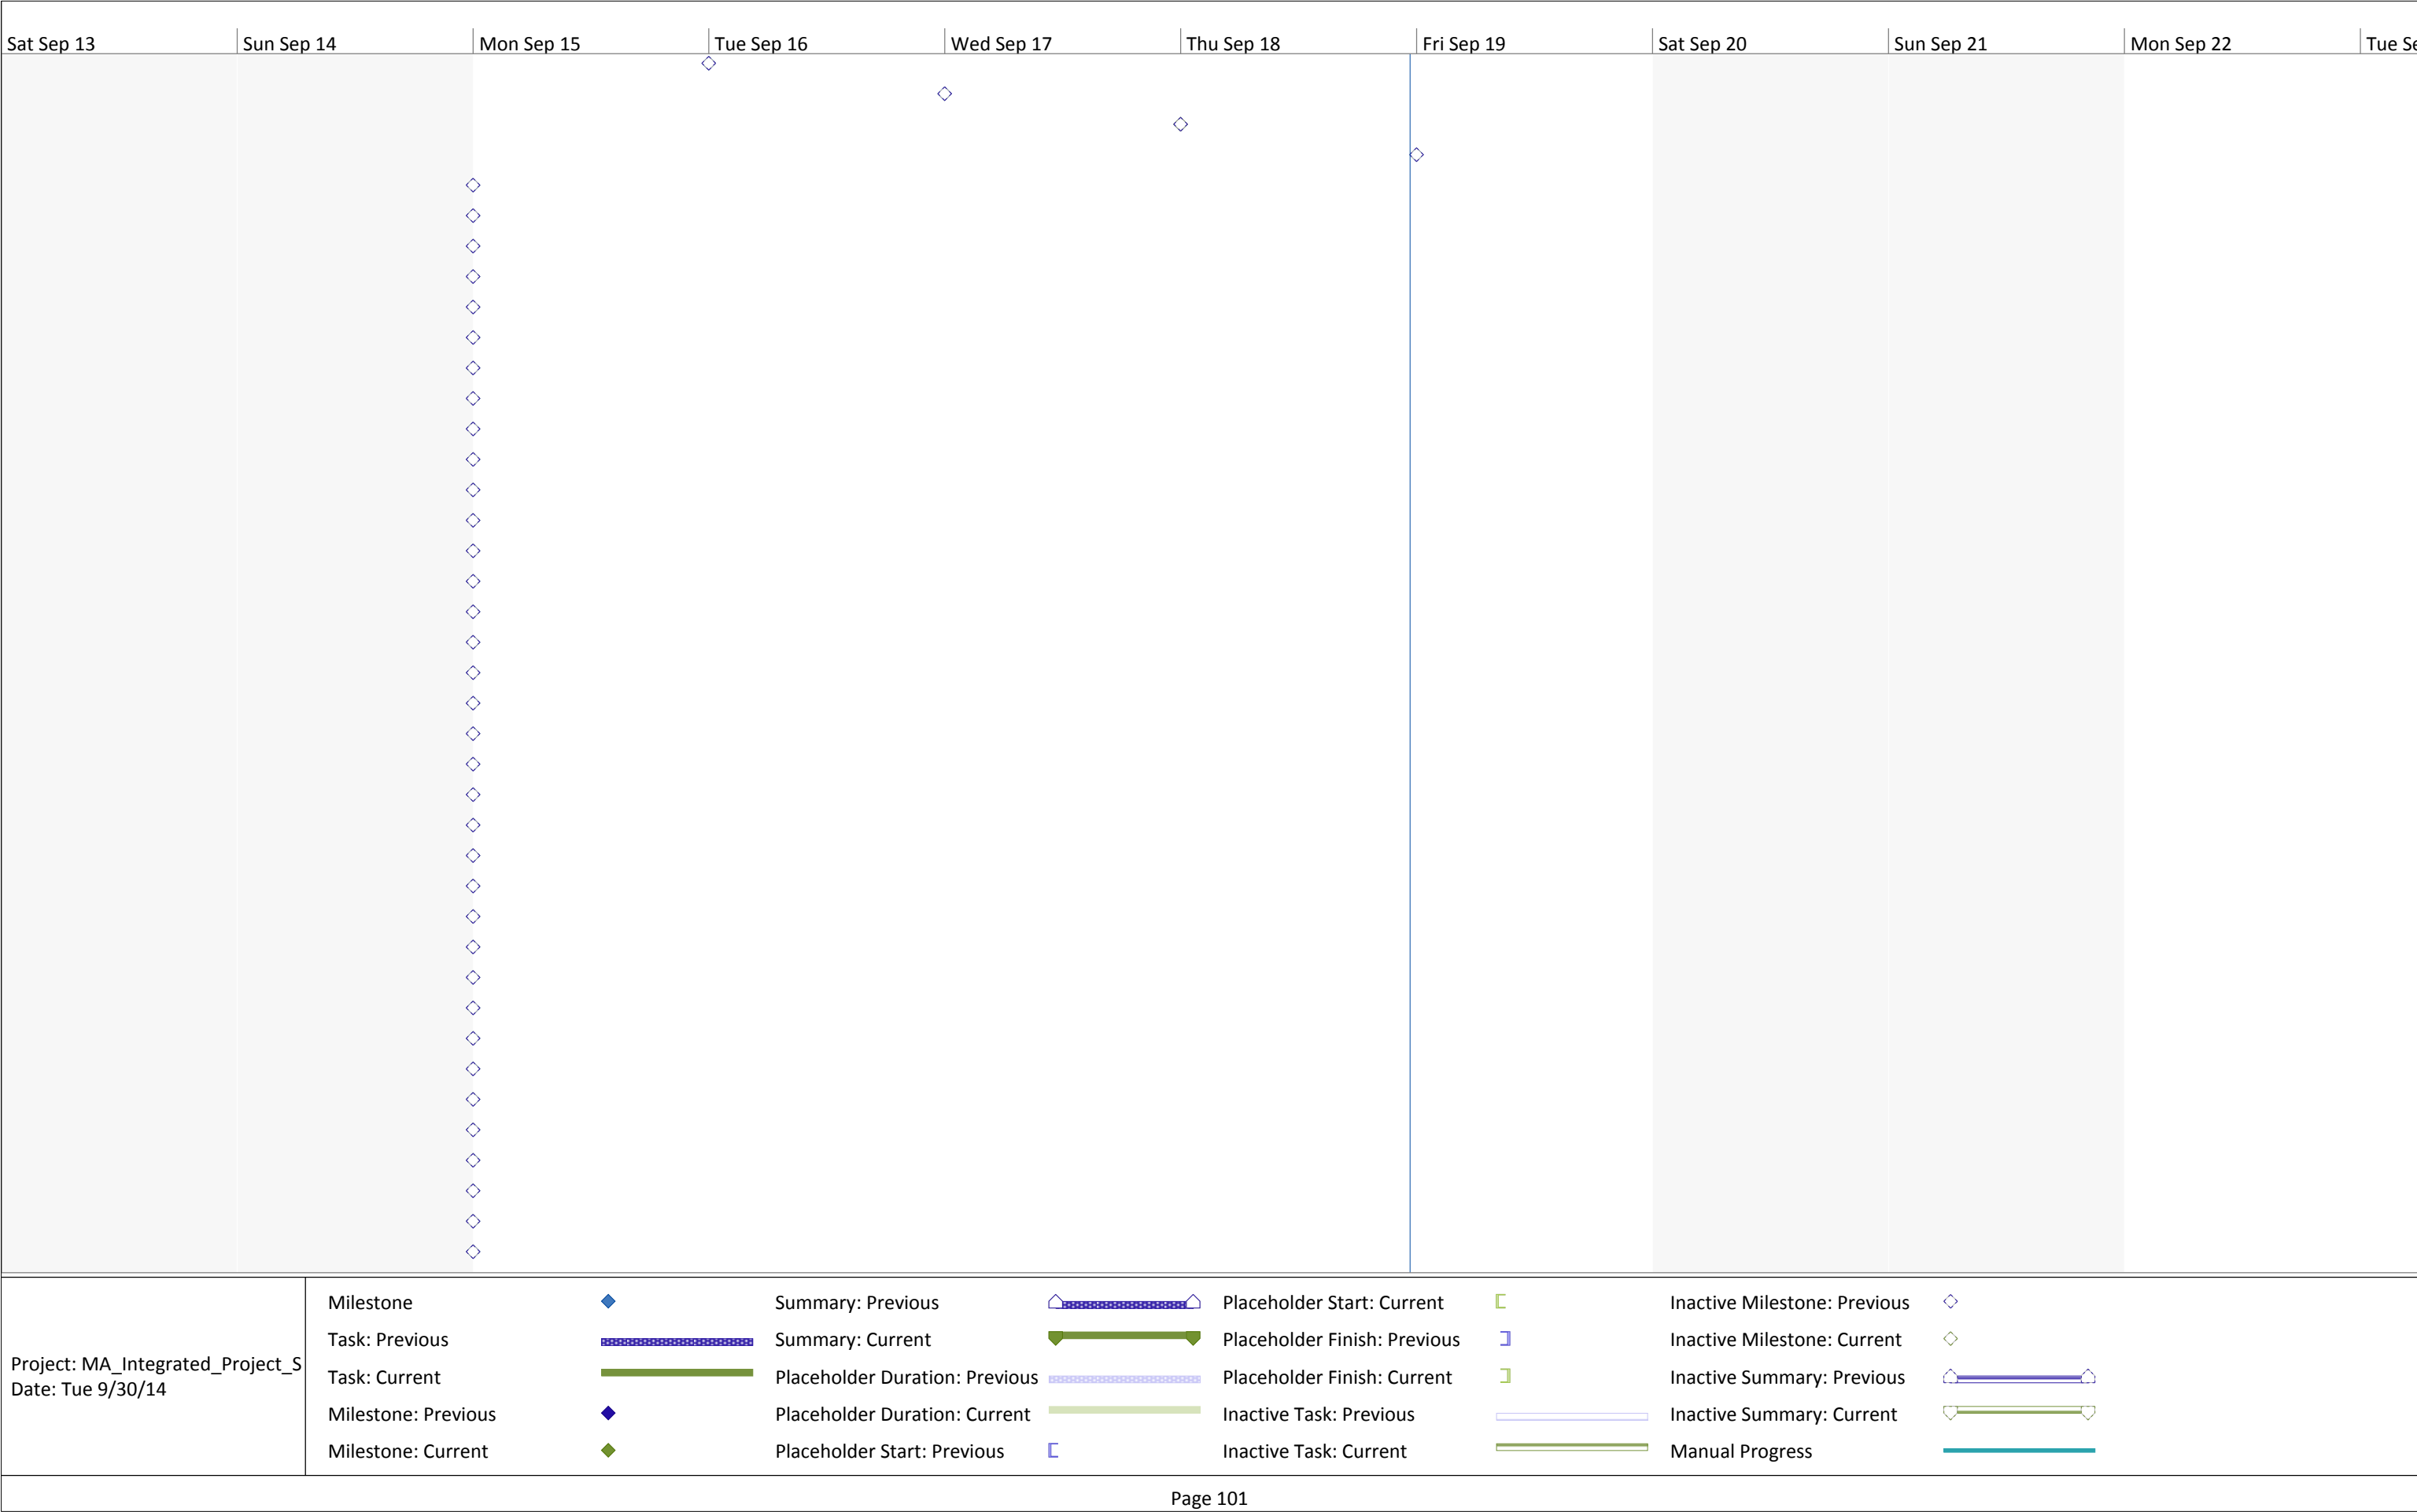



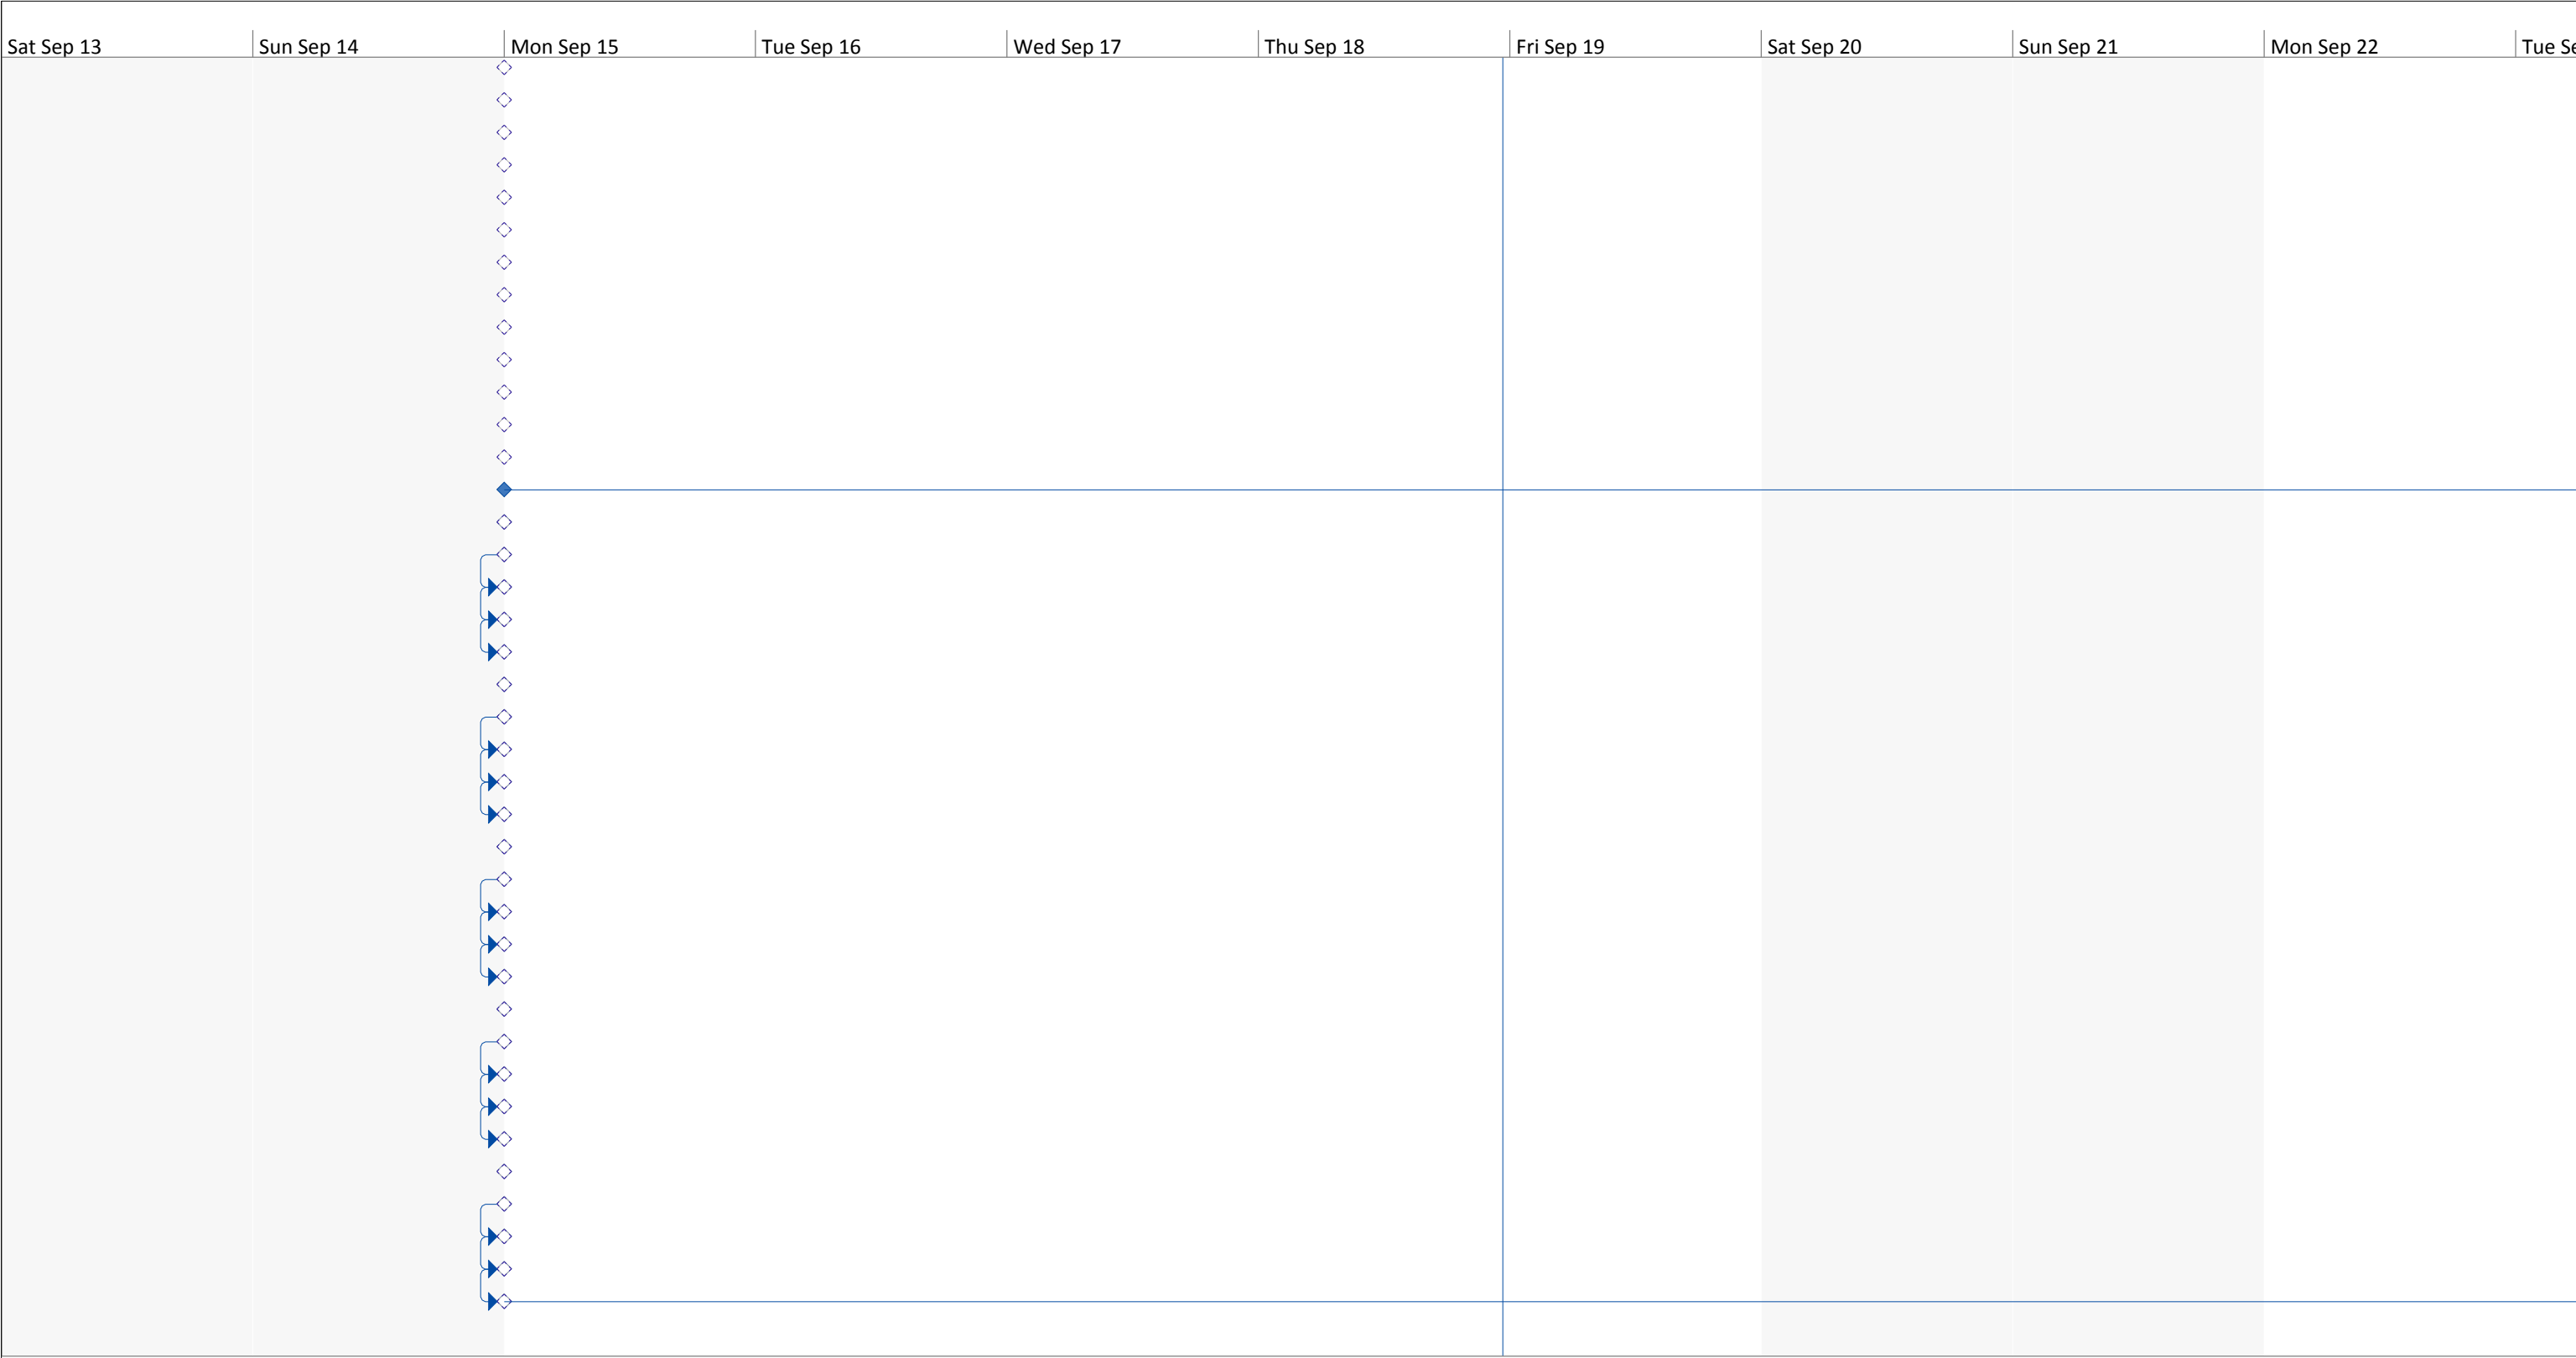



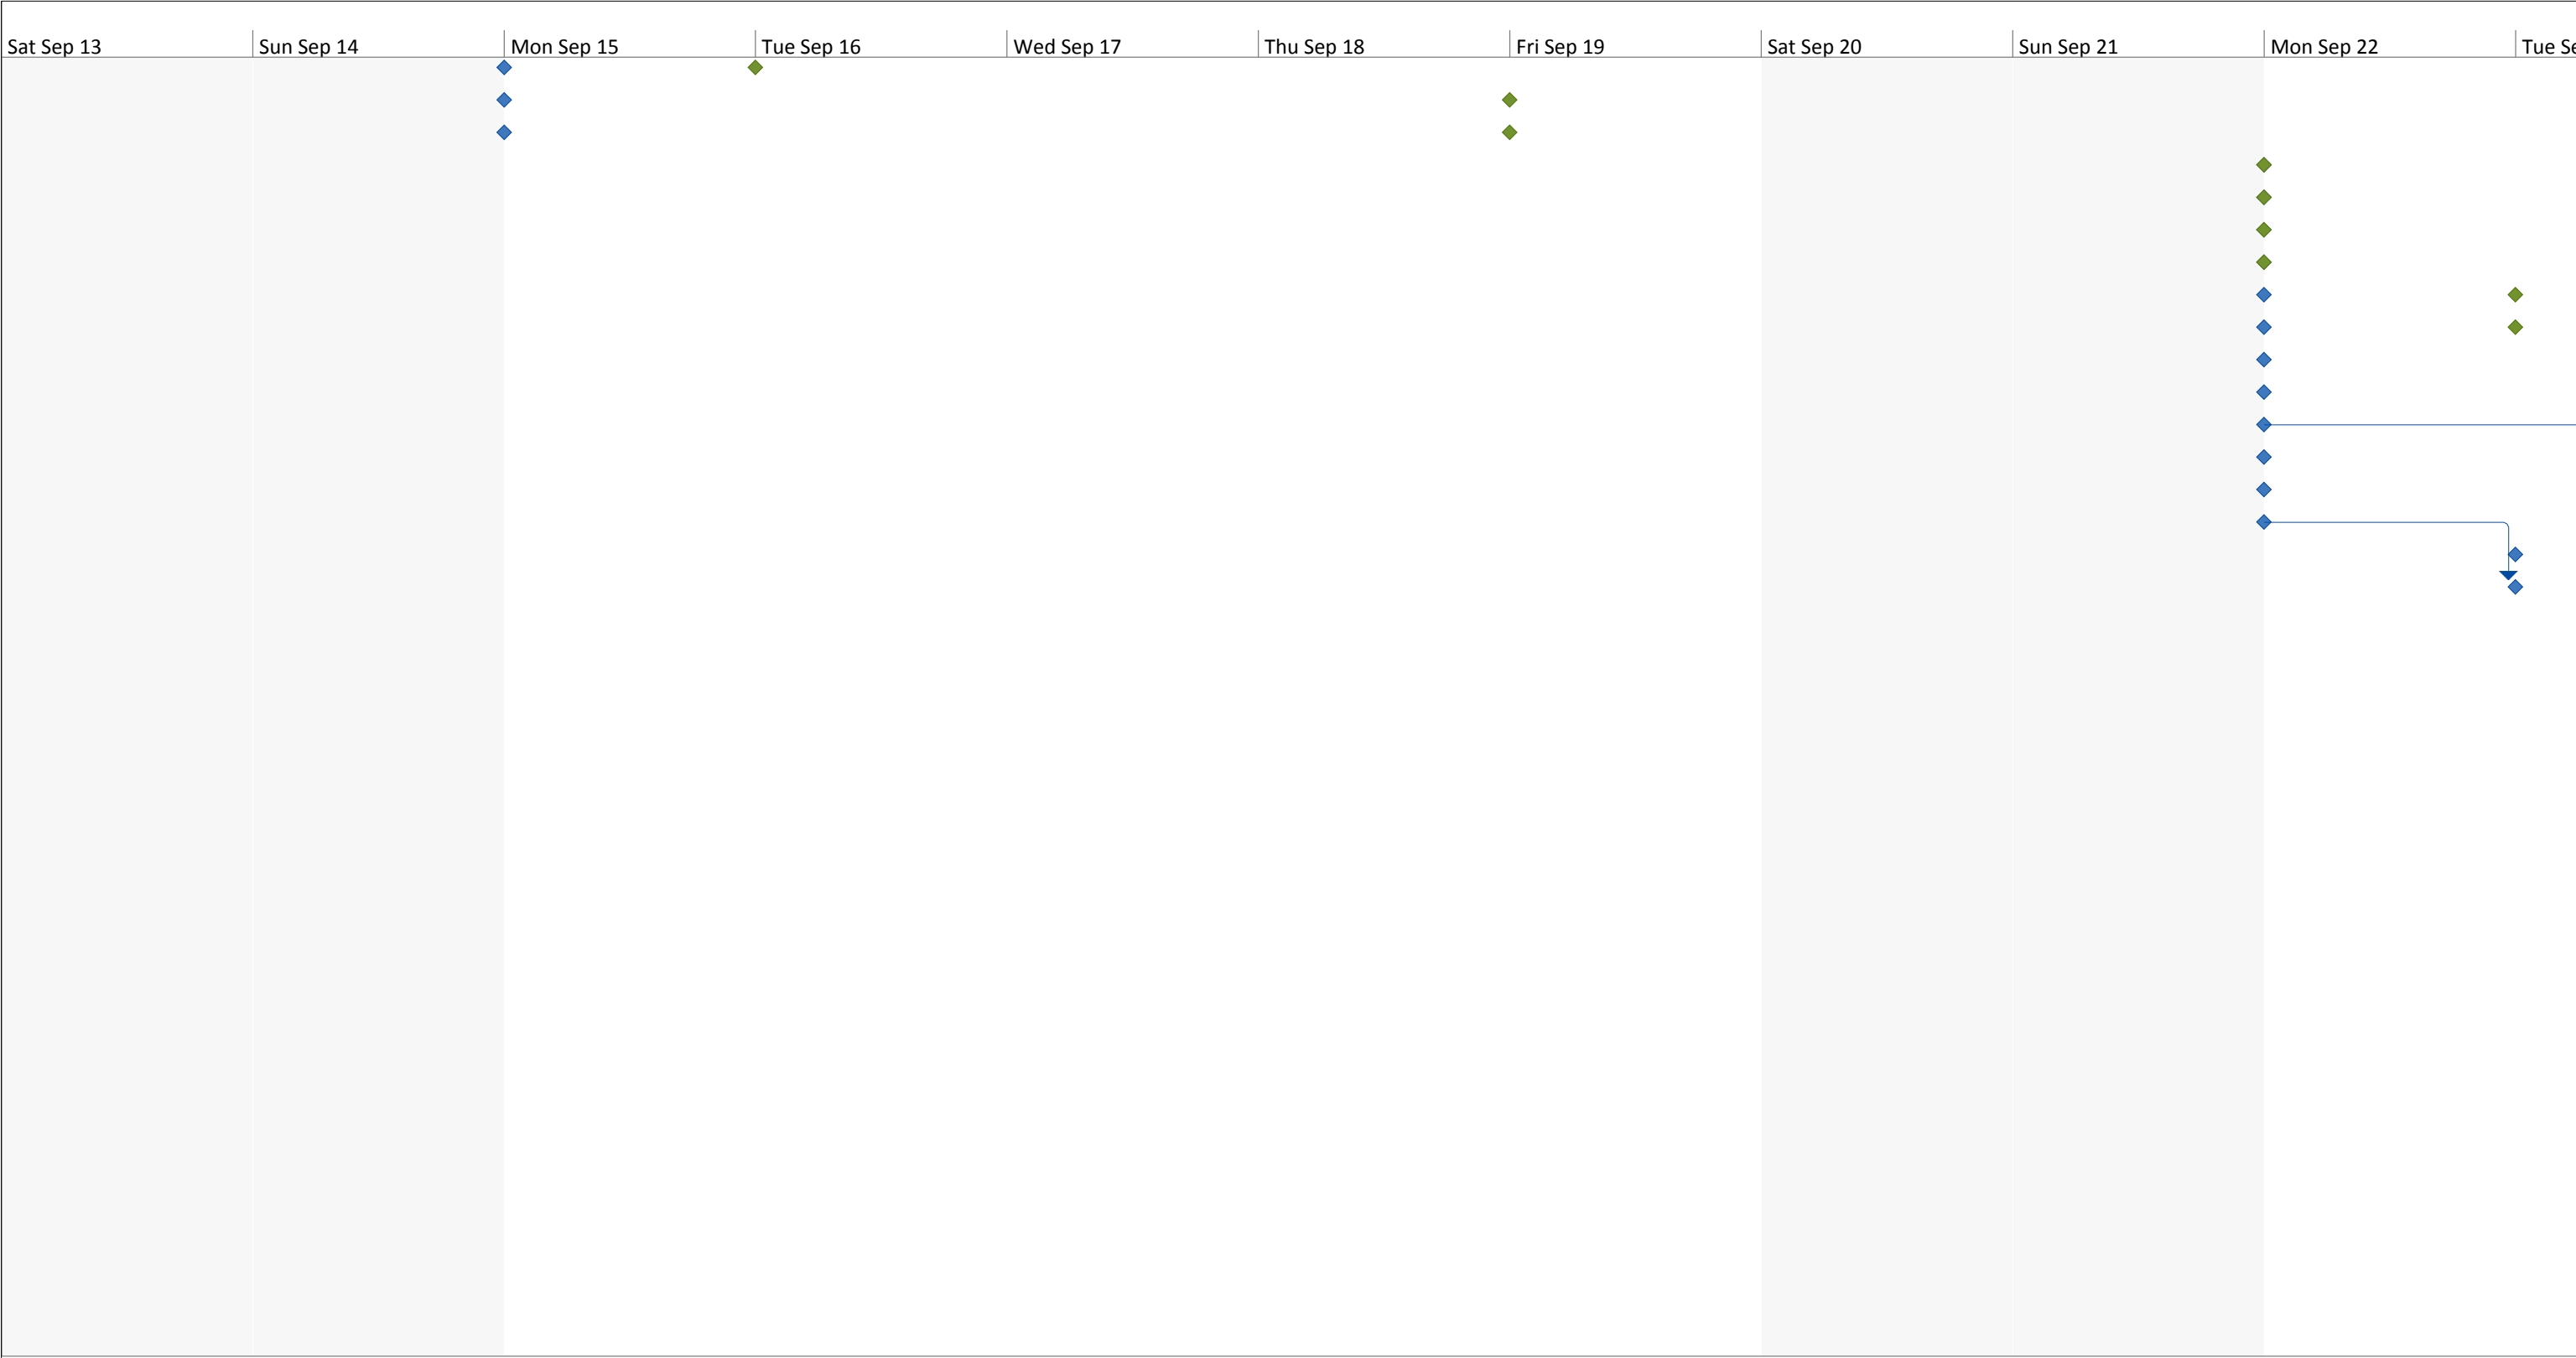














Page 101




Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	






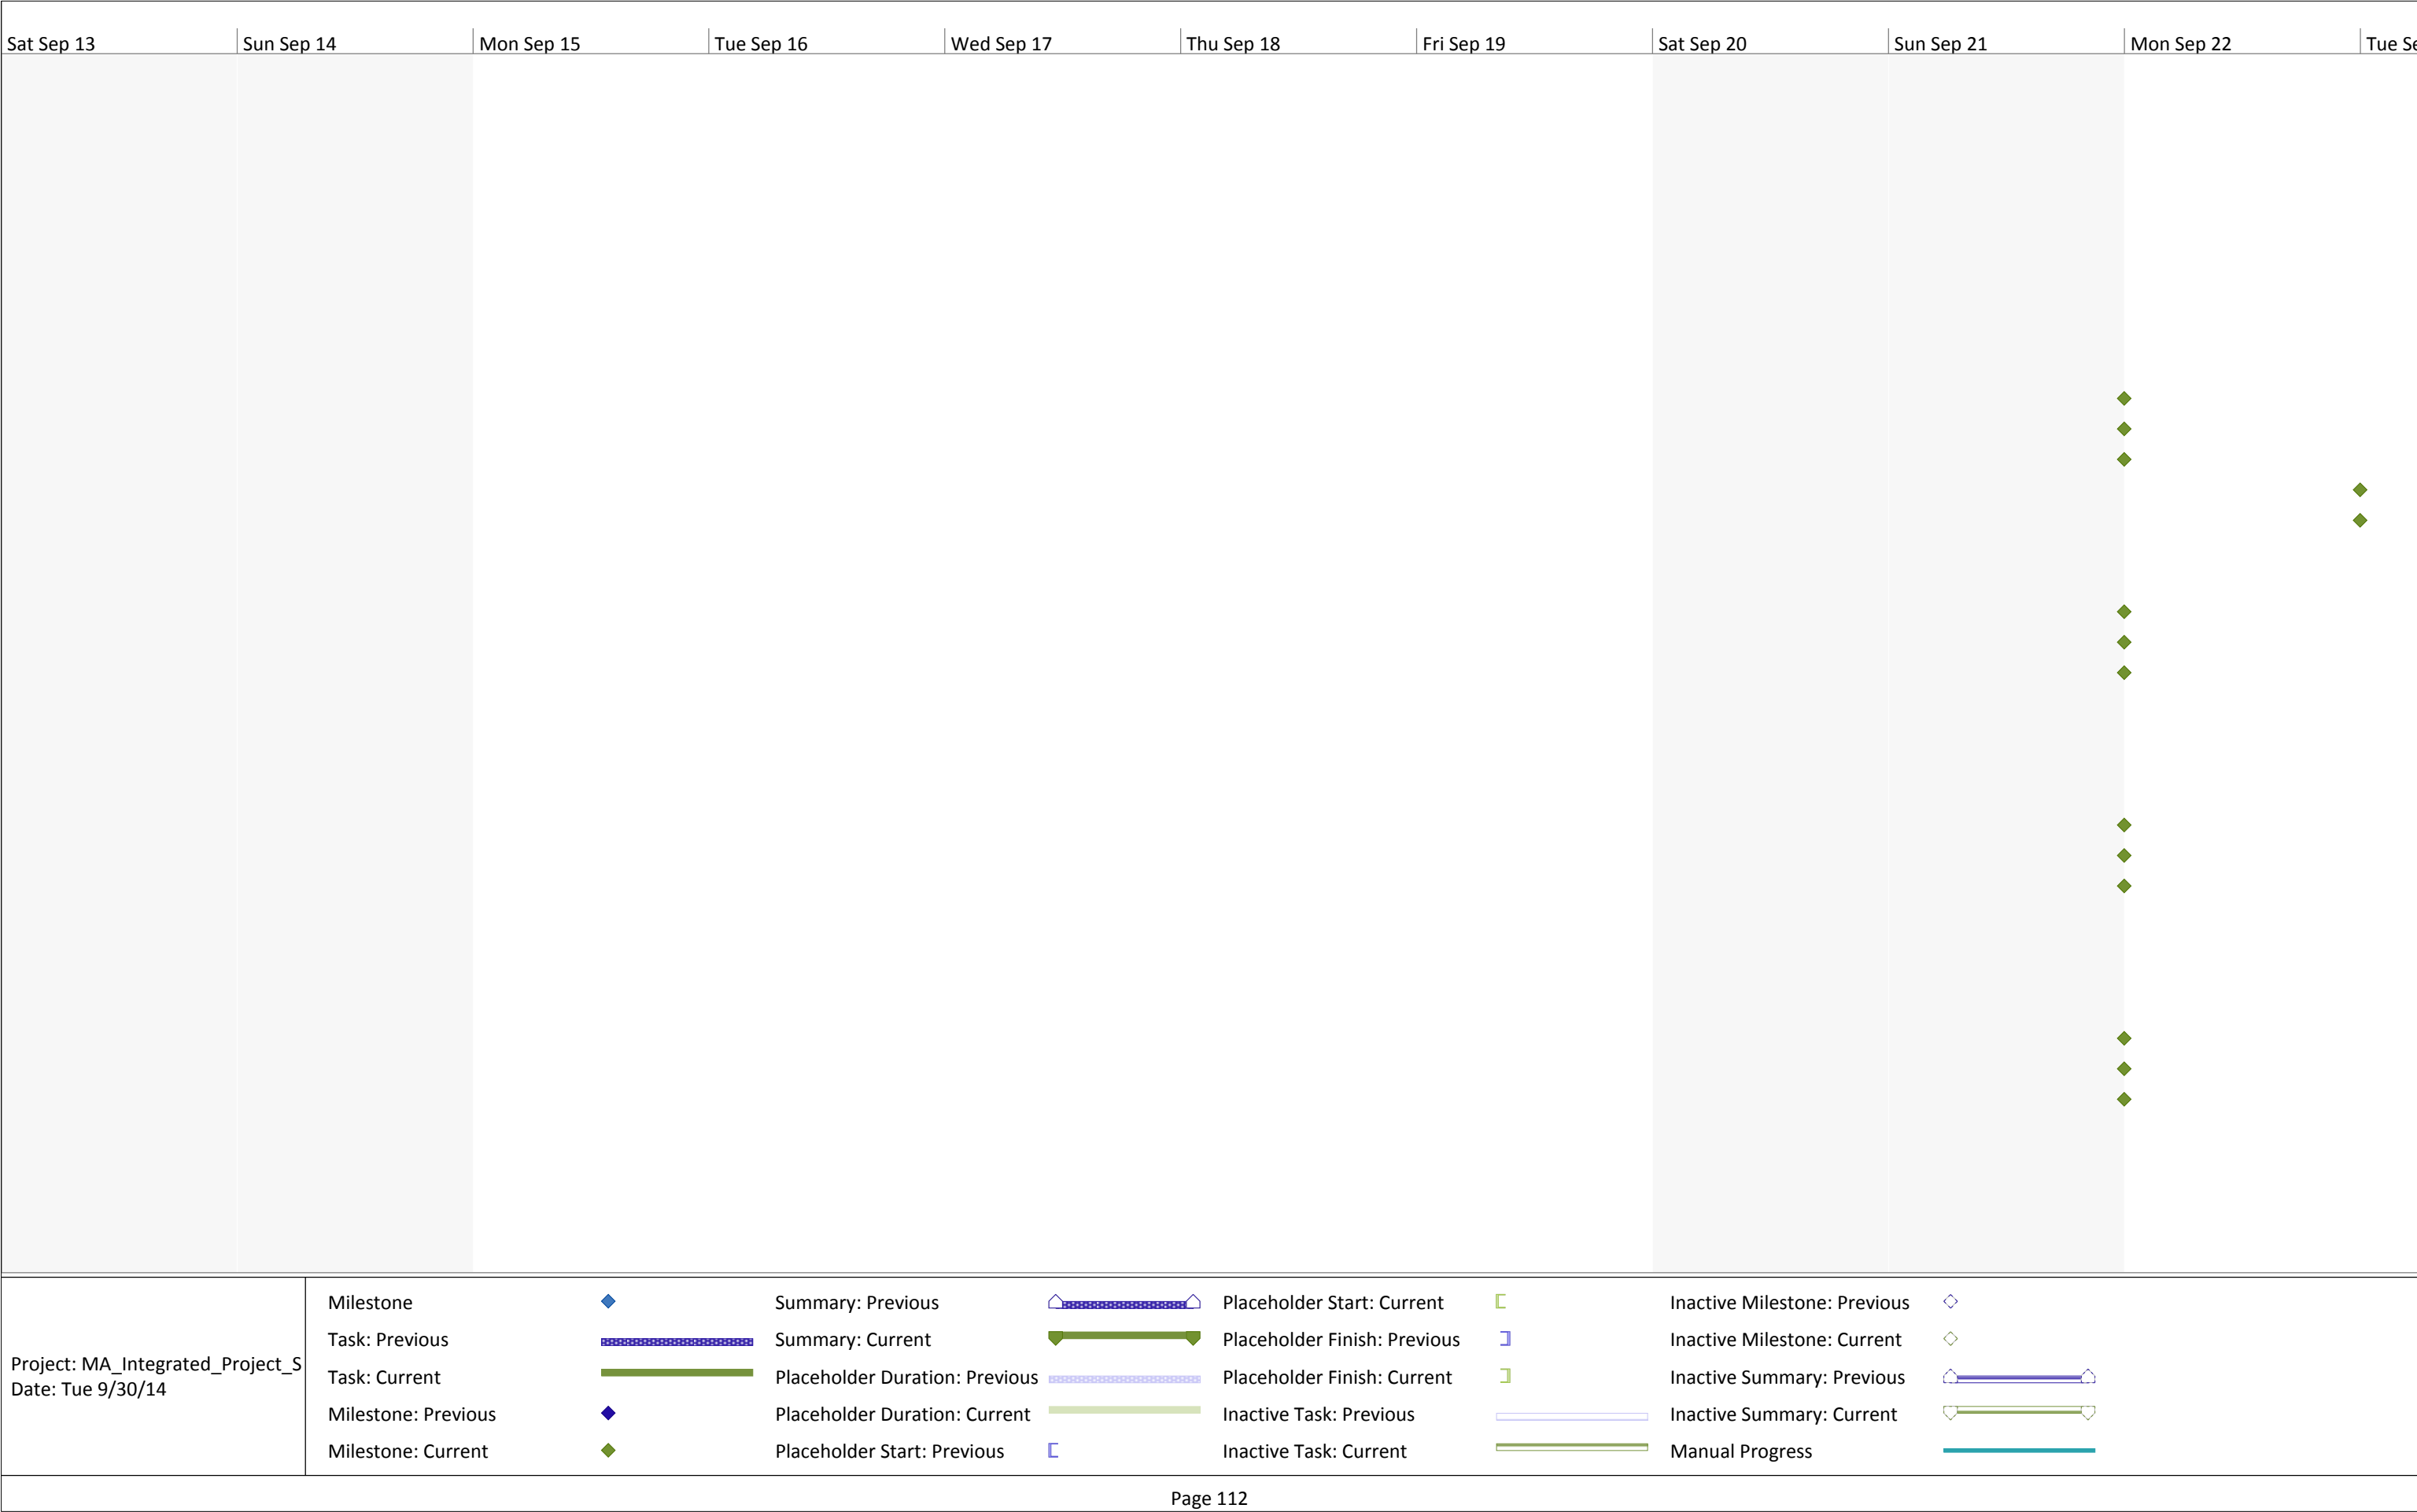

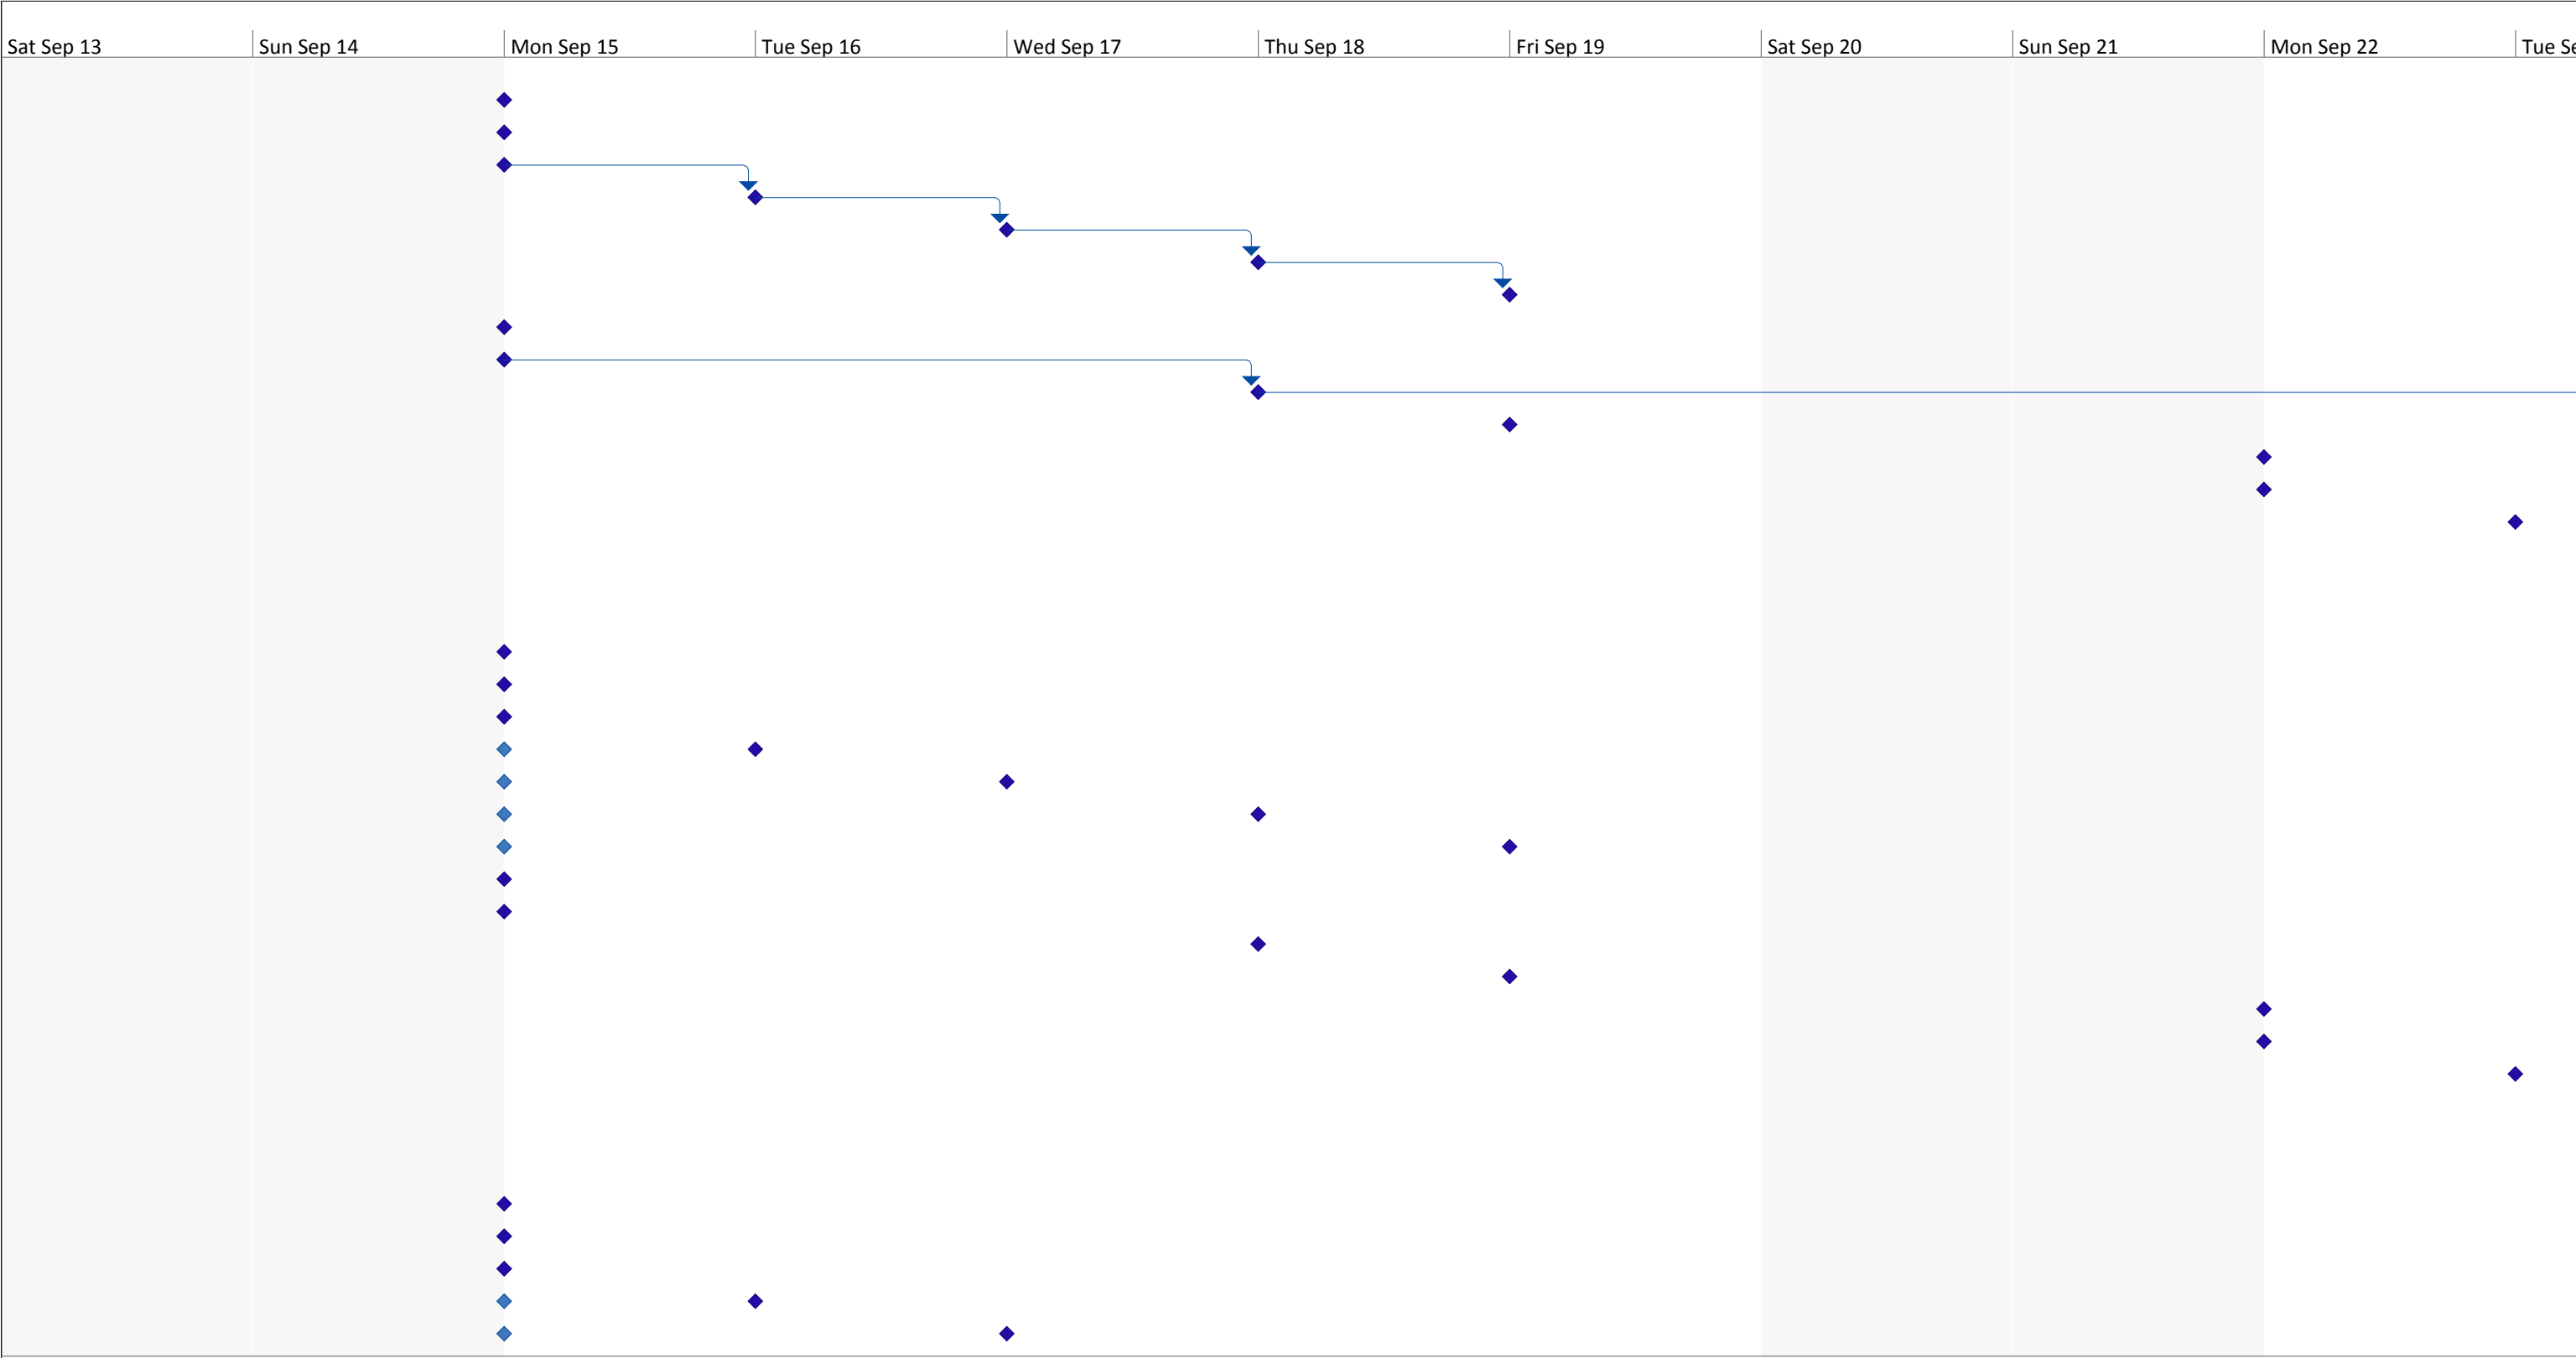



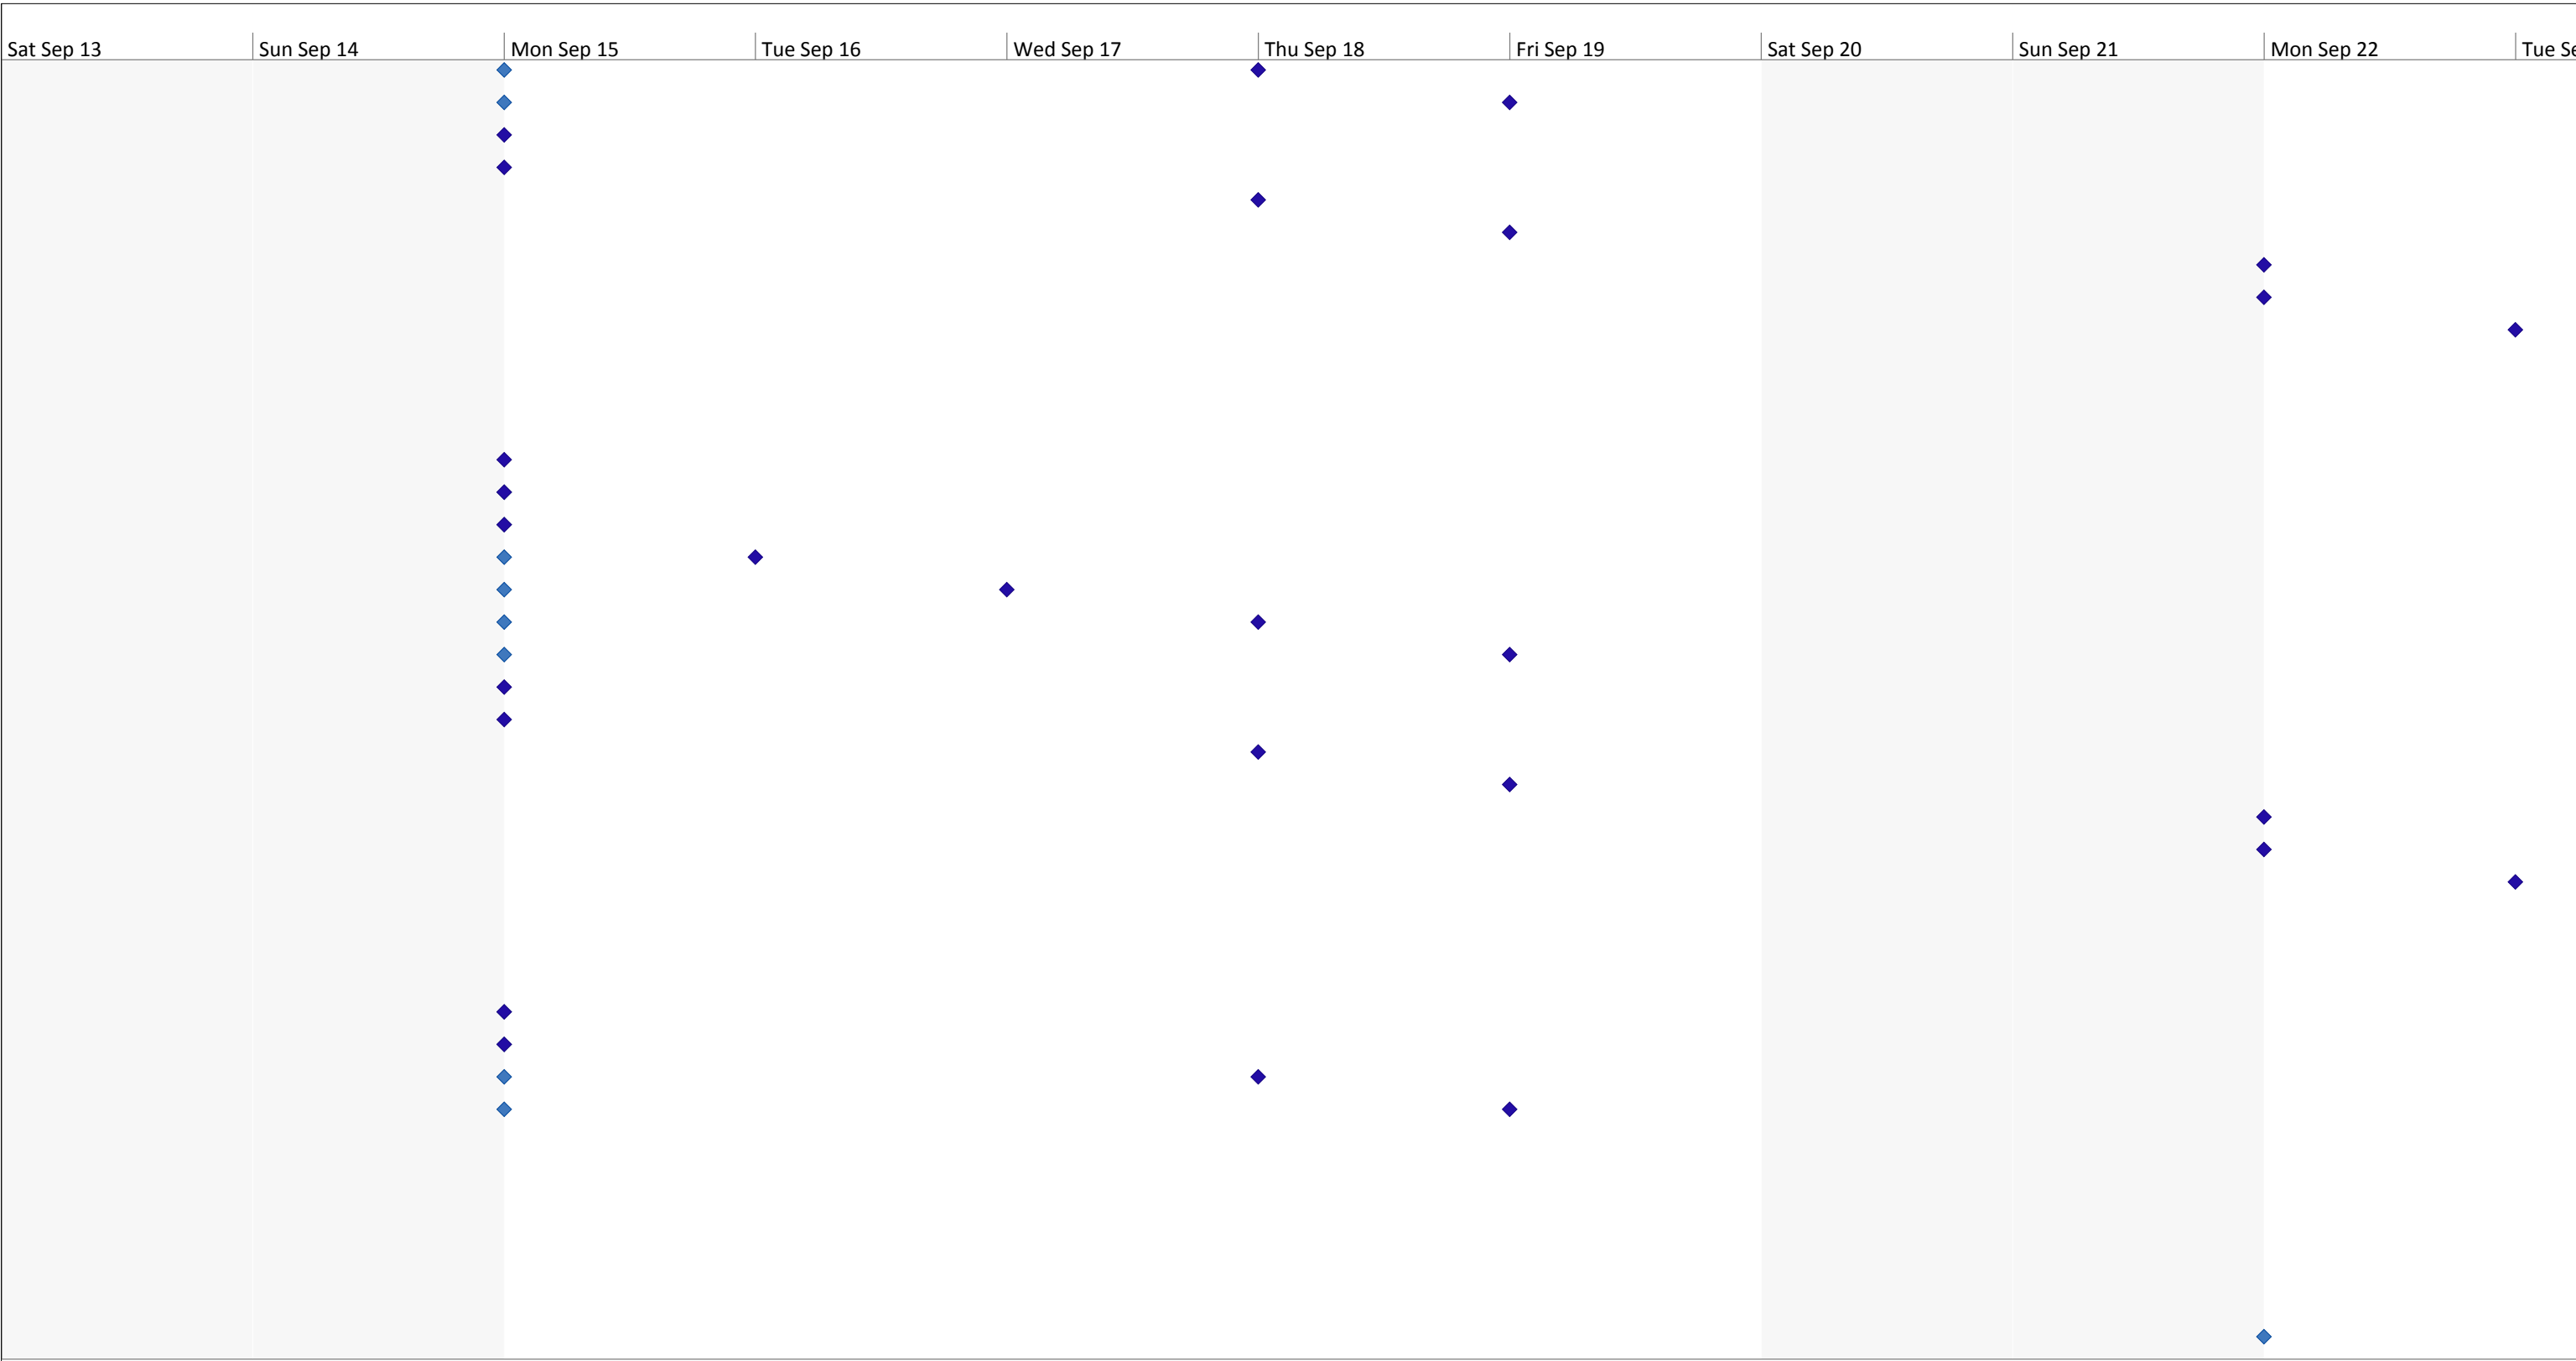











Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	












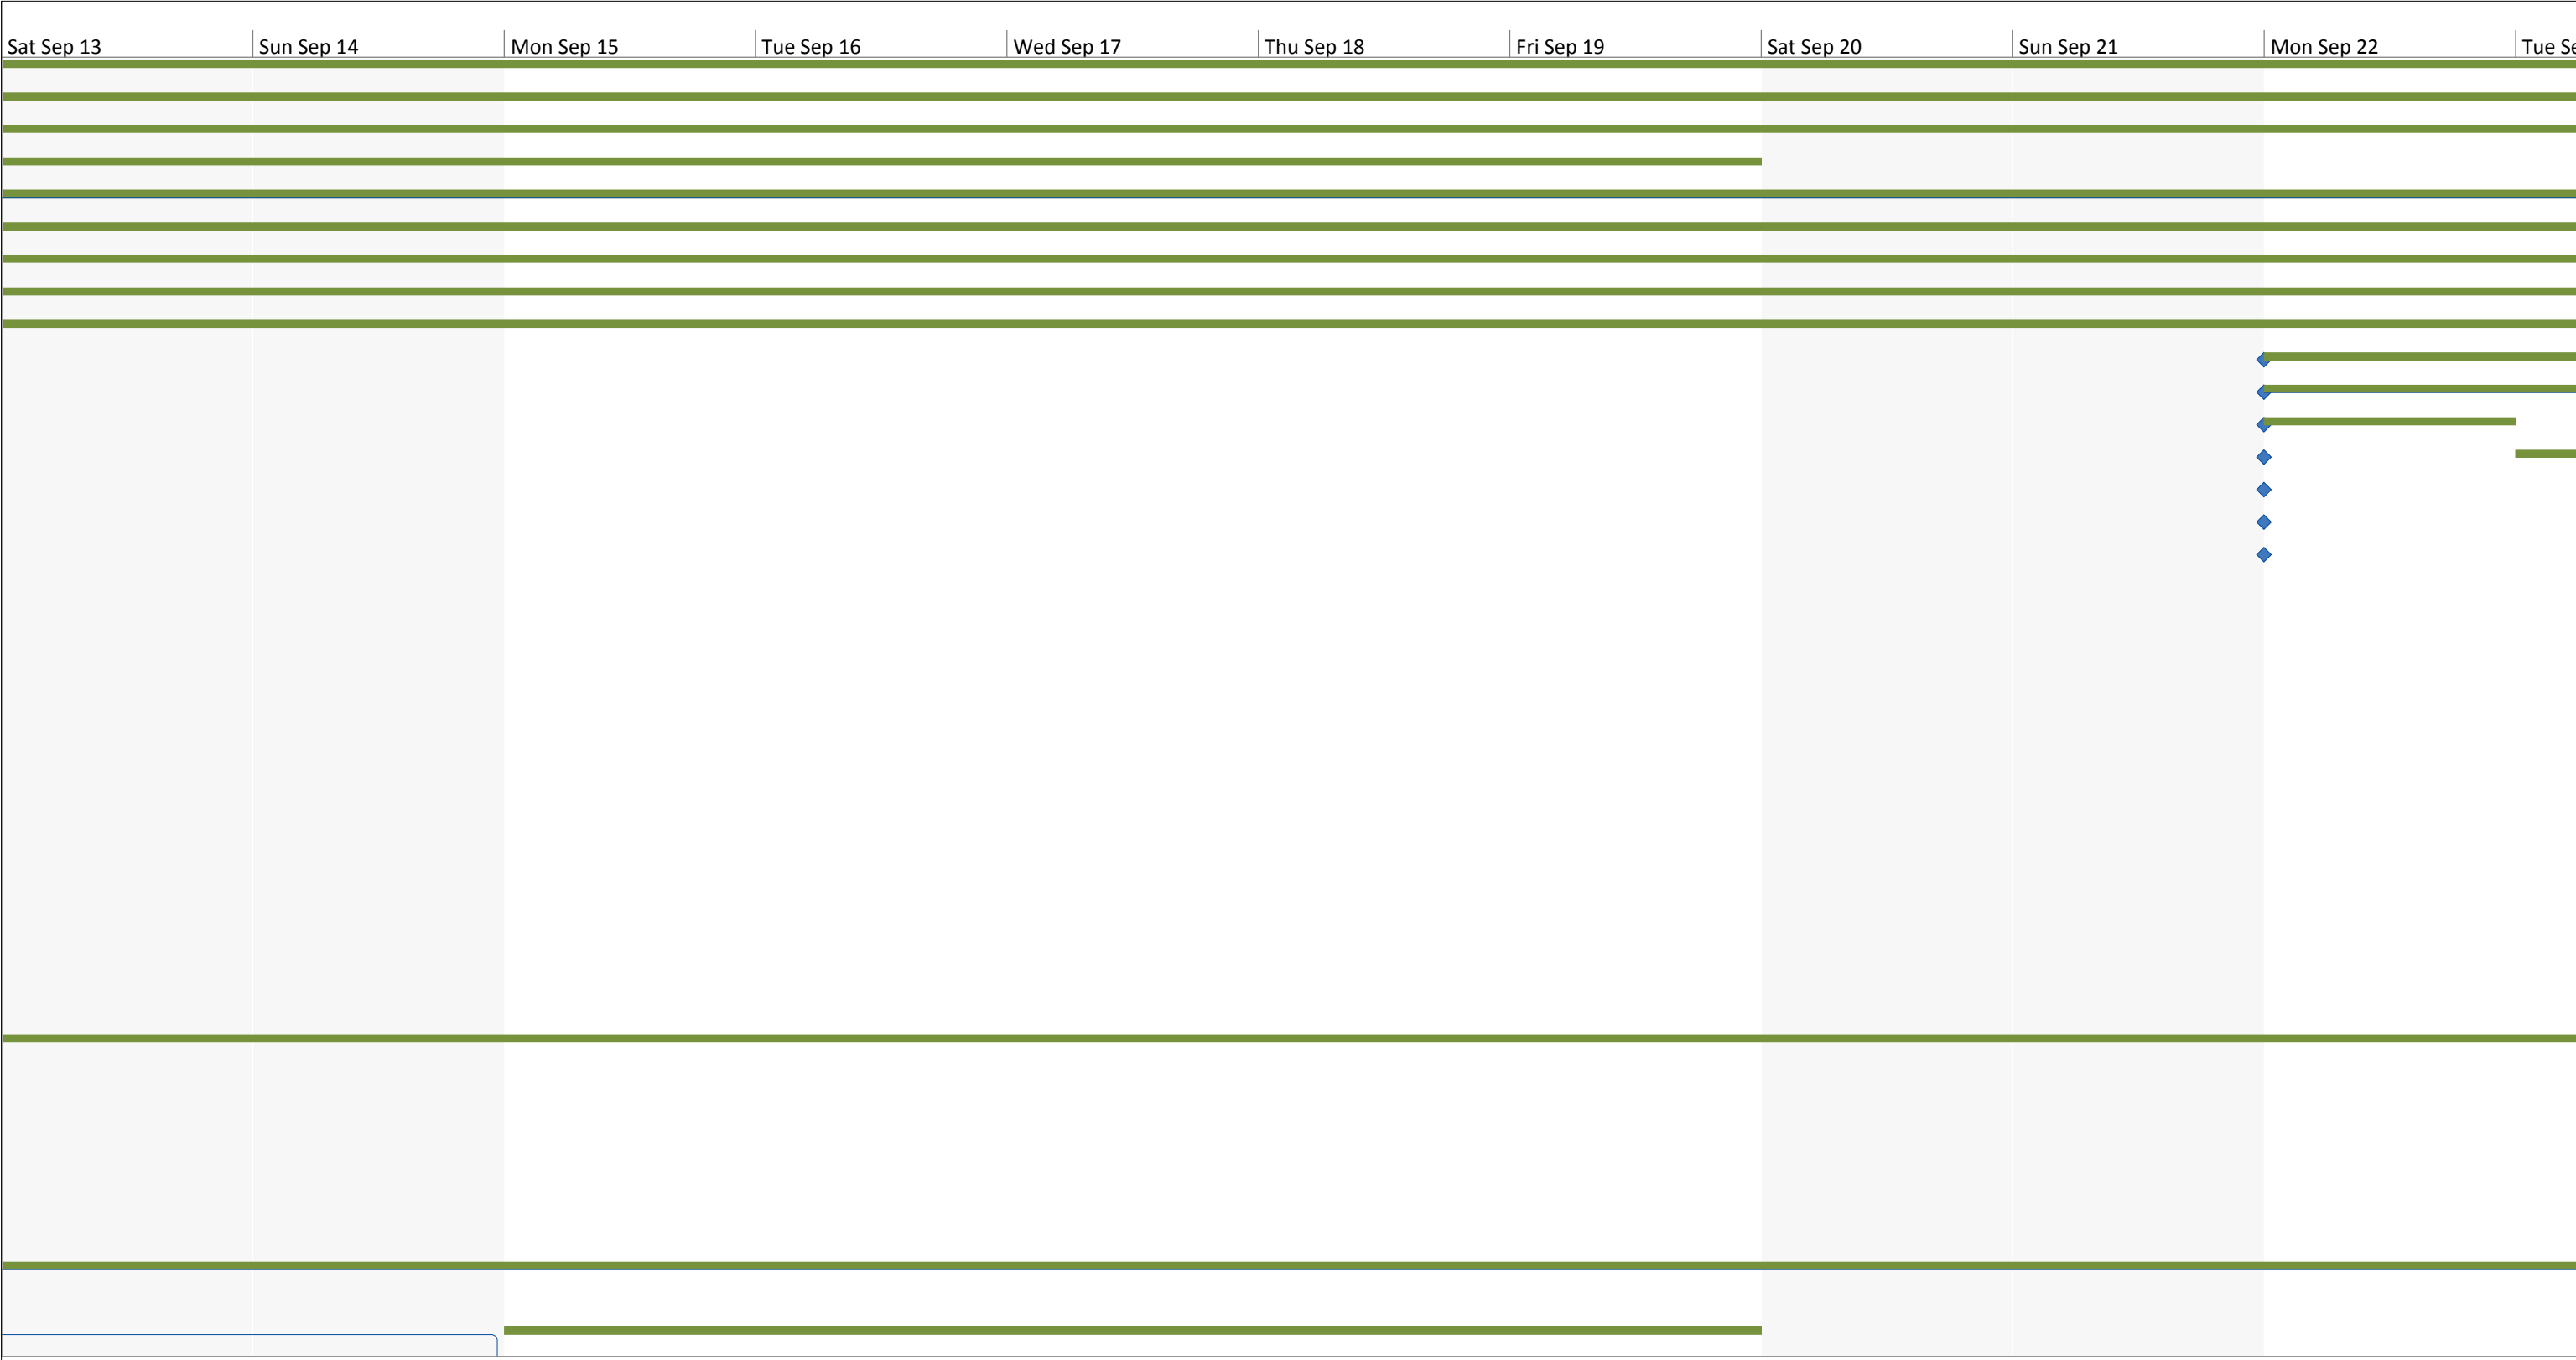














Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	



Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	





Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

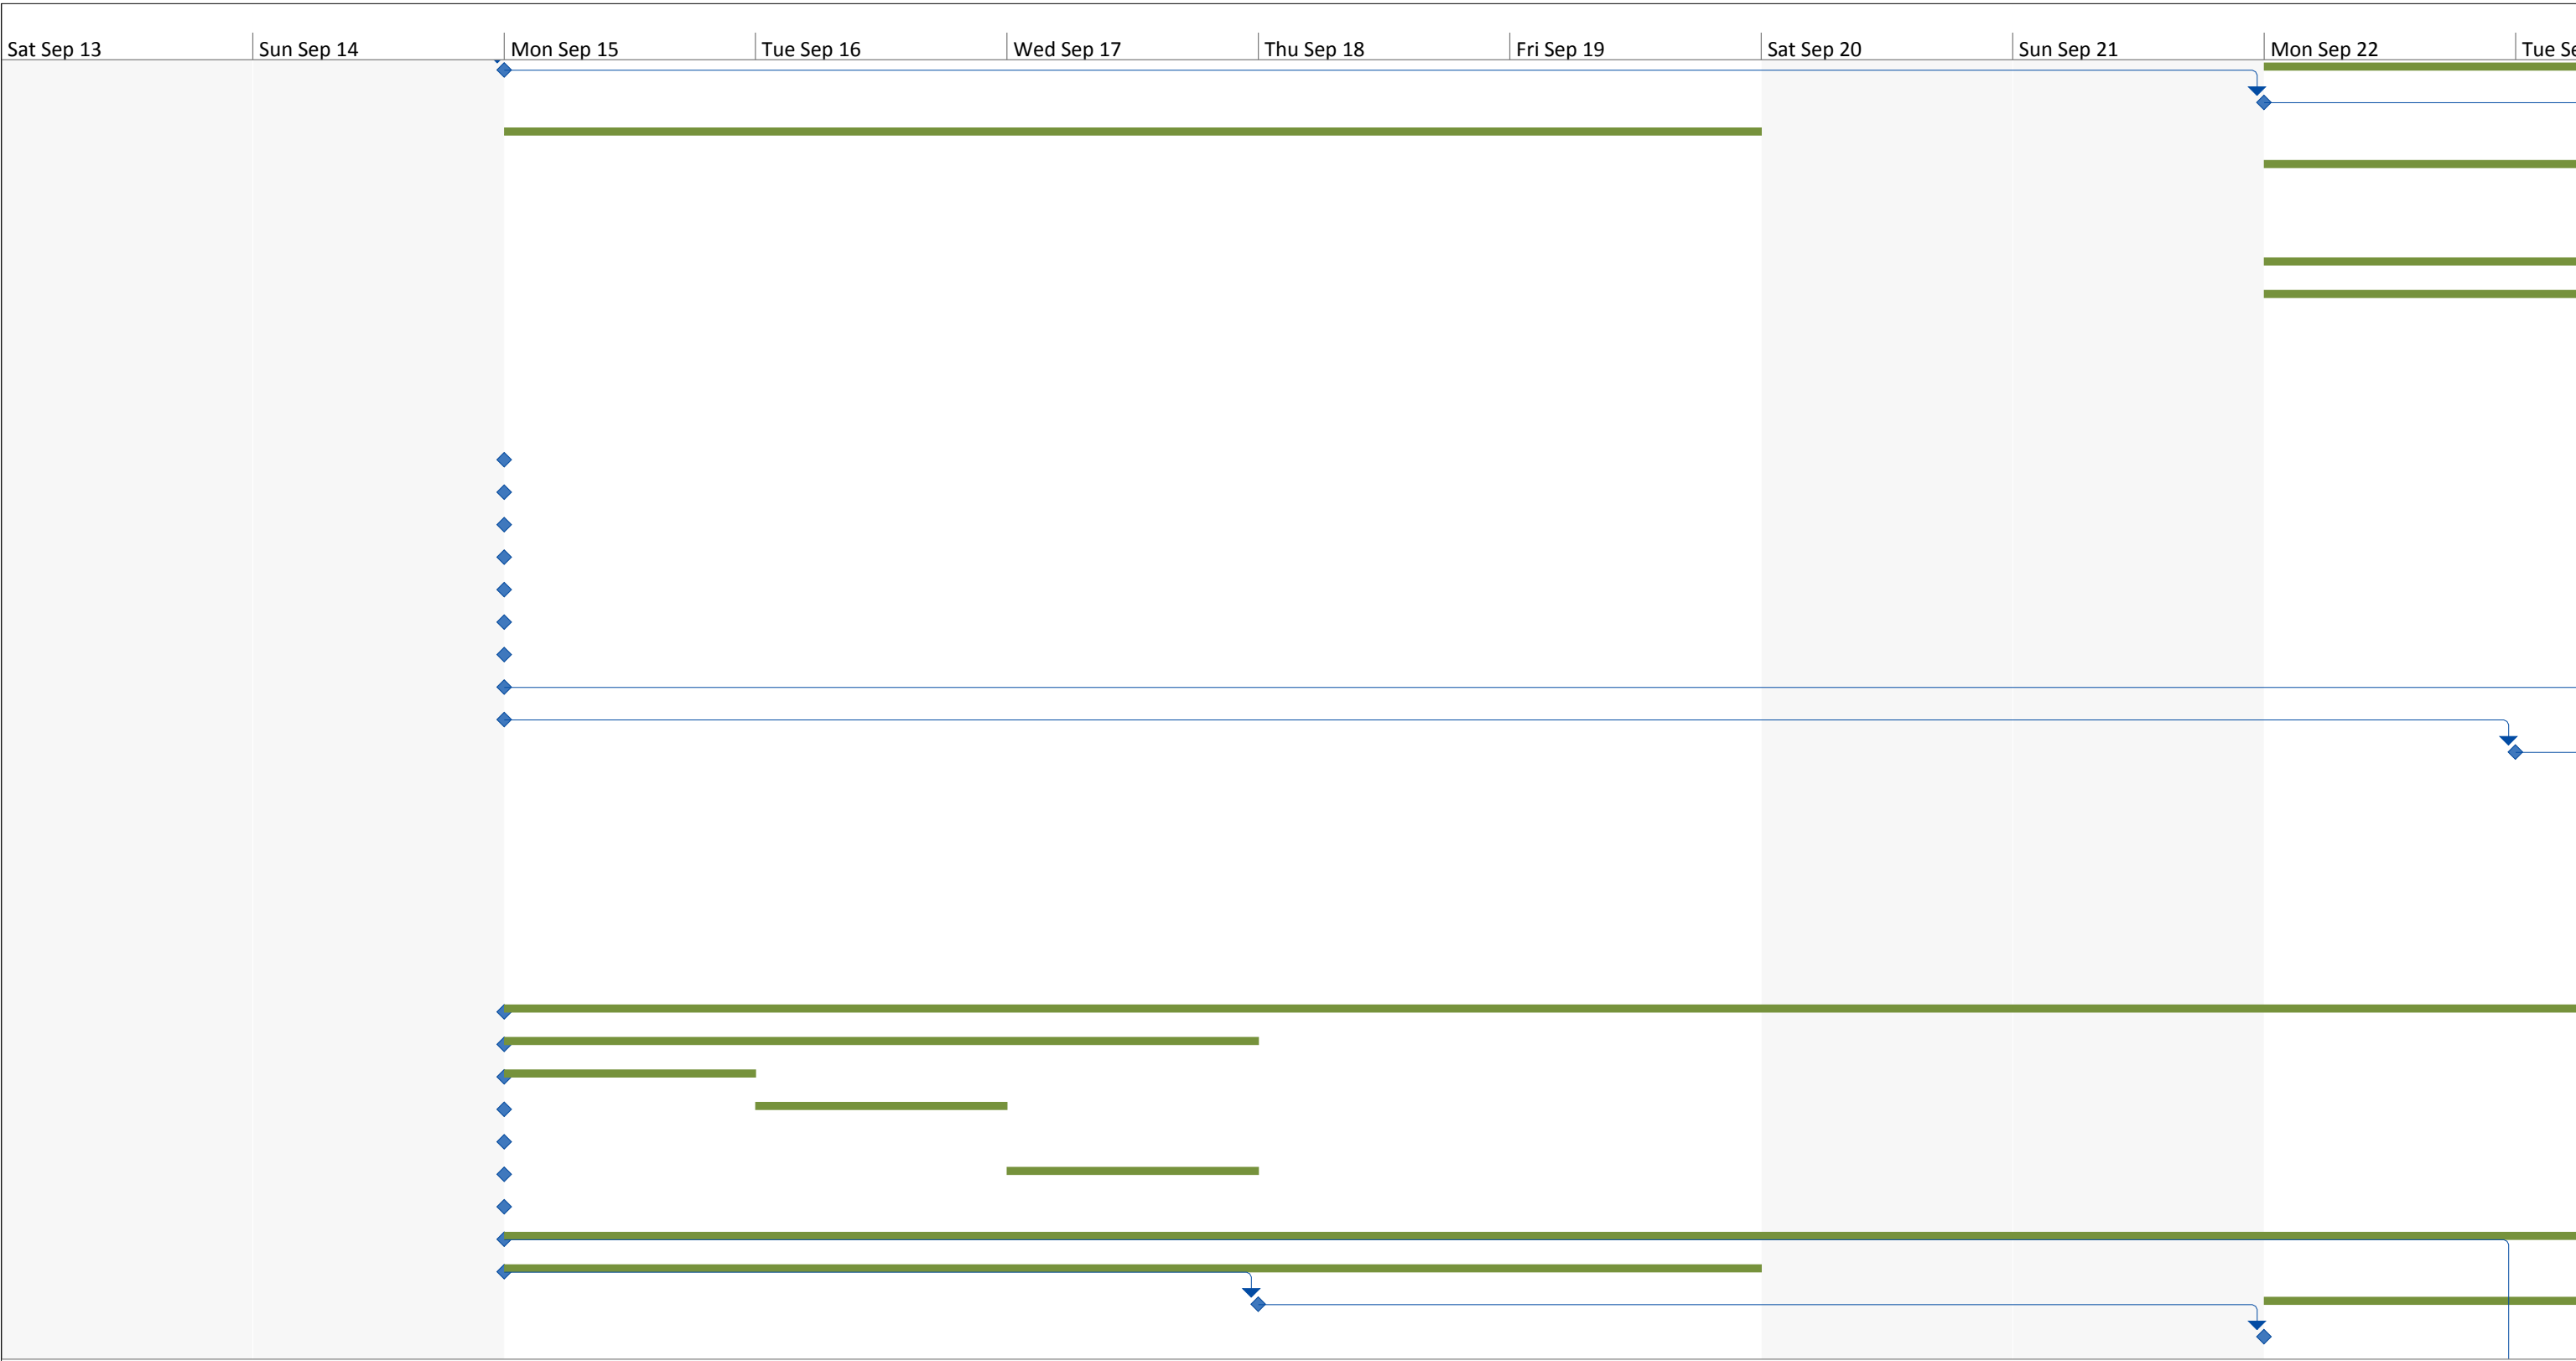


Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

Tue Sep 23		Wed Sep 24		Thu Sep 25		Fri Sep 26		Sat Sep 27		Sun Sep 28		Mon Sep 29		Tue Sep 30		Wed Oct 1		Thu Oct 2		Fri Oct 3	

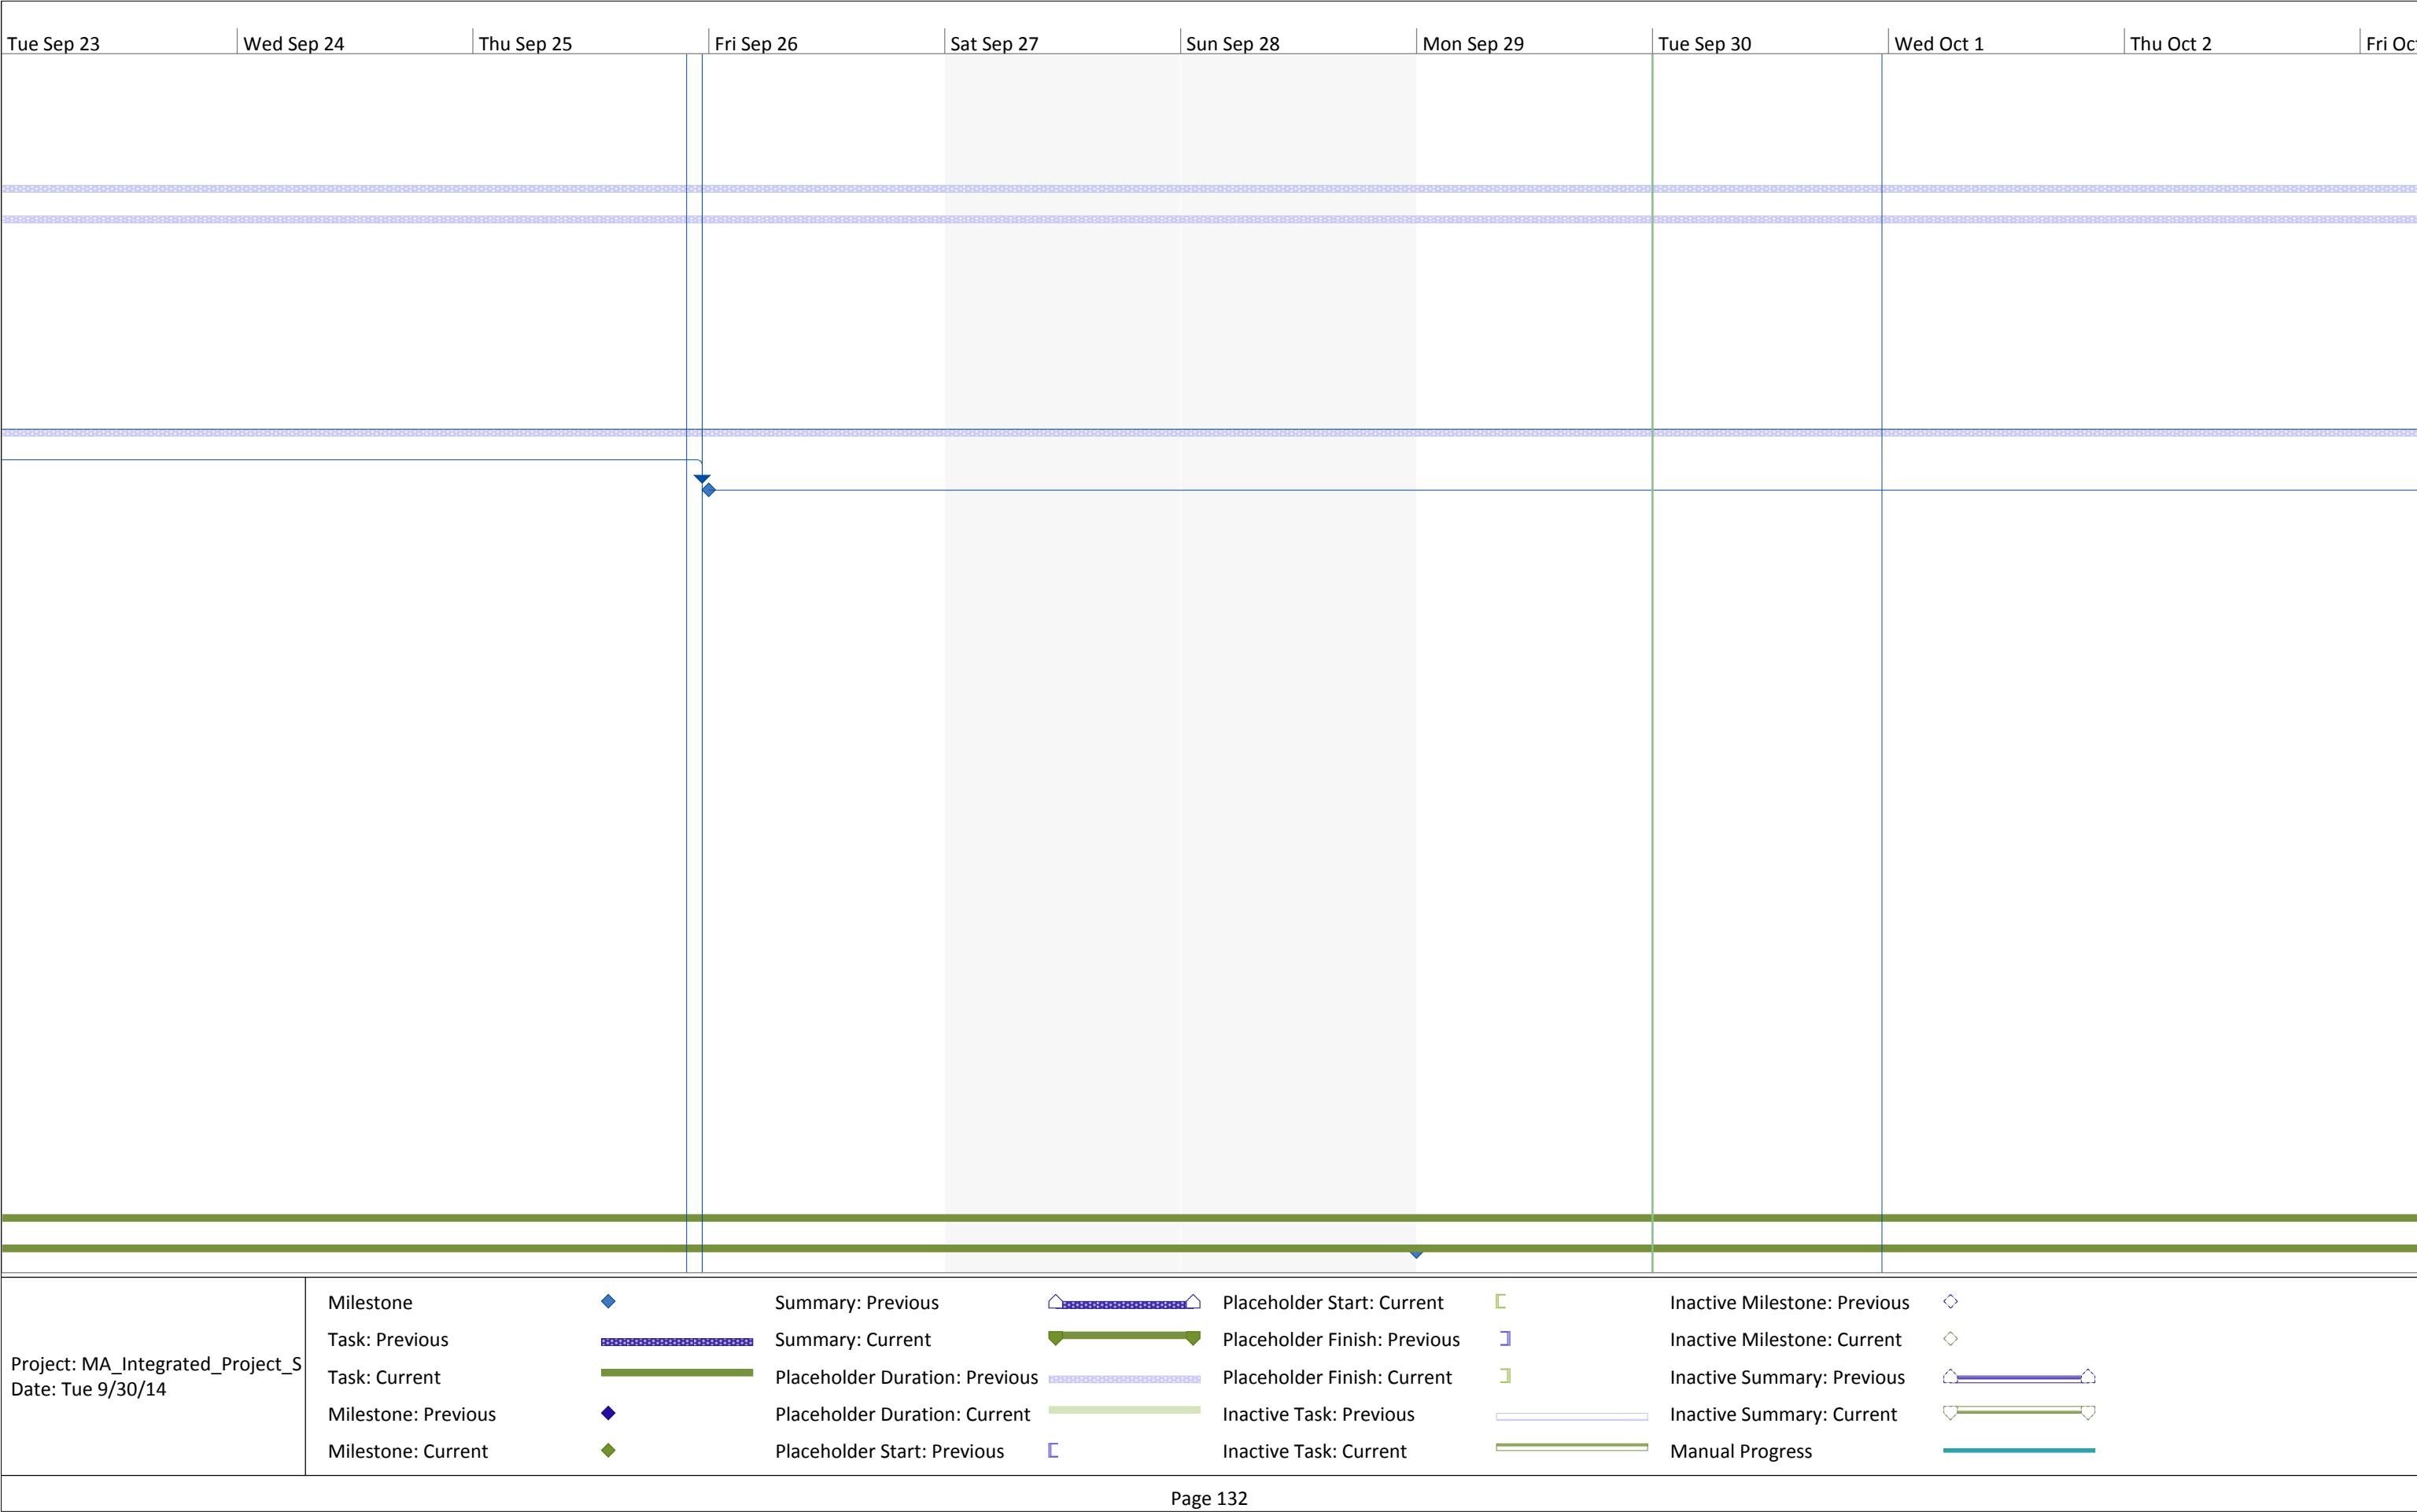


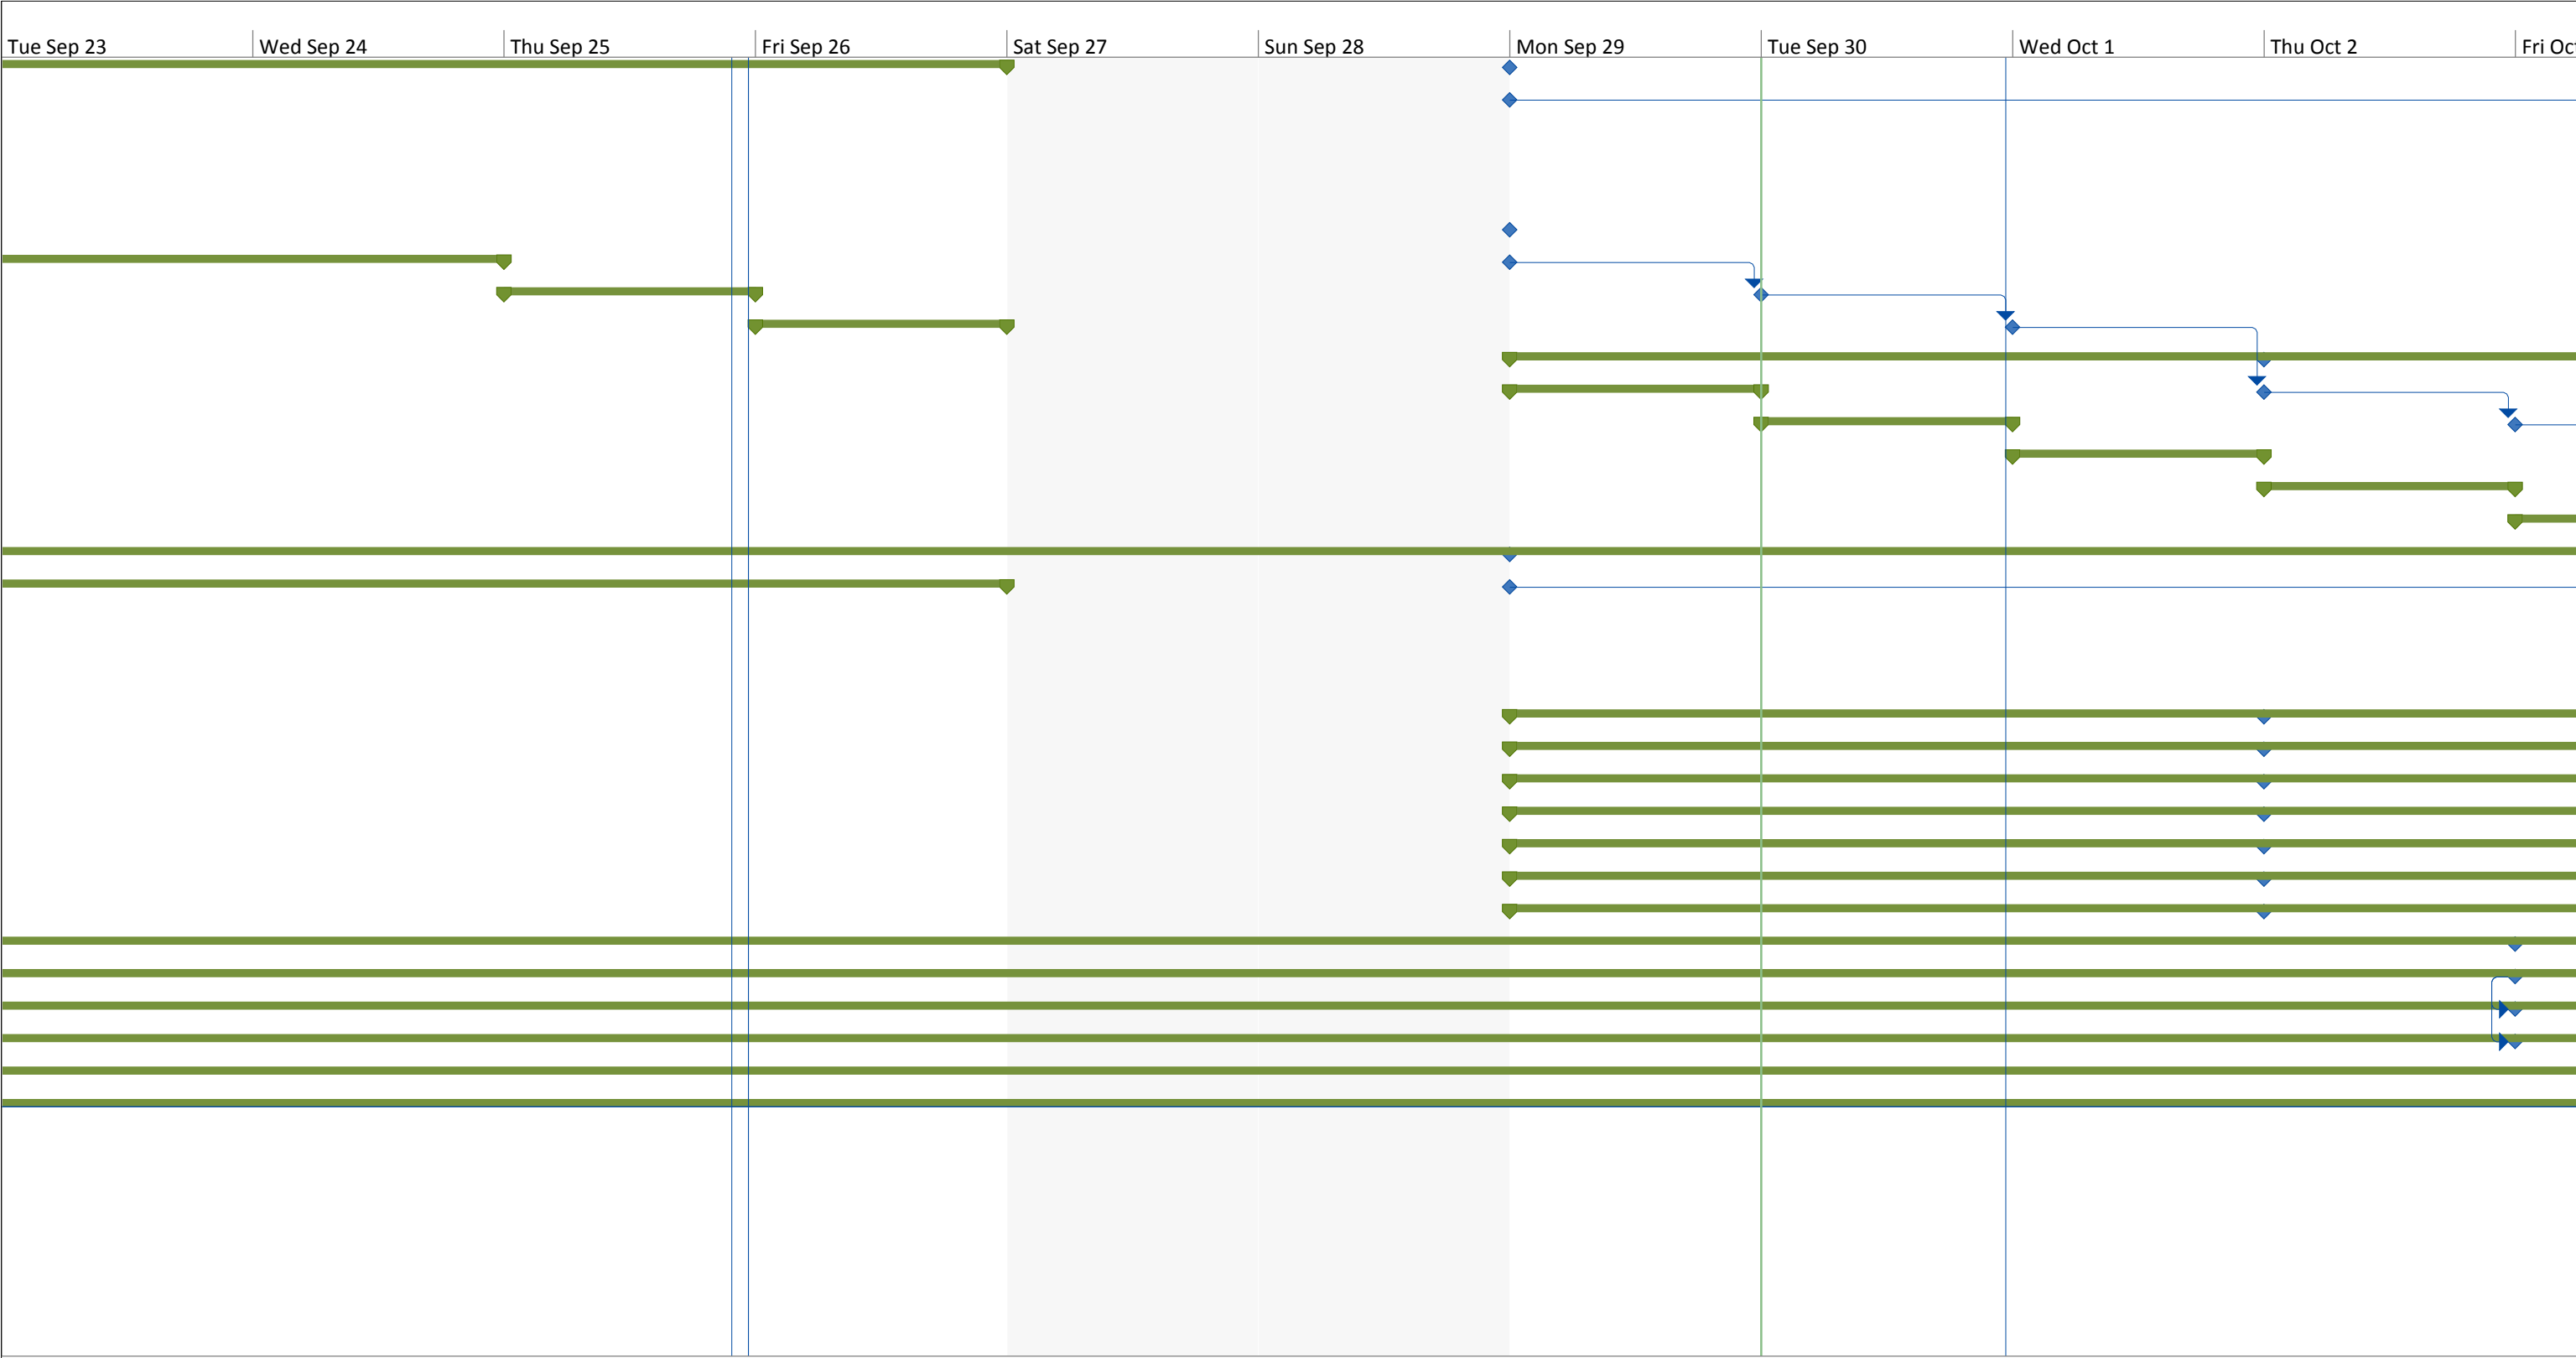


Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone	◆	Summary: Previous	▨	Placeholder Start: Current	▬	Inactive Milestone: Previous	◆
	Task: Previous	▨	Summary: Current	▬	Placeholder Finish: Previous	▬	Inactive Milestone: Current	◆
	Task: Current	▬	Placeholder Duration: Previous	▨	Placeholder Finish: Current	▬	Inactive Summary: Previous	▬
	Milestone: Previous	◆	Placeholder Duration: Current	▬	Inactive Task: Previous	▬	Inactive Summary: Current	▬
	Milestone: Current	◆	Placeholder Start: Previous	▬	Inactive Task: Current	▬	Manual Progress	▬

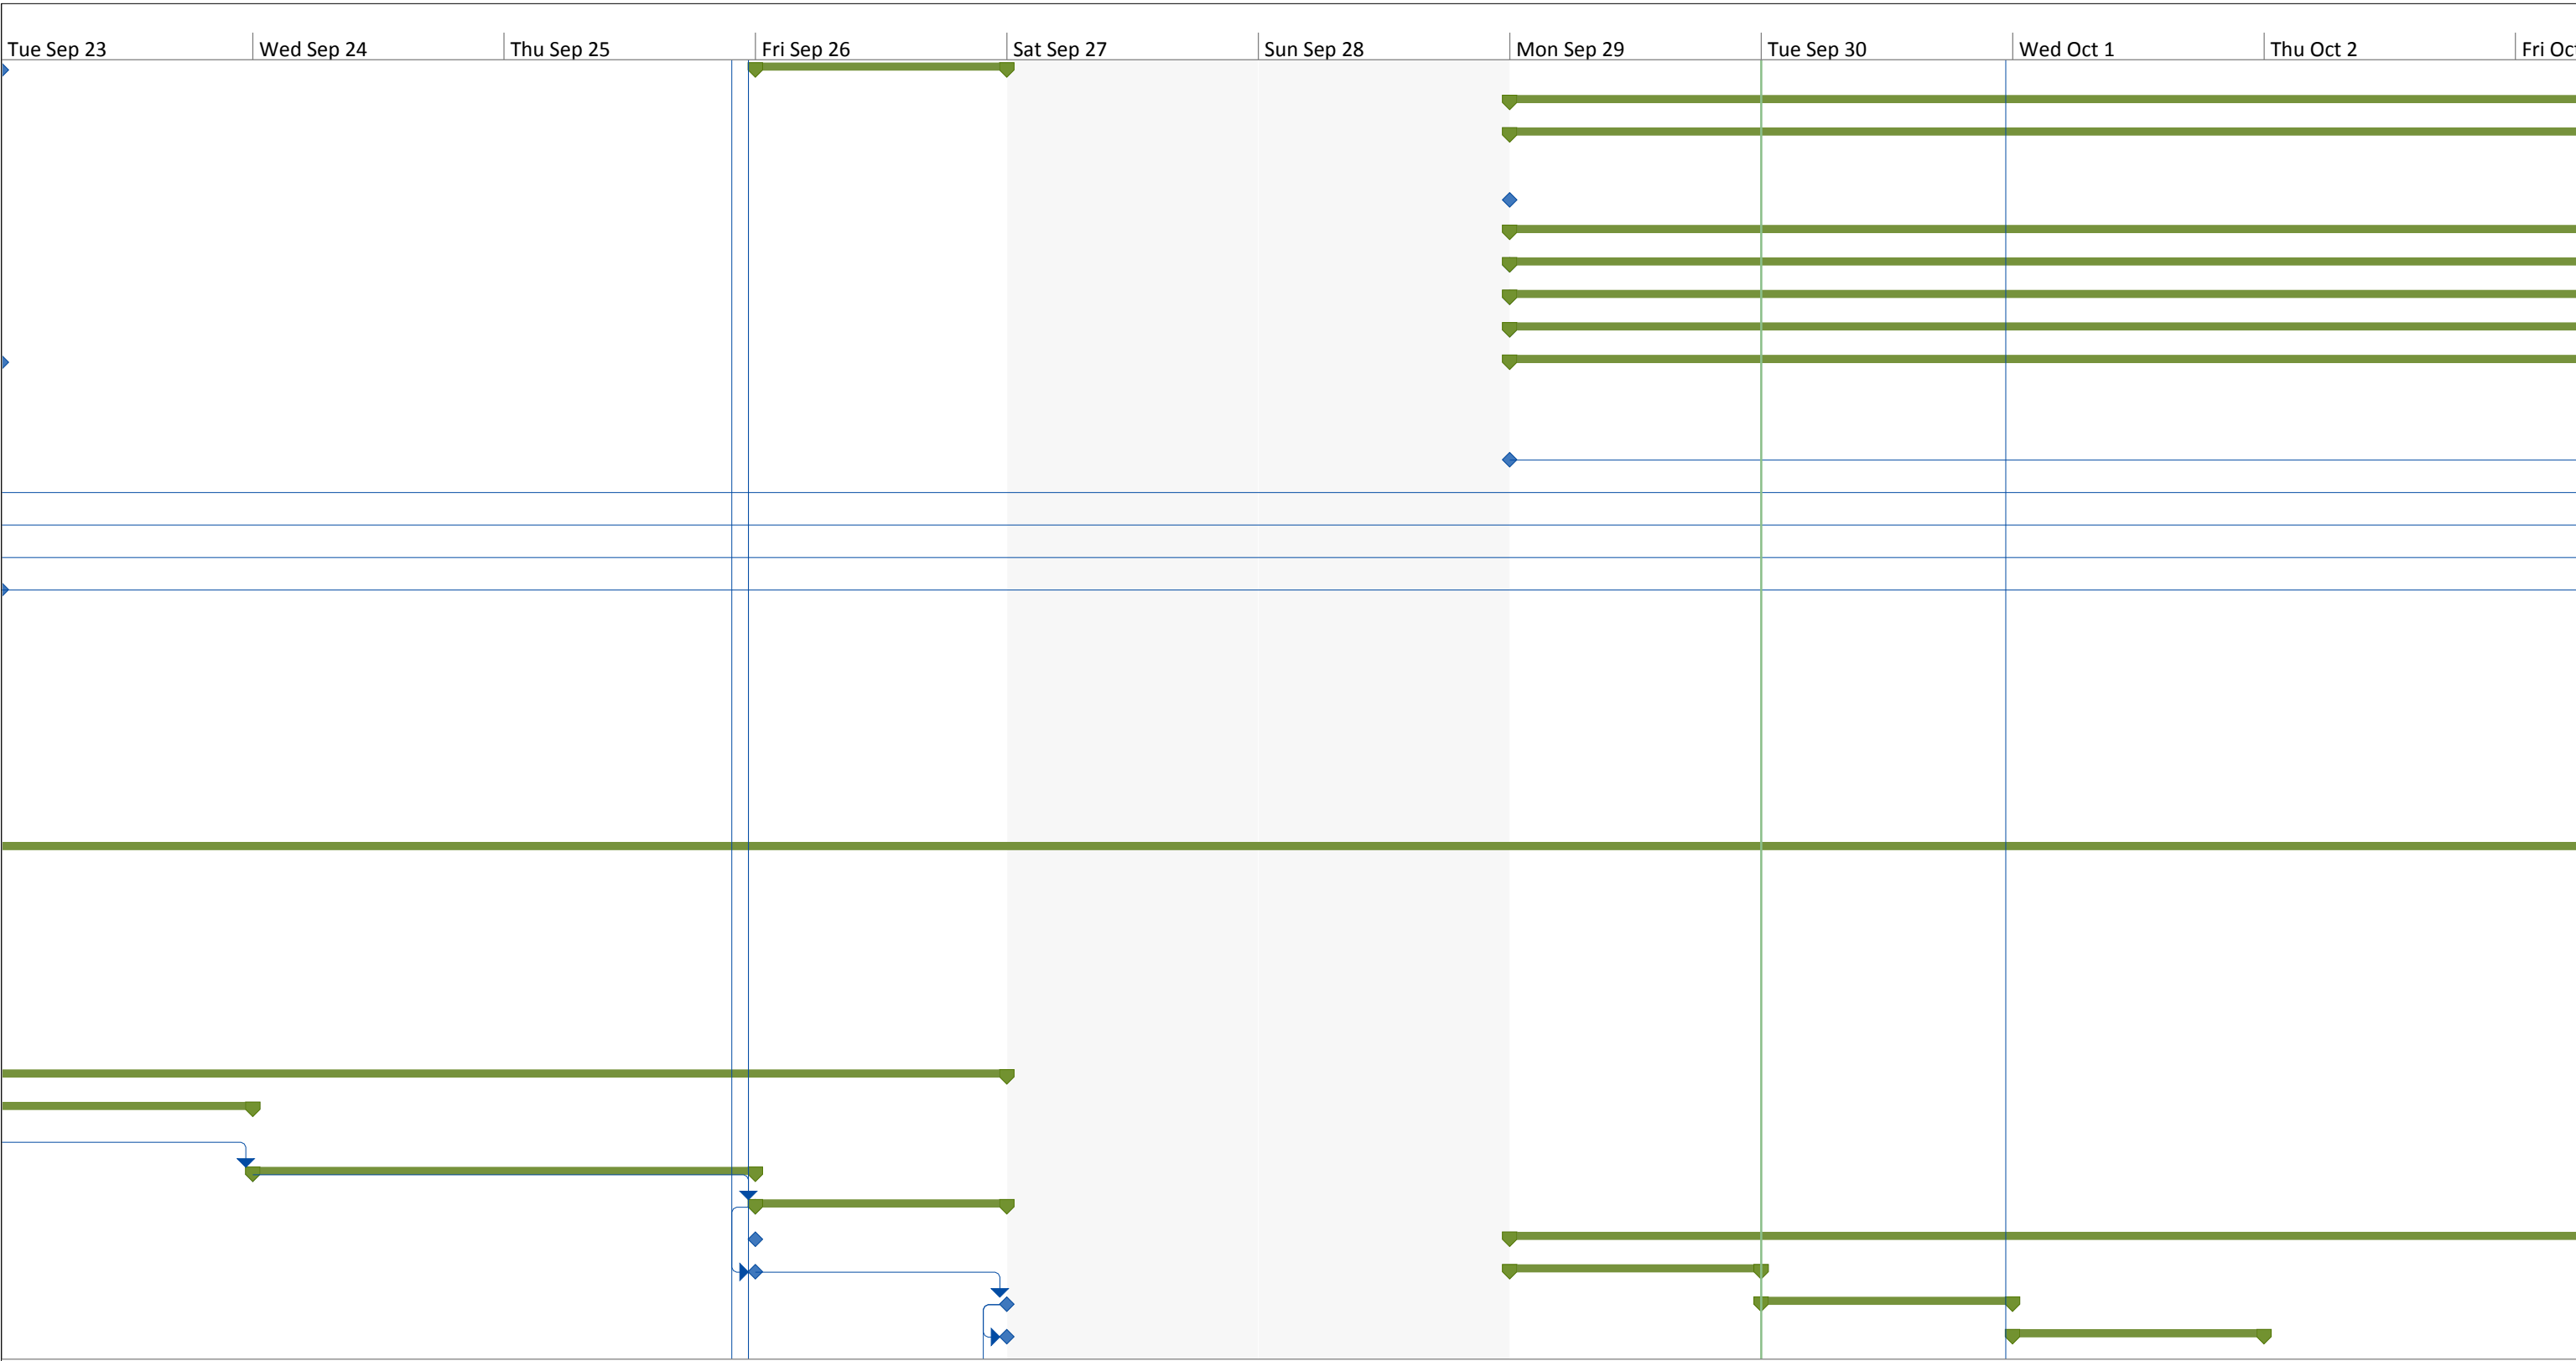


Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

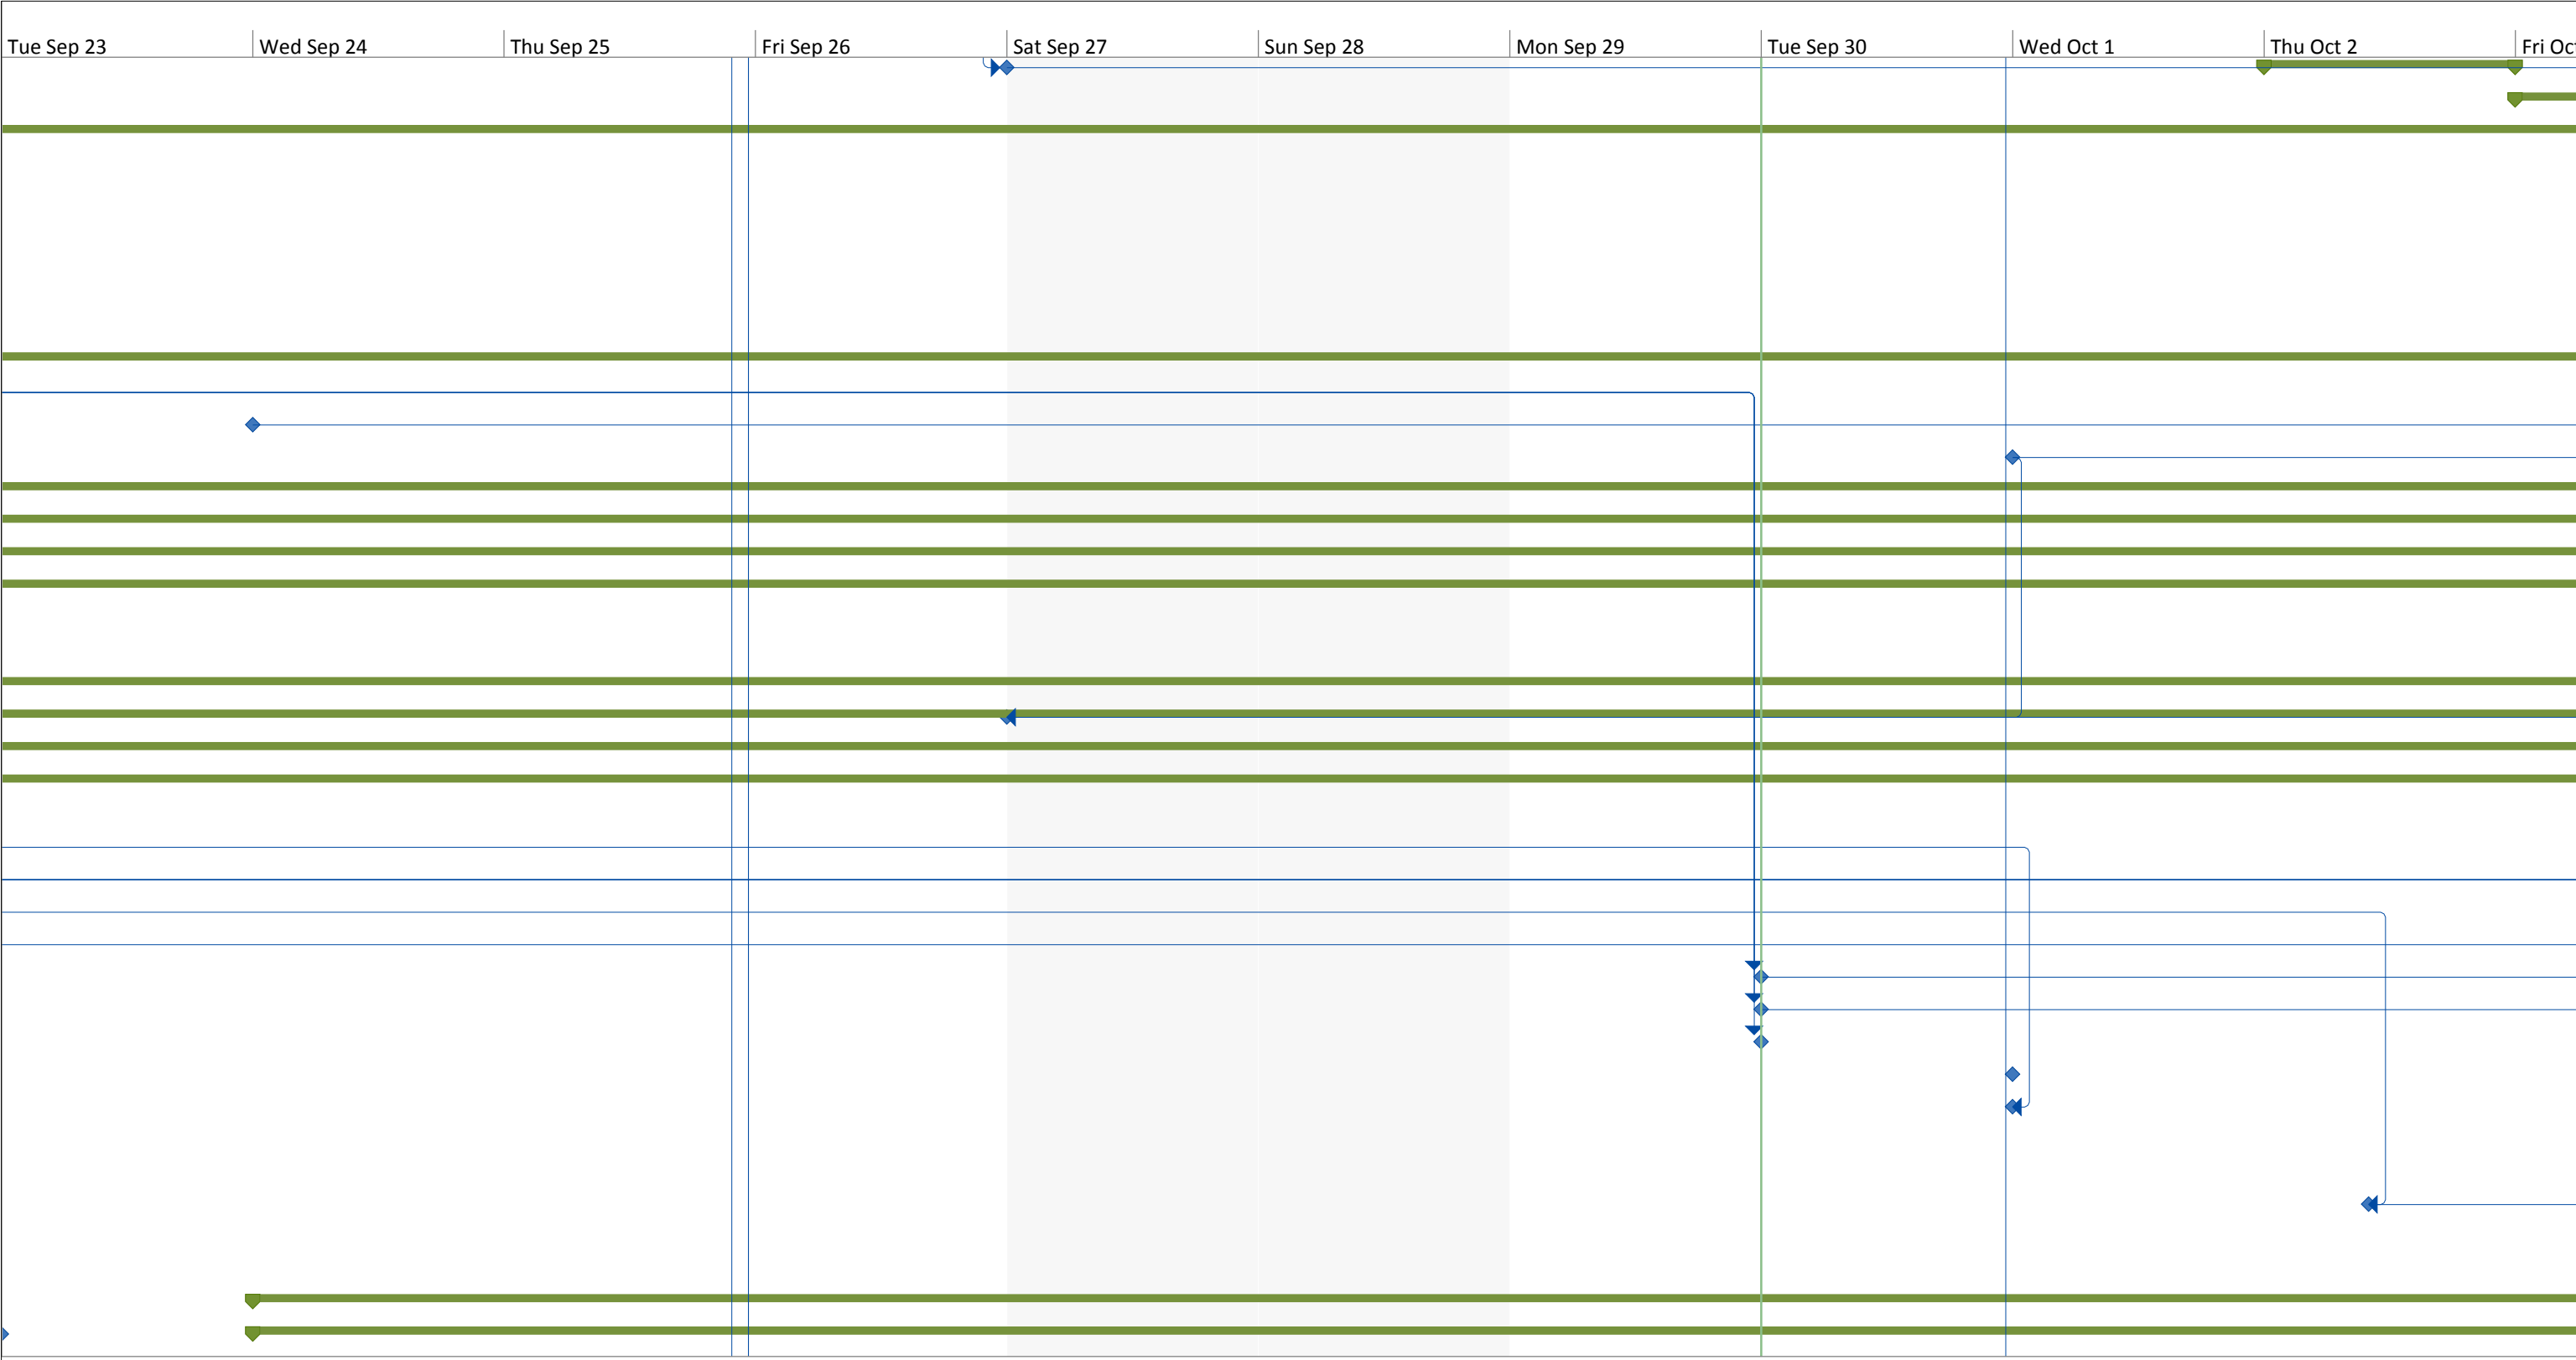



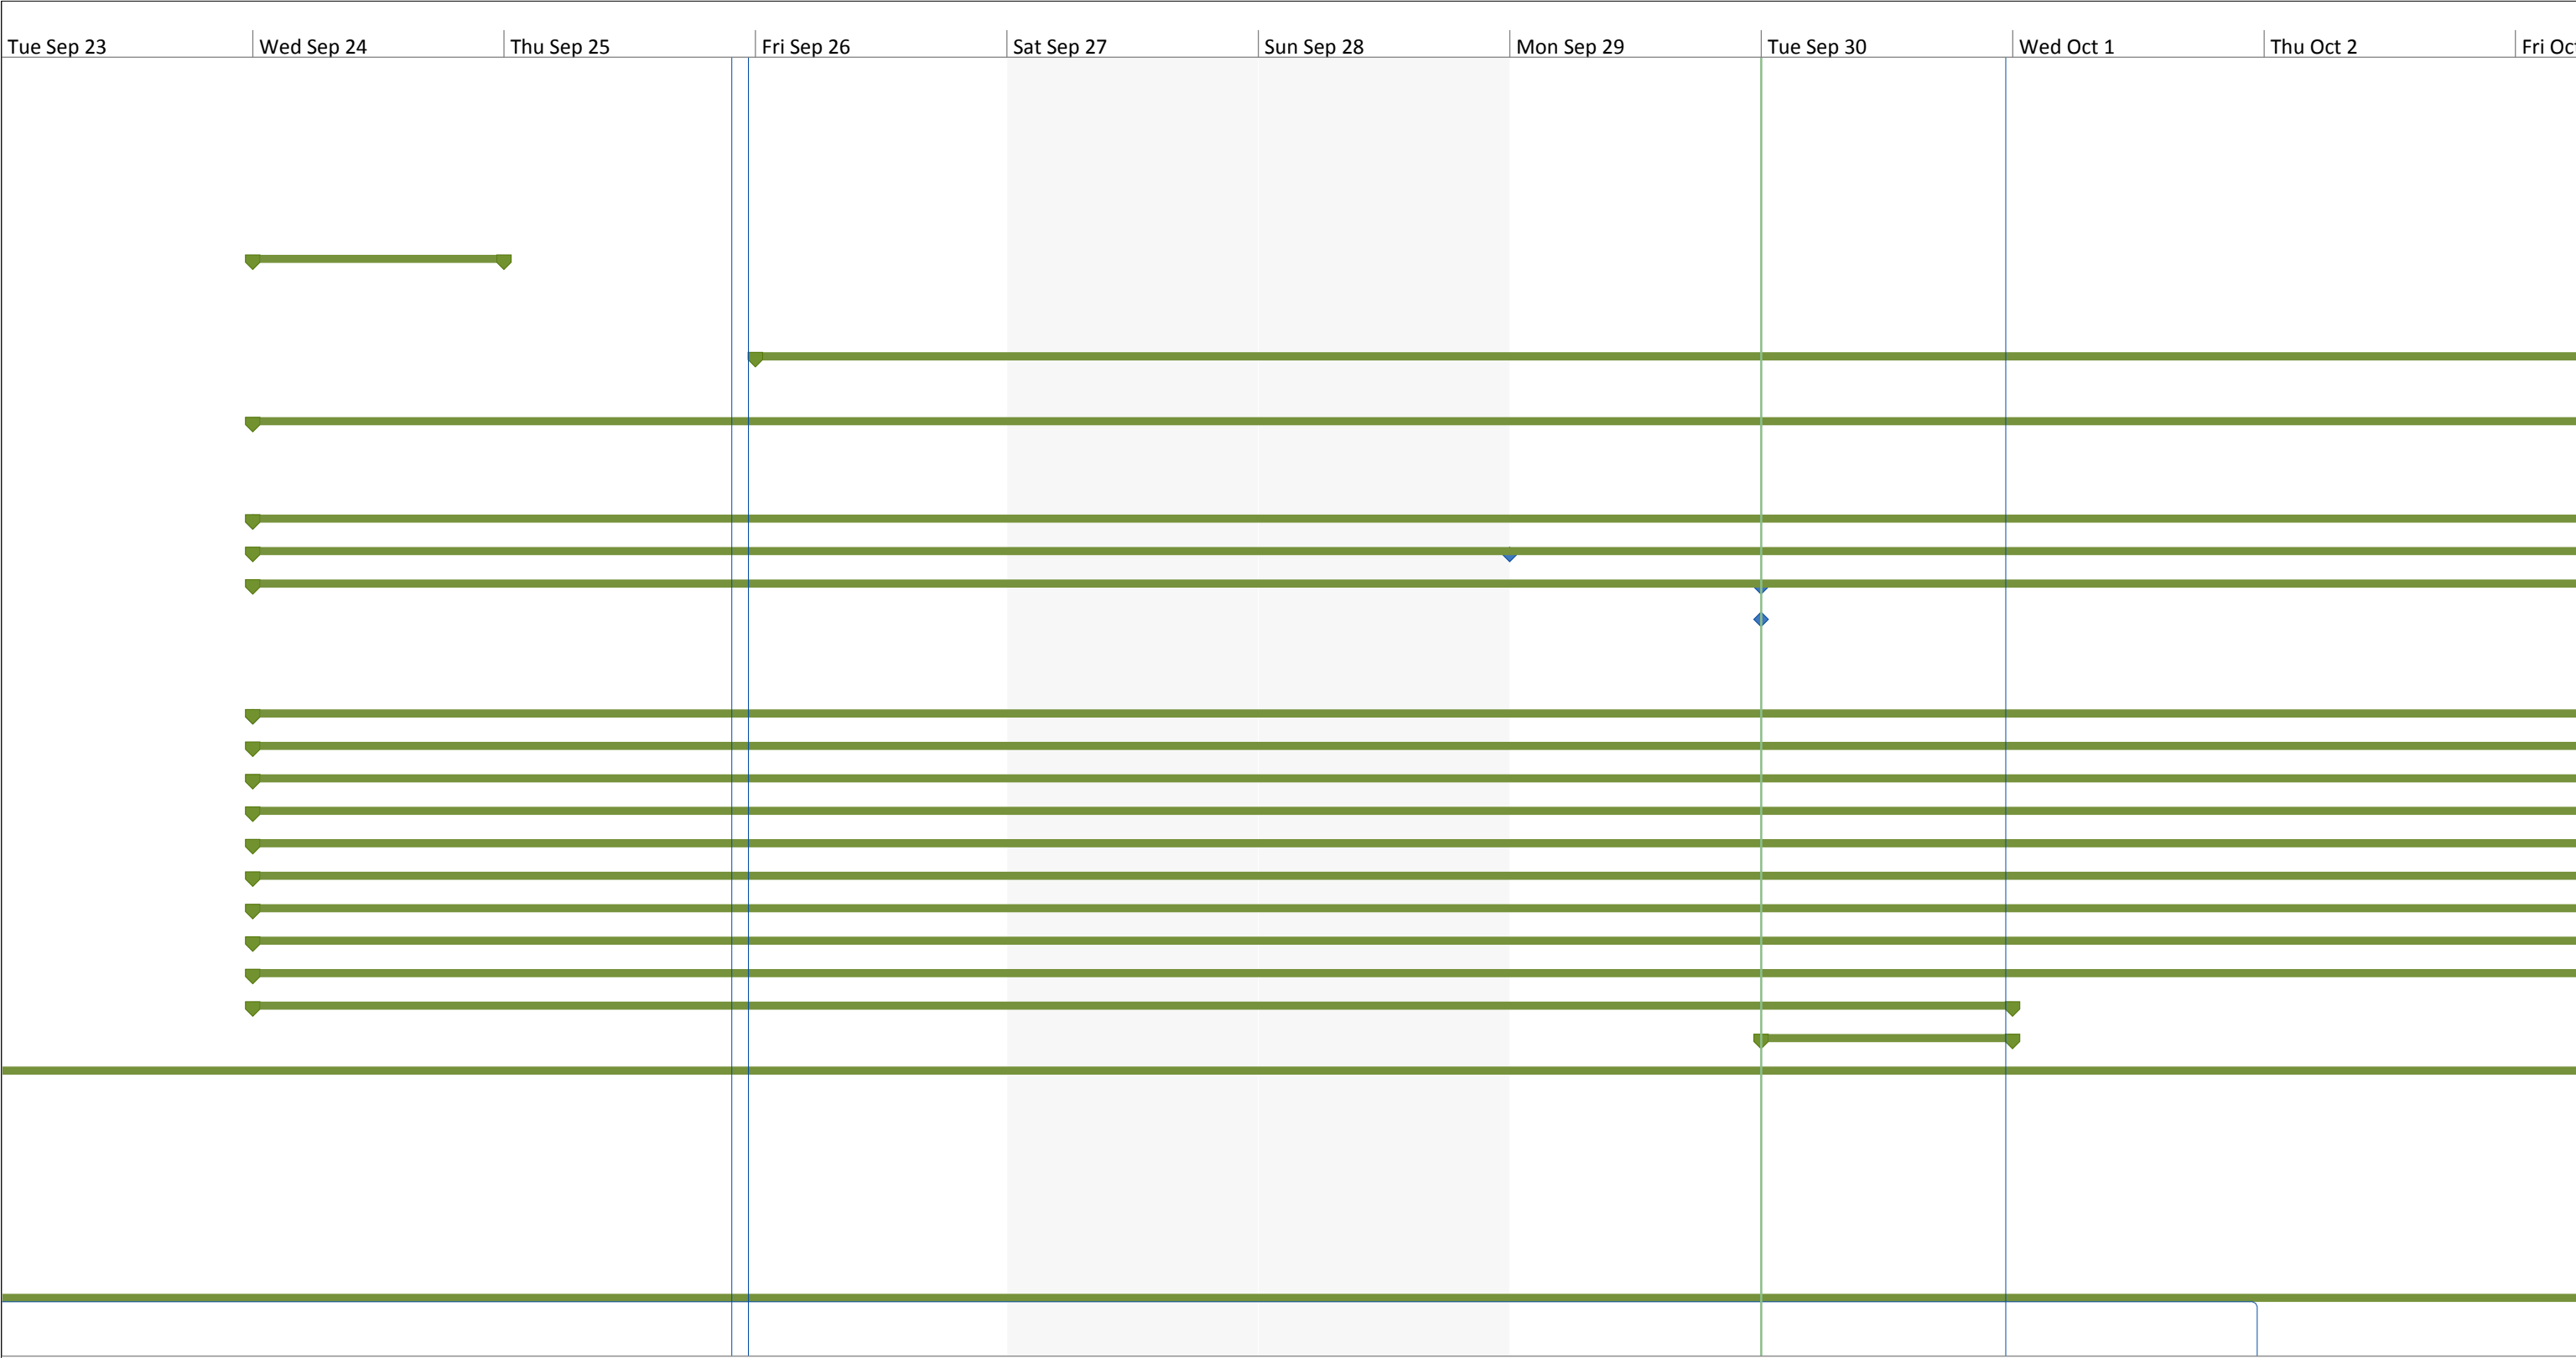



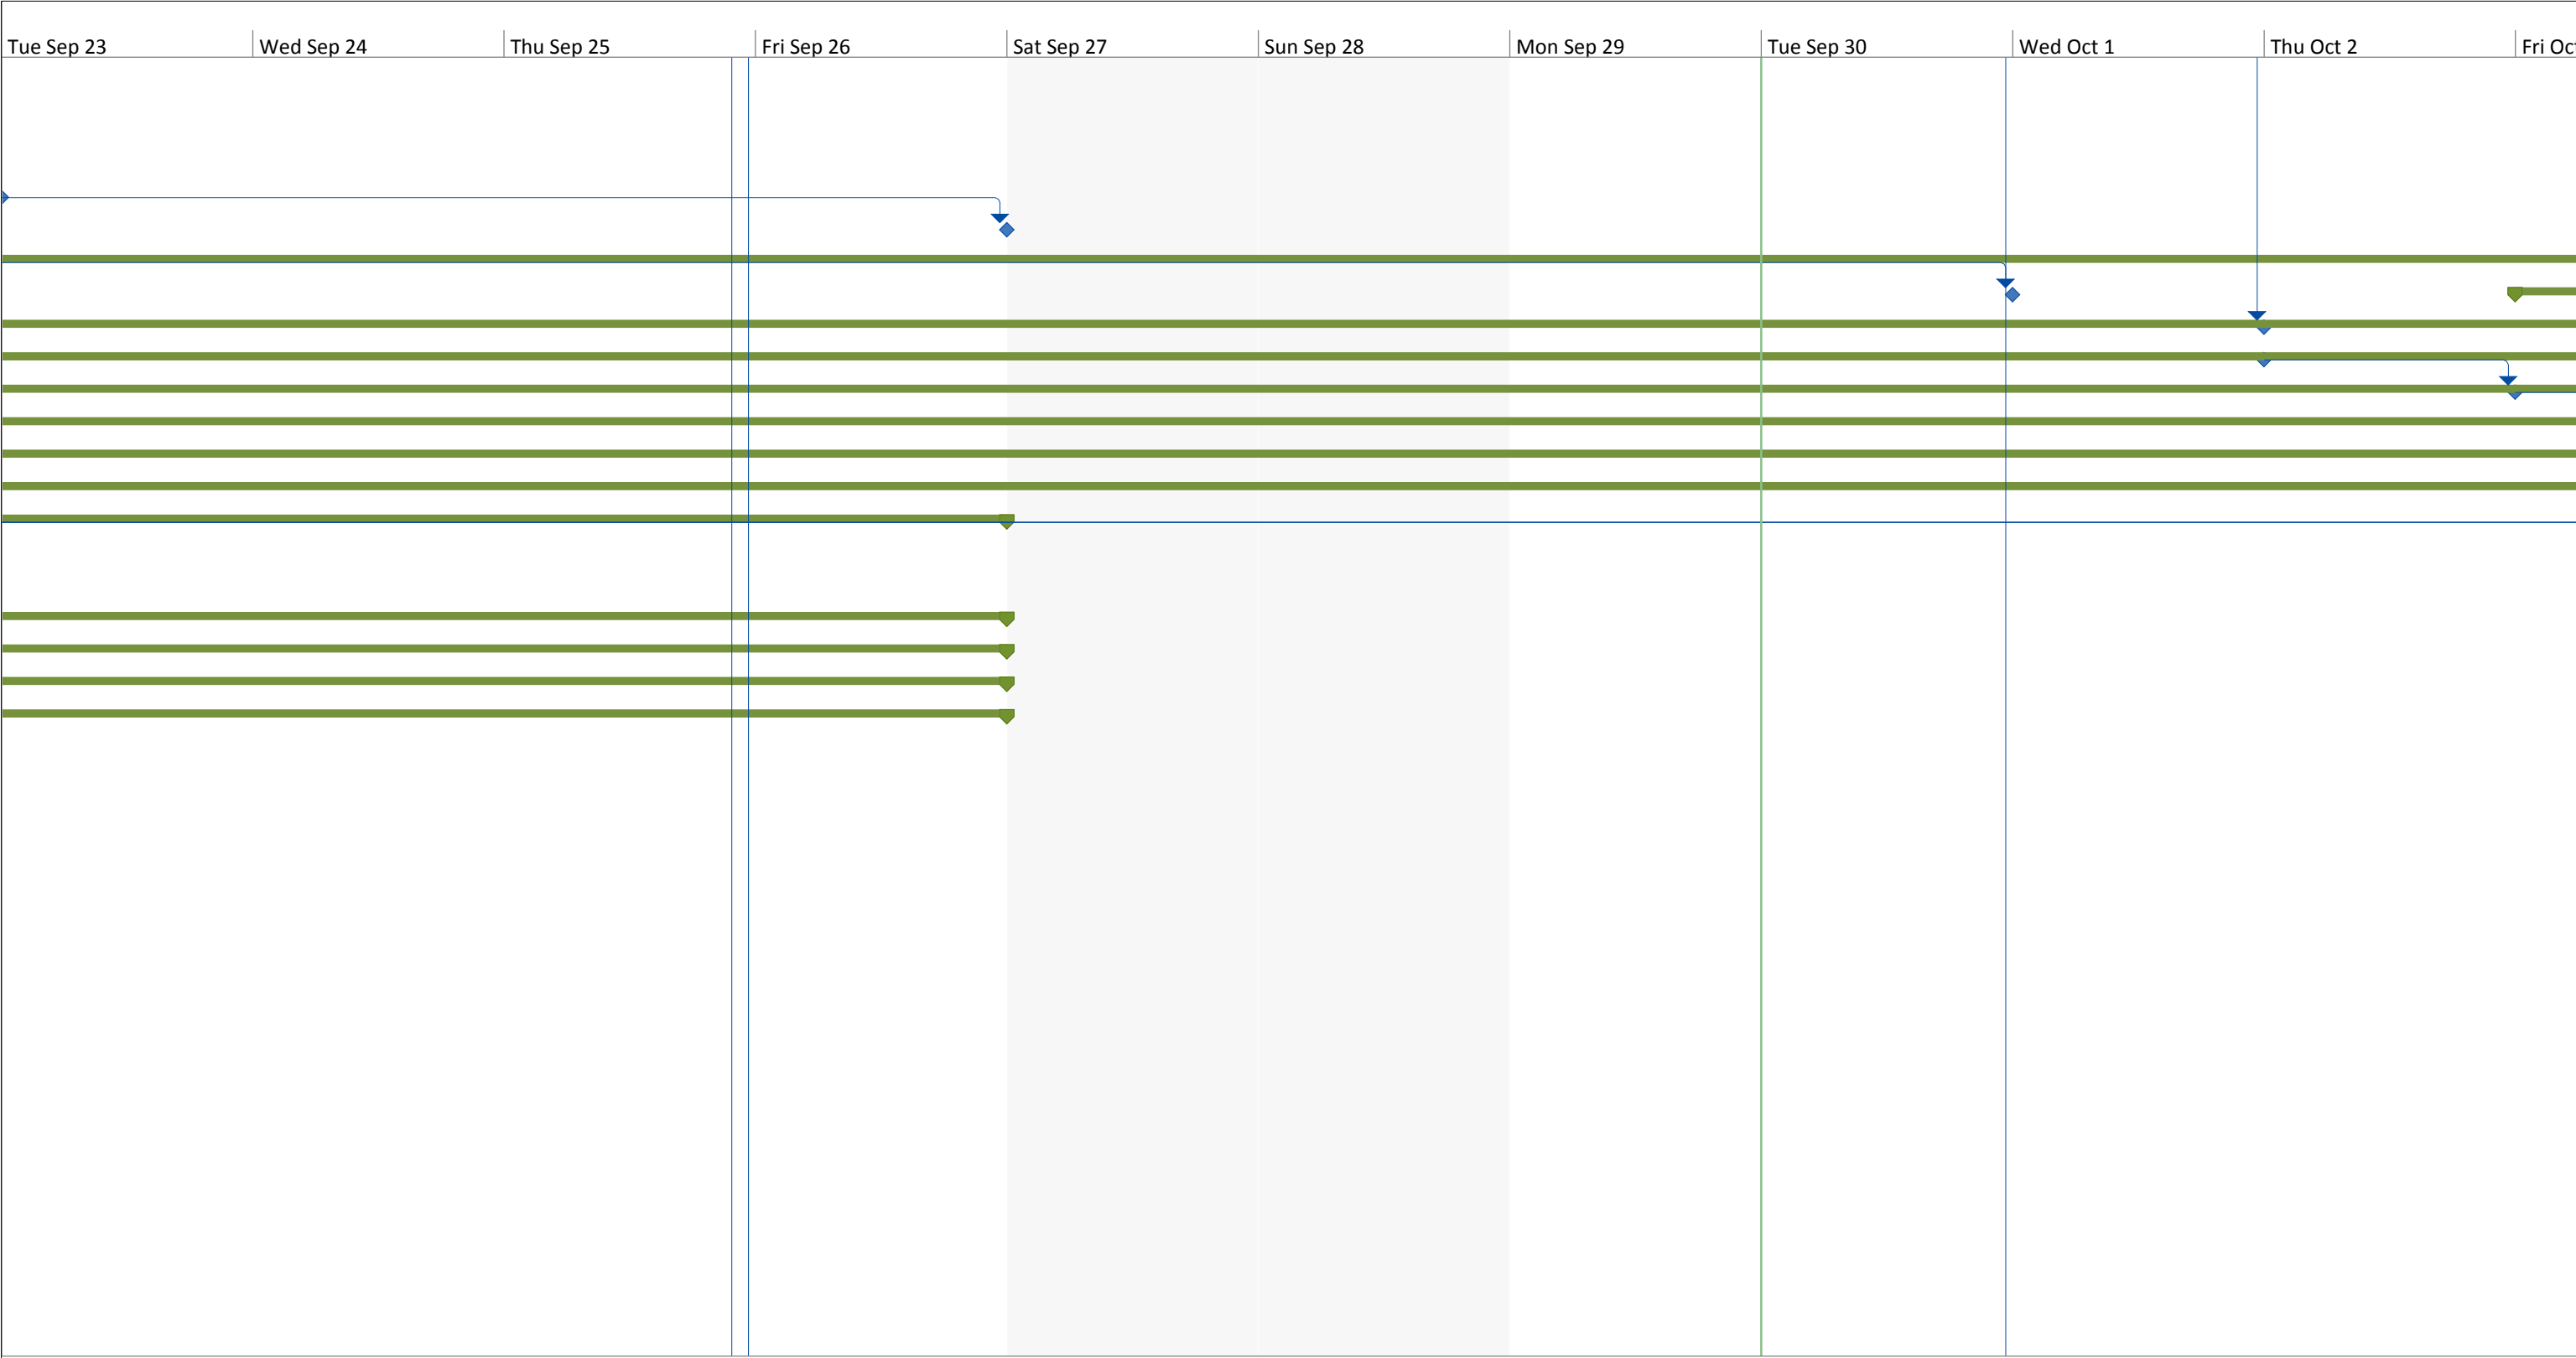














Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	



Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	



Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

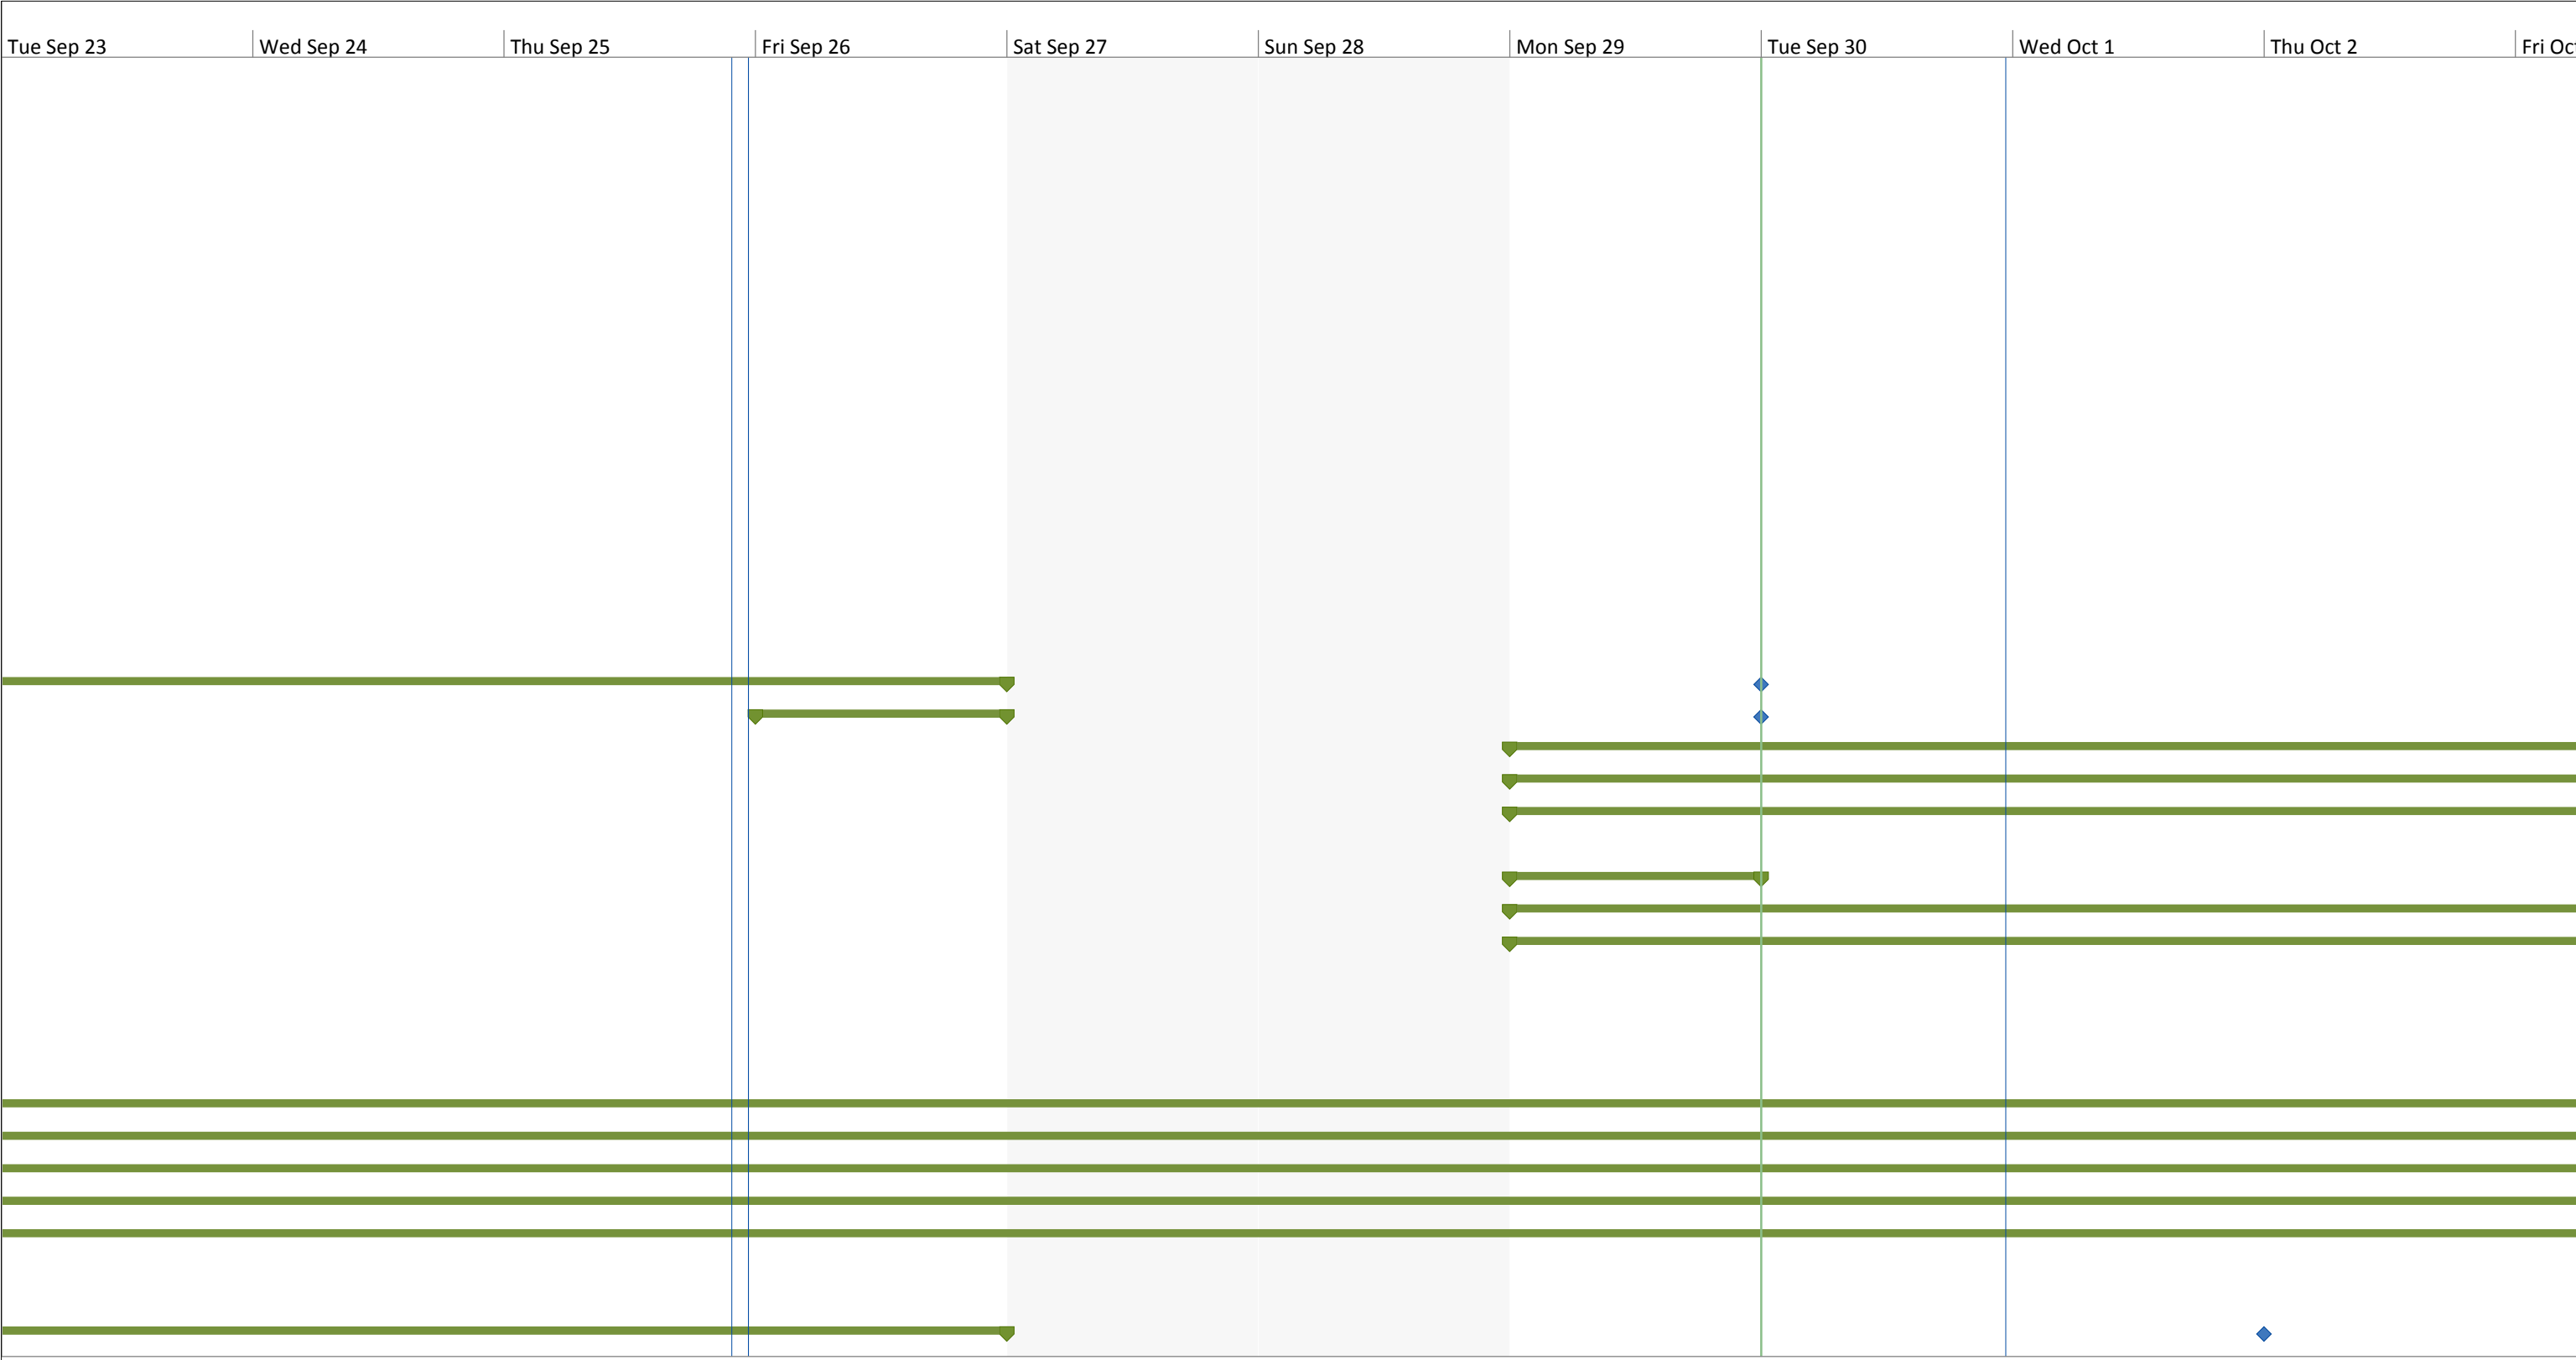

Project: MA_Integrated_Project_S
Date: Tue 9/30/14

Milestone

Task: Previous

Task: Current

Milestone: Previous

Milestone: Current

Summary: Previous

Summary: Current

Placeholder Duration: Previous

Placeholder Duration: Current

Placeholder Start: Previous

Placeholder Start: Current

Placeholder Finish: Previous

Placeholder Finish: Current

Inactive Task: Previous

Inactive Task: Current


Inactive Milestone: Previous


Inactive Milestone: Current


Inactive Summary: Previous


Inactive Summary: Current


Manual Progress

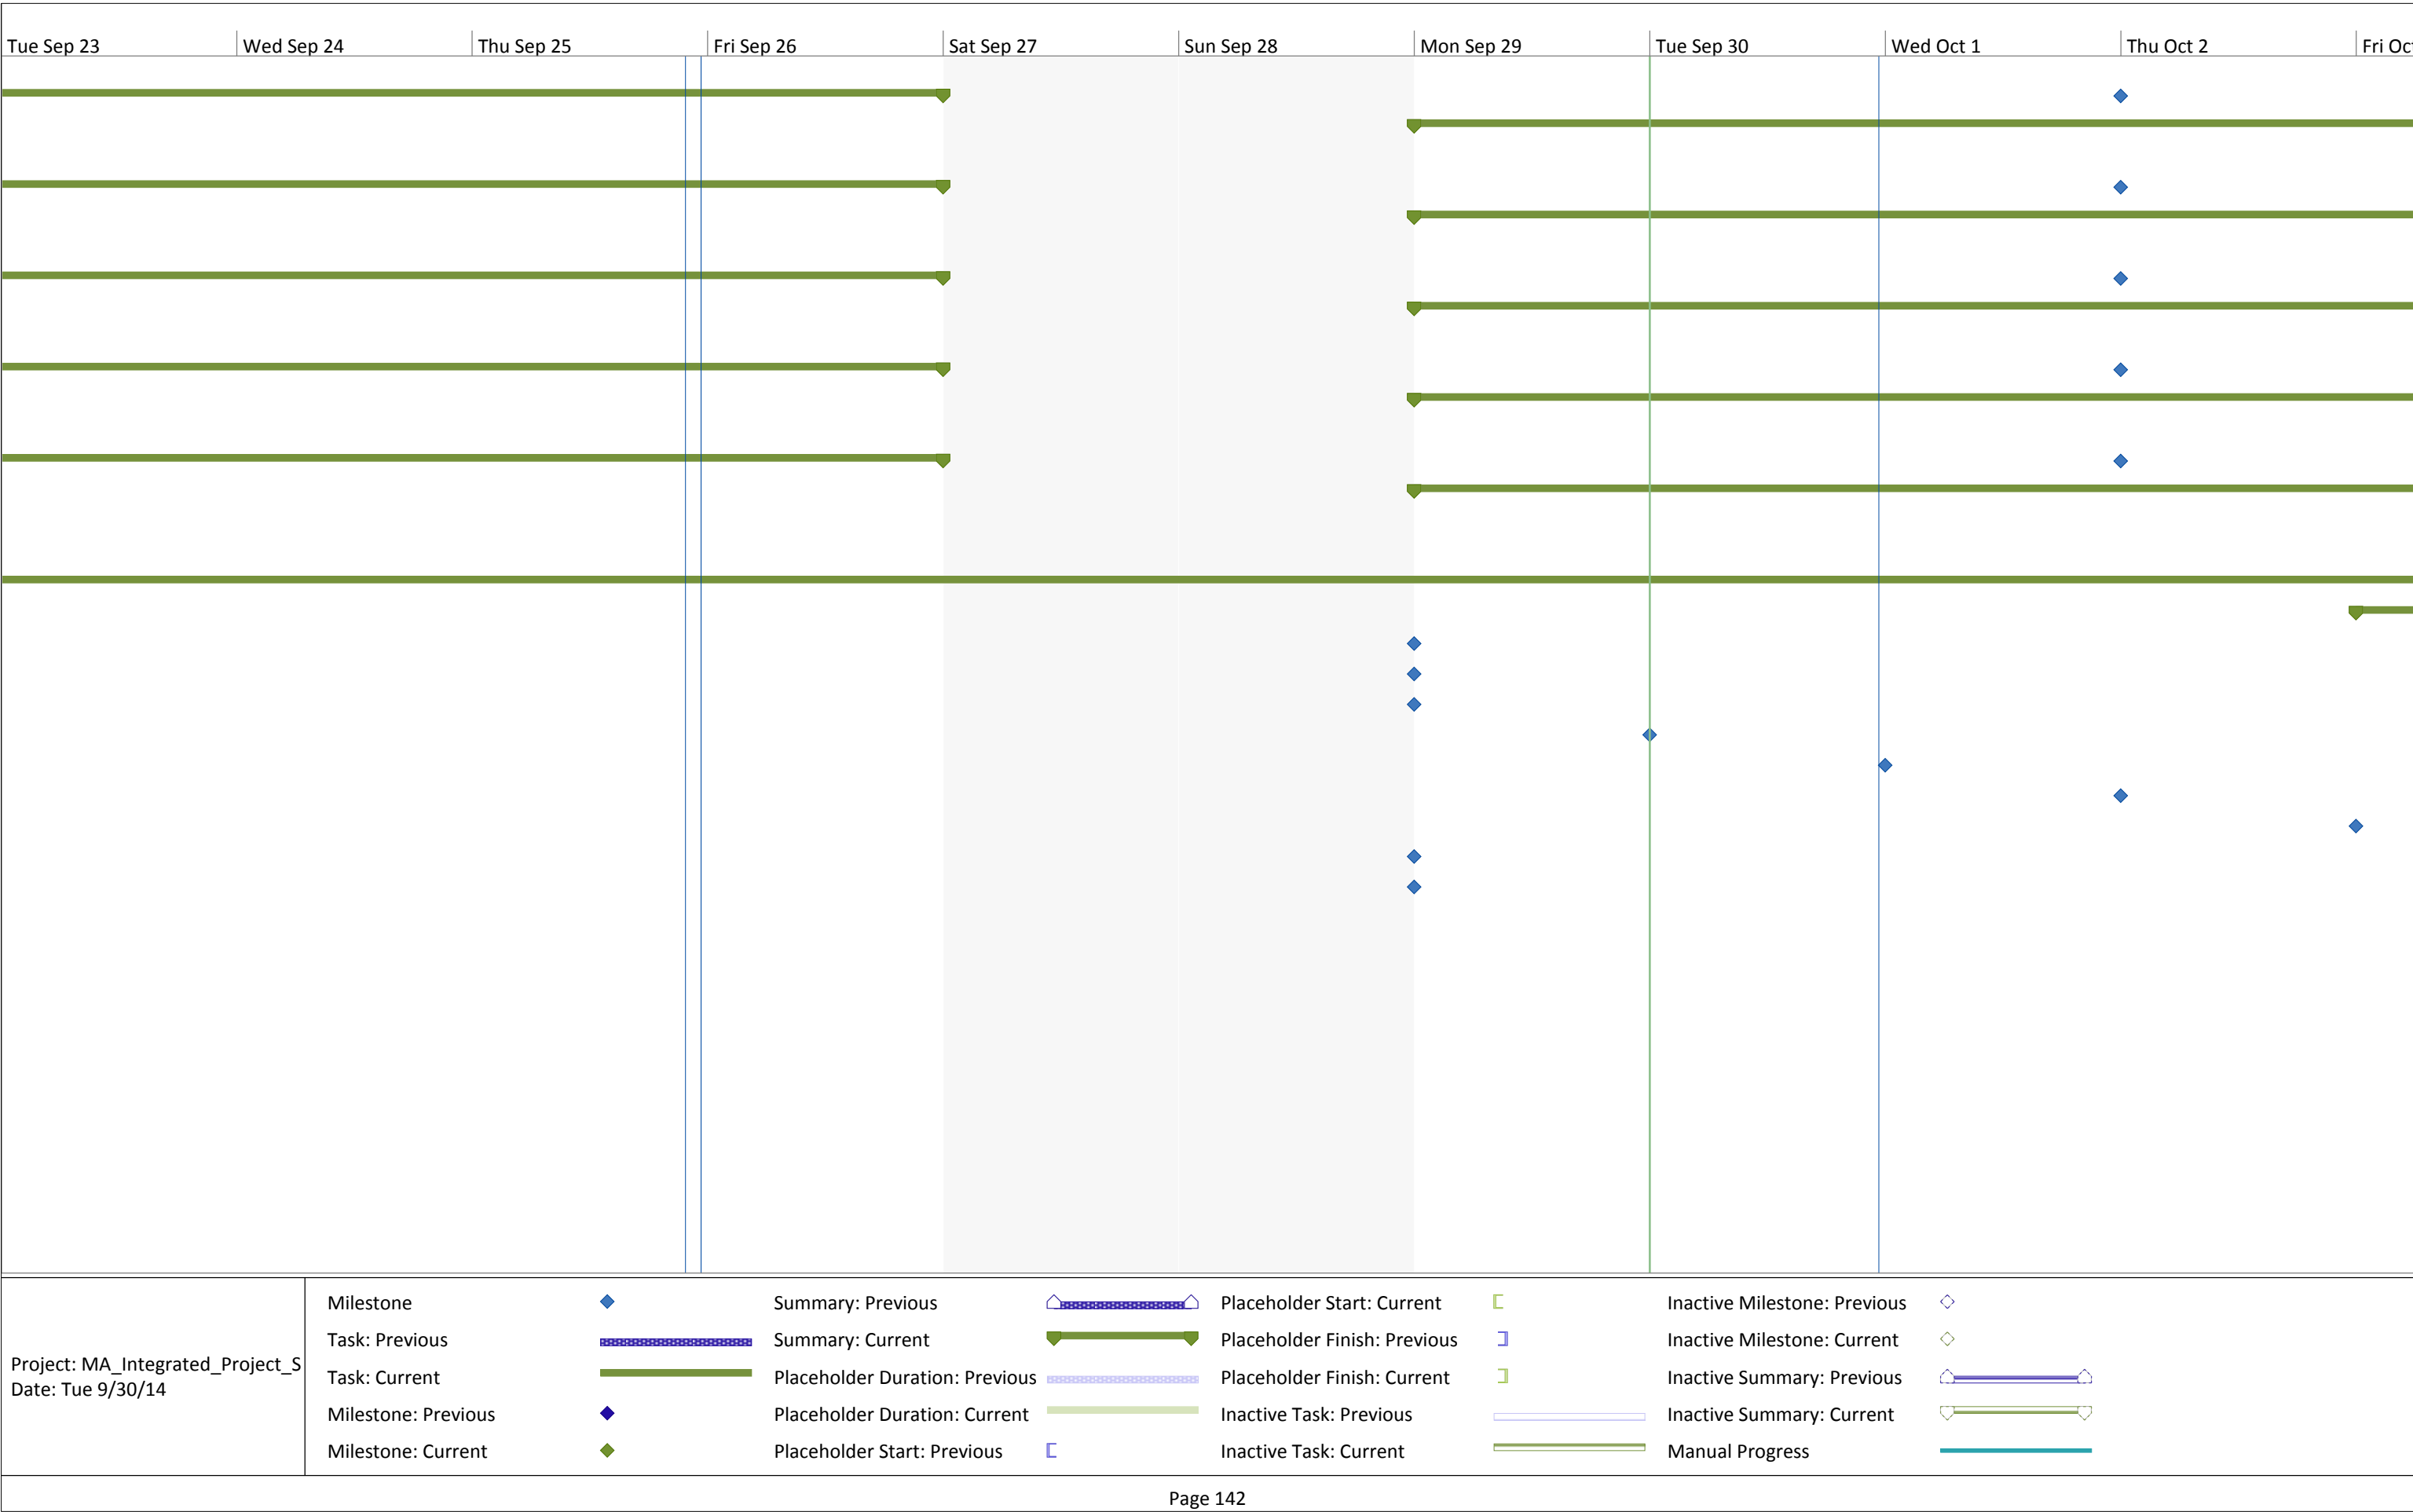


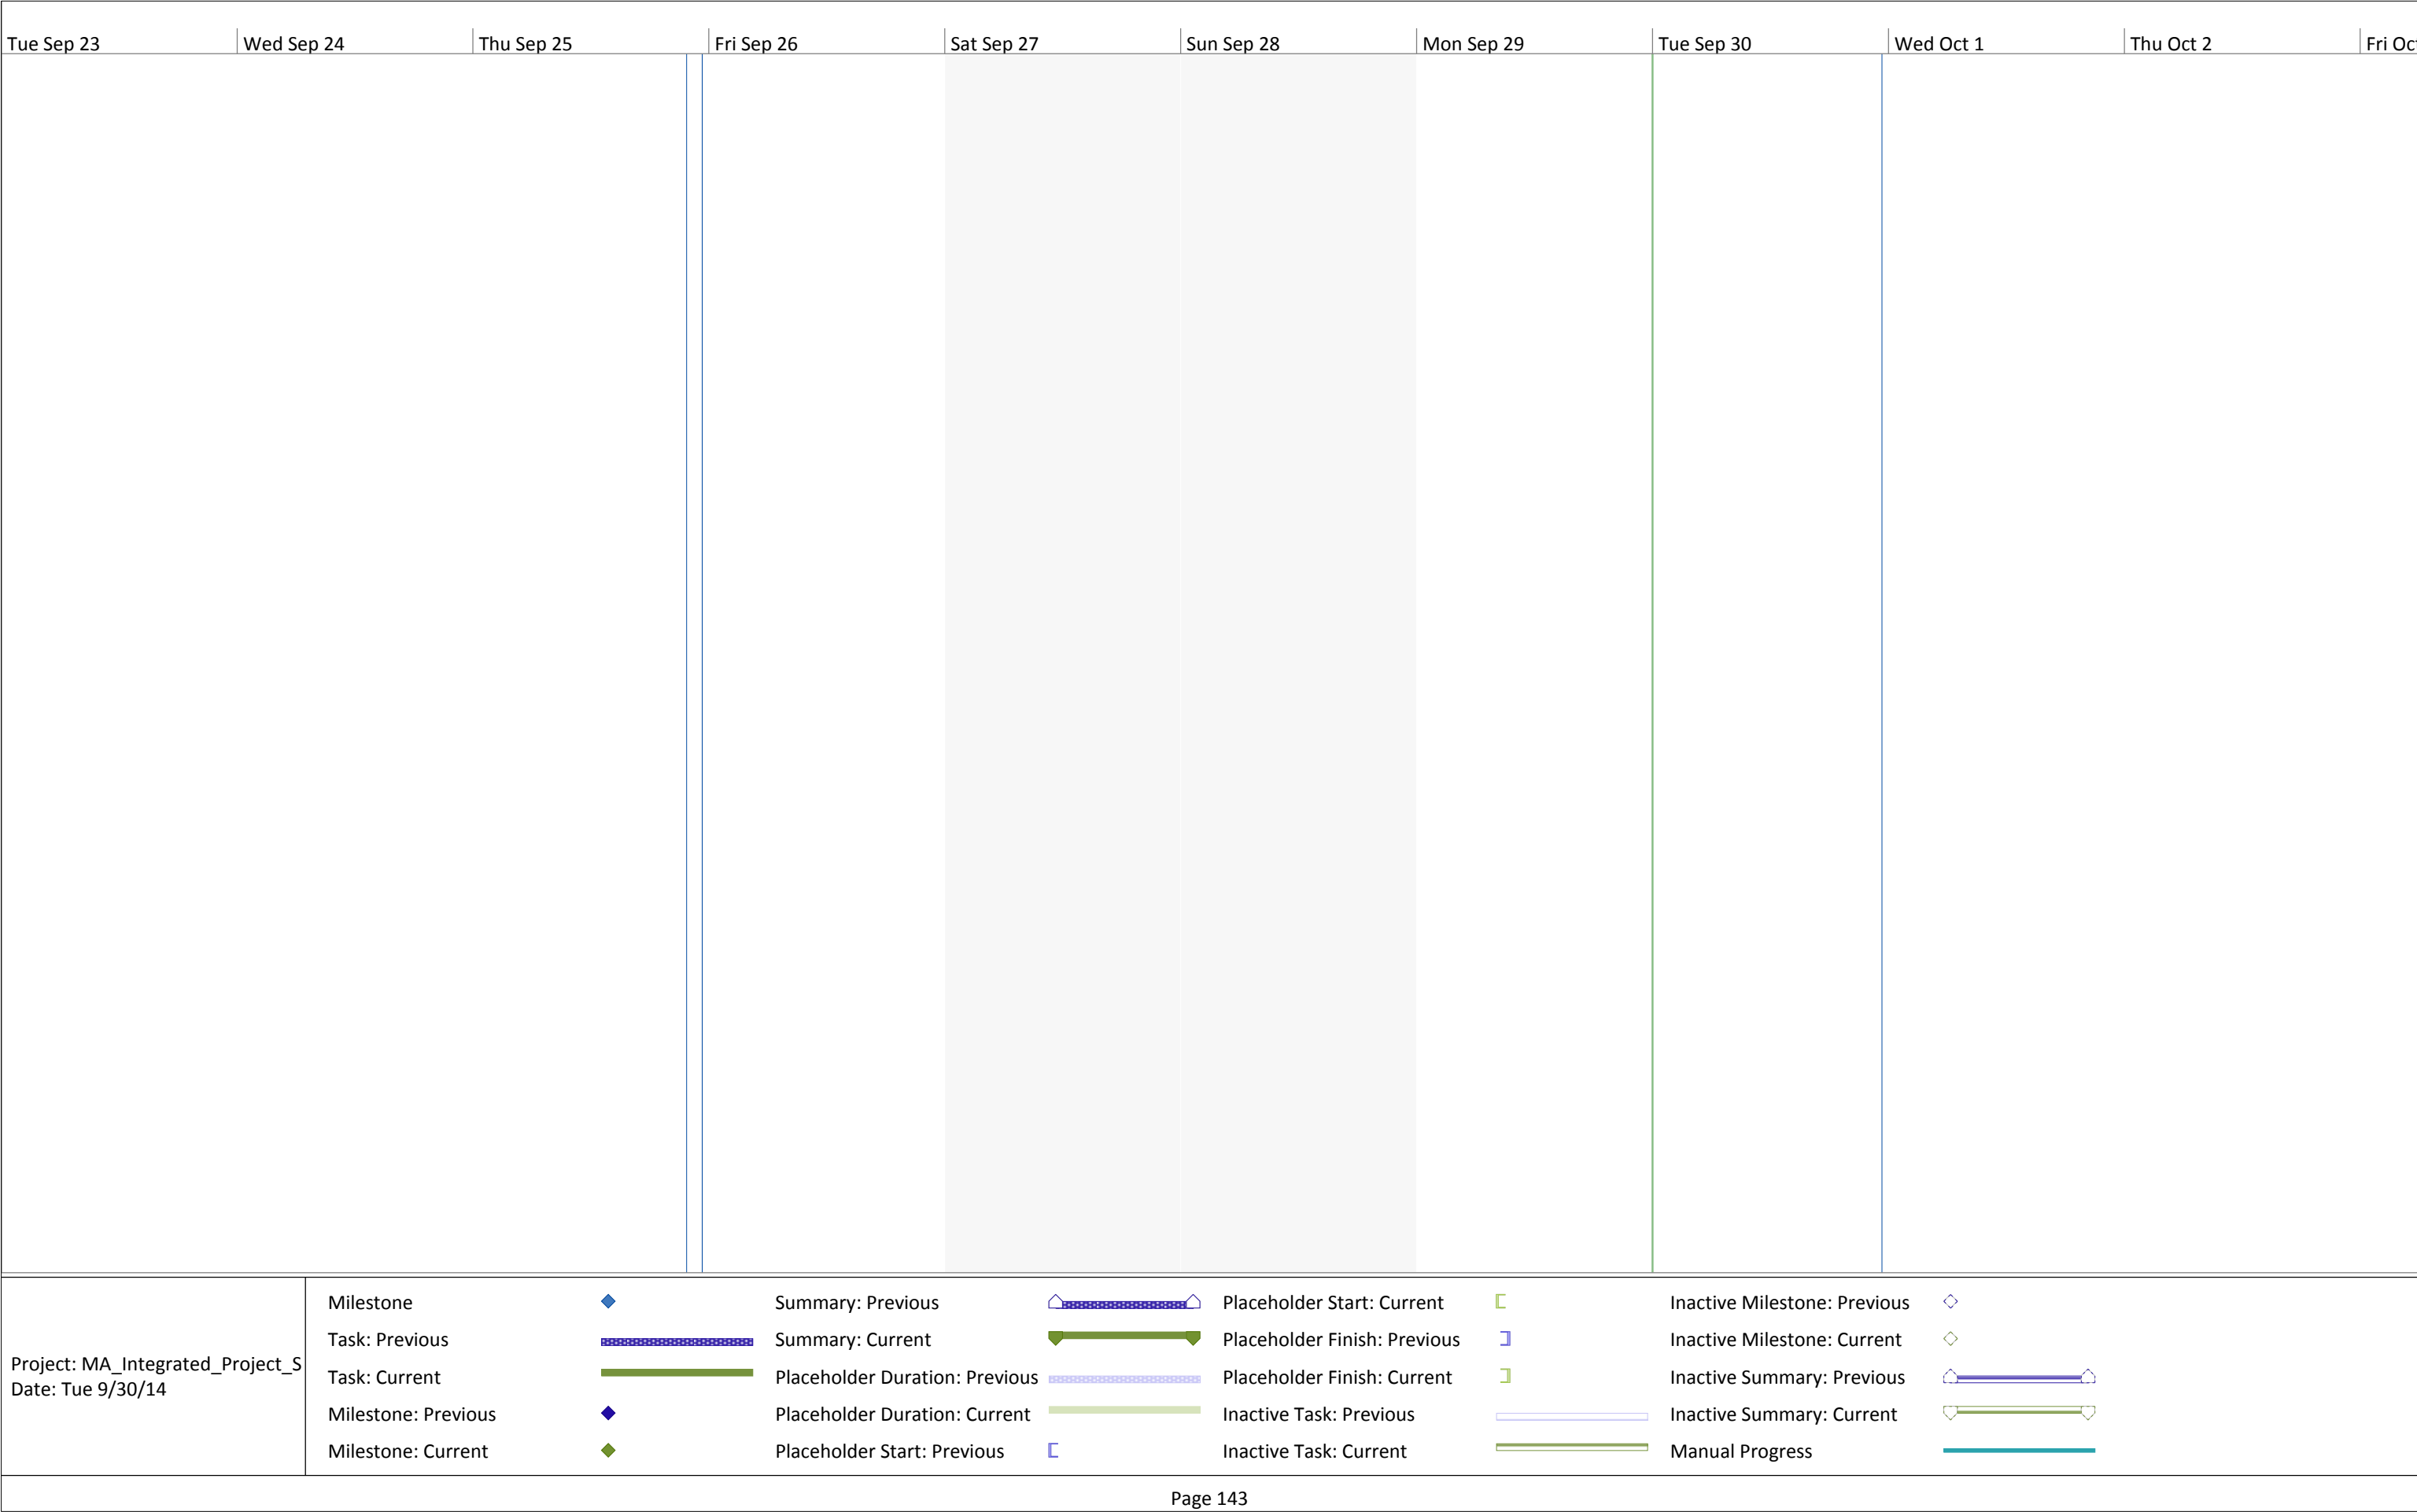


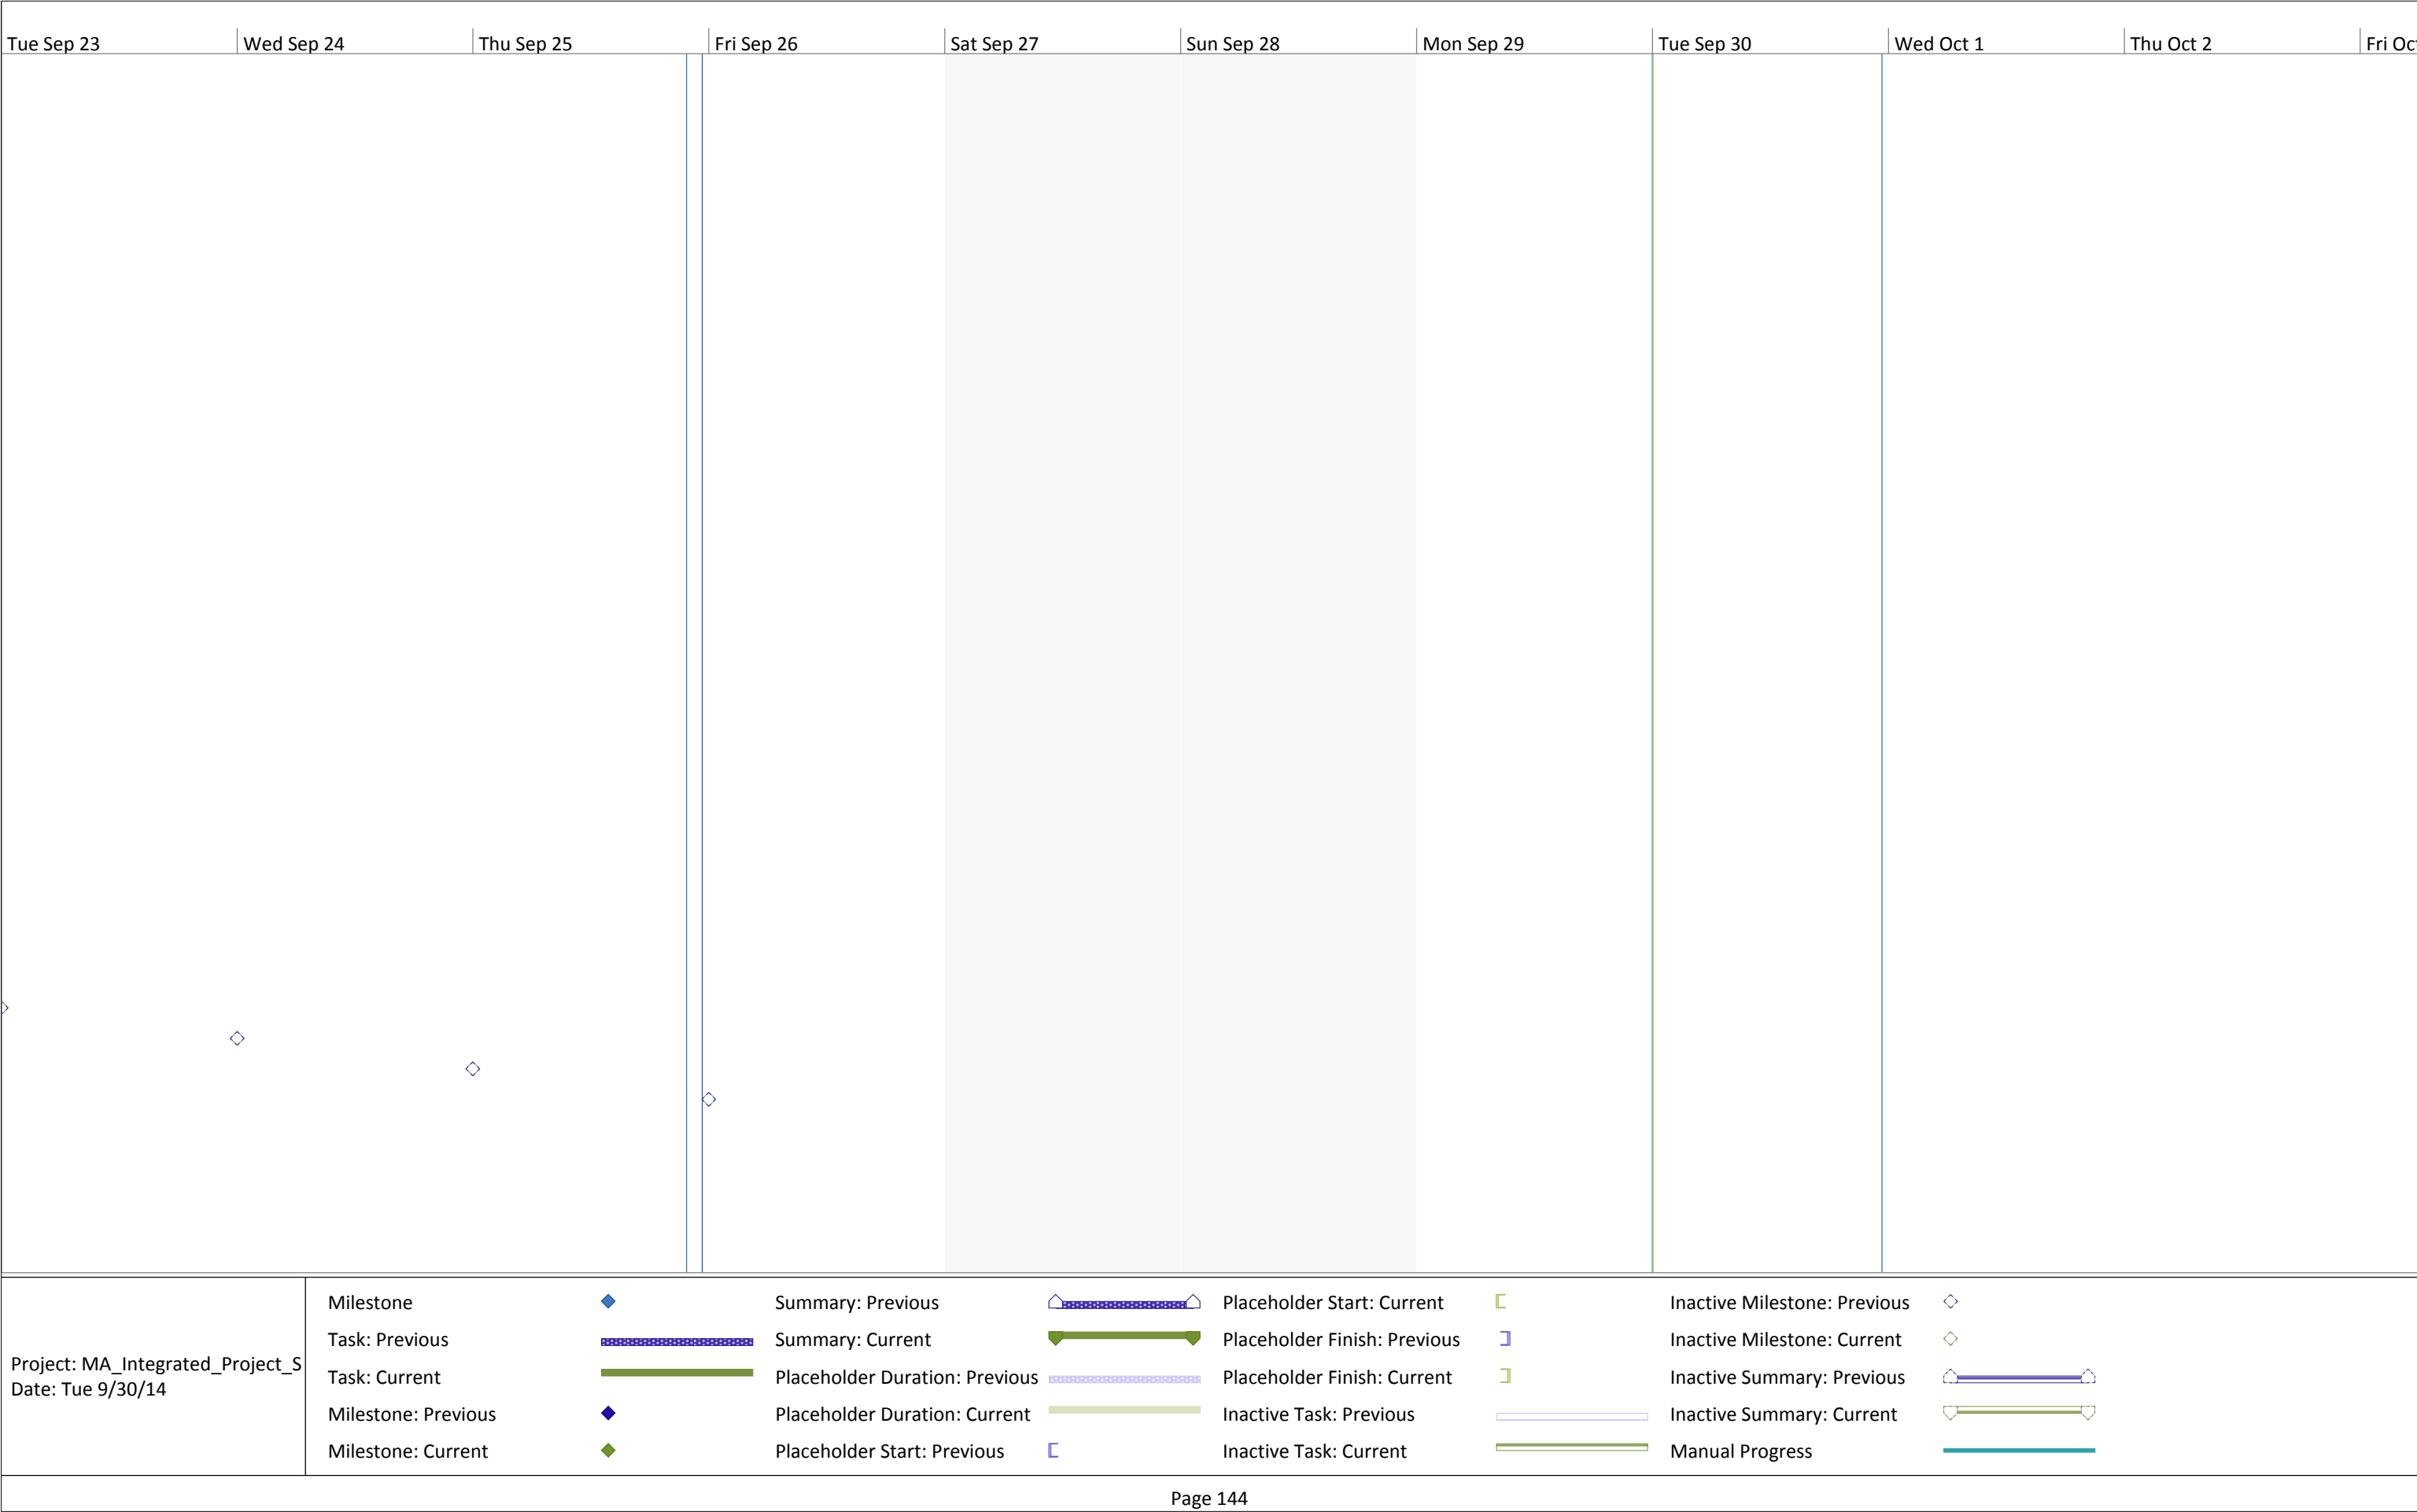

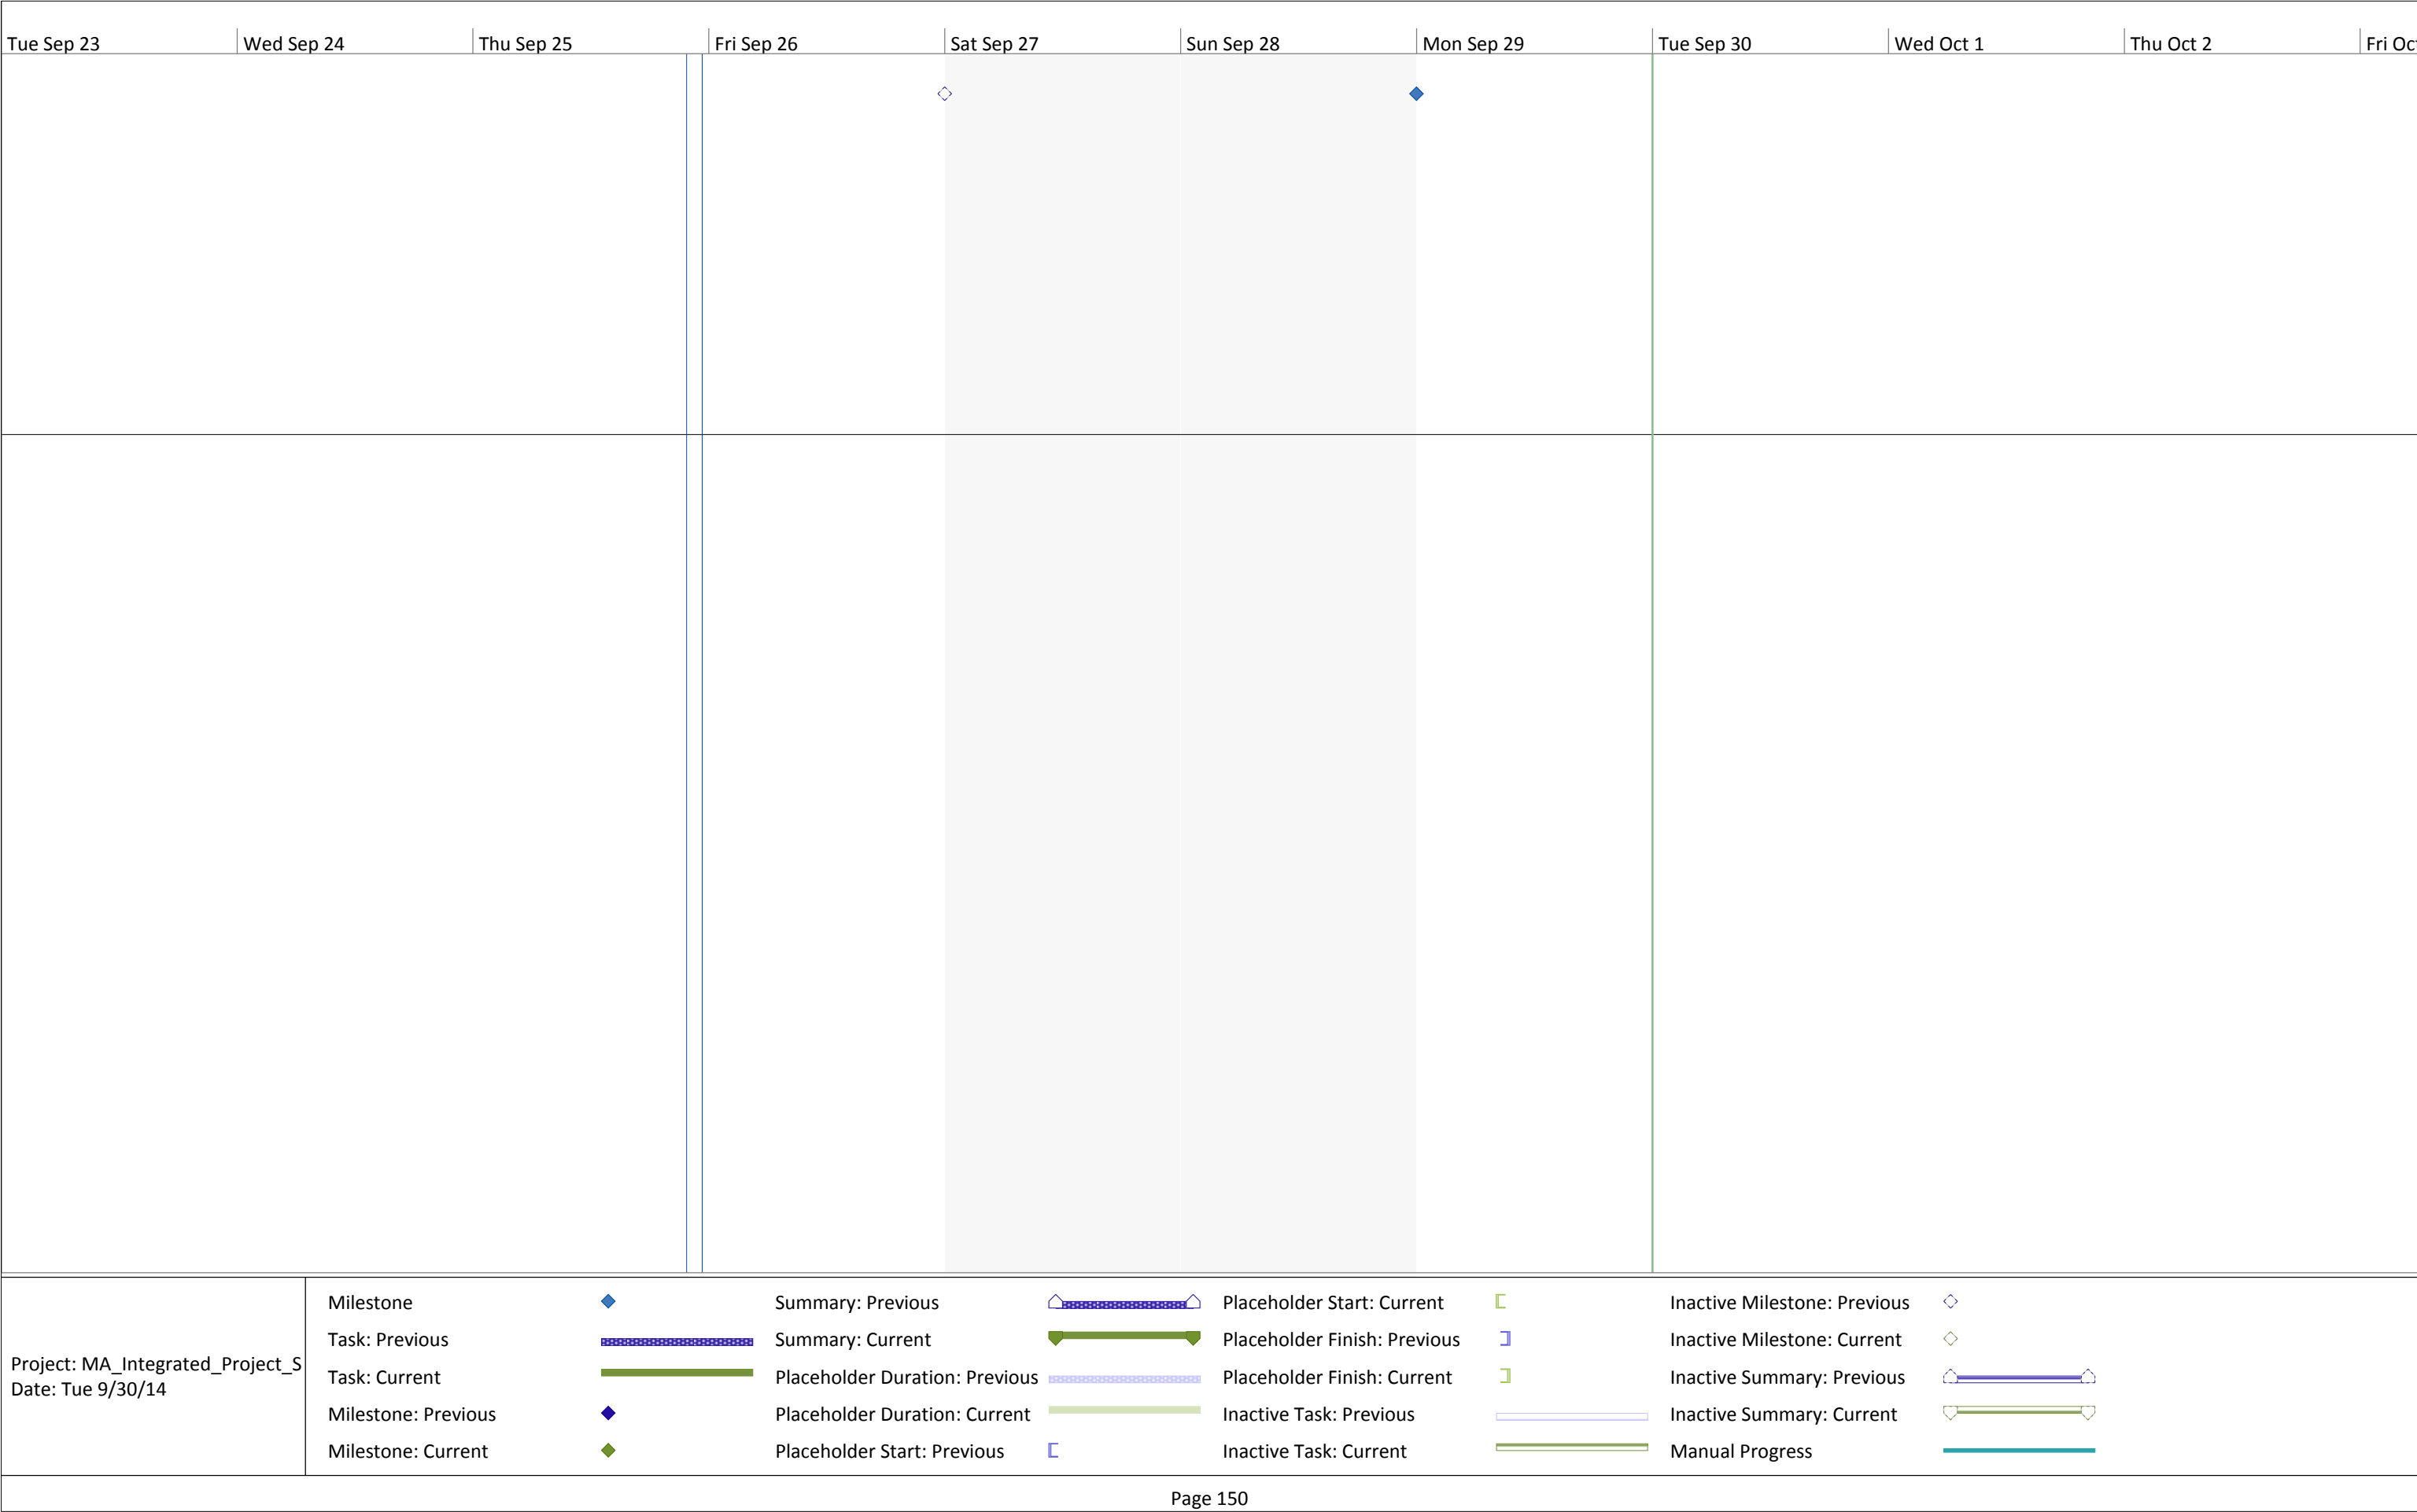

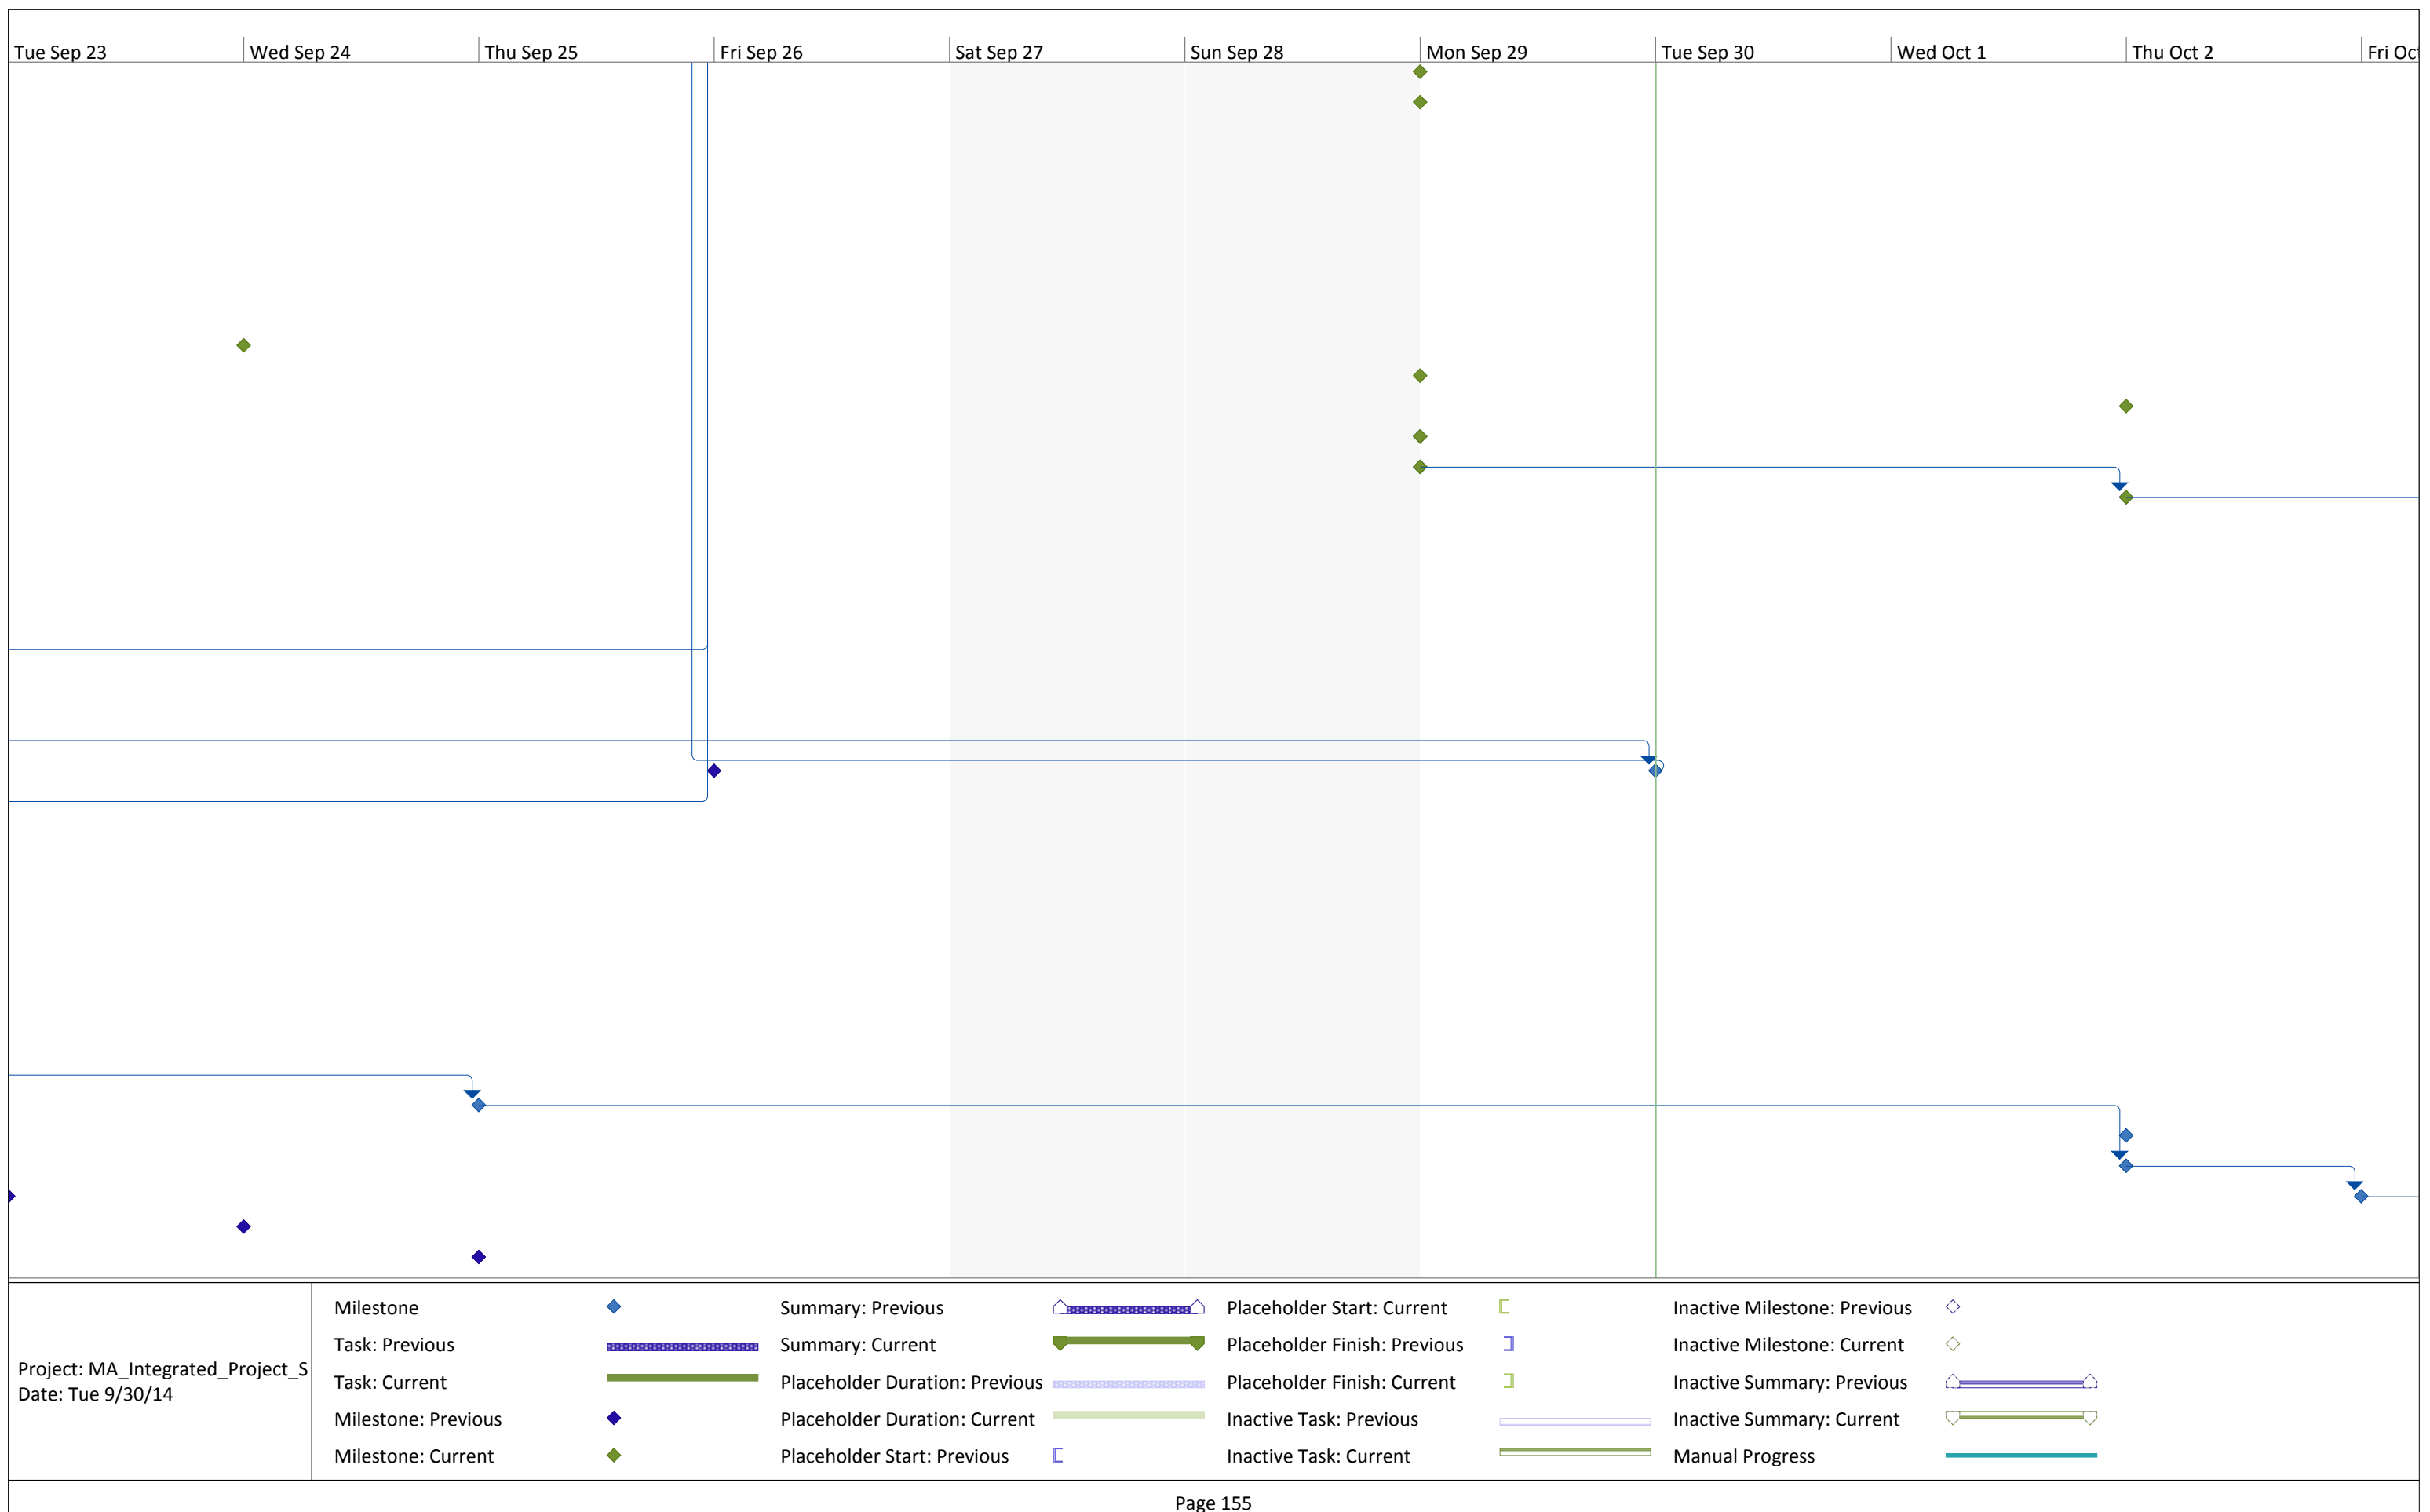

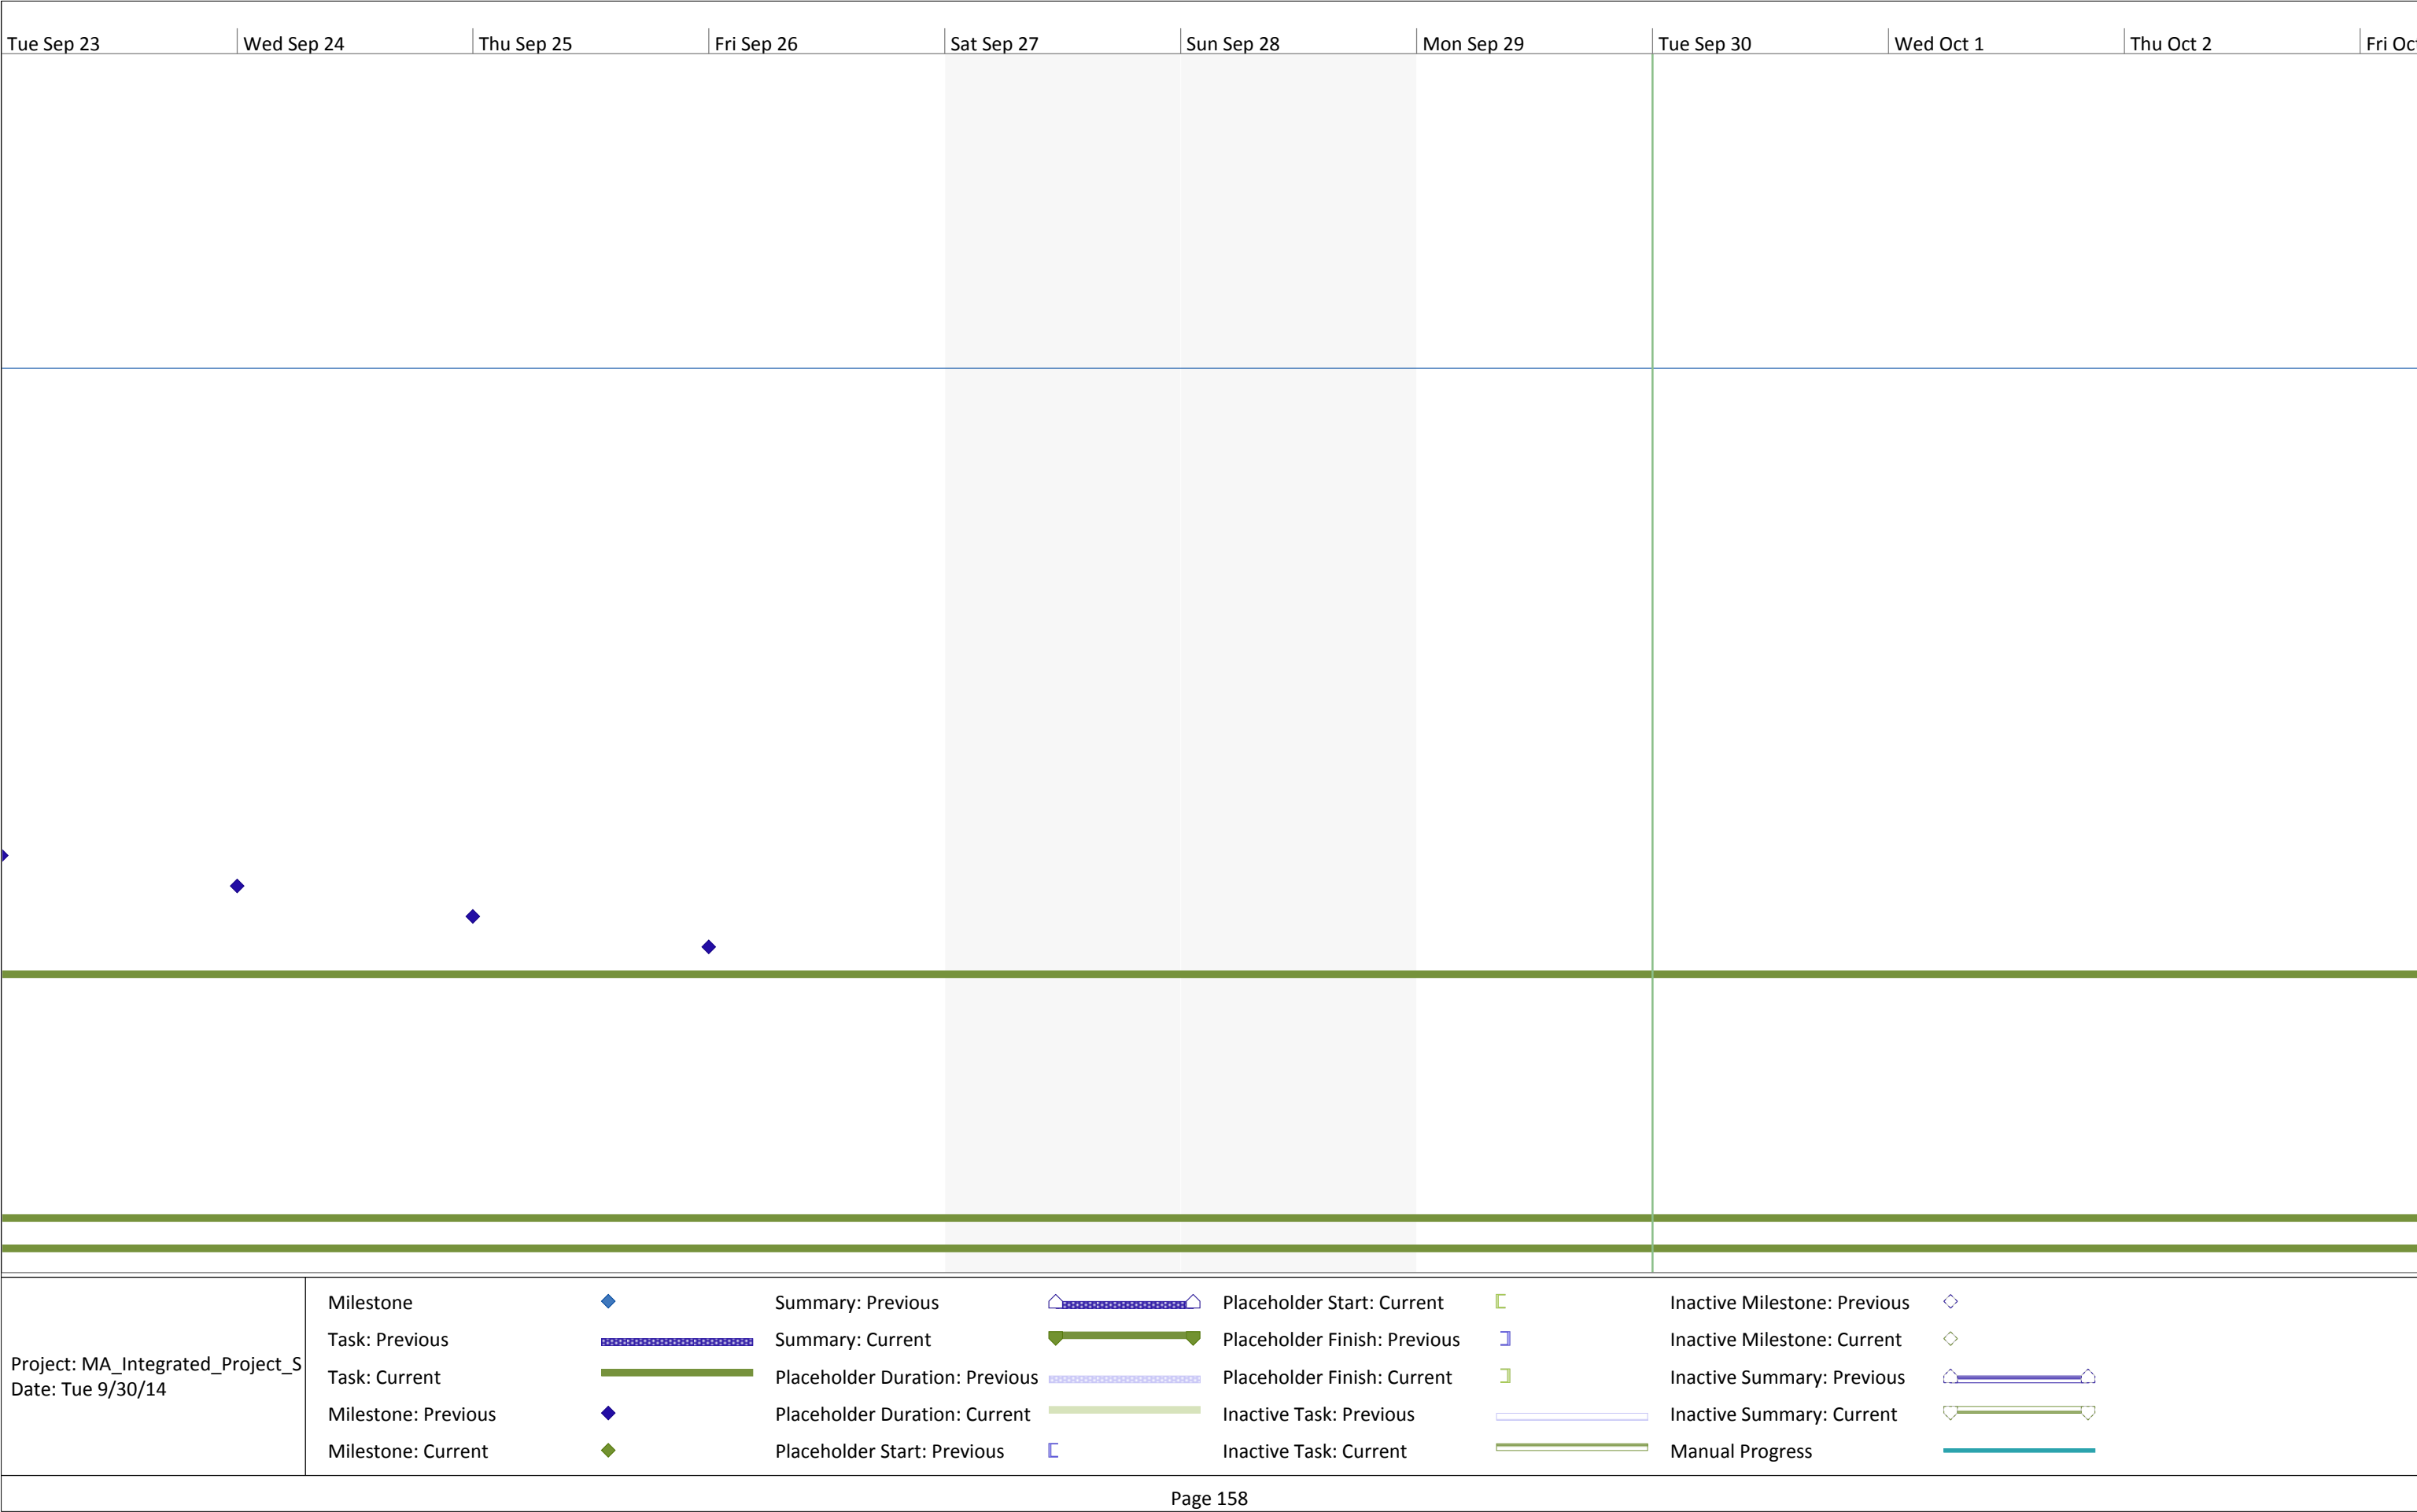

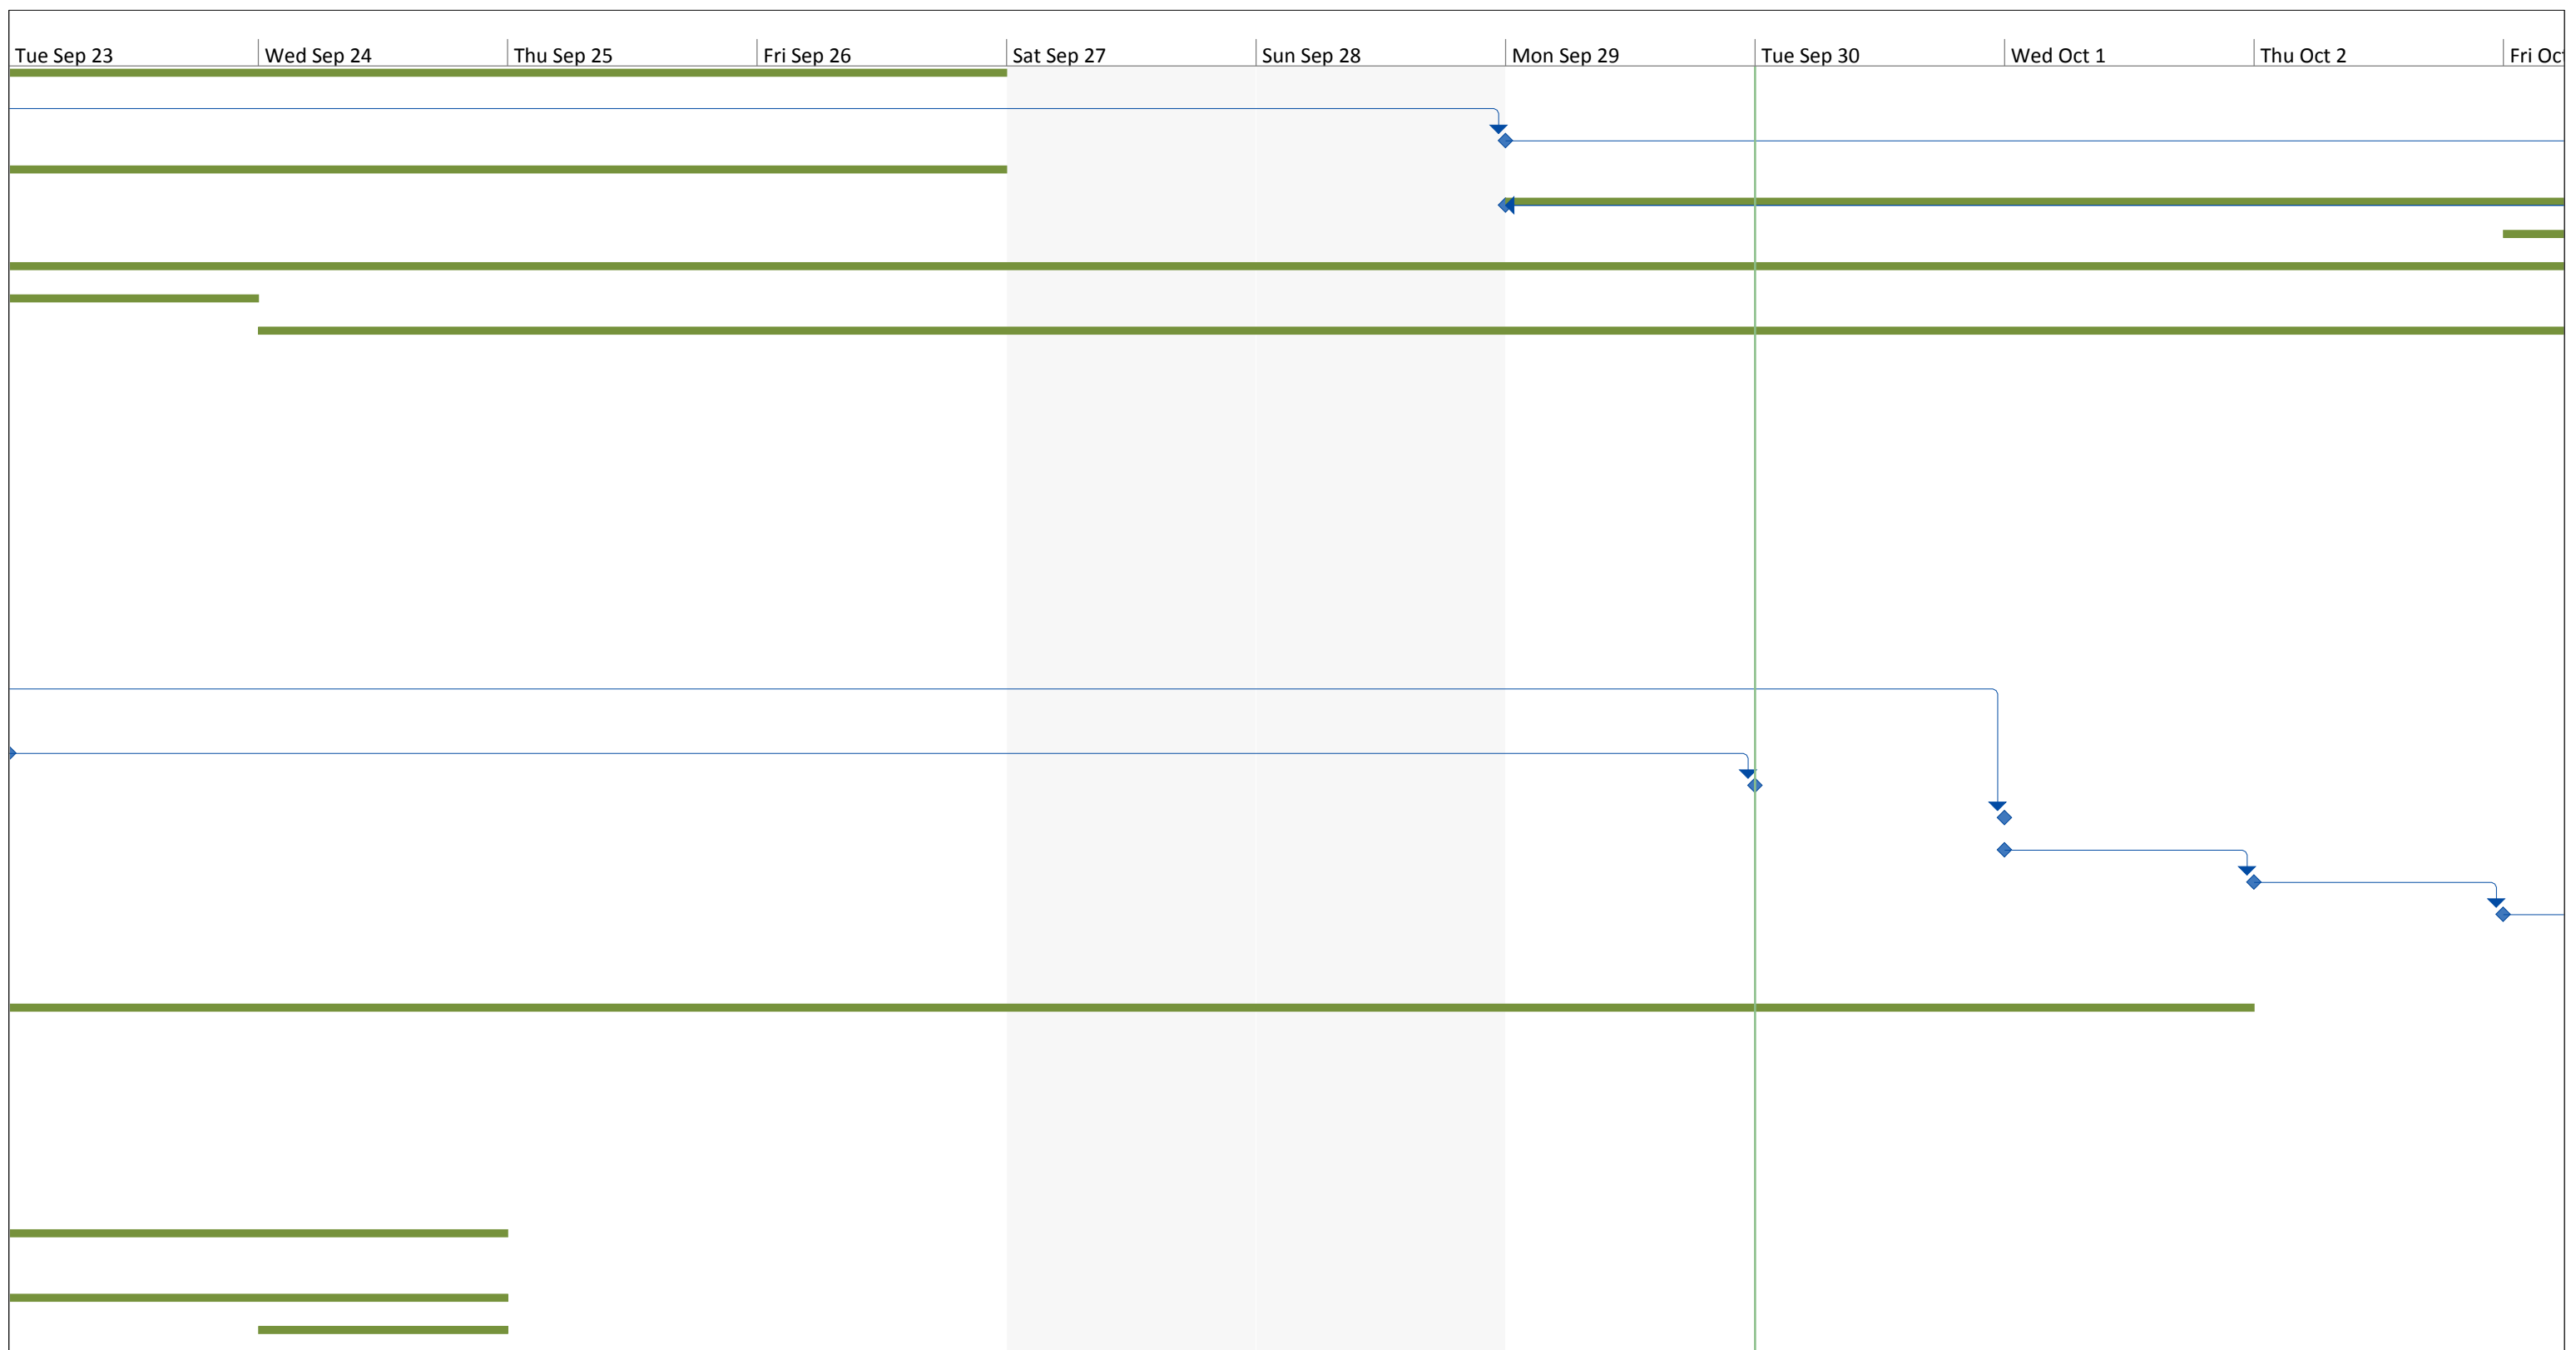

























Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

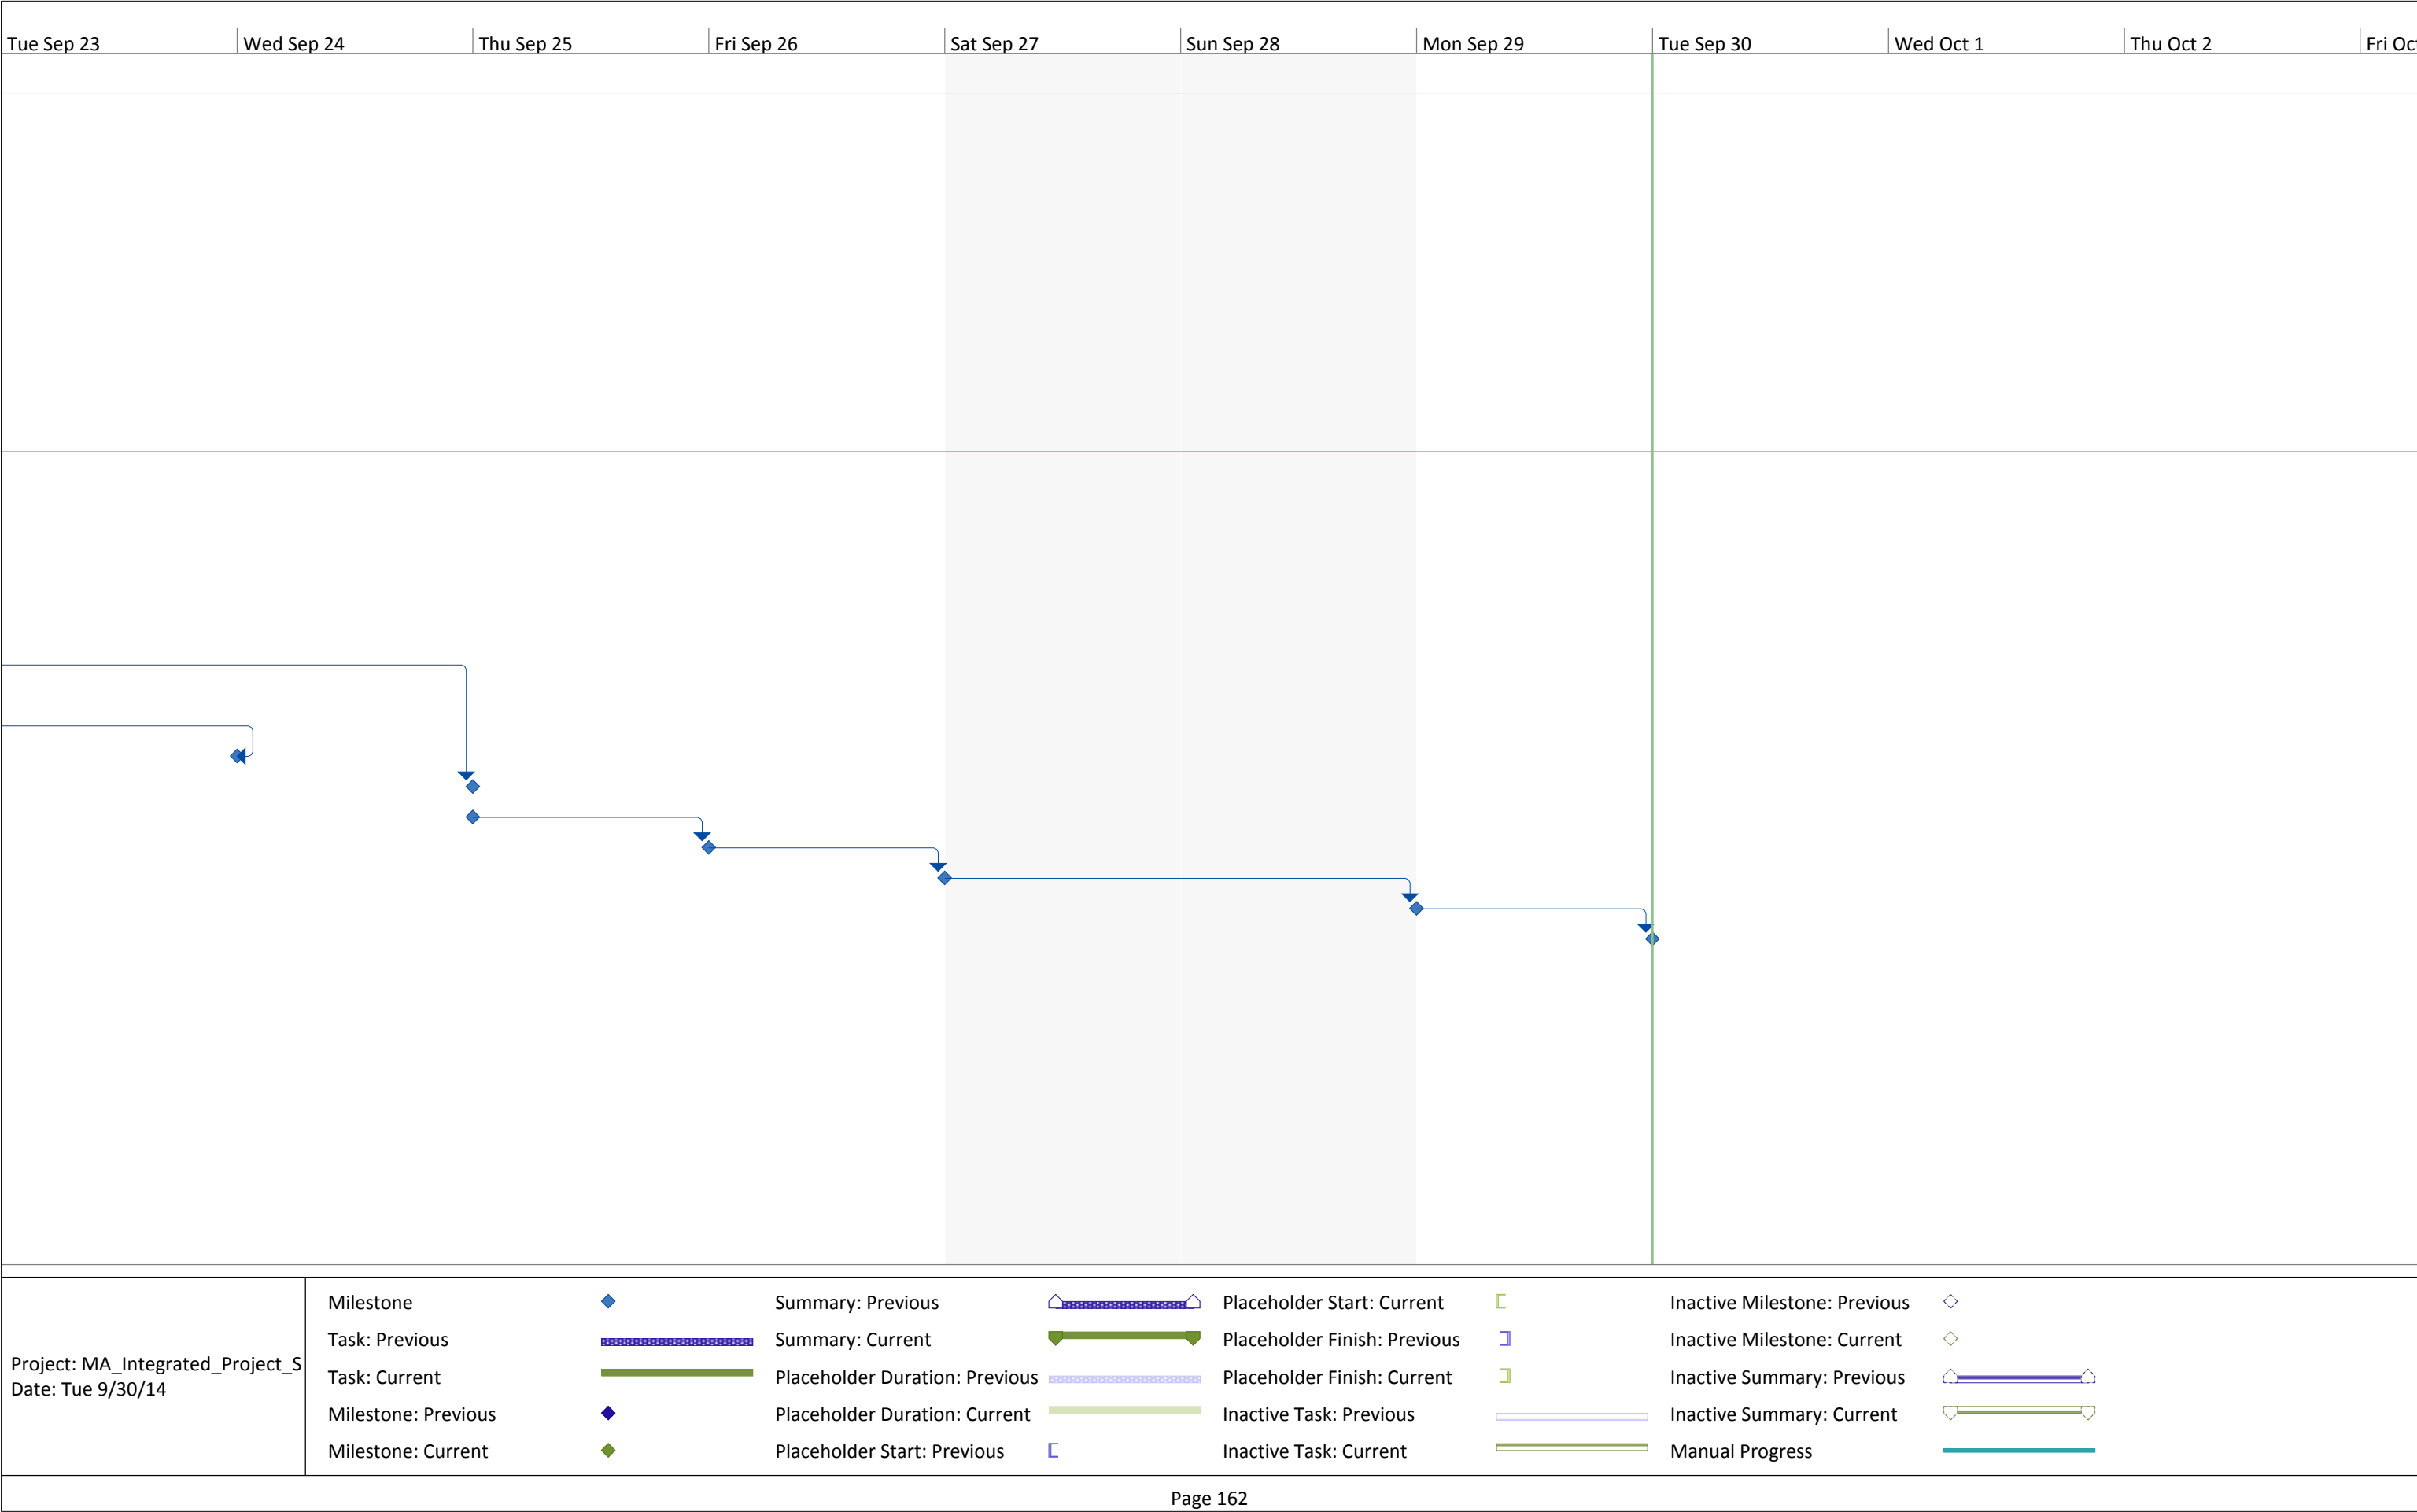


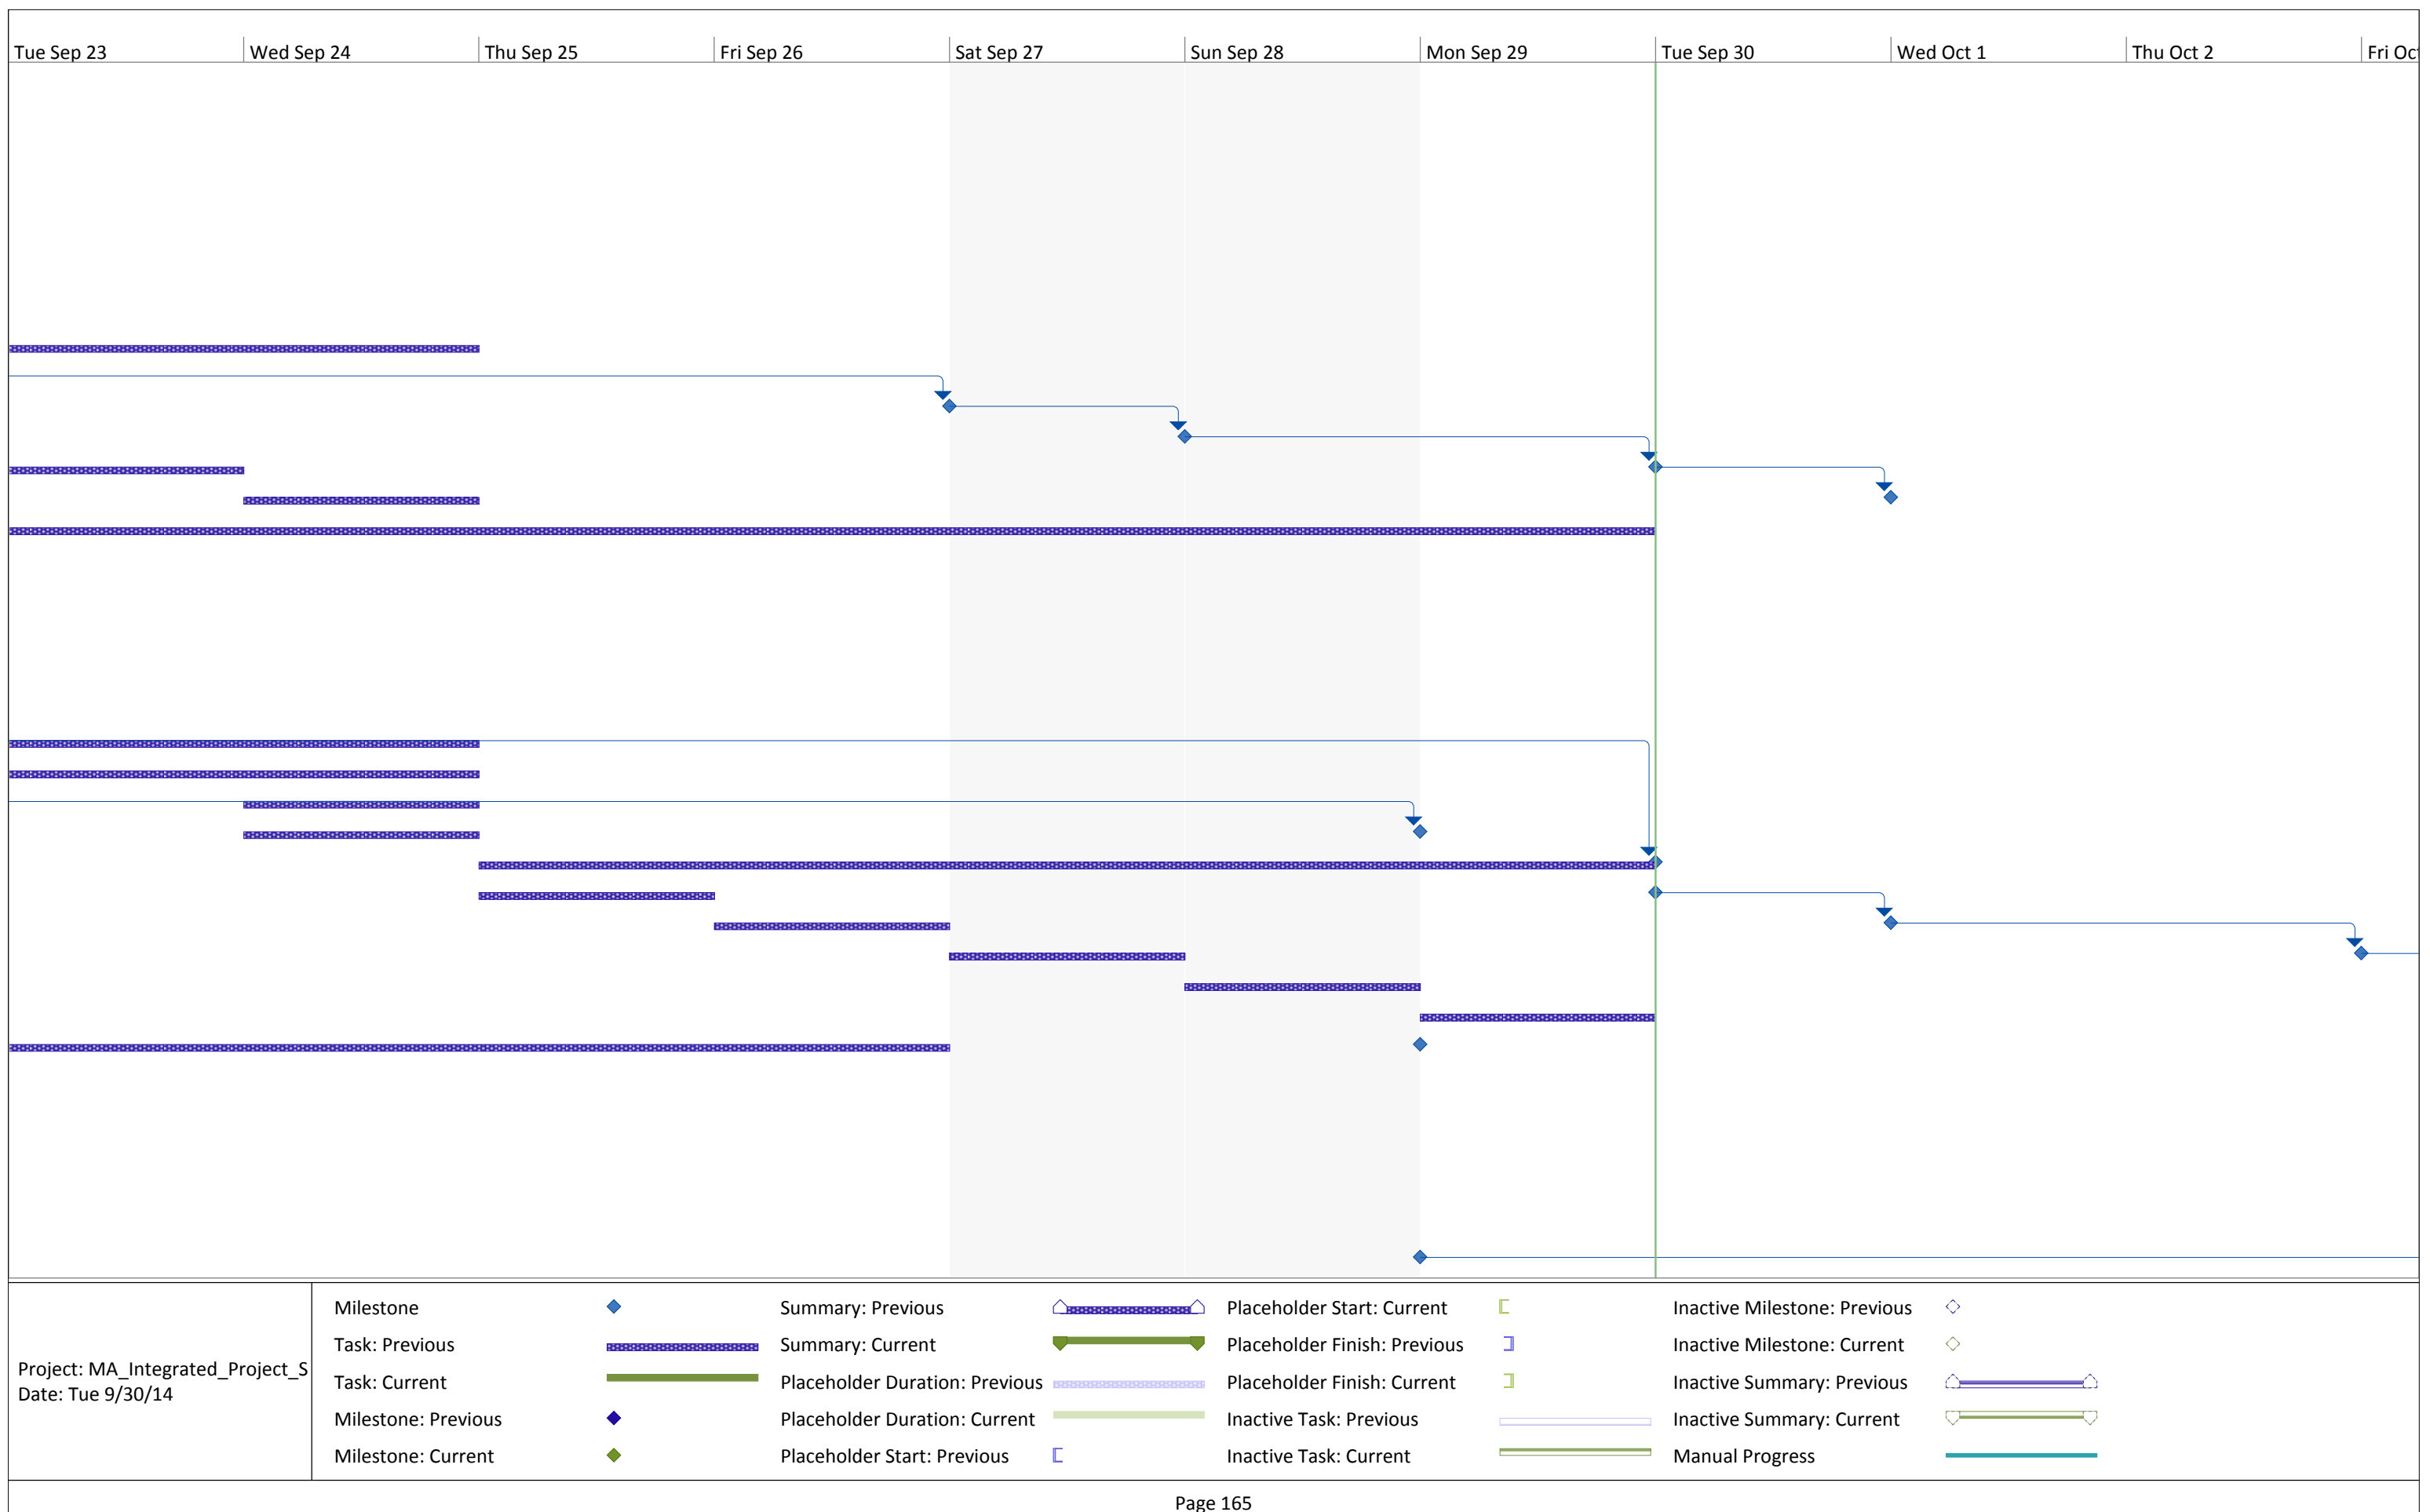


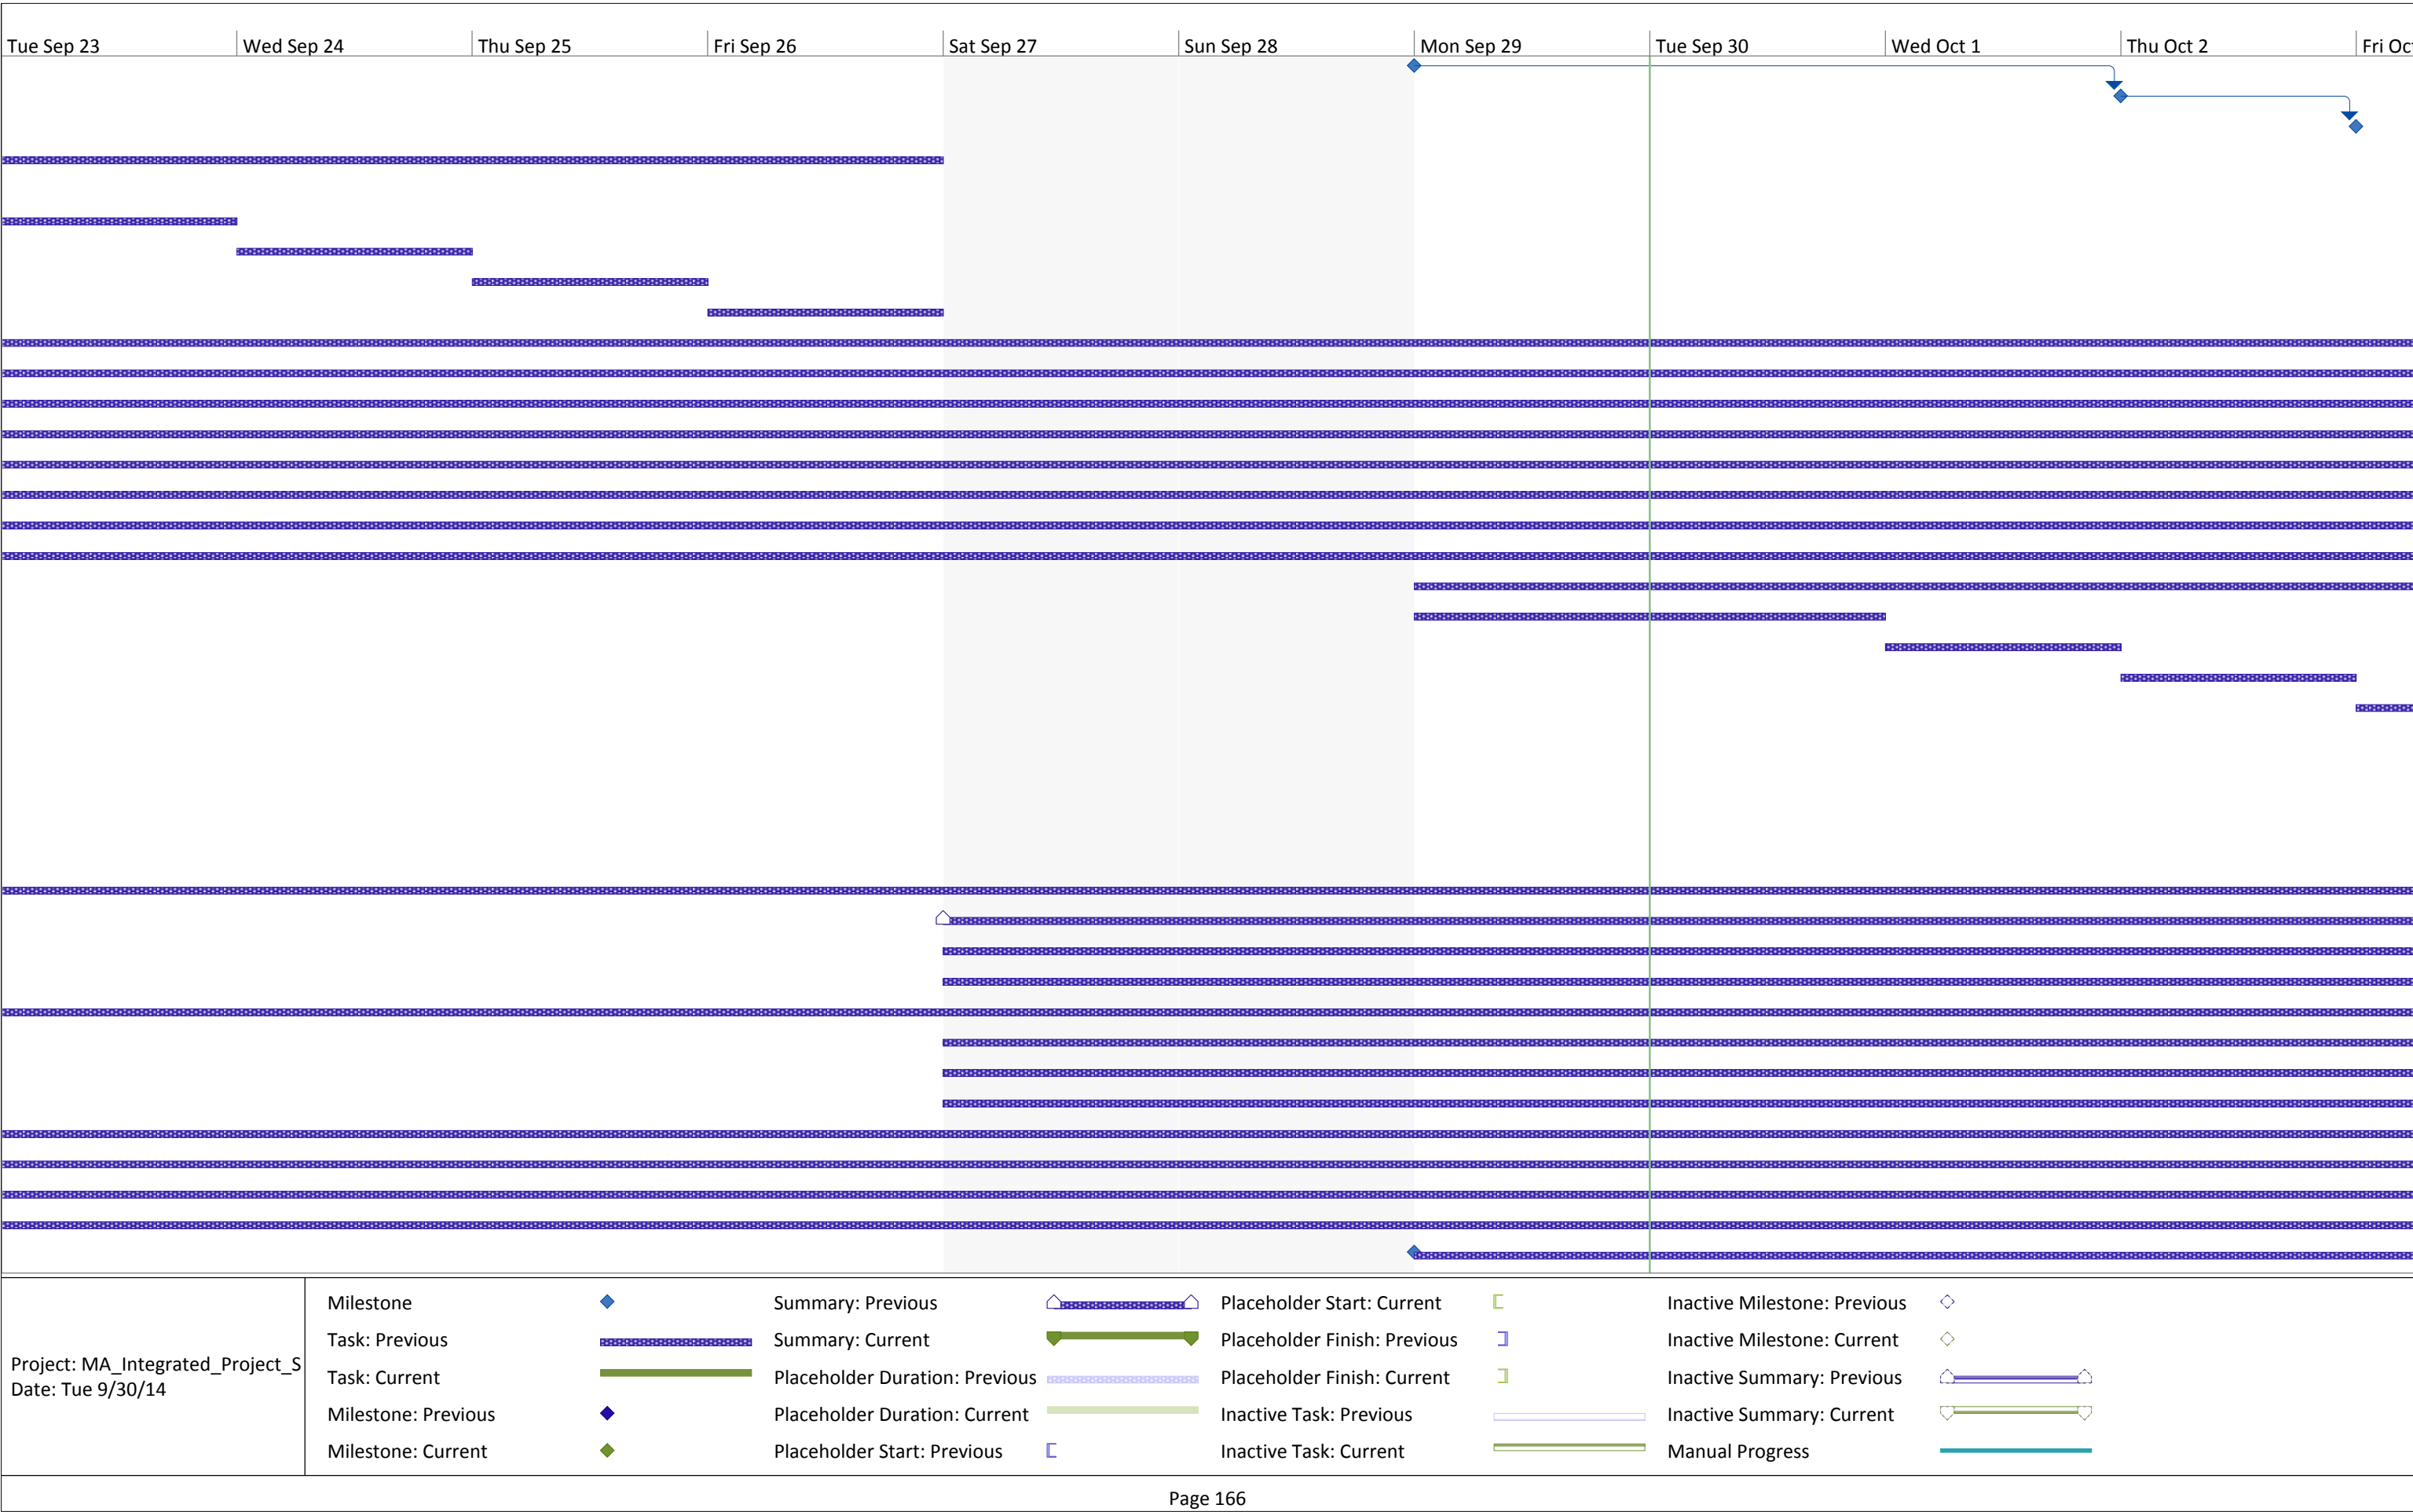

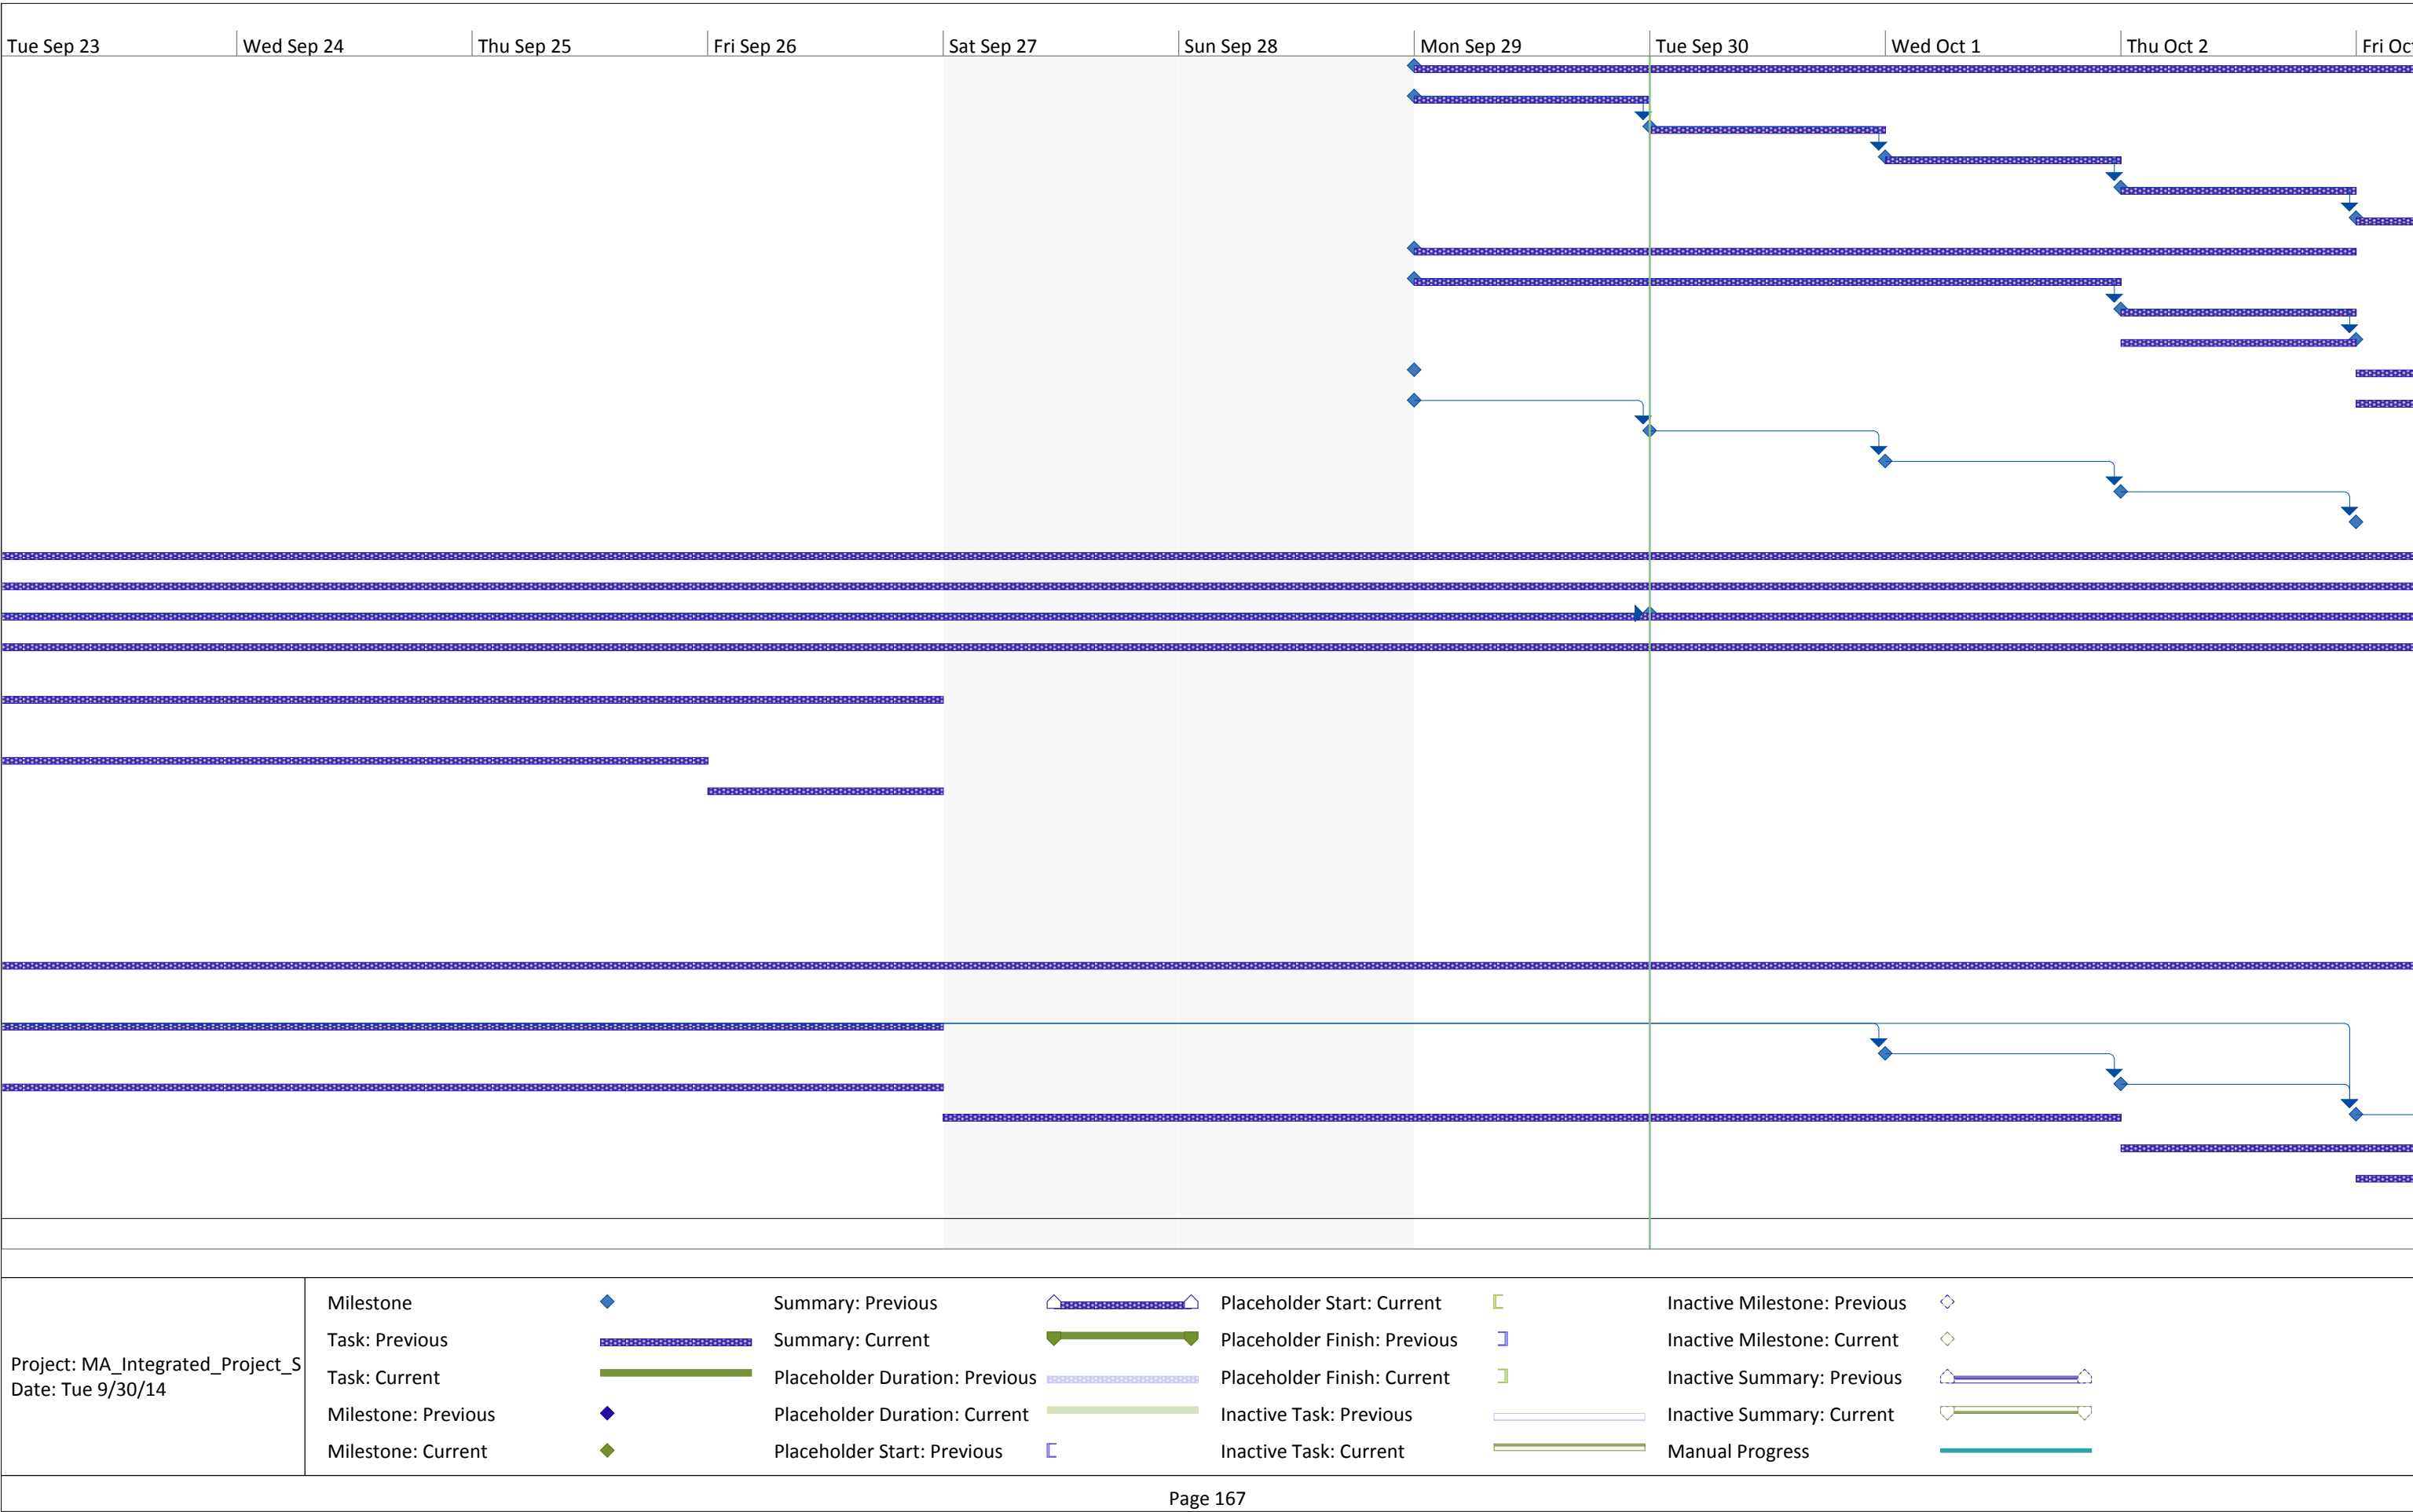



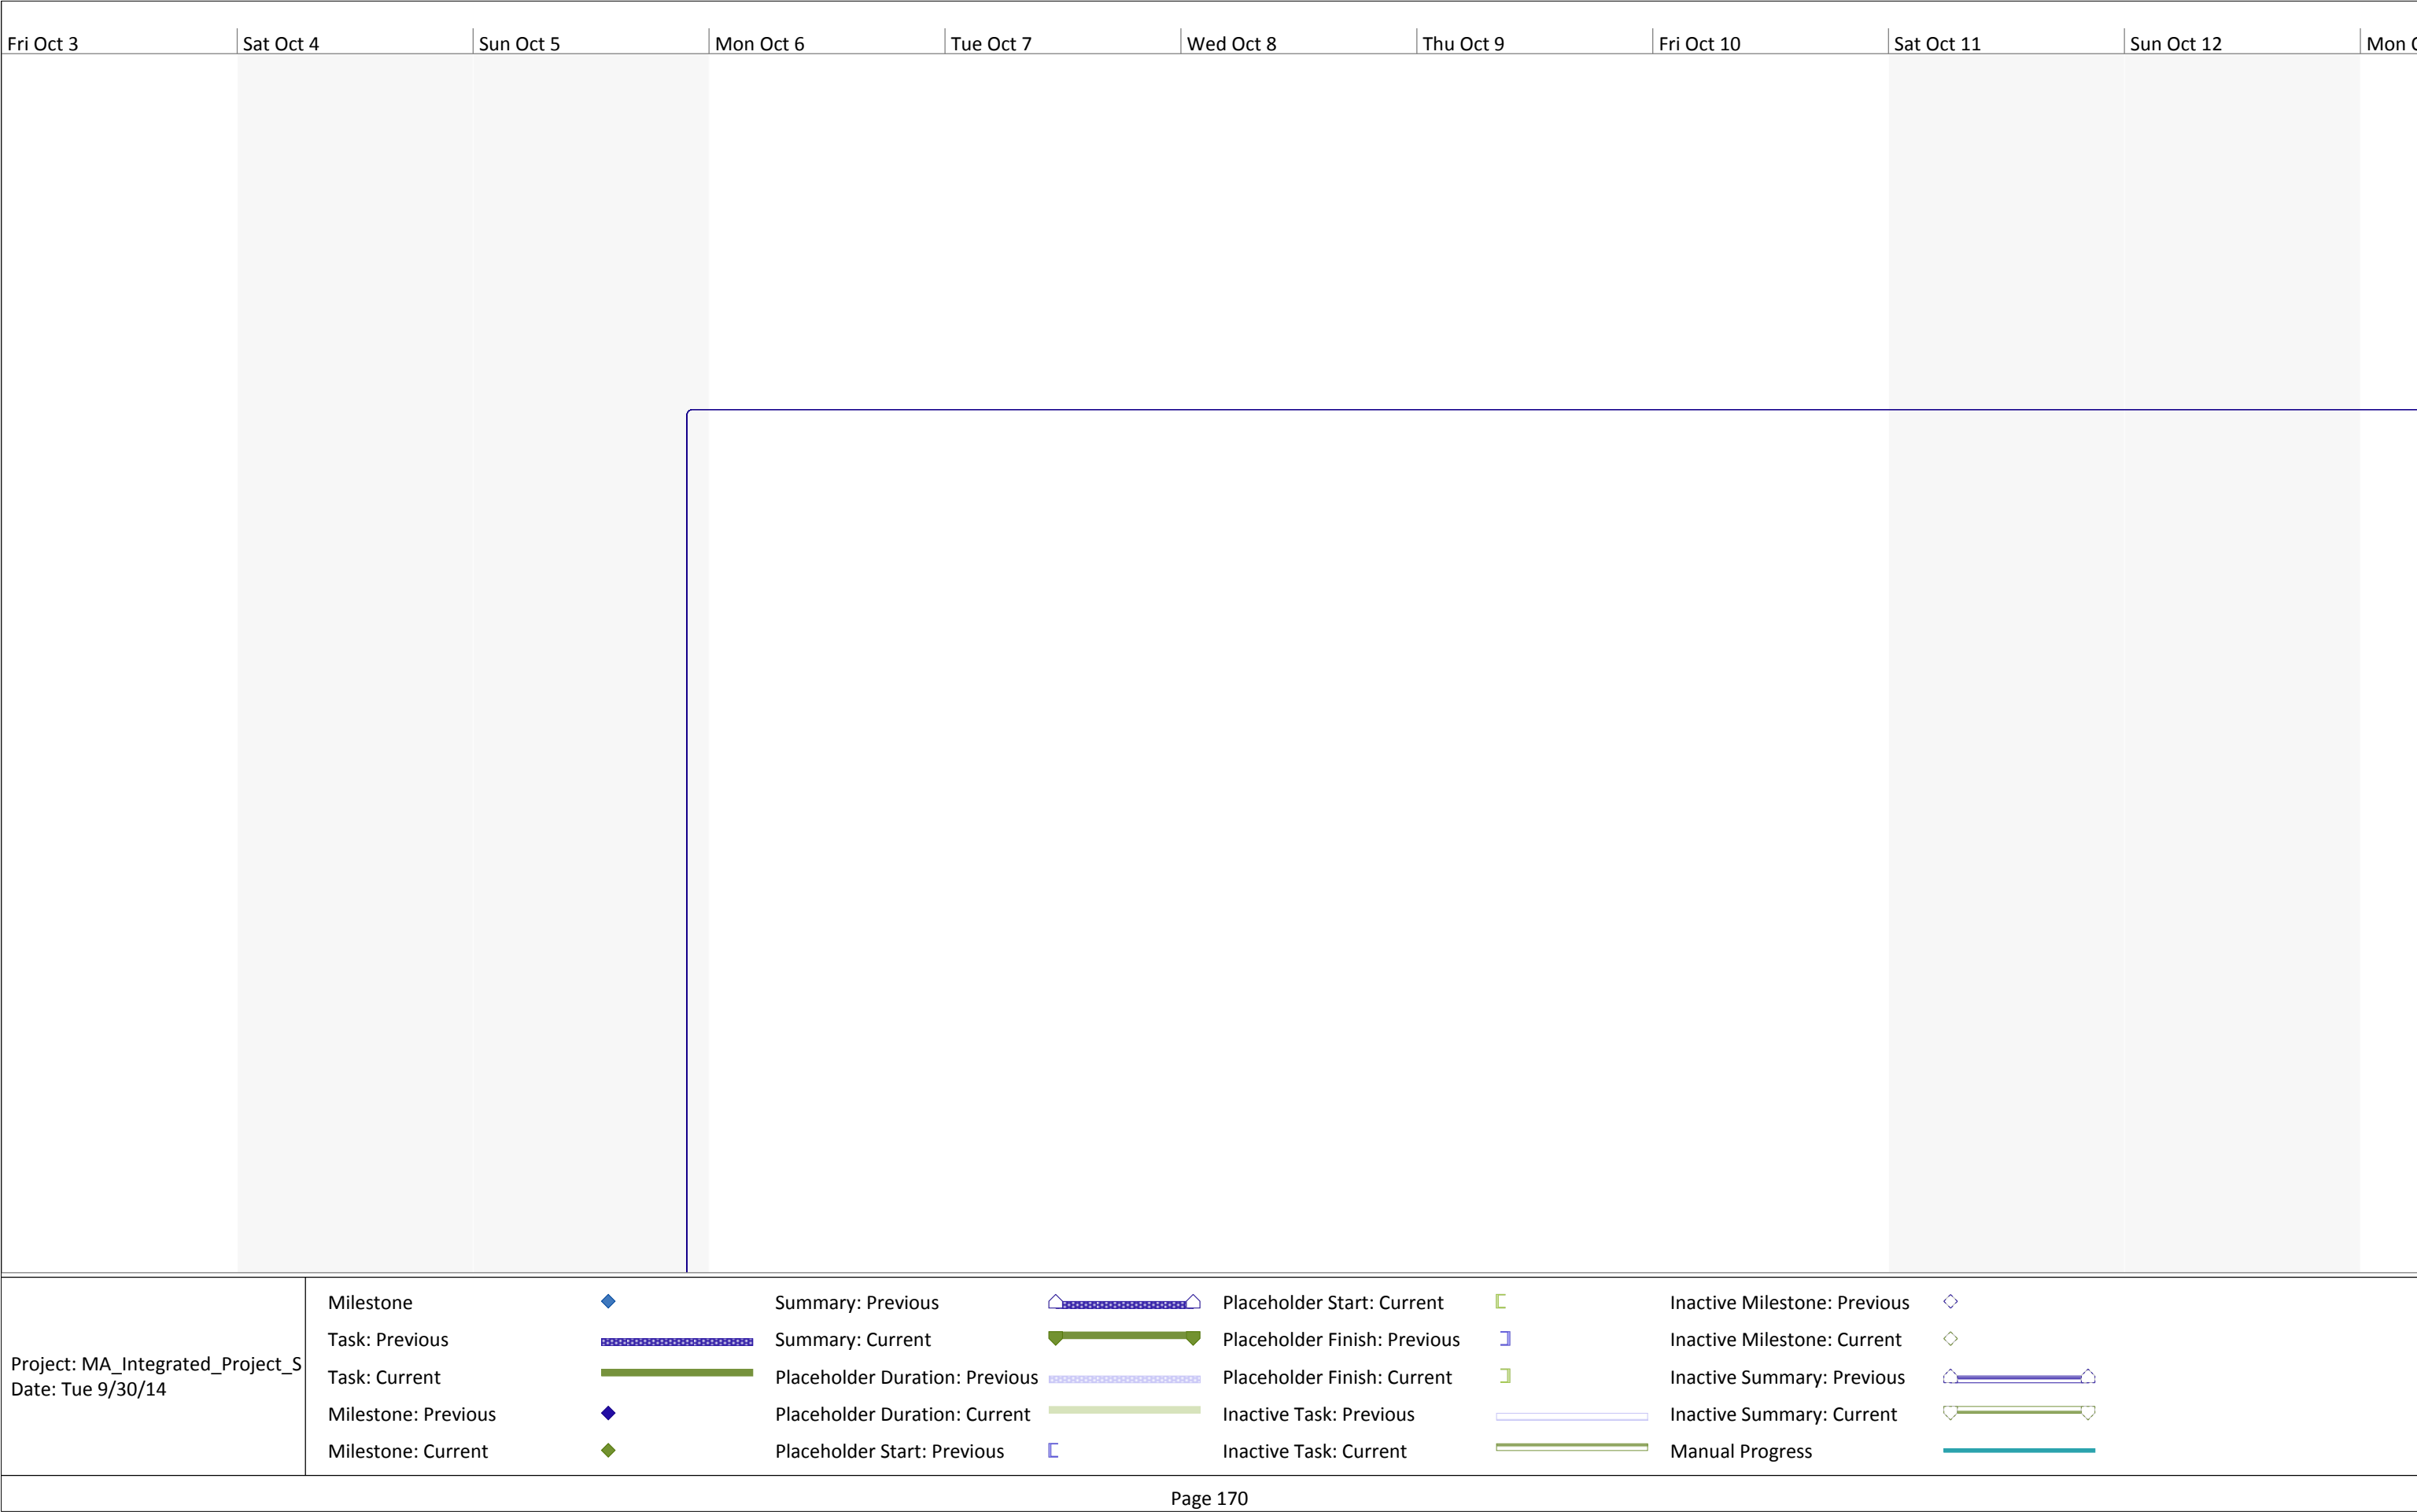

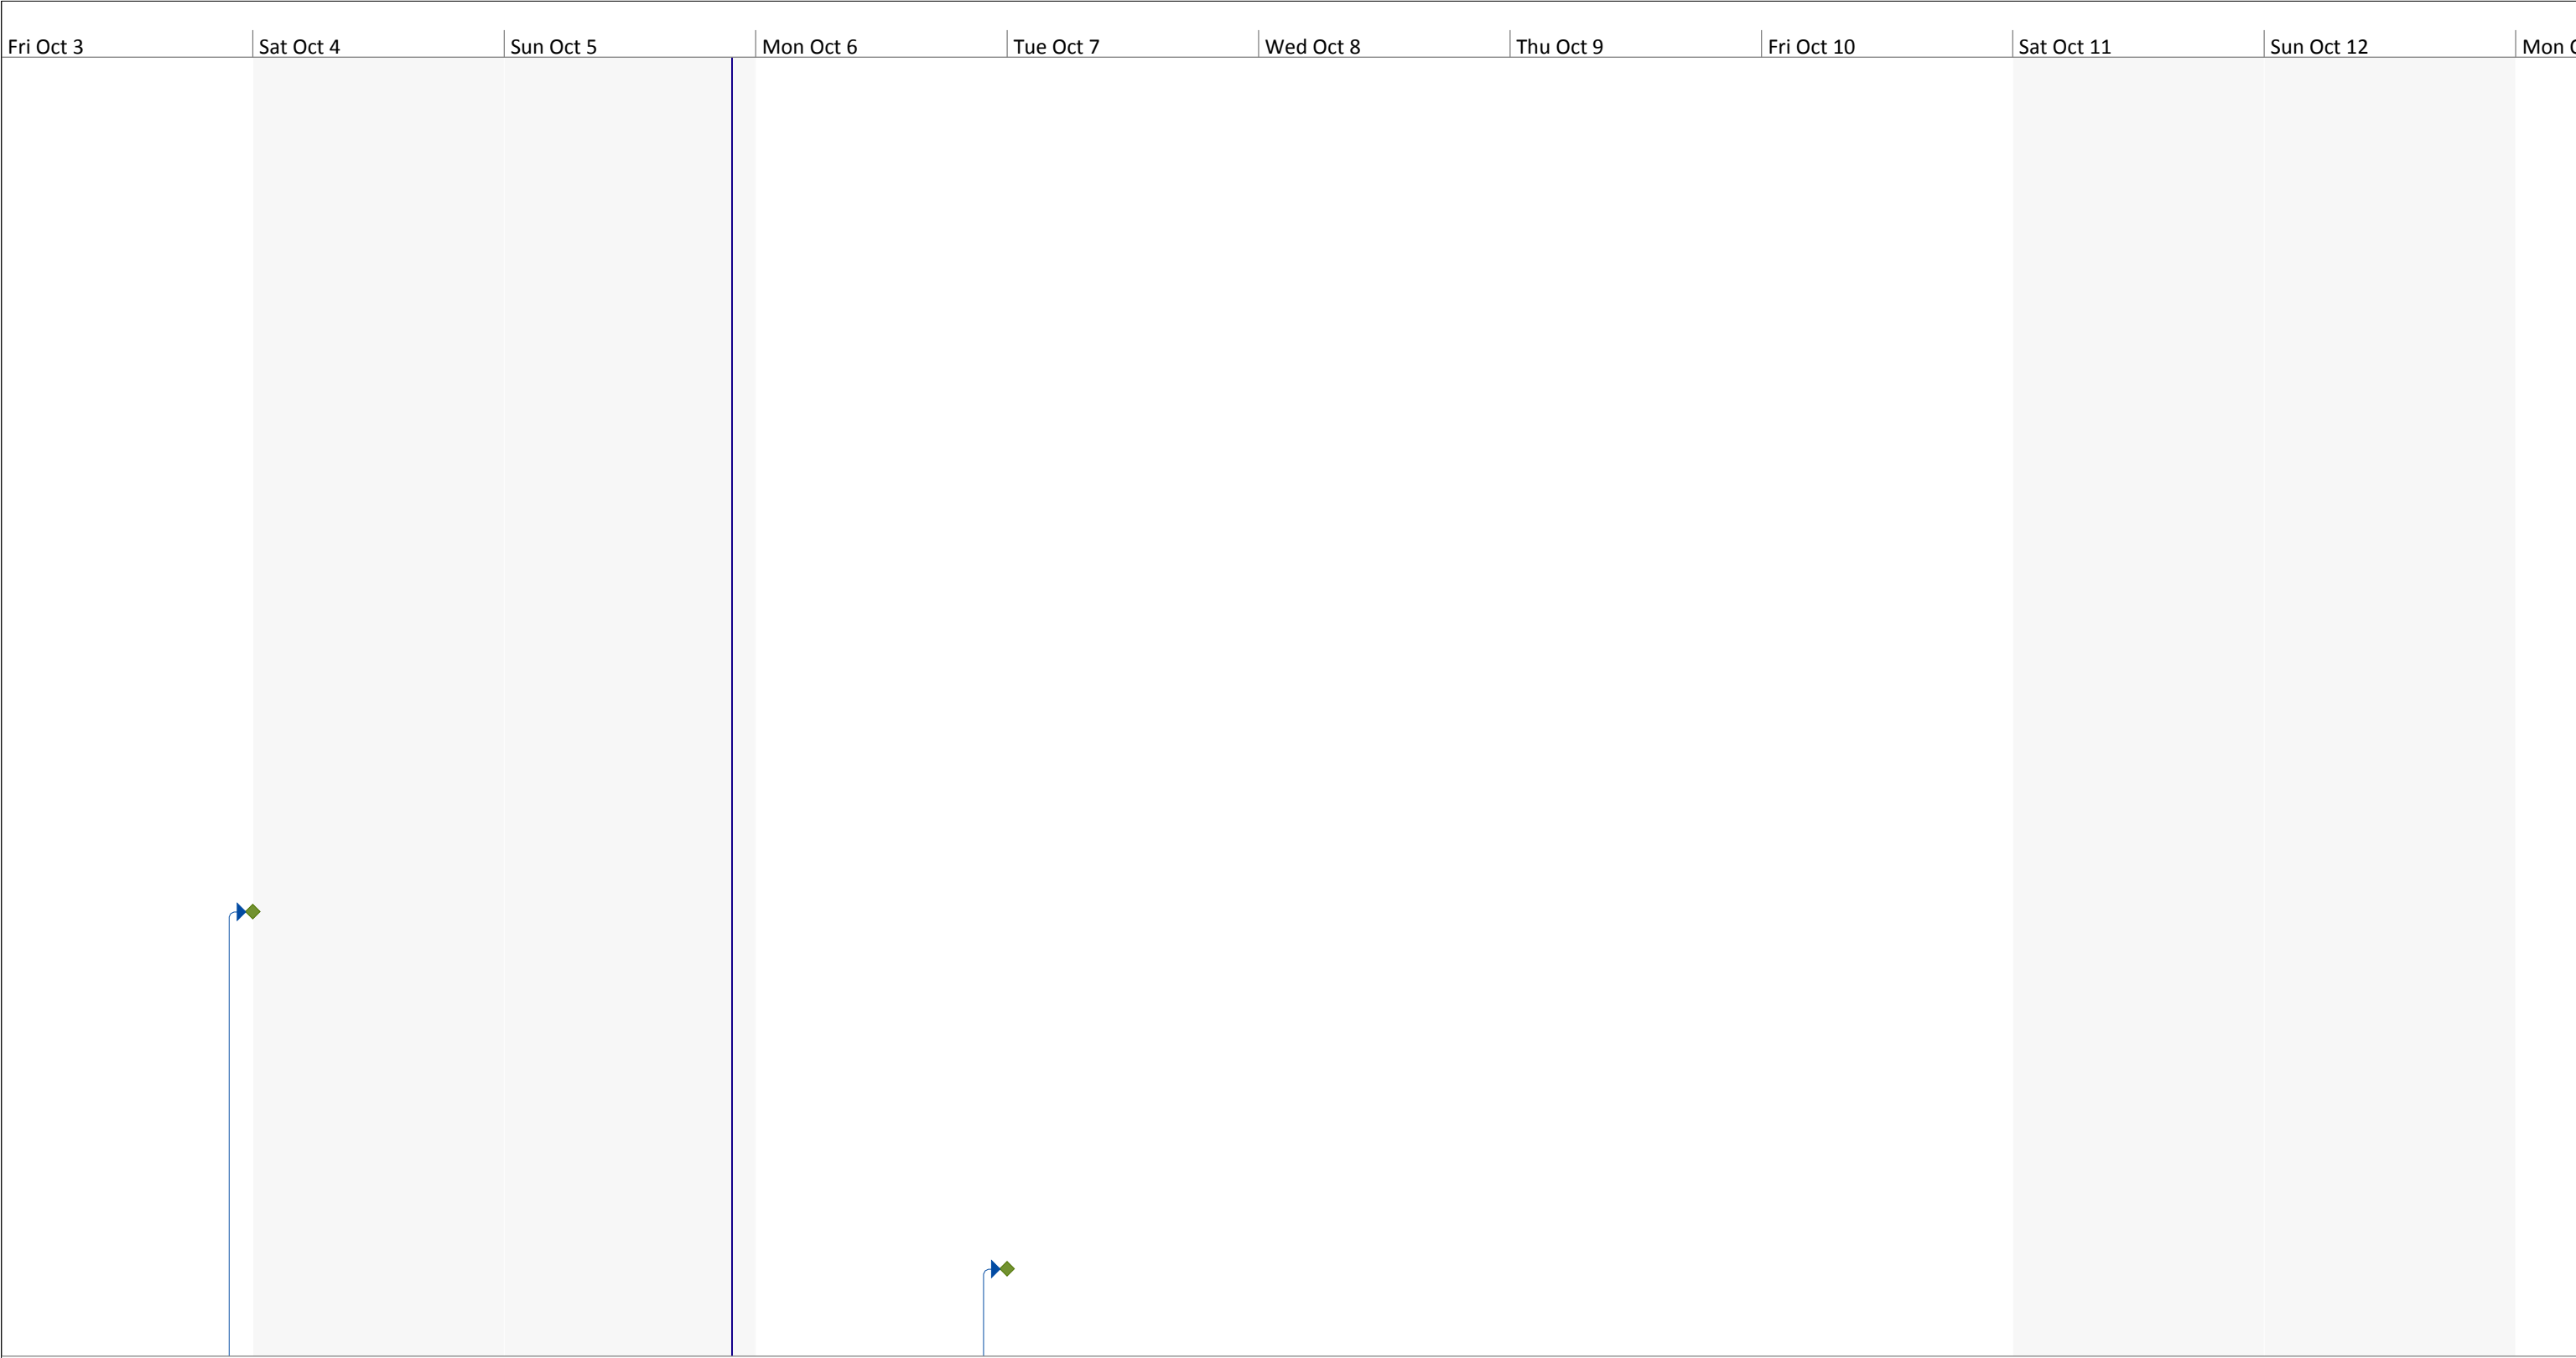

















Fri Oct 3		Sat Oct 4		Sun Oct 5		Mon Oct 6		Tue Oct 7		Wed Oct 8		Thu Oct 9		Fri Oct 10		Sat Oct 11		Sun Oct 12		Mon Oct 13	






Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

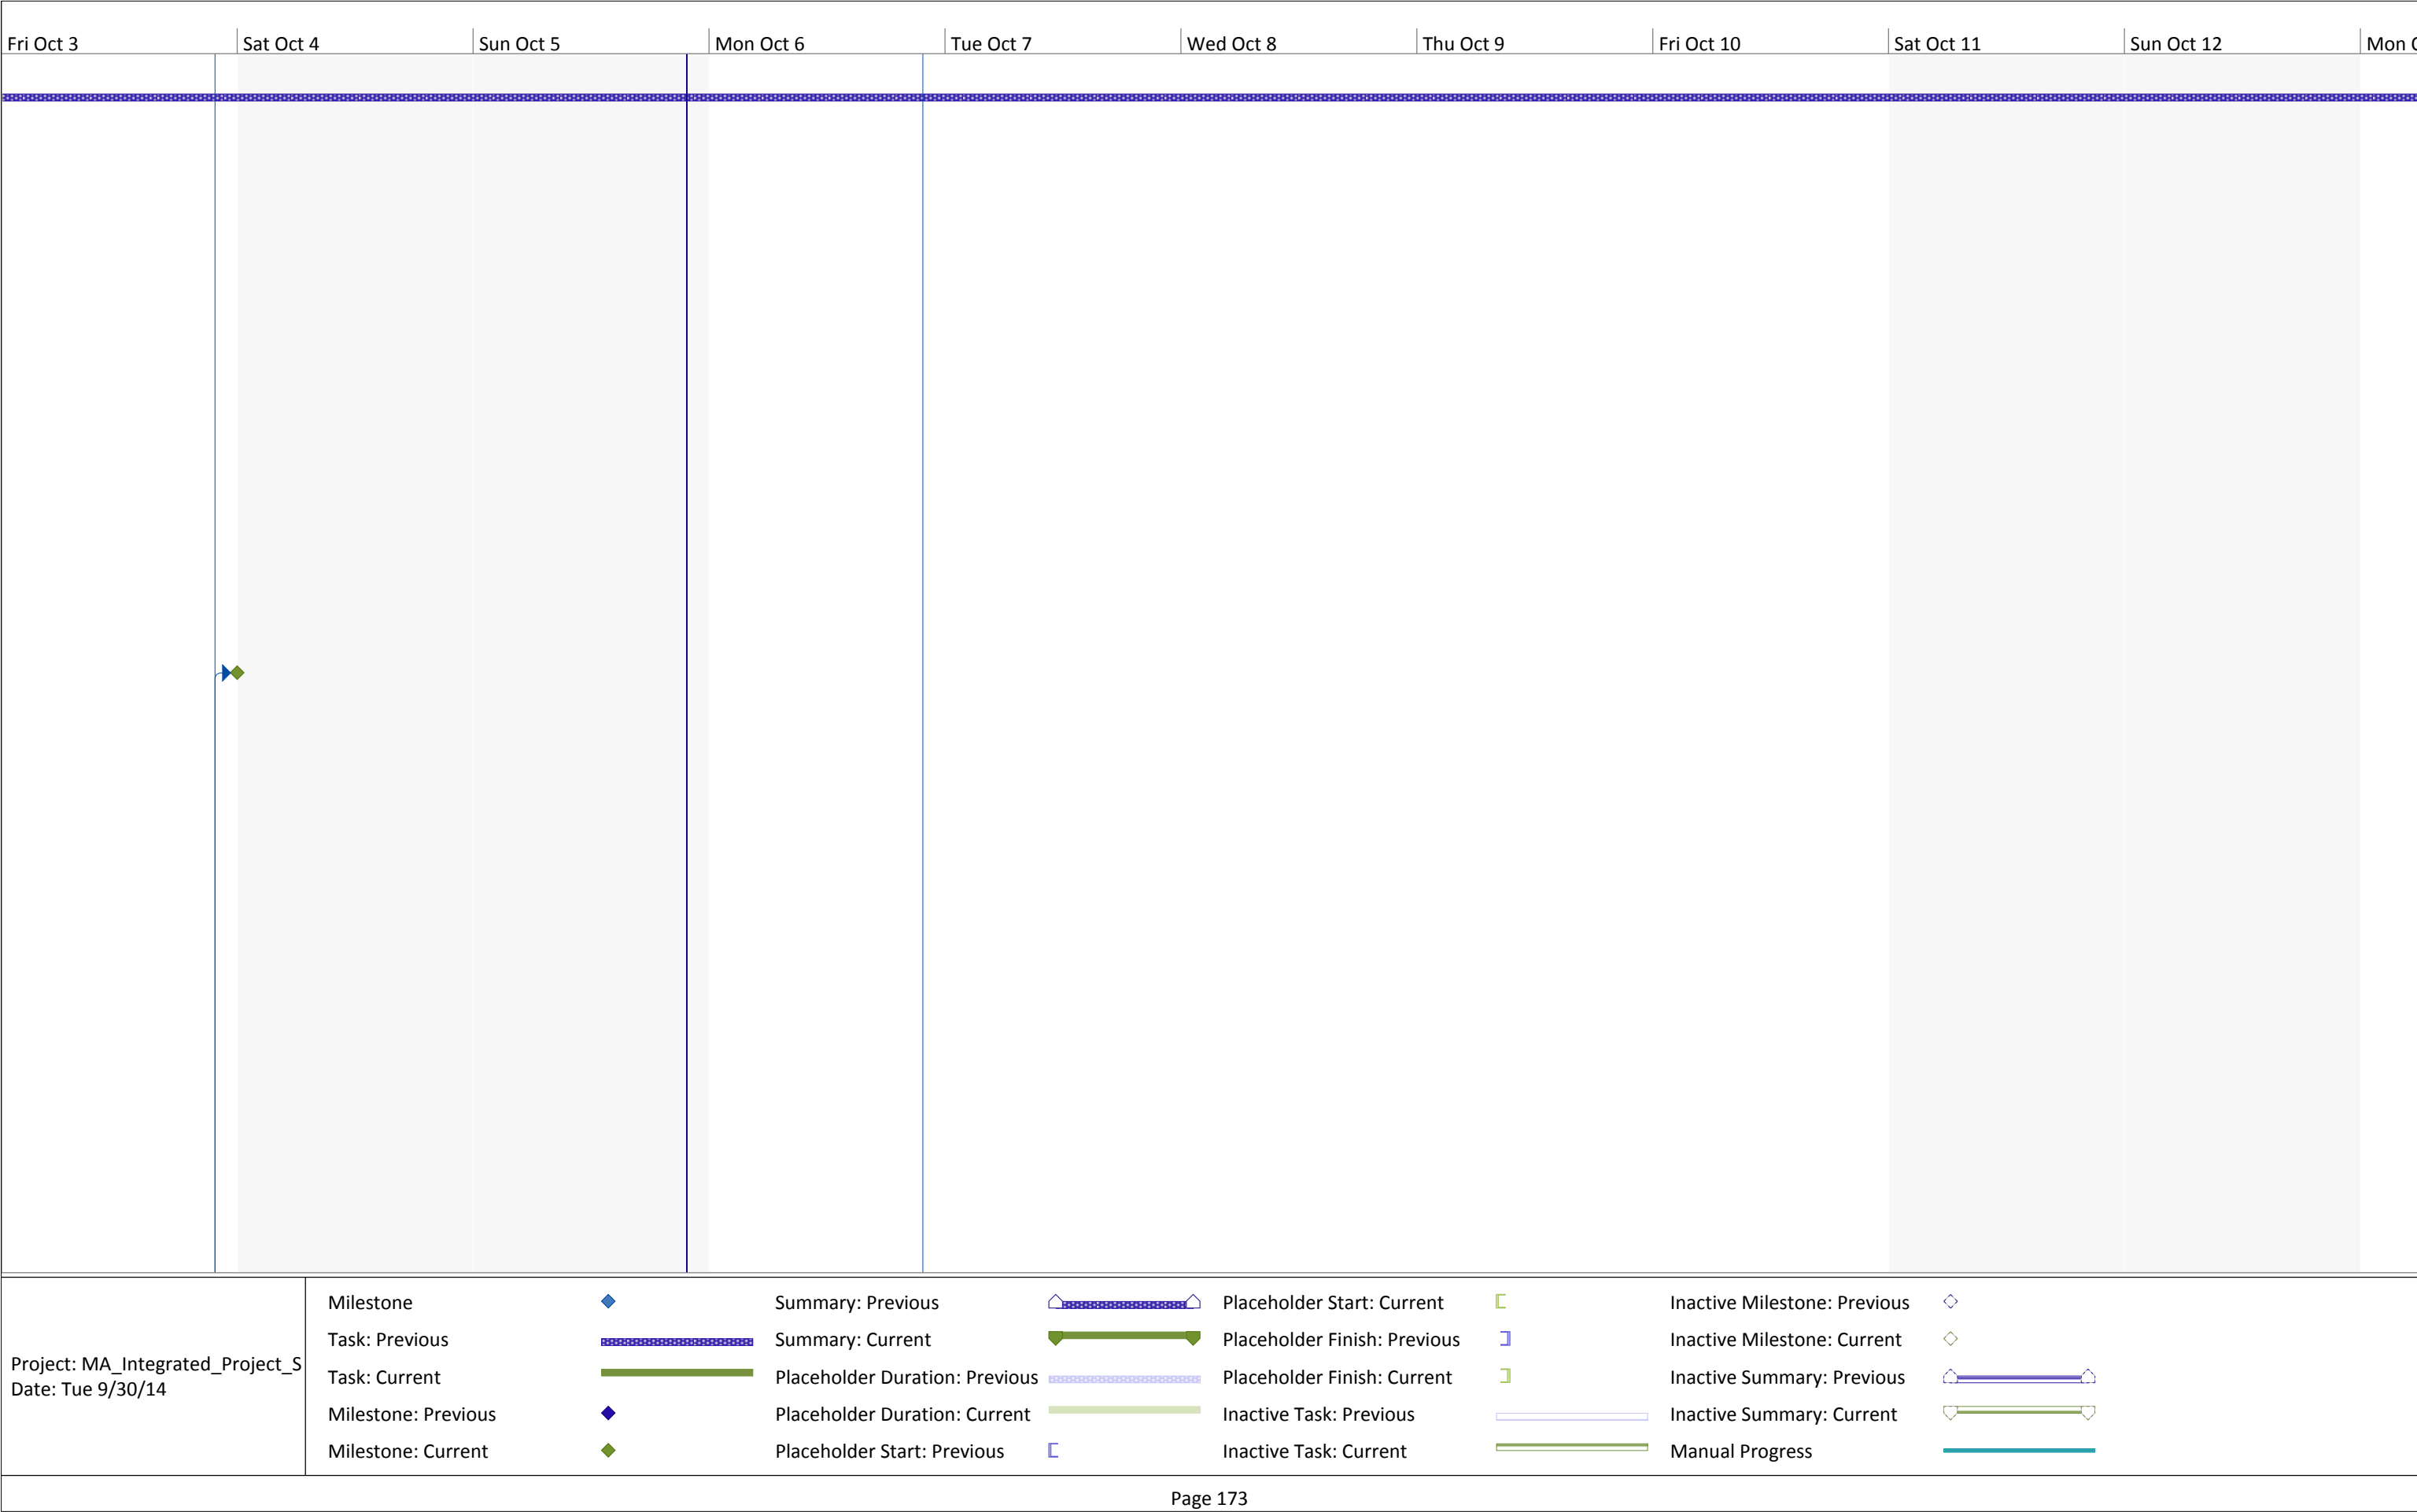


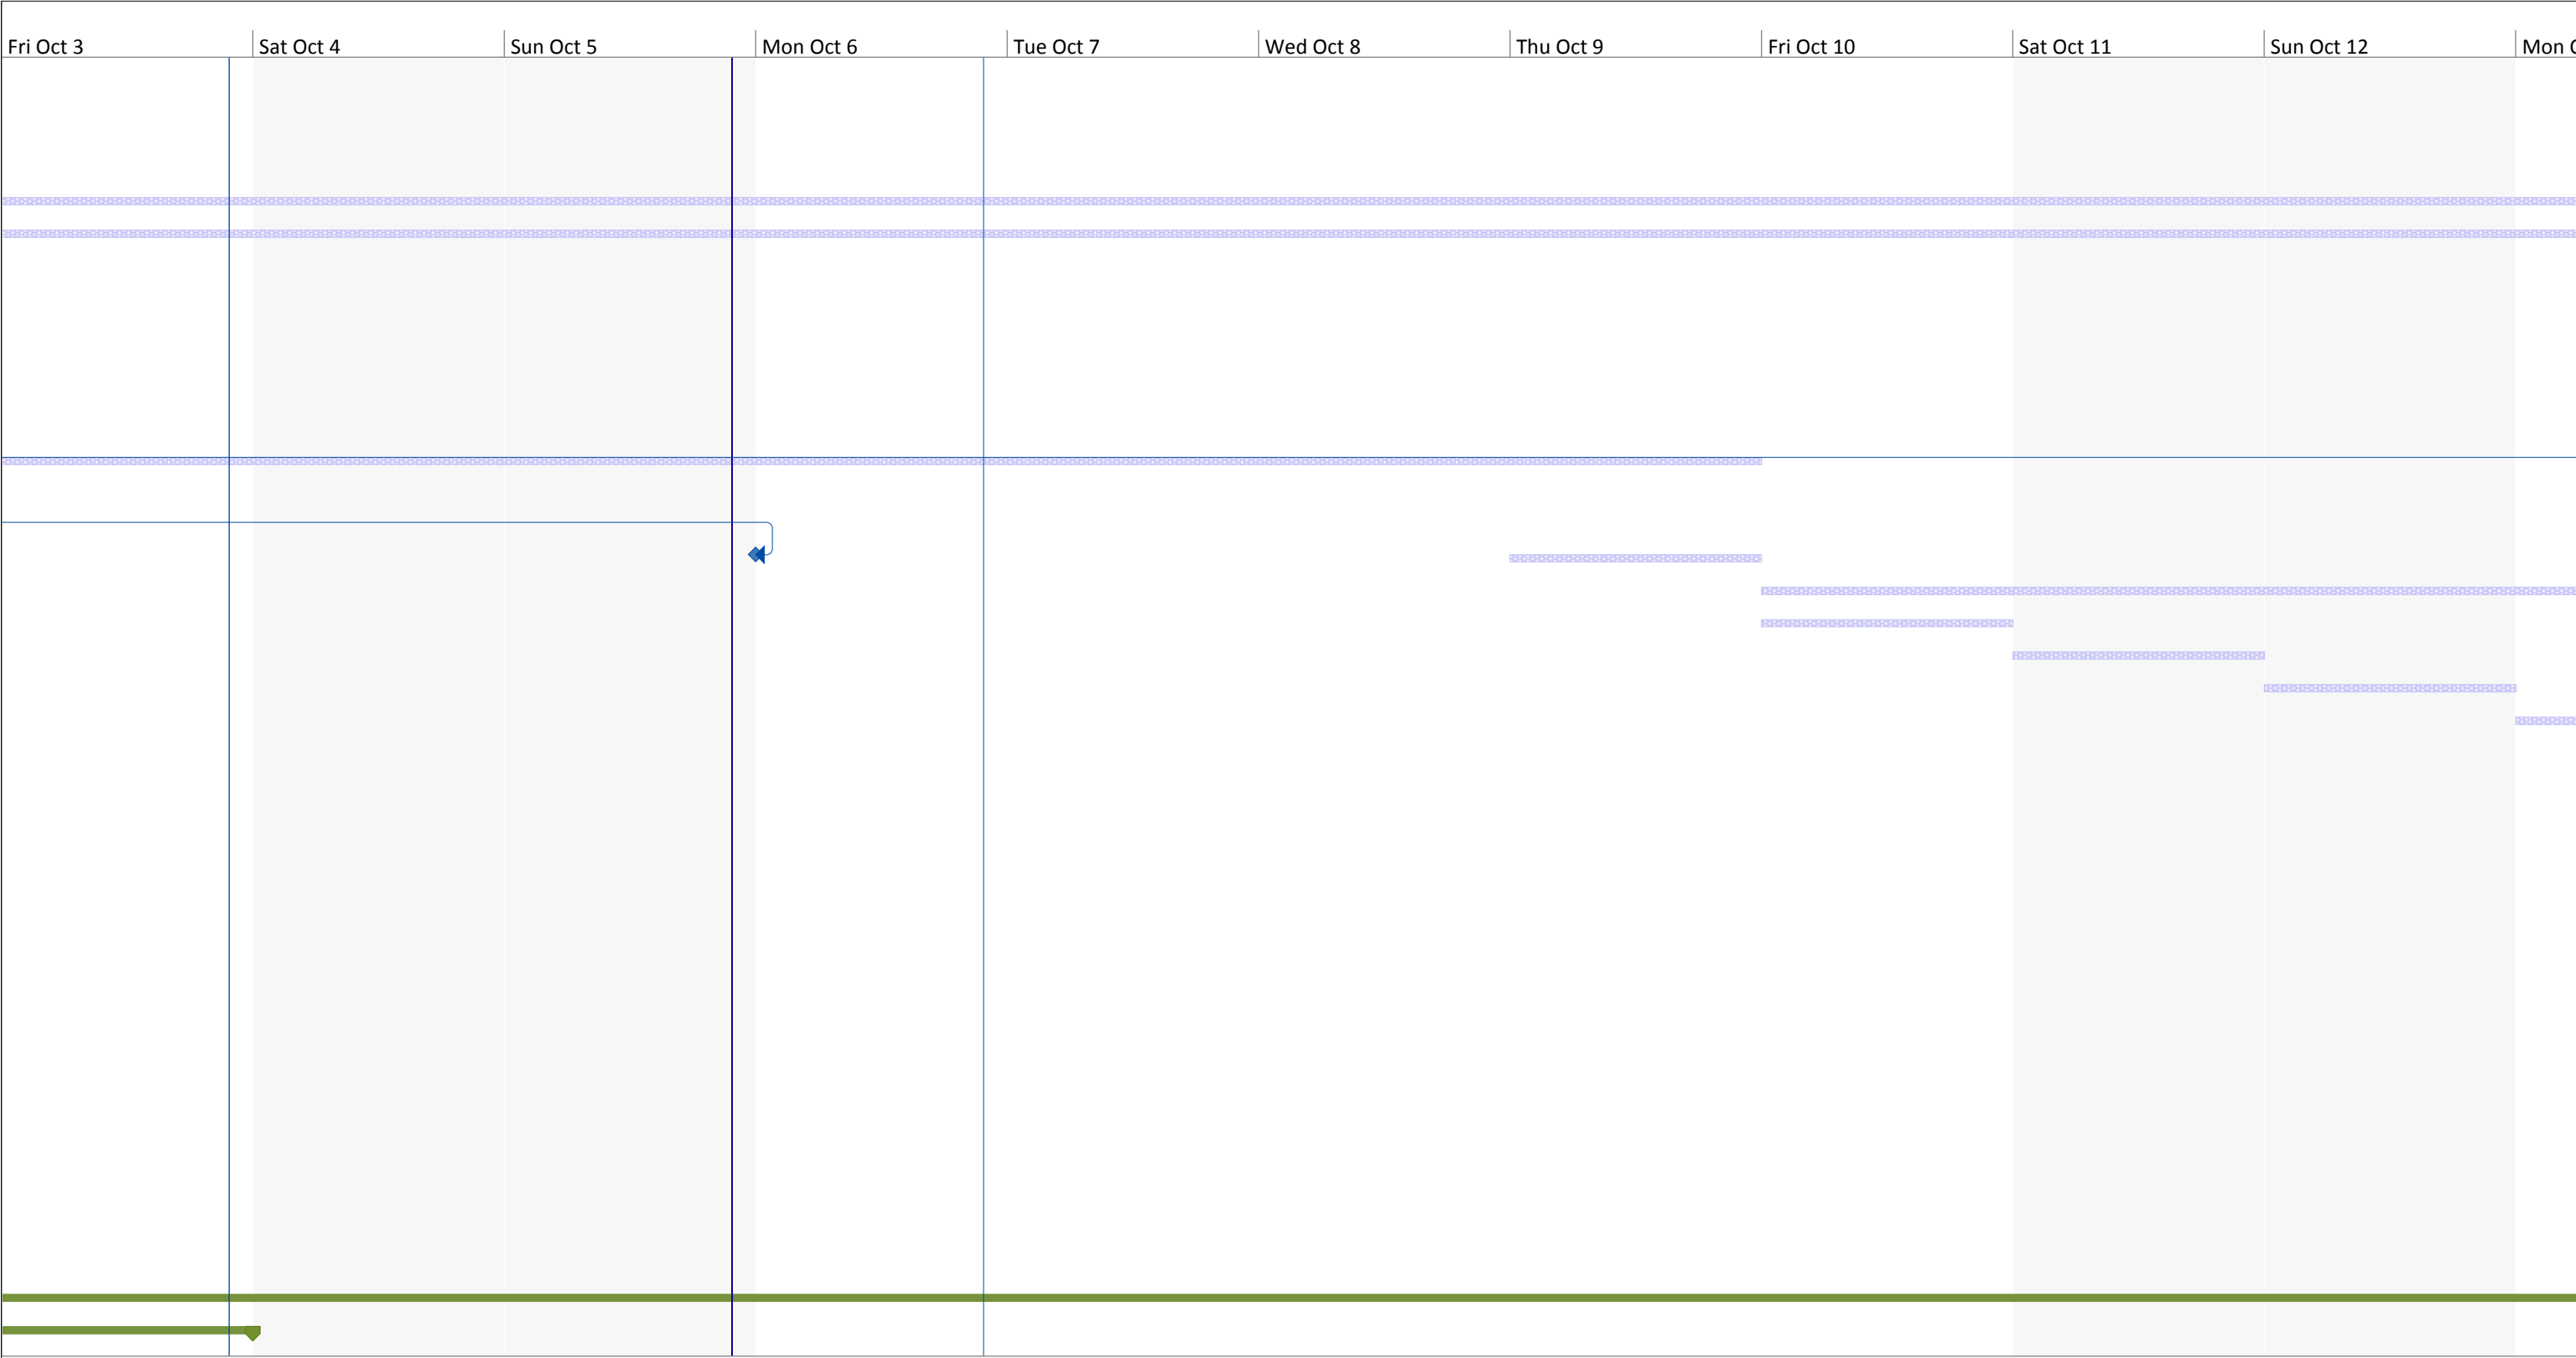



Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone	◆	Summary: Previous	▤	Placeholder Start: Current	▤	Inactive Milestone: Previous	◇
	Task: Previous	▤	Summary: Current	▤	Placeholder Finish: Previous	▤	Inactive Milestone: Current	◇
	Task: Current	▤	Placeholder Duration: Previous	▤	Placeholder Finish: Current	▤	Inactive Summary: Previous	▤
	Milestone: Previous	◆	Placeholder Duration: Current	▤	Inactive Task: Previous	▤	Inactive Summary: Current	▤
	Milestone: Current	◆	Placeholder Start: Previous	▤	Inactive Task: Current	▤	Manual Progress	▤

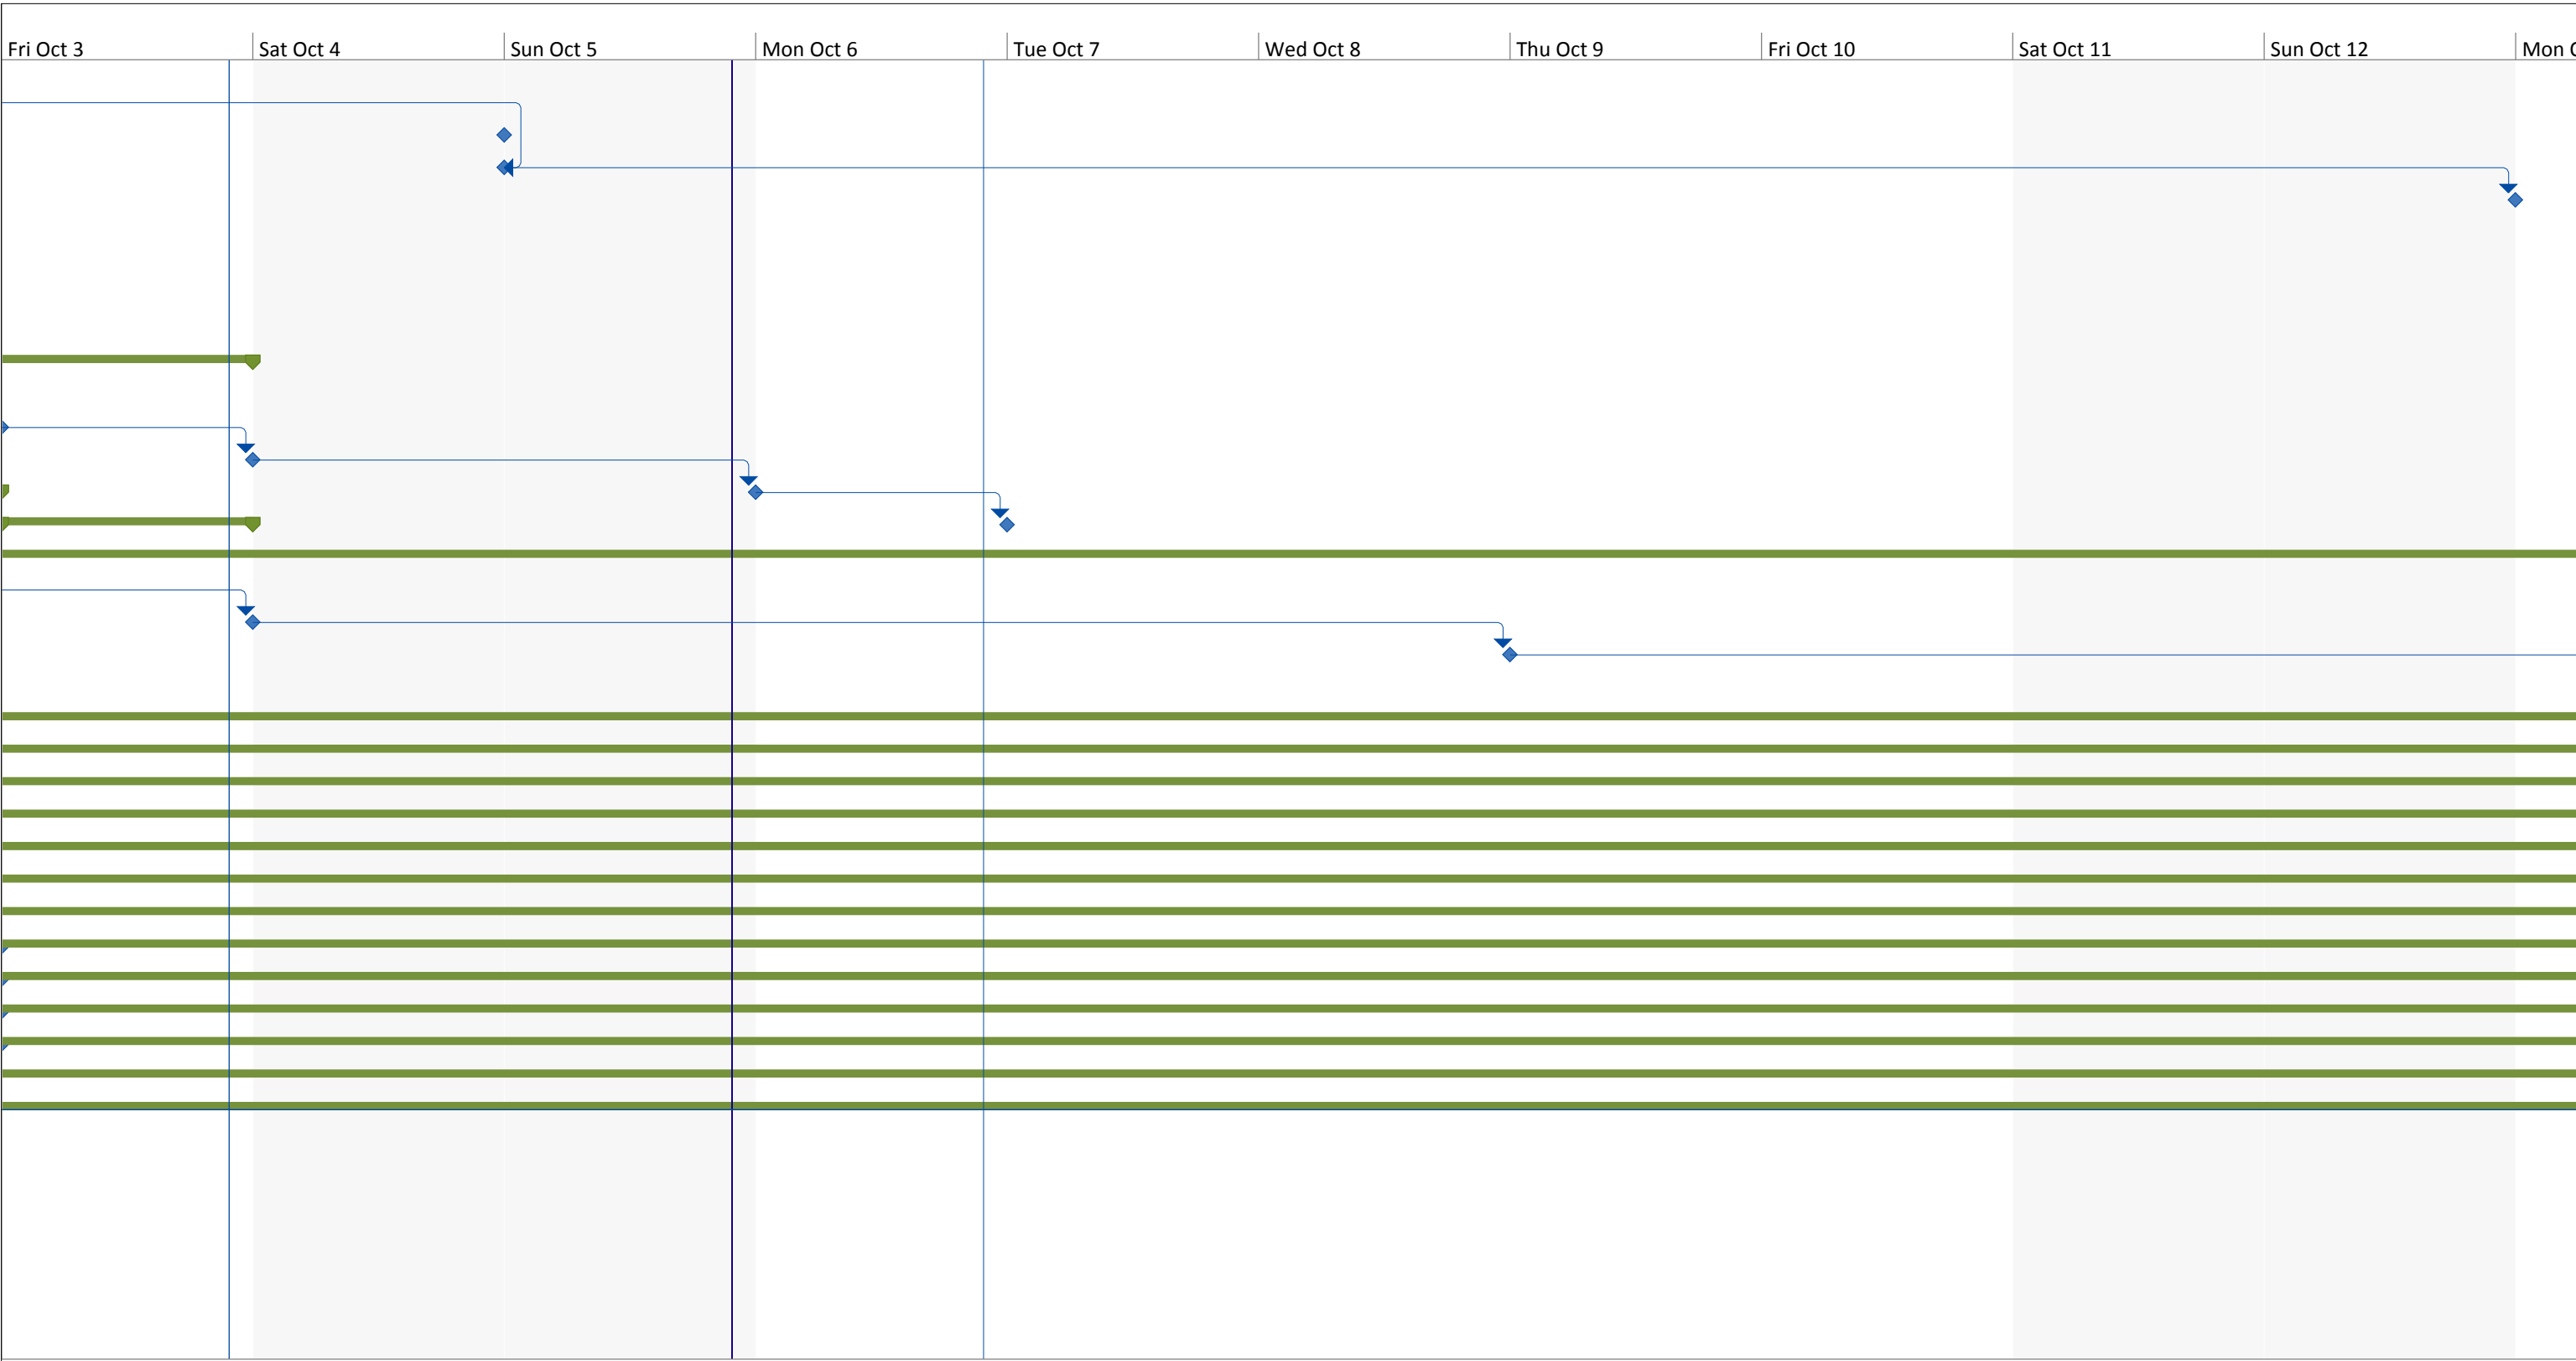


Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

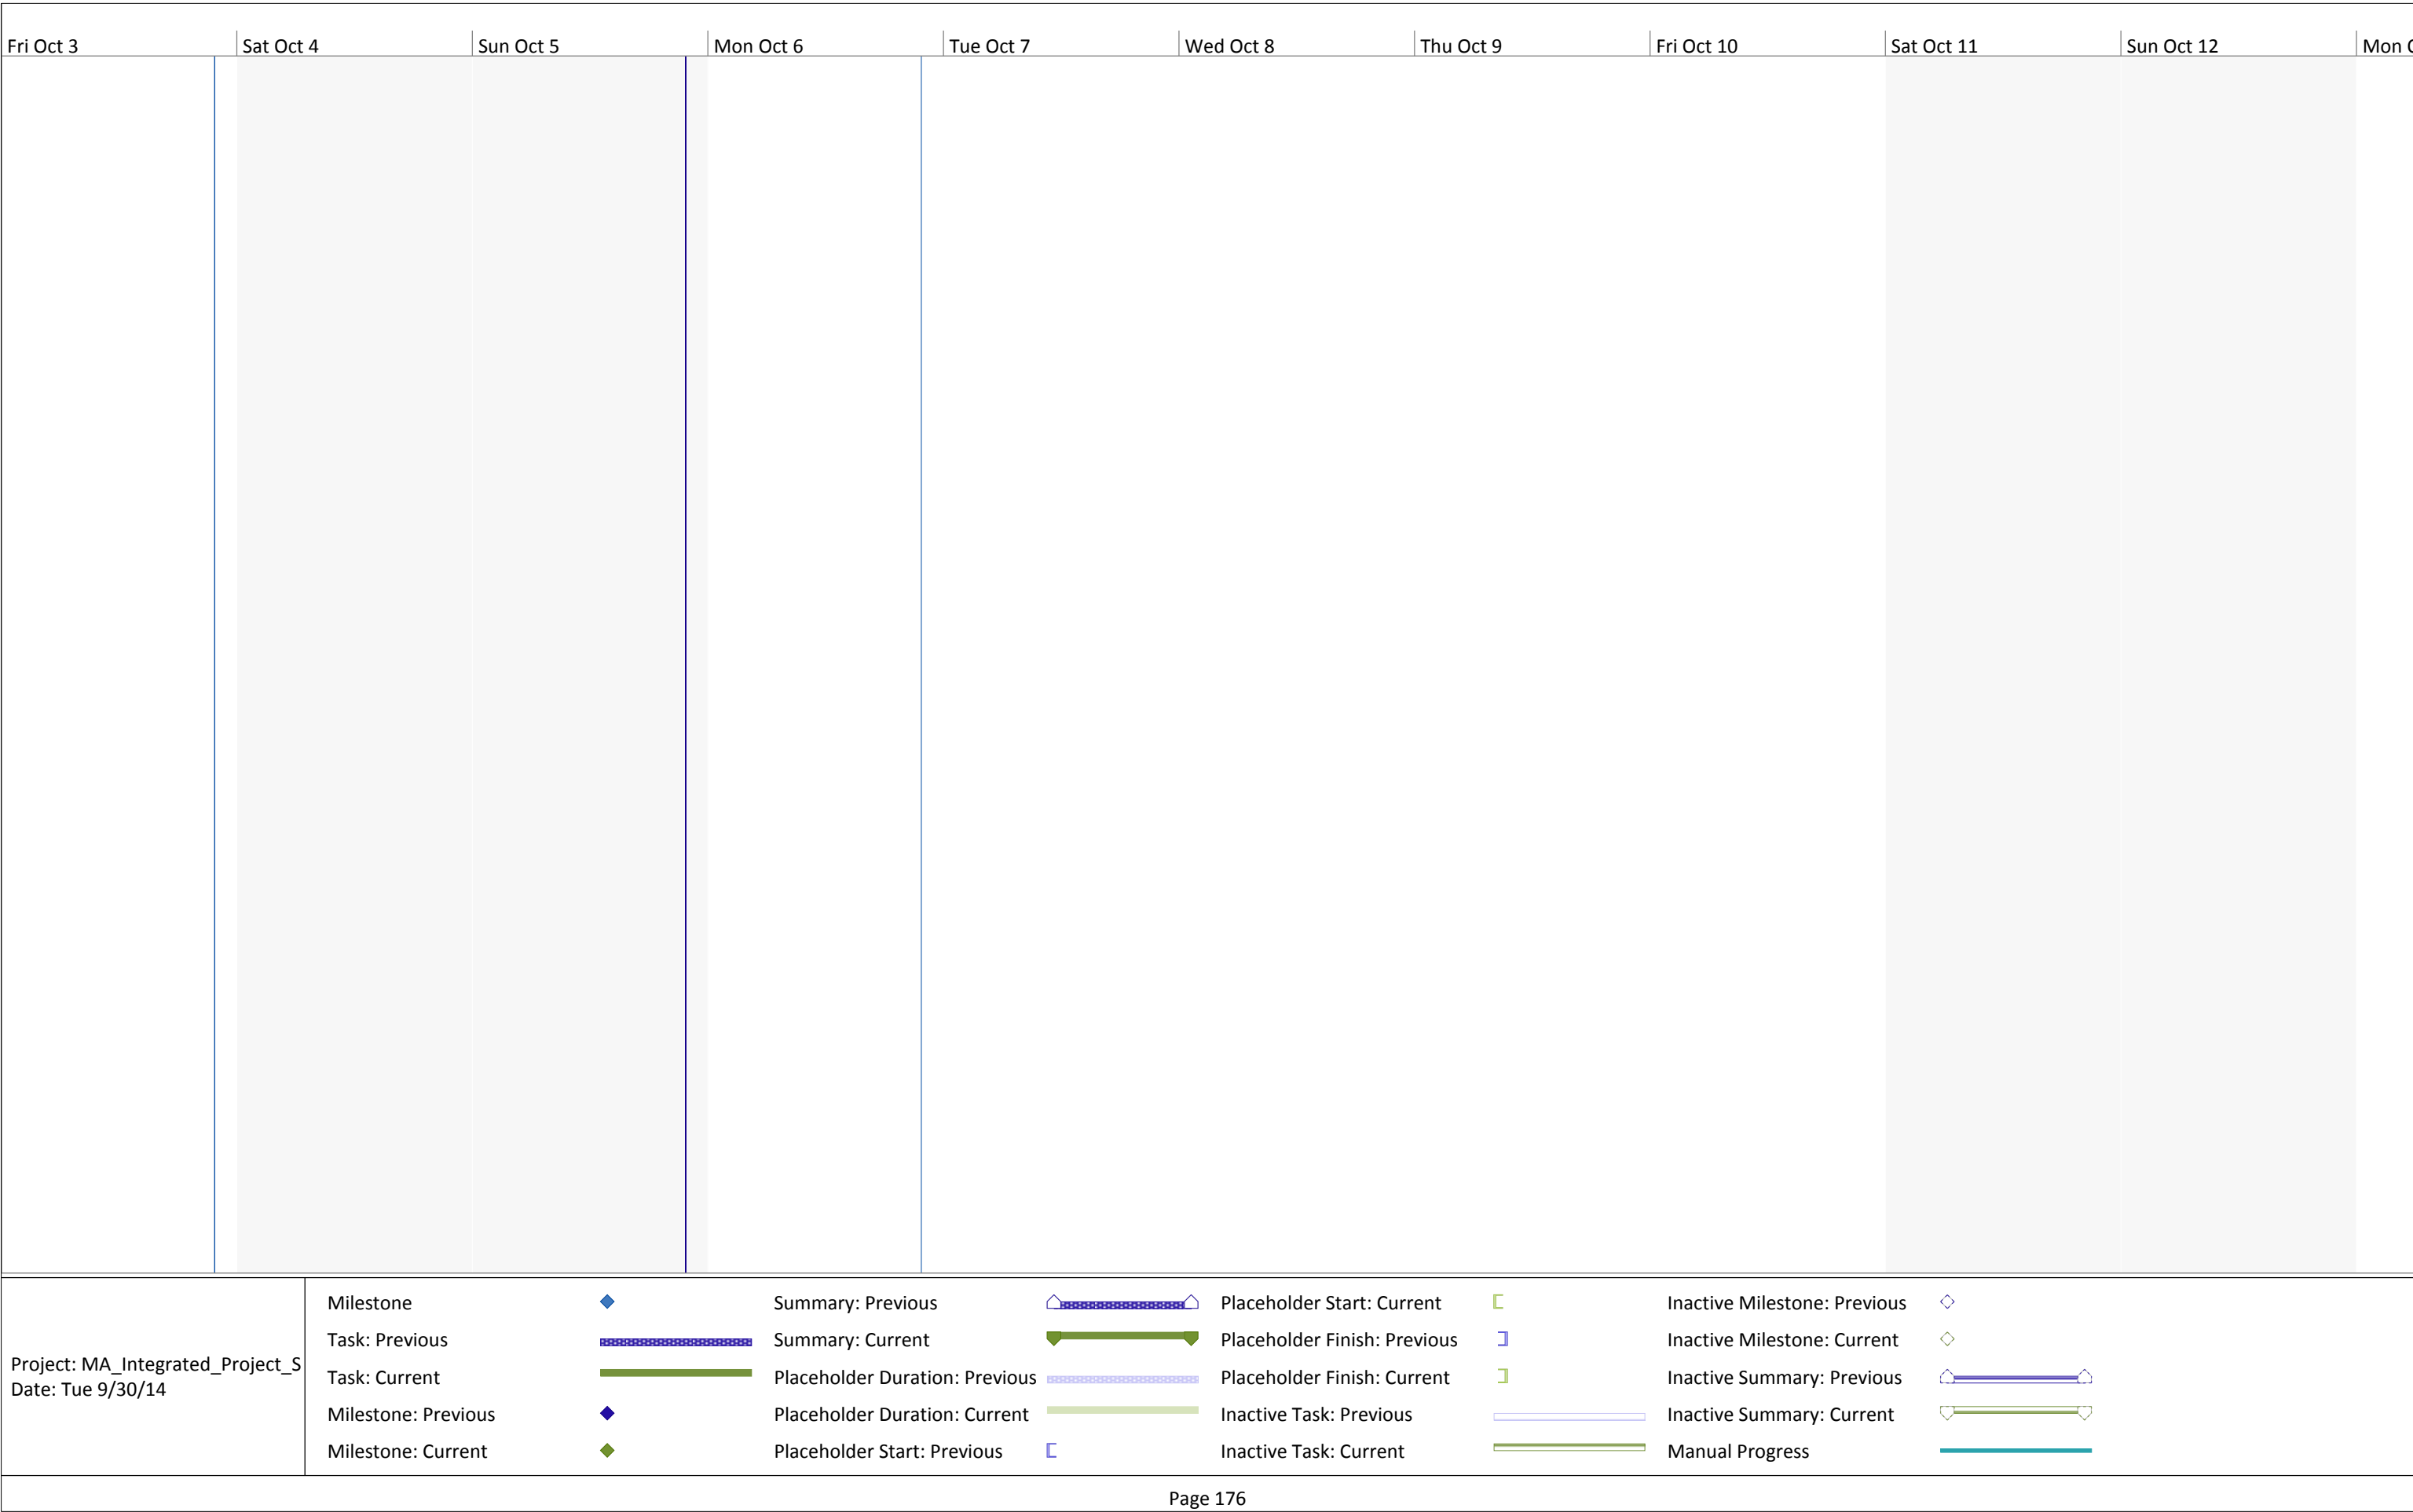

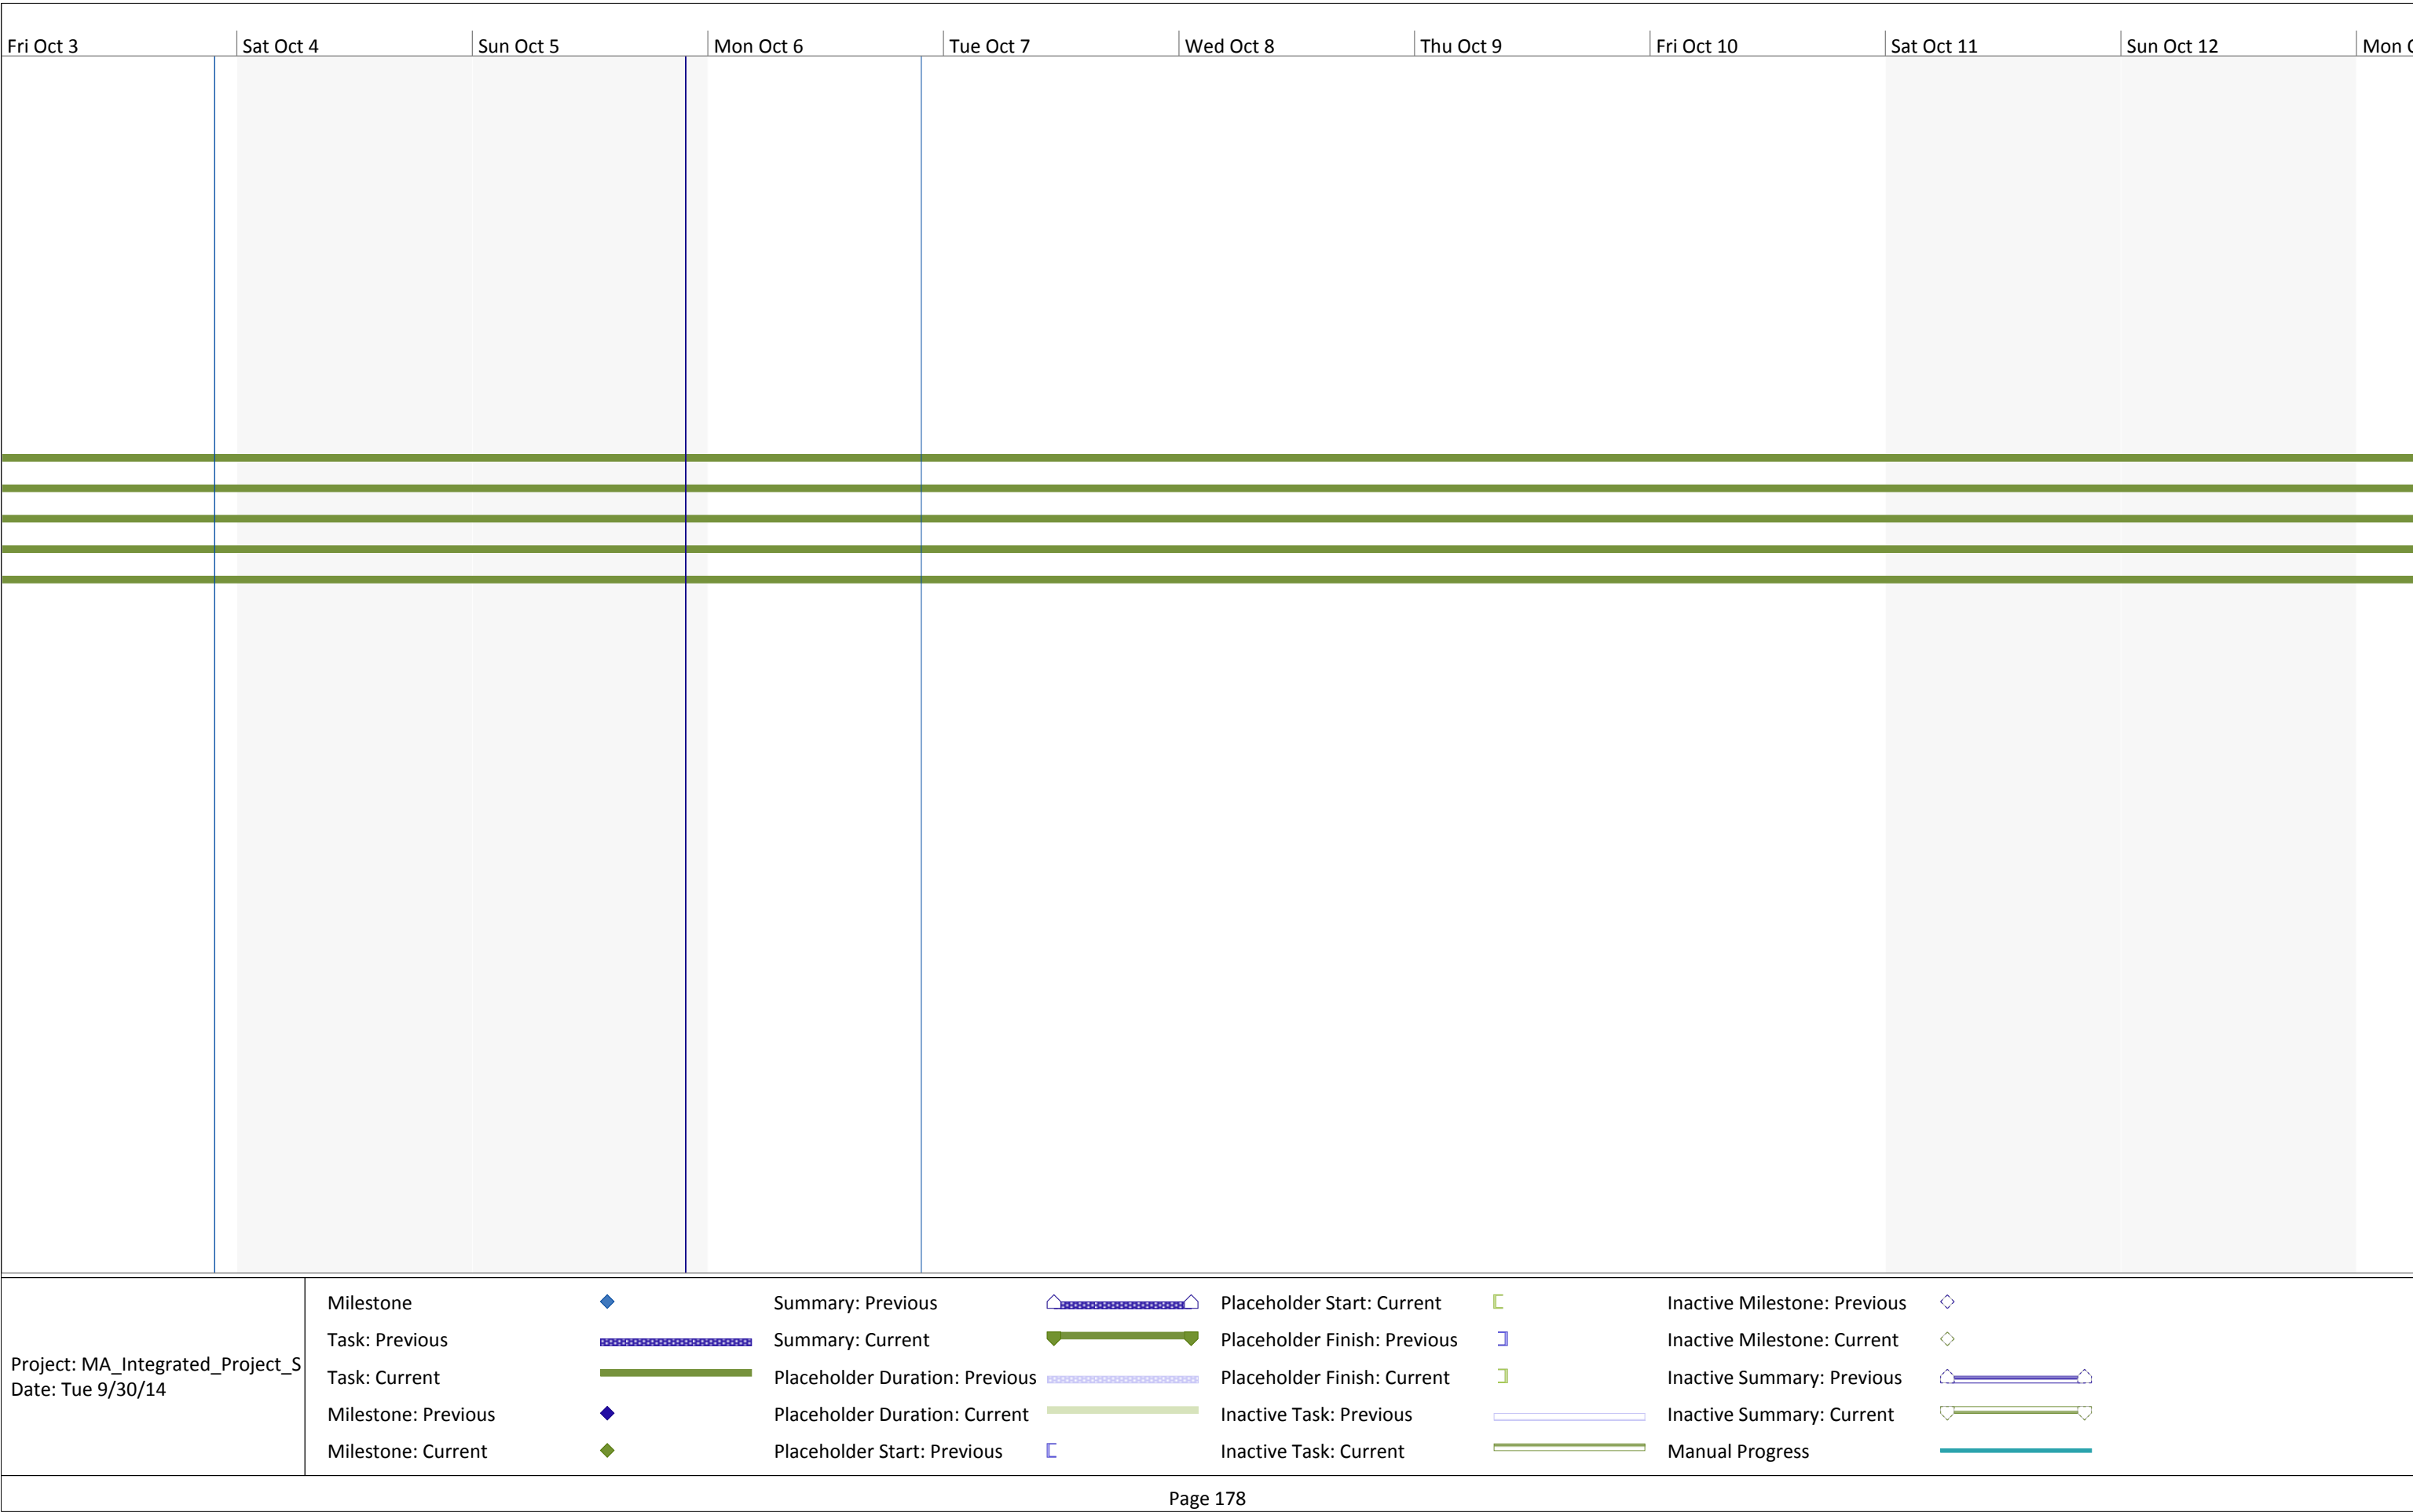


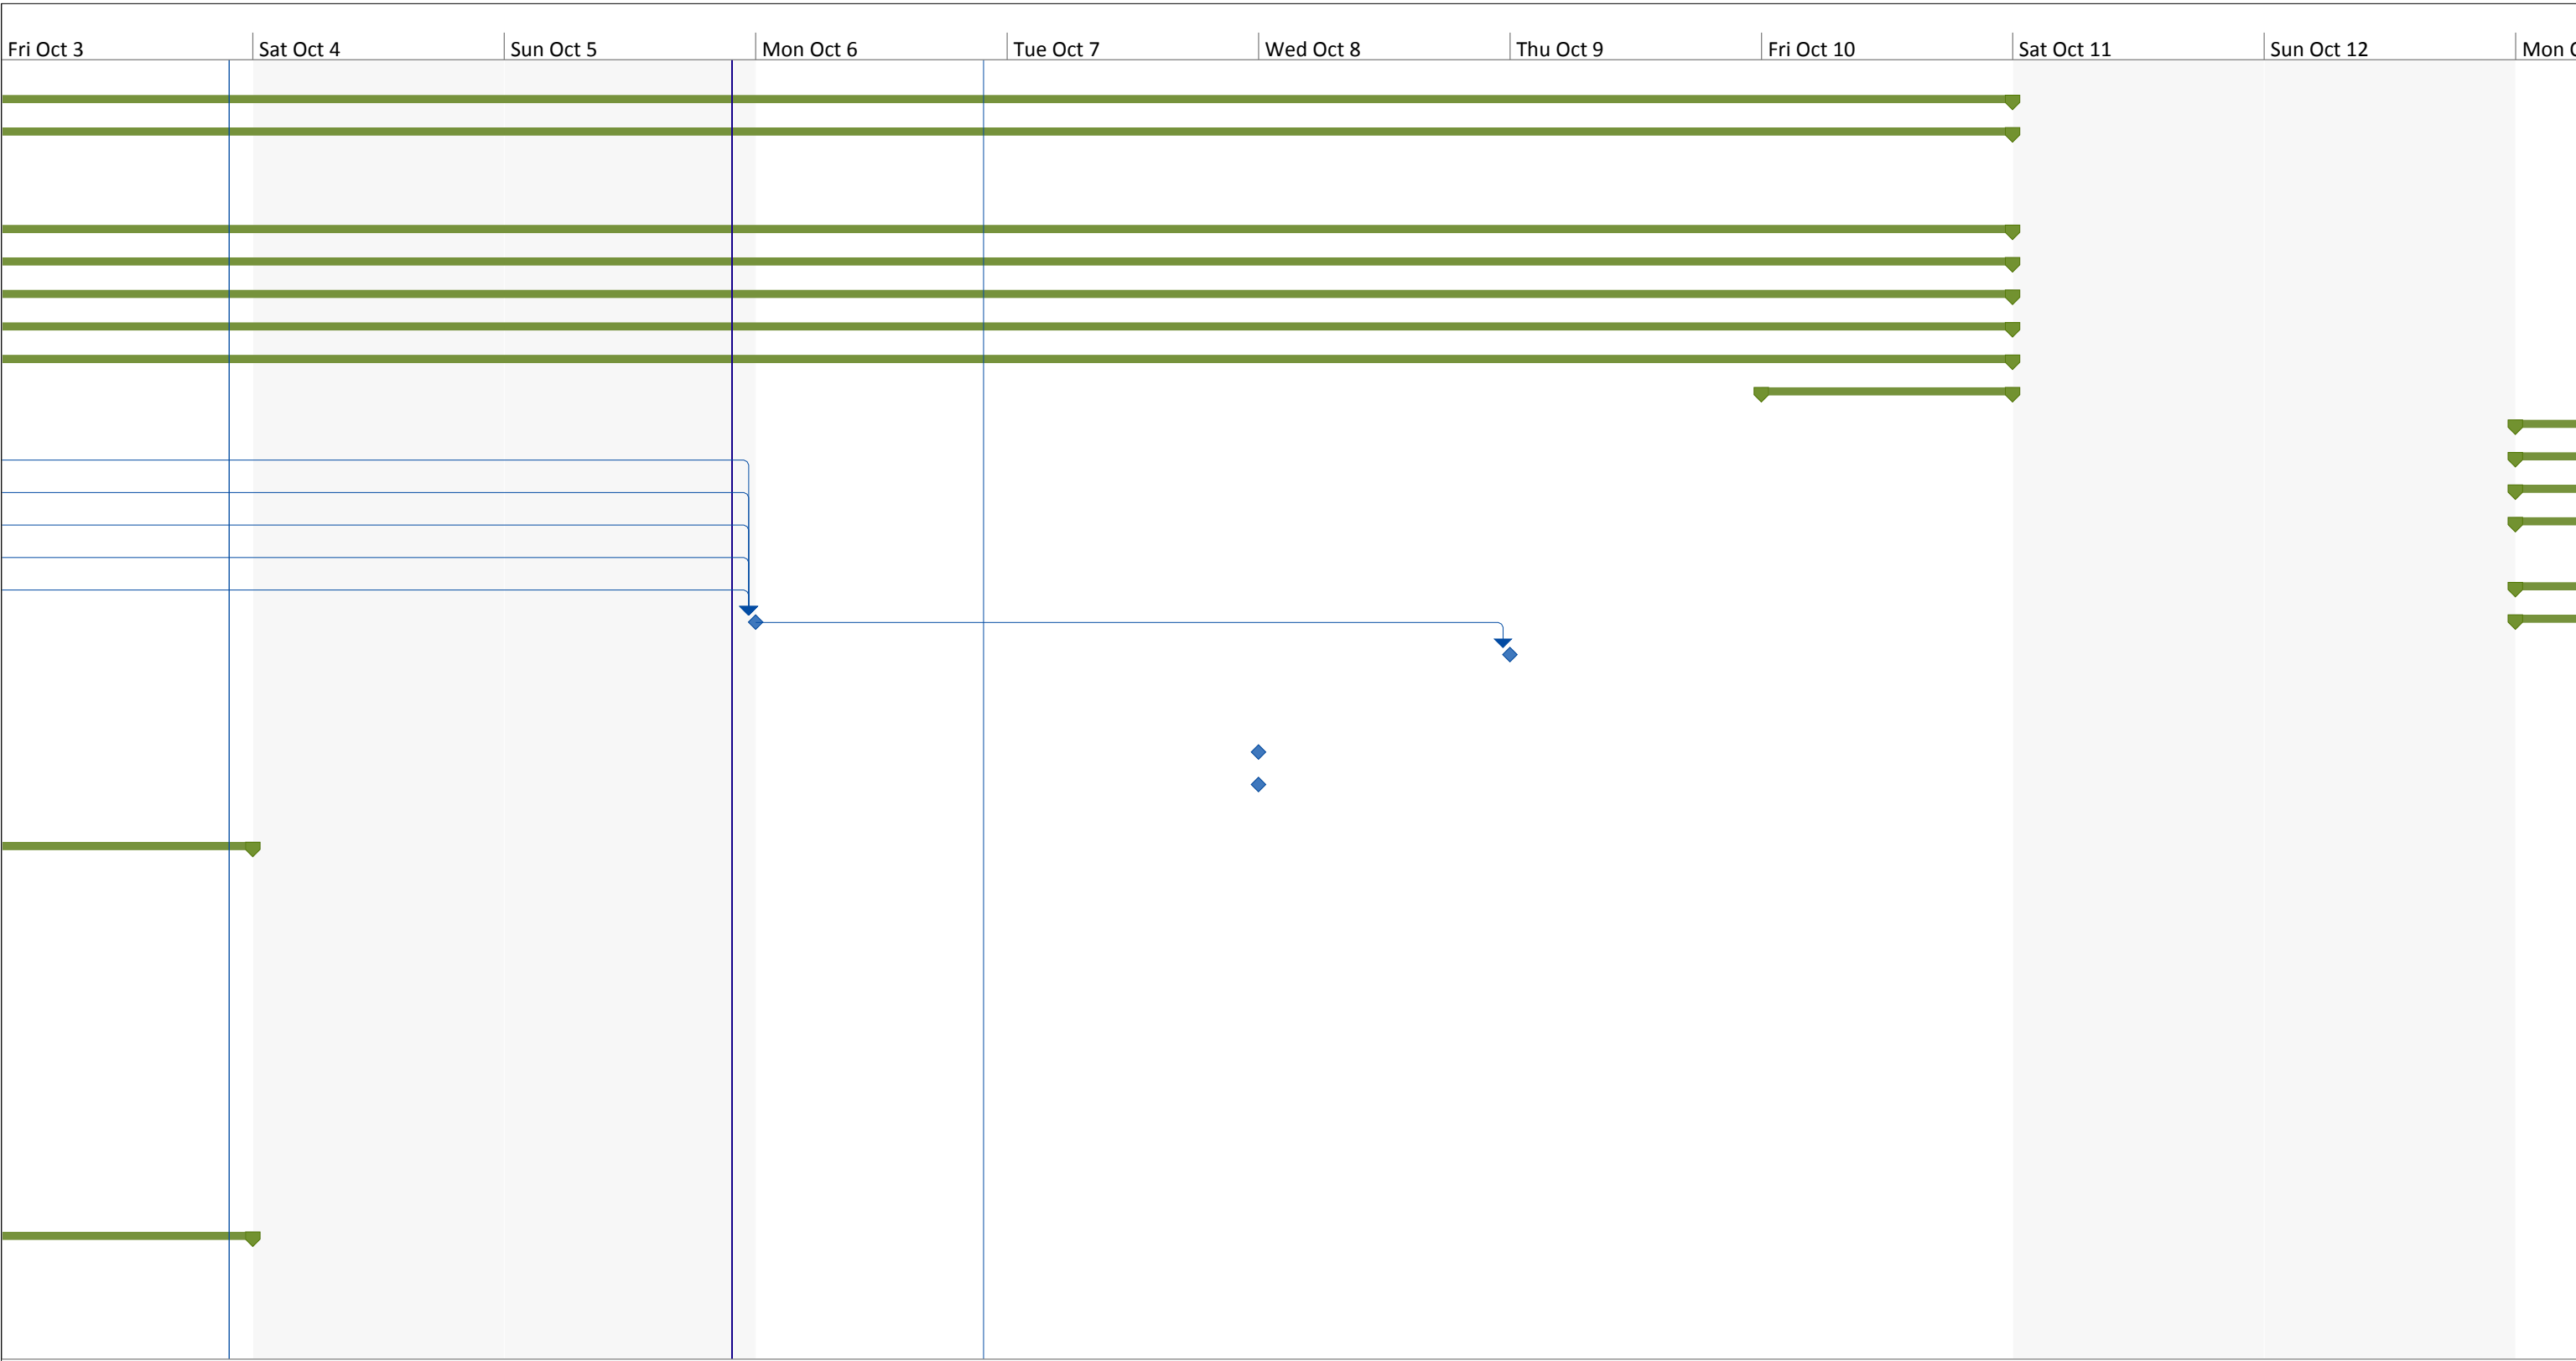

Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

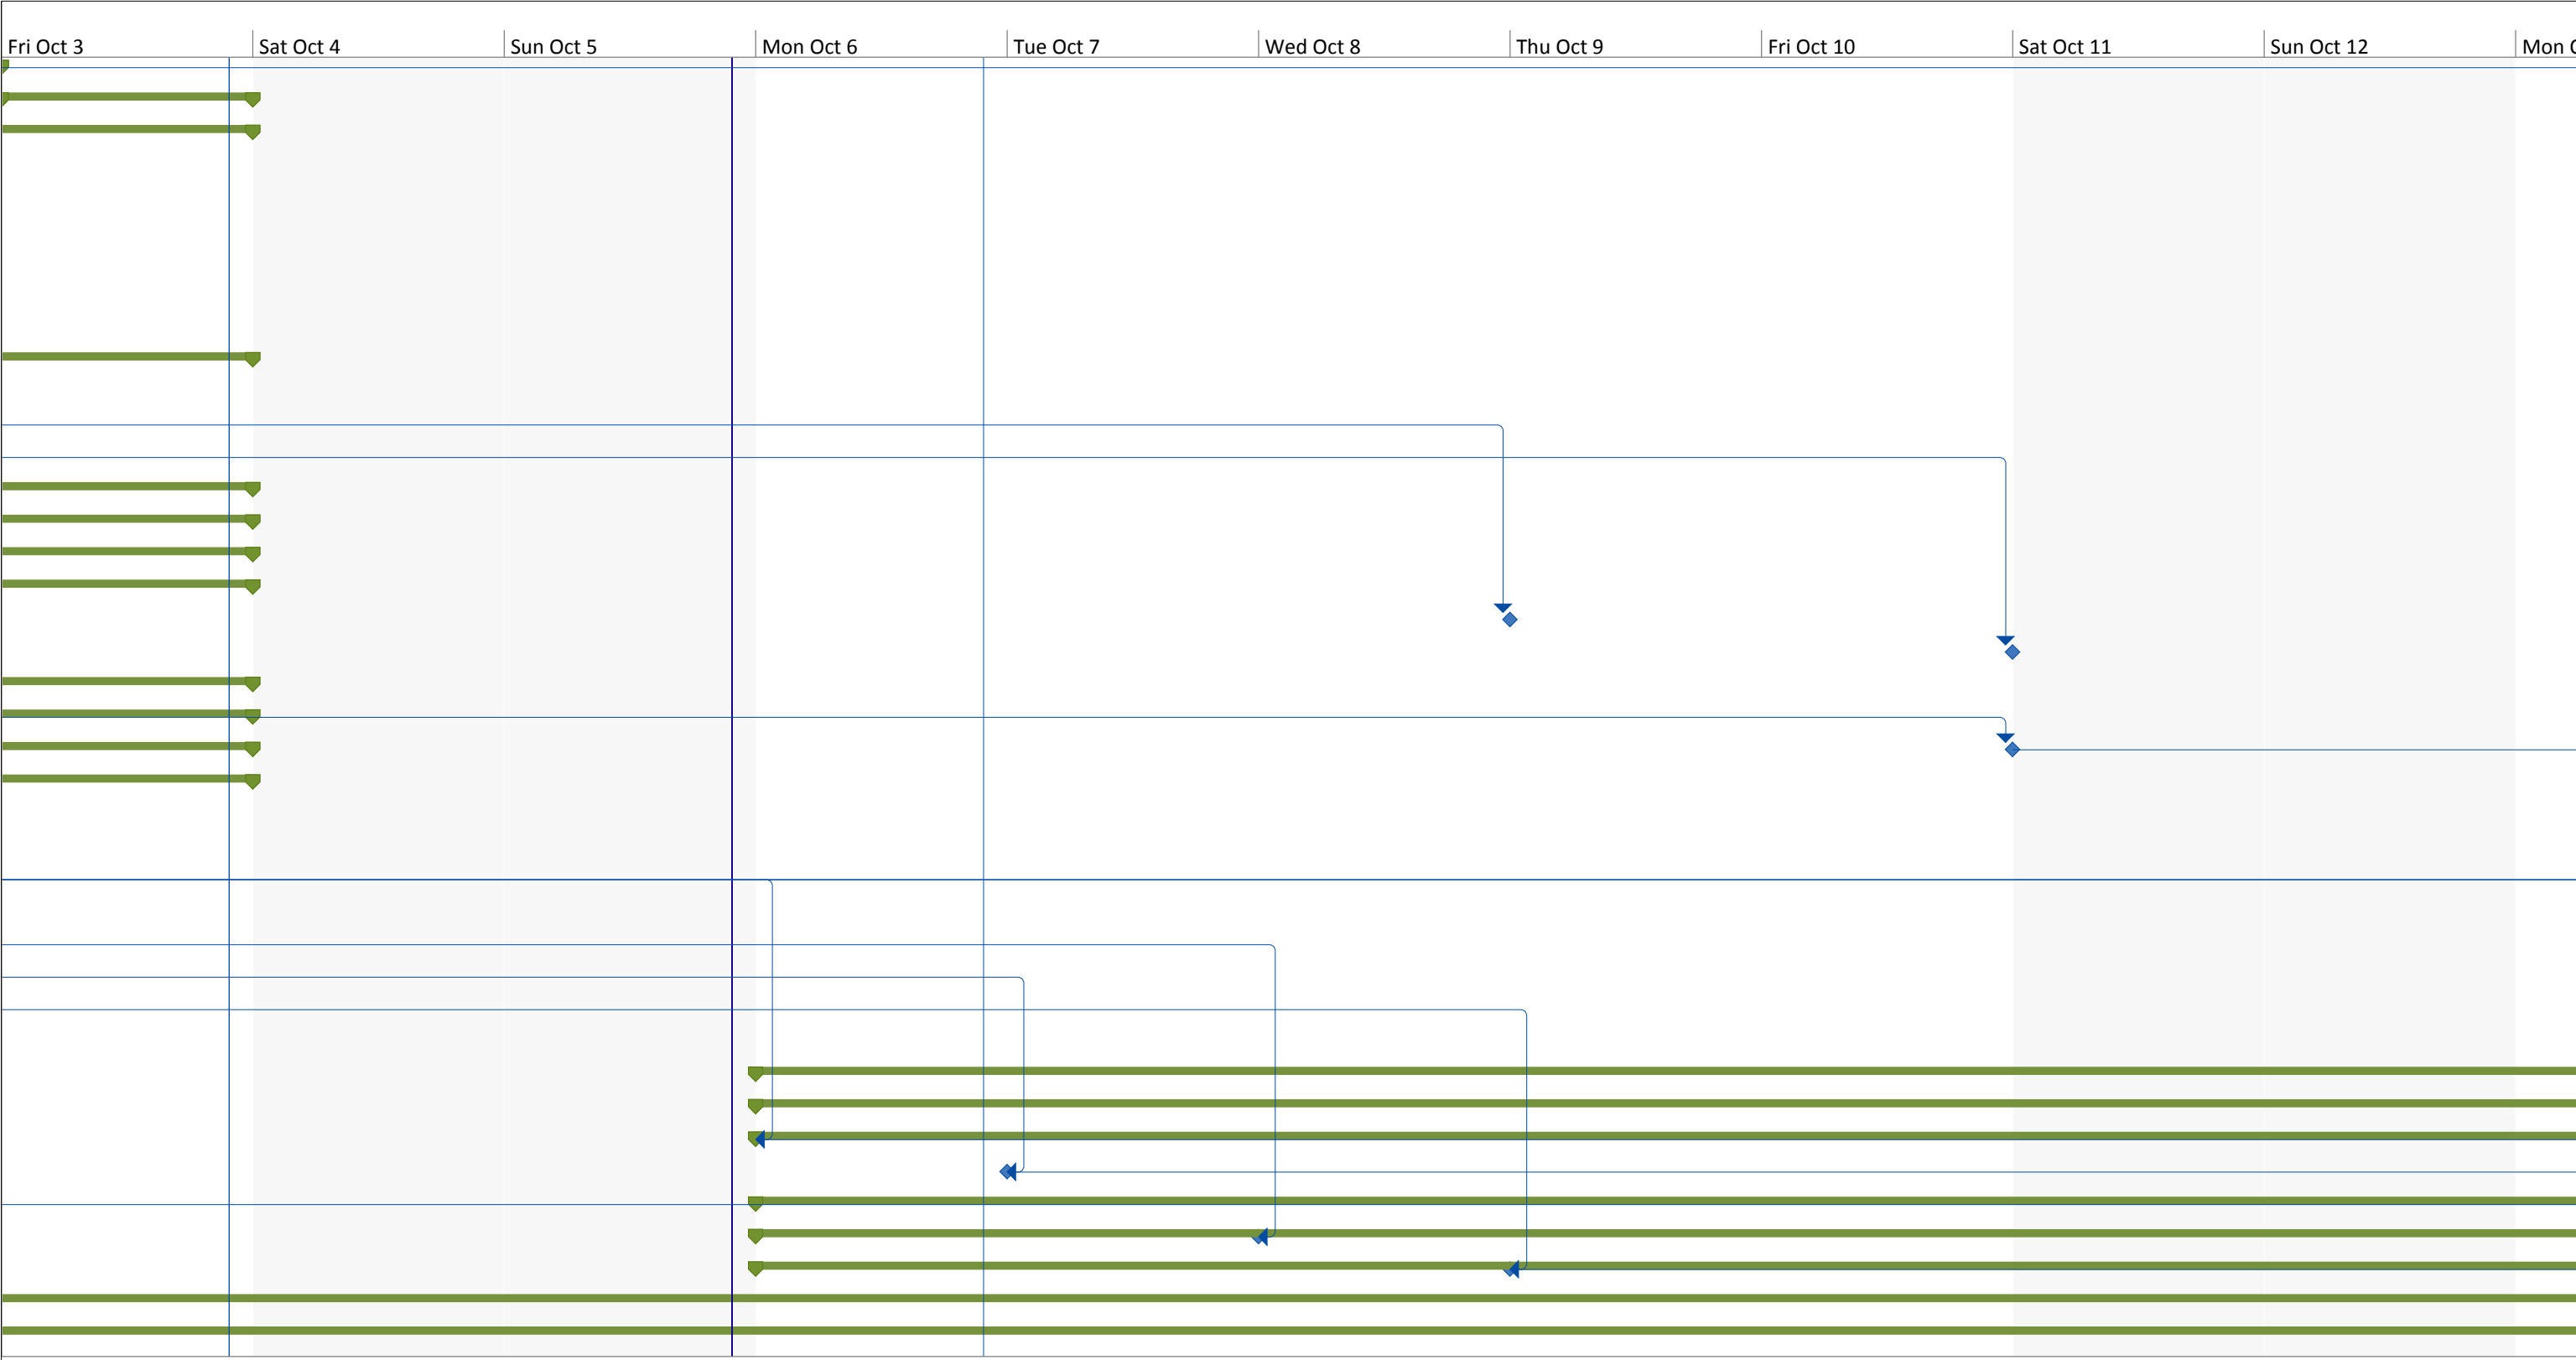




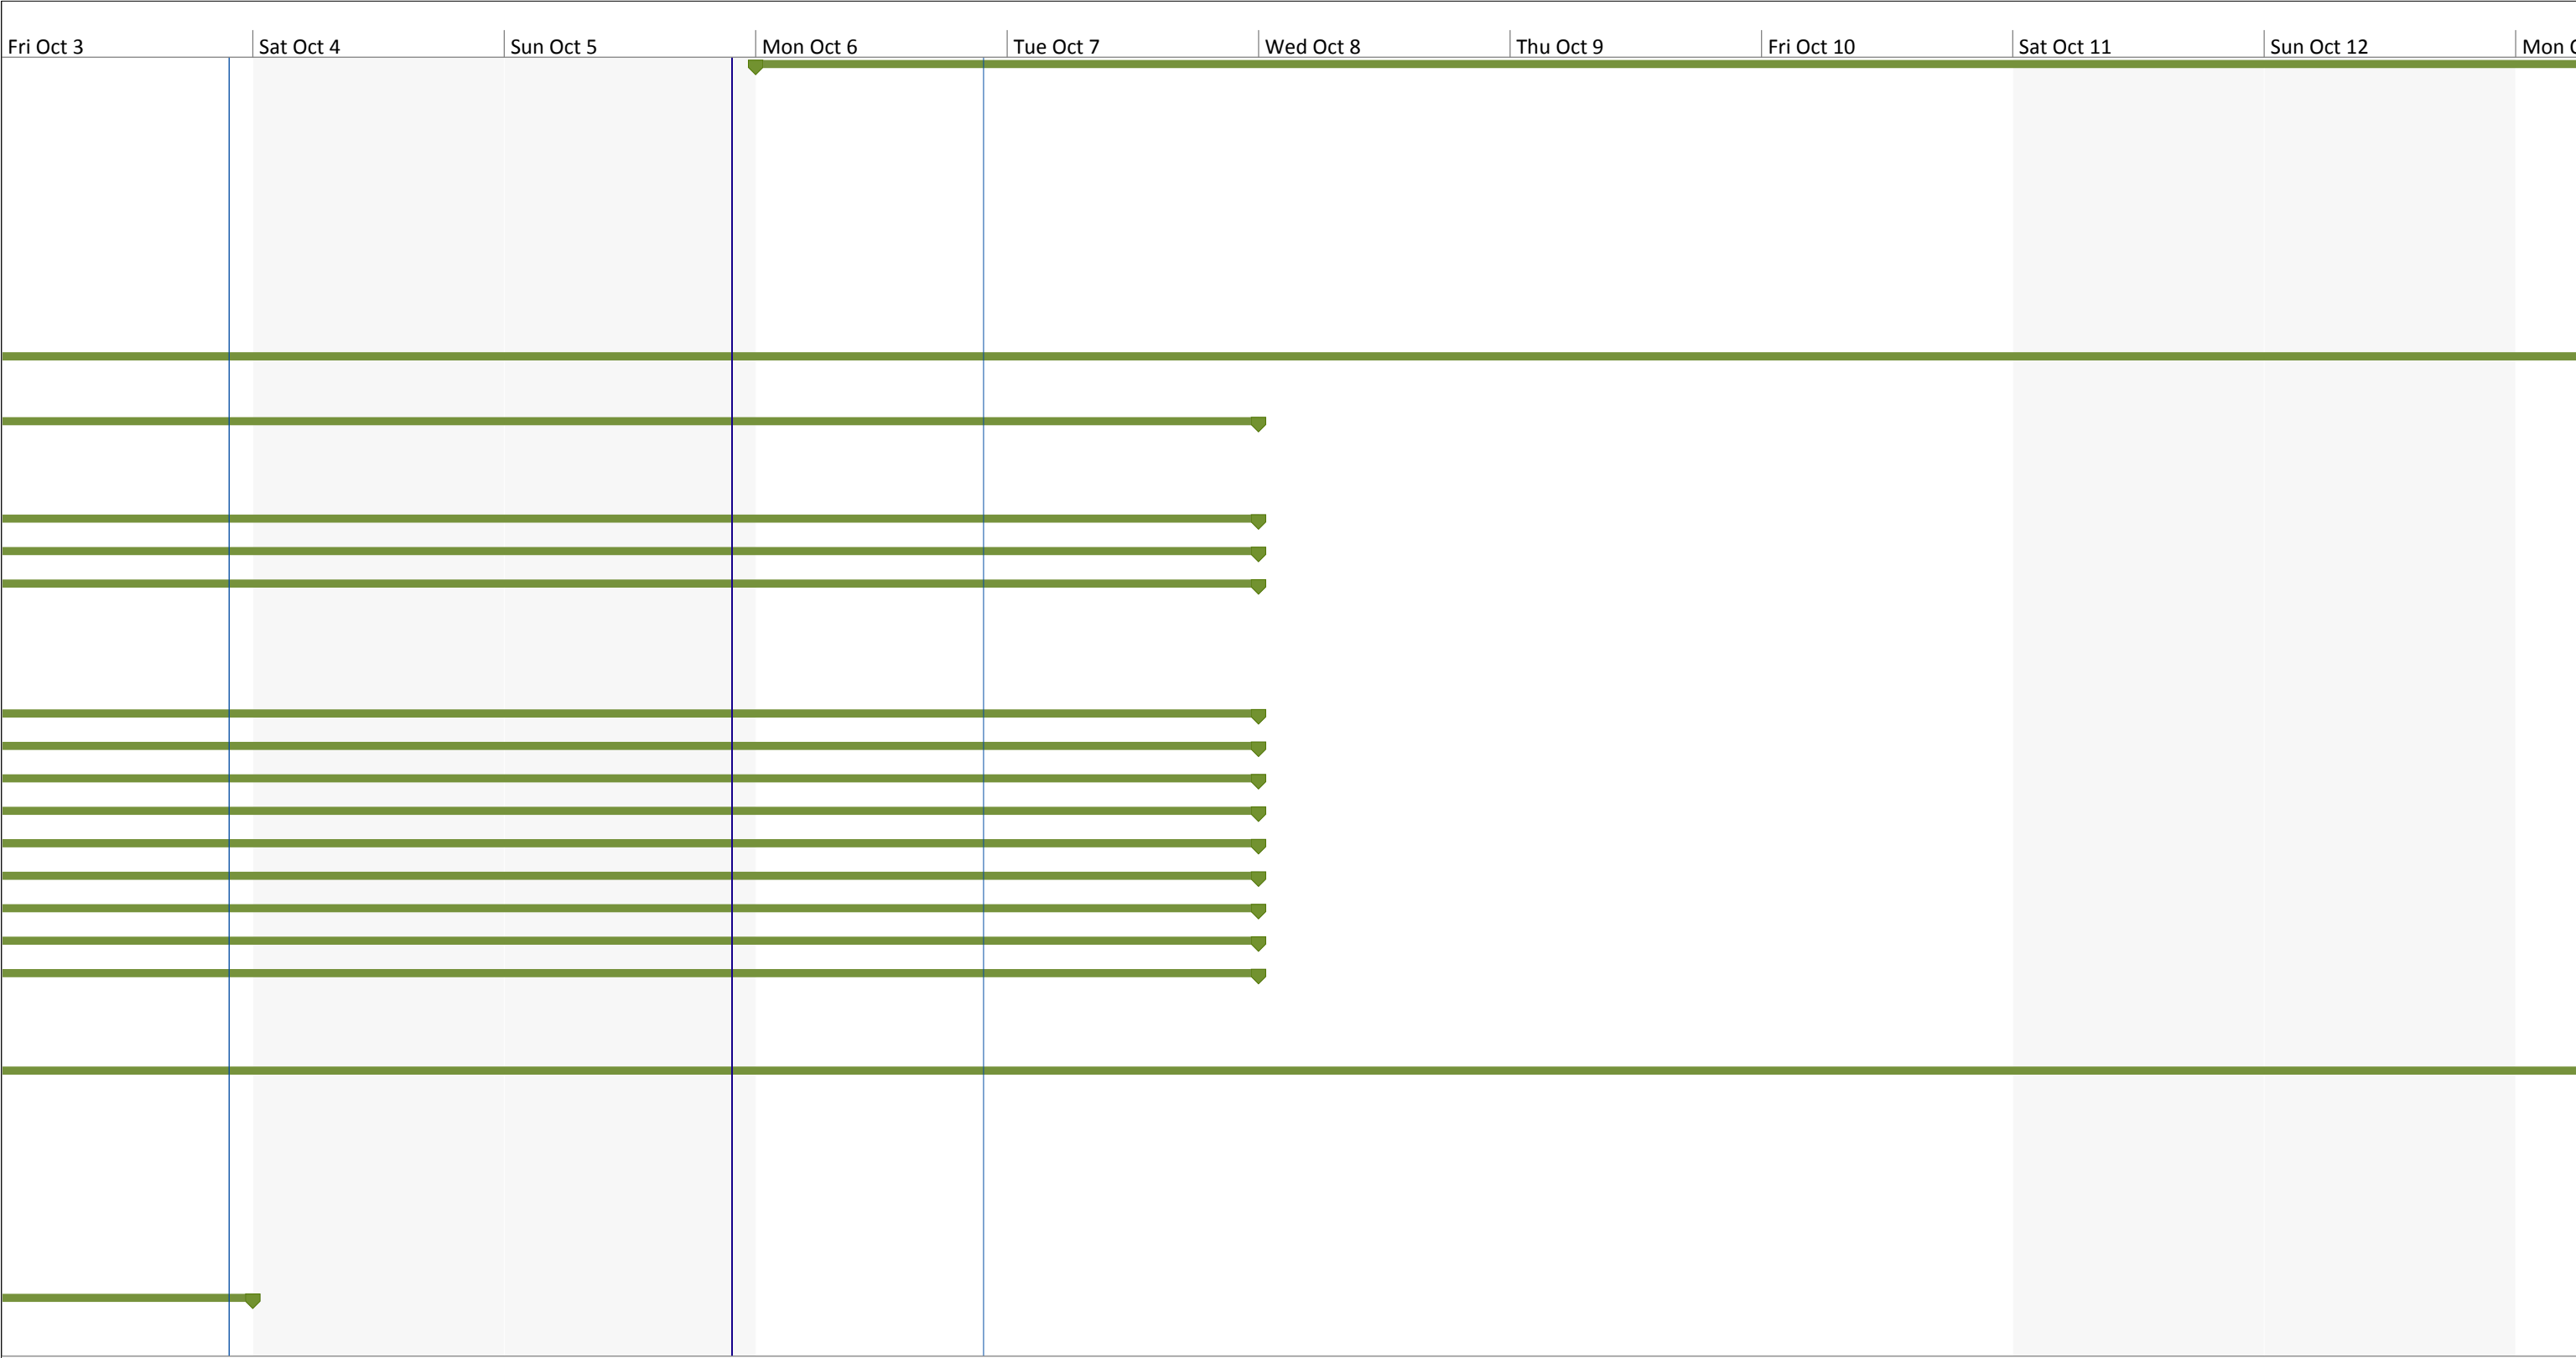





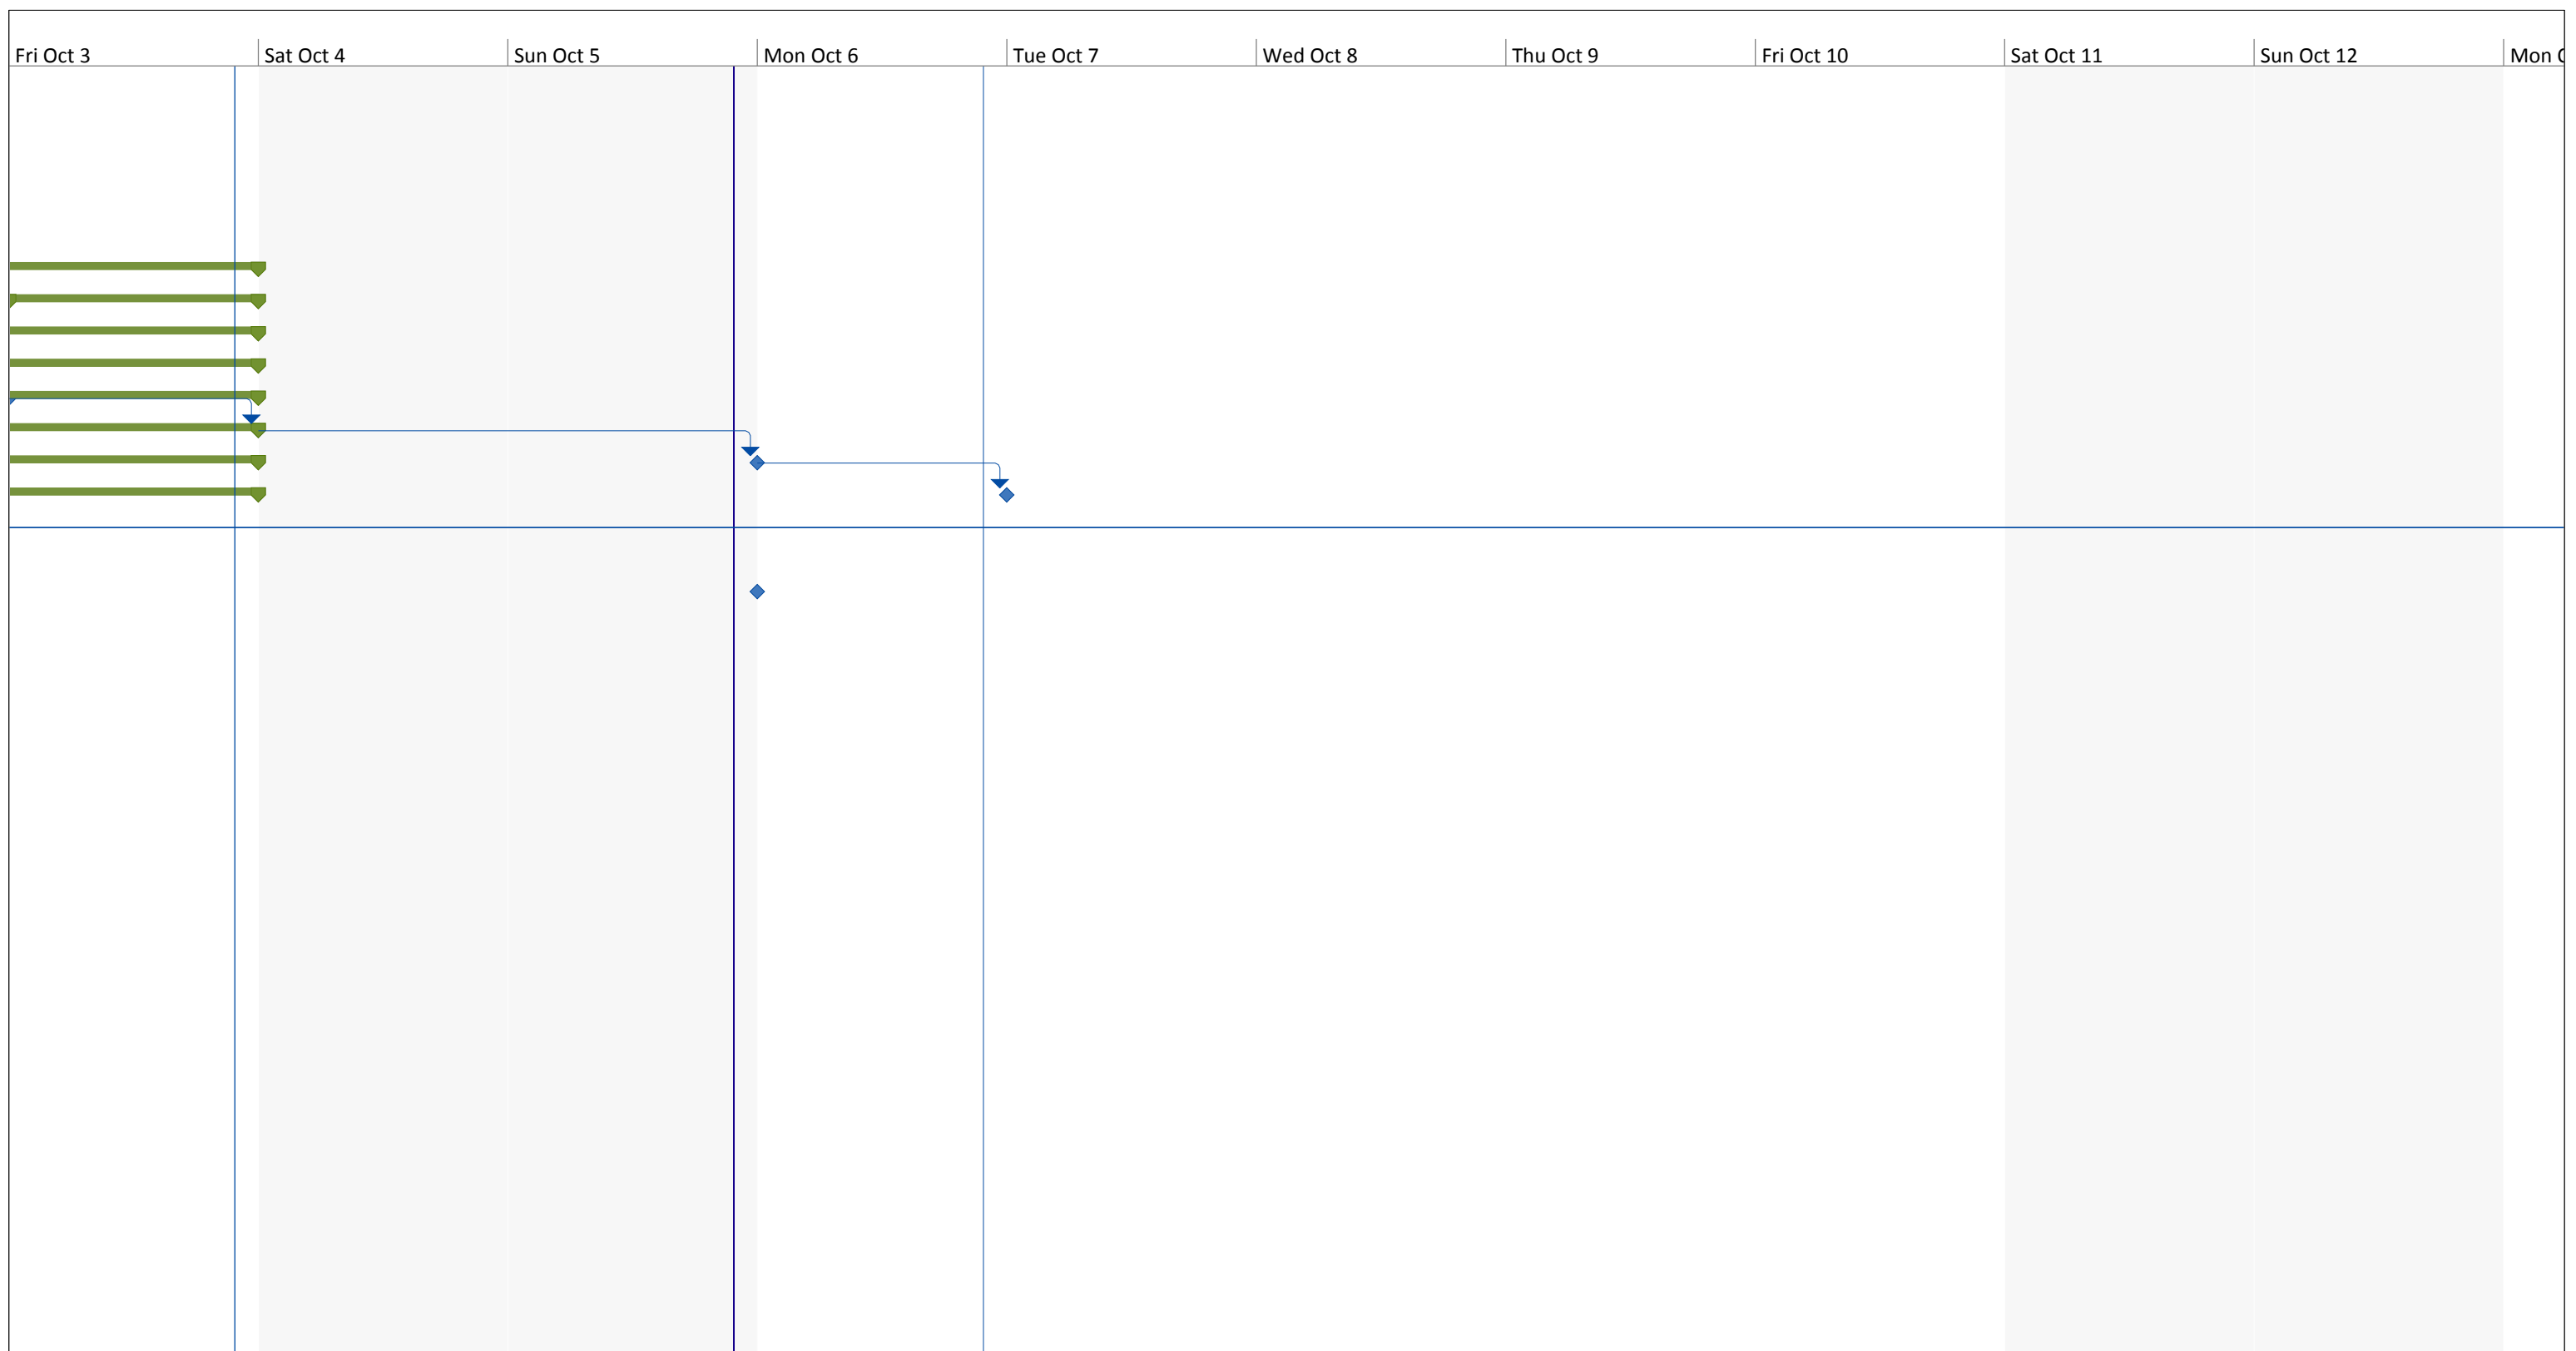











Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	




Project: MA_Integrated_Project_S
Date: Tue 9/30/14


Milestone	◆	Summary: Previous	▤	Placeholder Start: Current	▤	Inactive Milestone: Previous	◇
Task: Previous	▤	Summary: Current	▤	Placeholder Finish: Previous	▤	Inactive Milestone: Current	◇
Task: Current	▤	Placeholder Duration: Previous	▤	Placeholder Finish: Current	▤	Inactive Summary: Previous	▤
Milestone: Previous	◆	Placeholder Duration: Current	▤	Inactive Task: Previous	▤	Inactive Summary: Current	▤
Milestone: Current	◆	Placeholder Start: Previous	▤	Inactive Task: Current	▤	Manual Progress	▤





Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

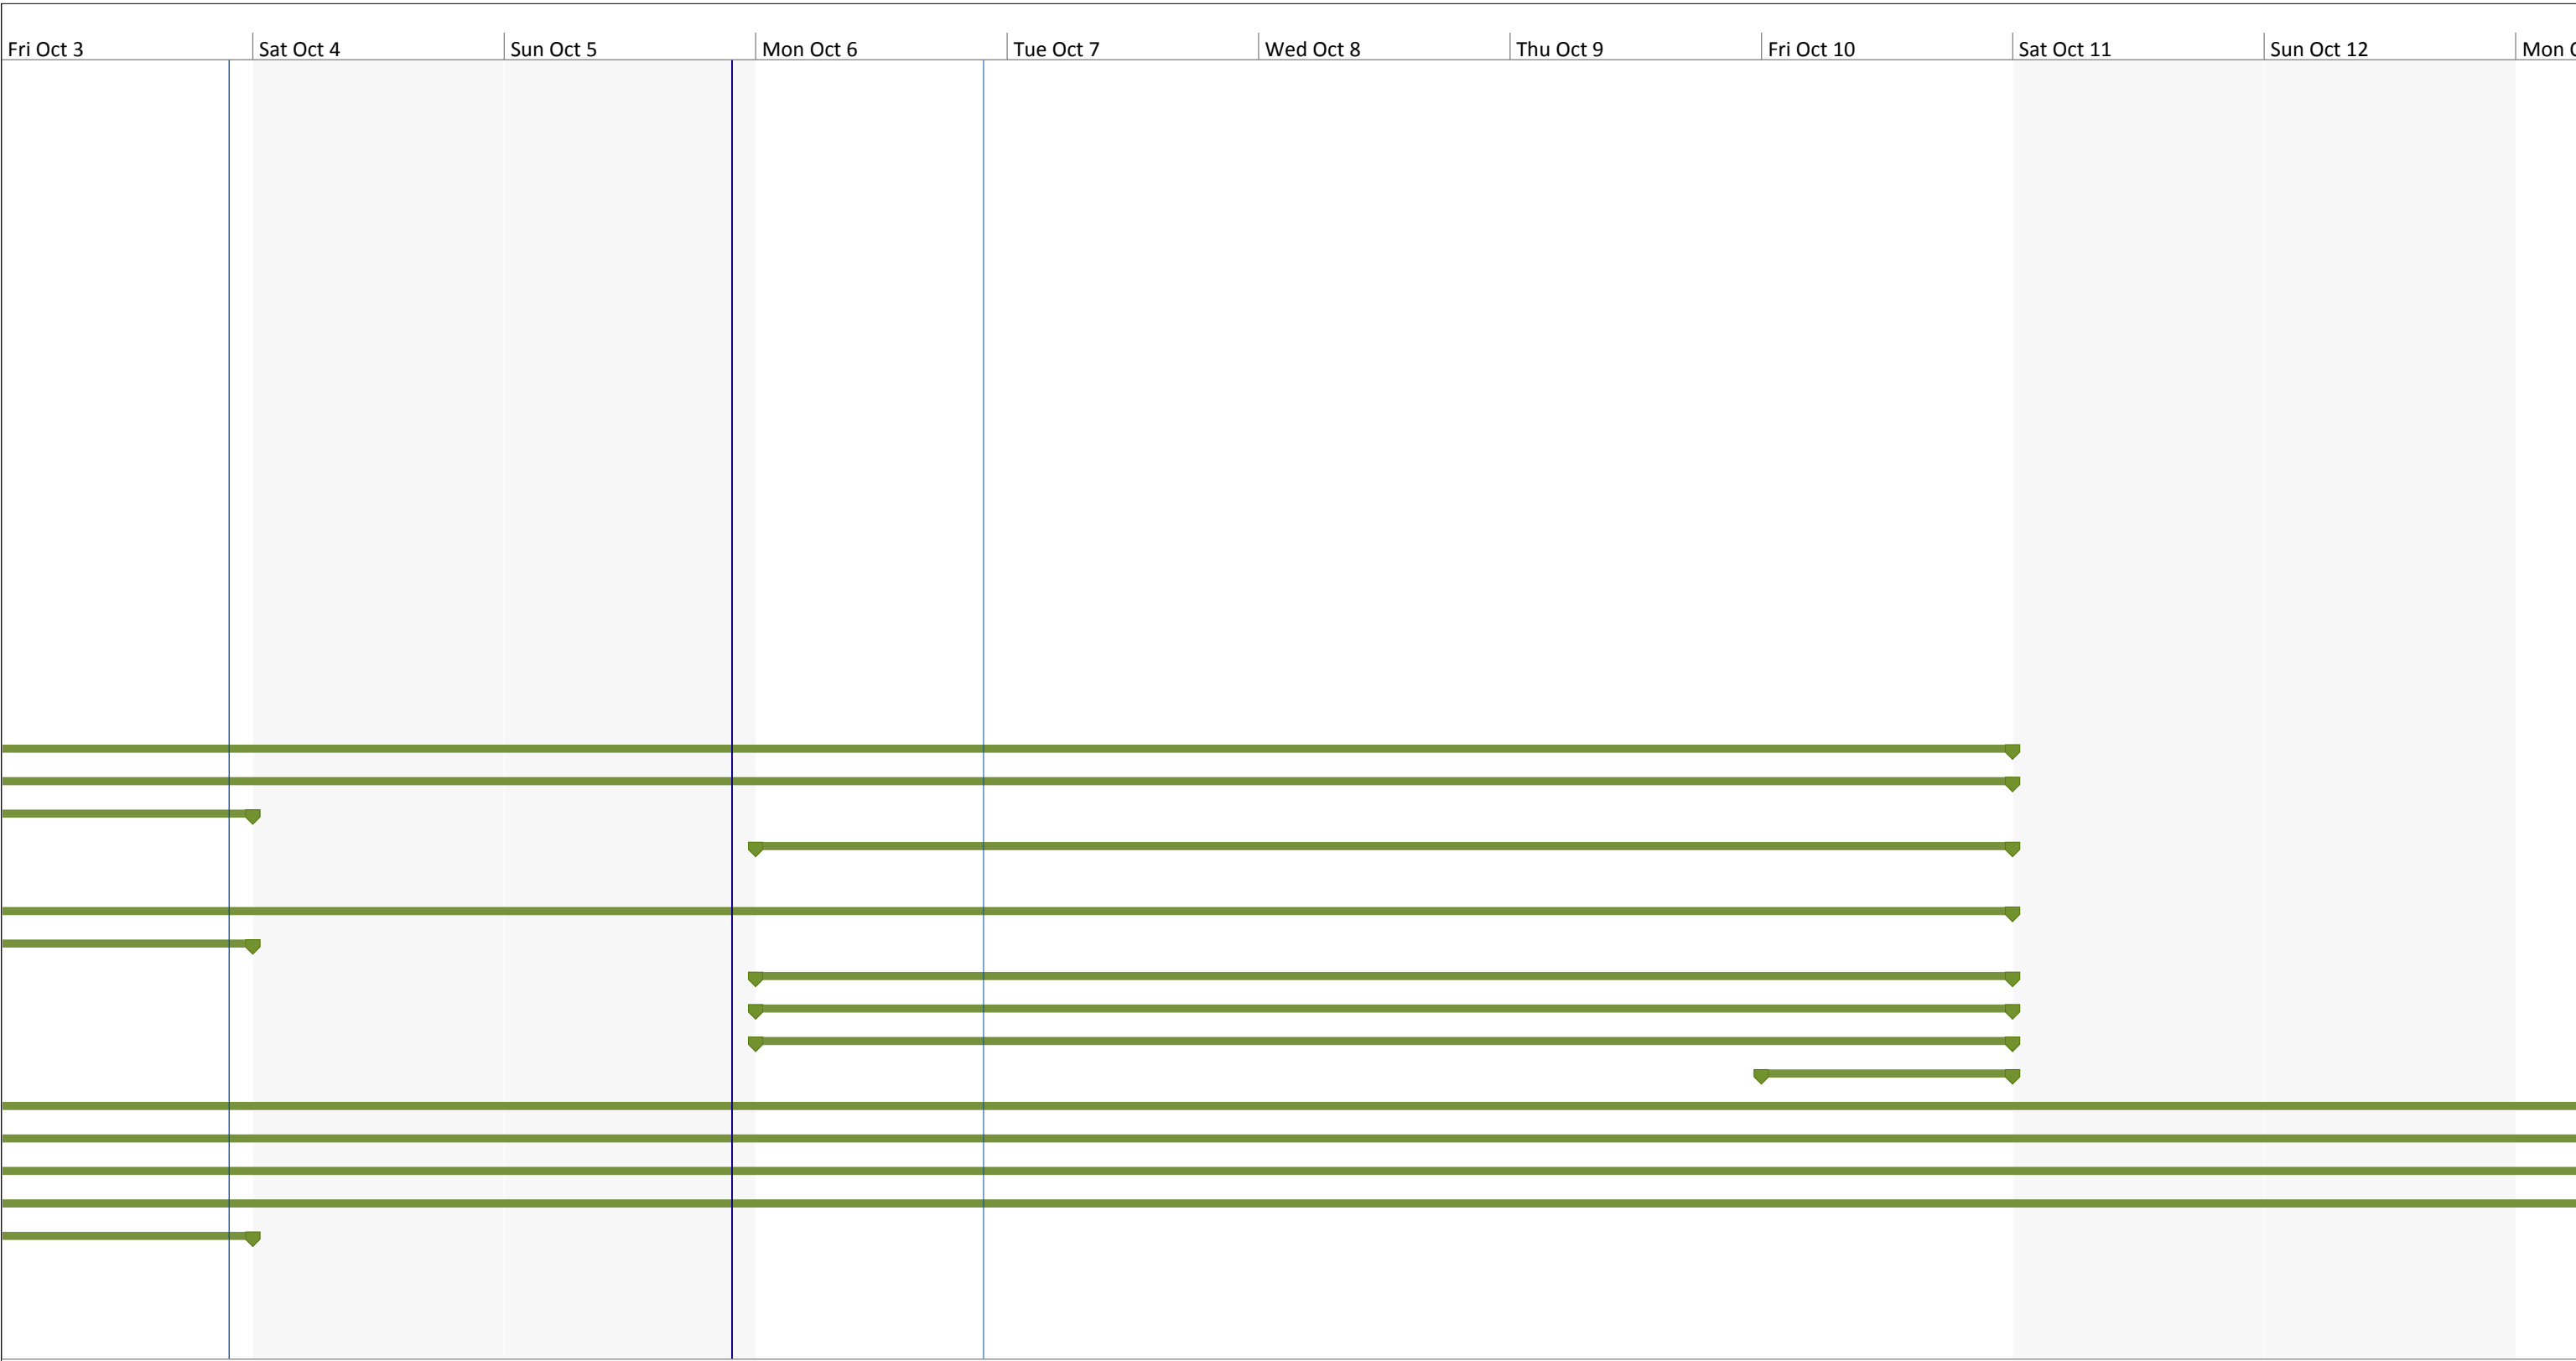






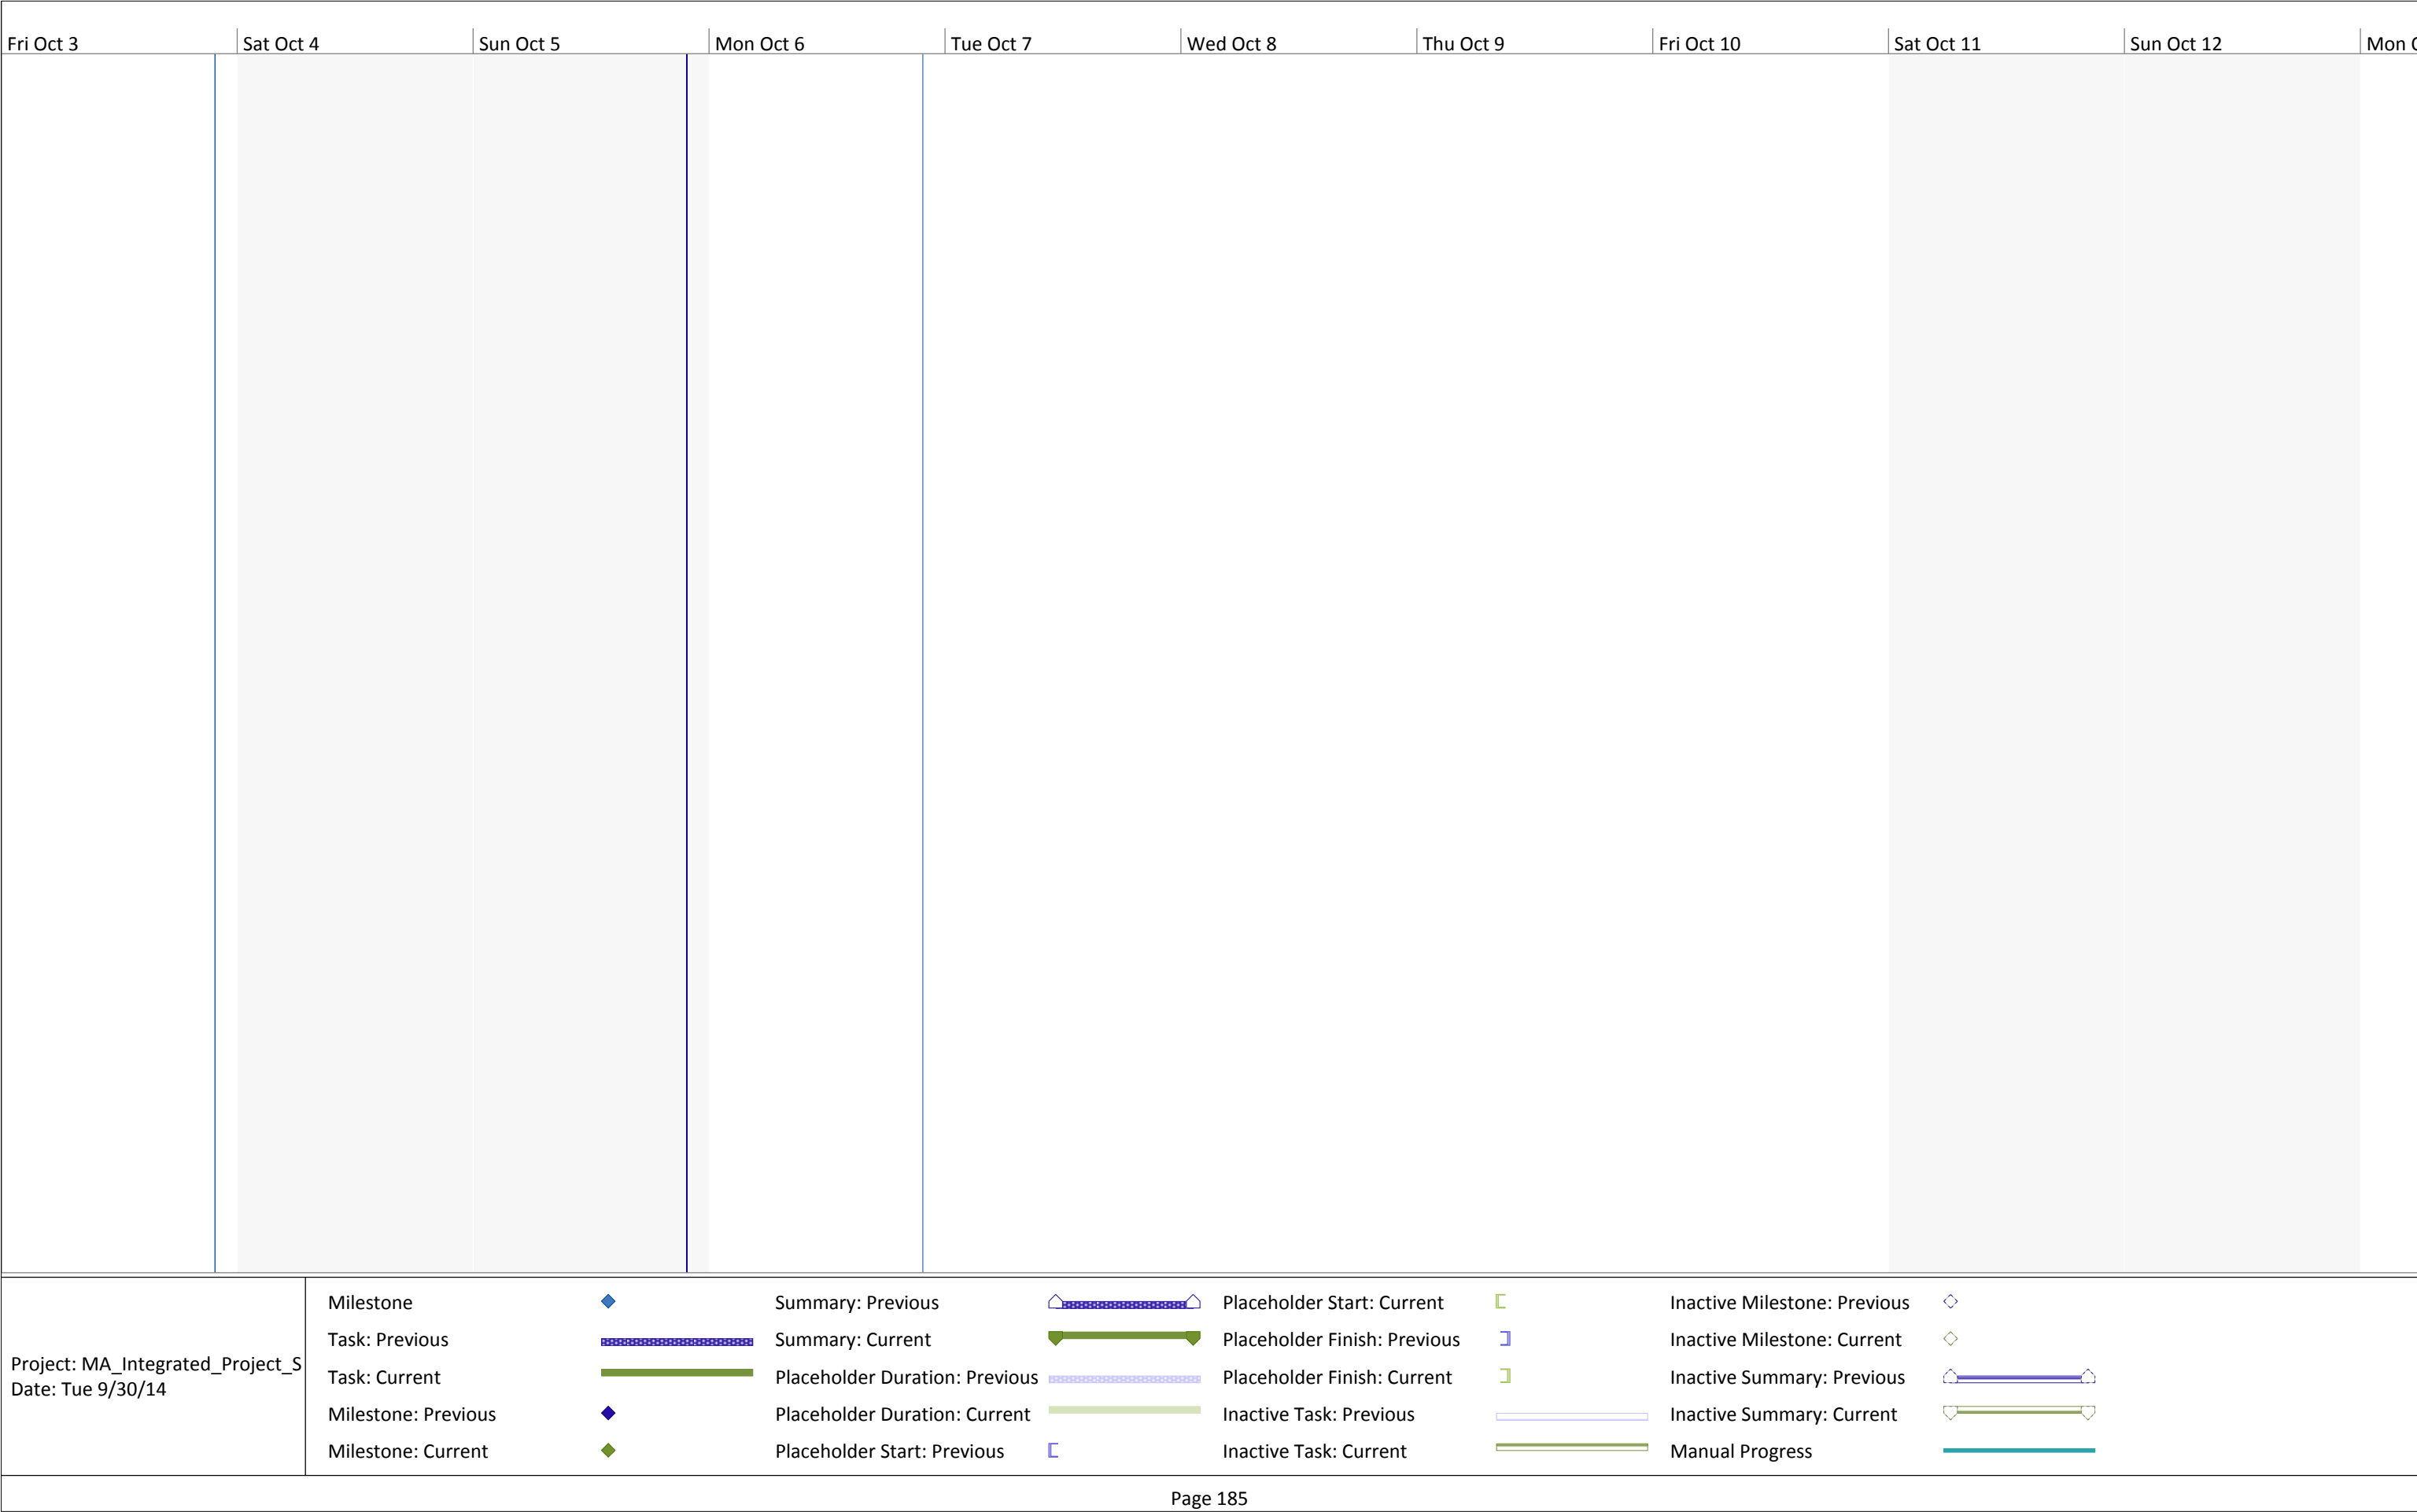

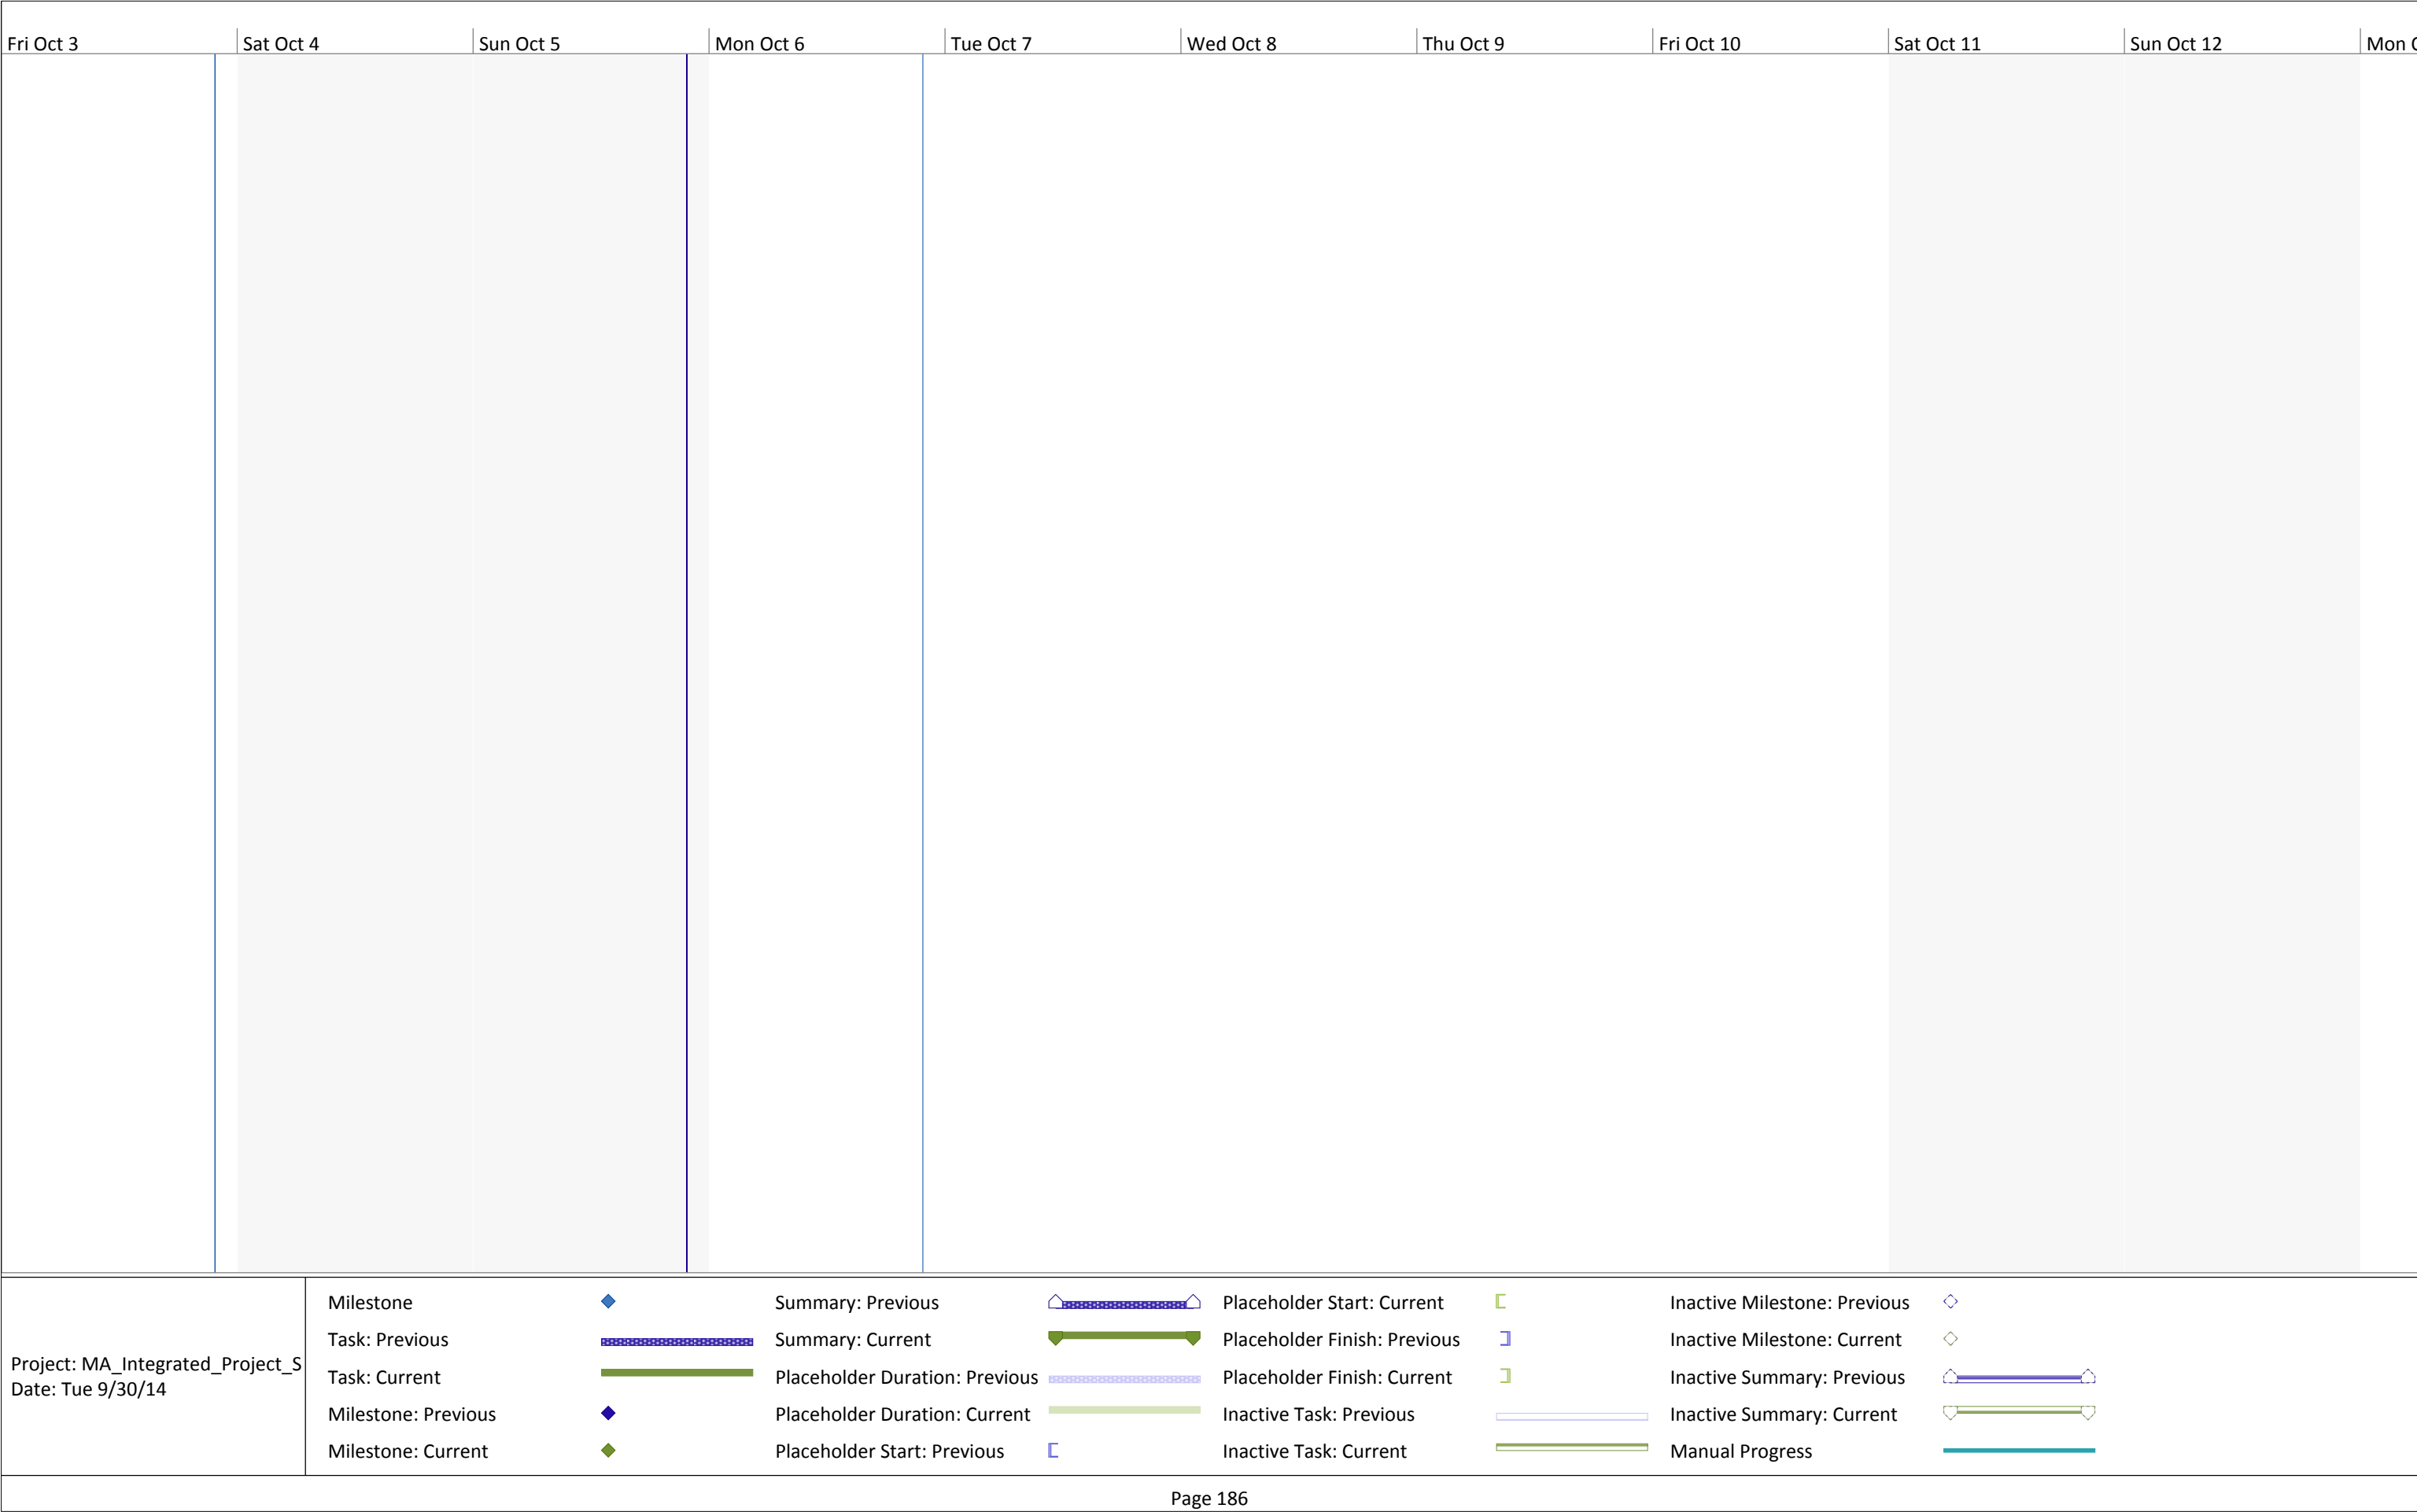

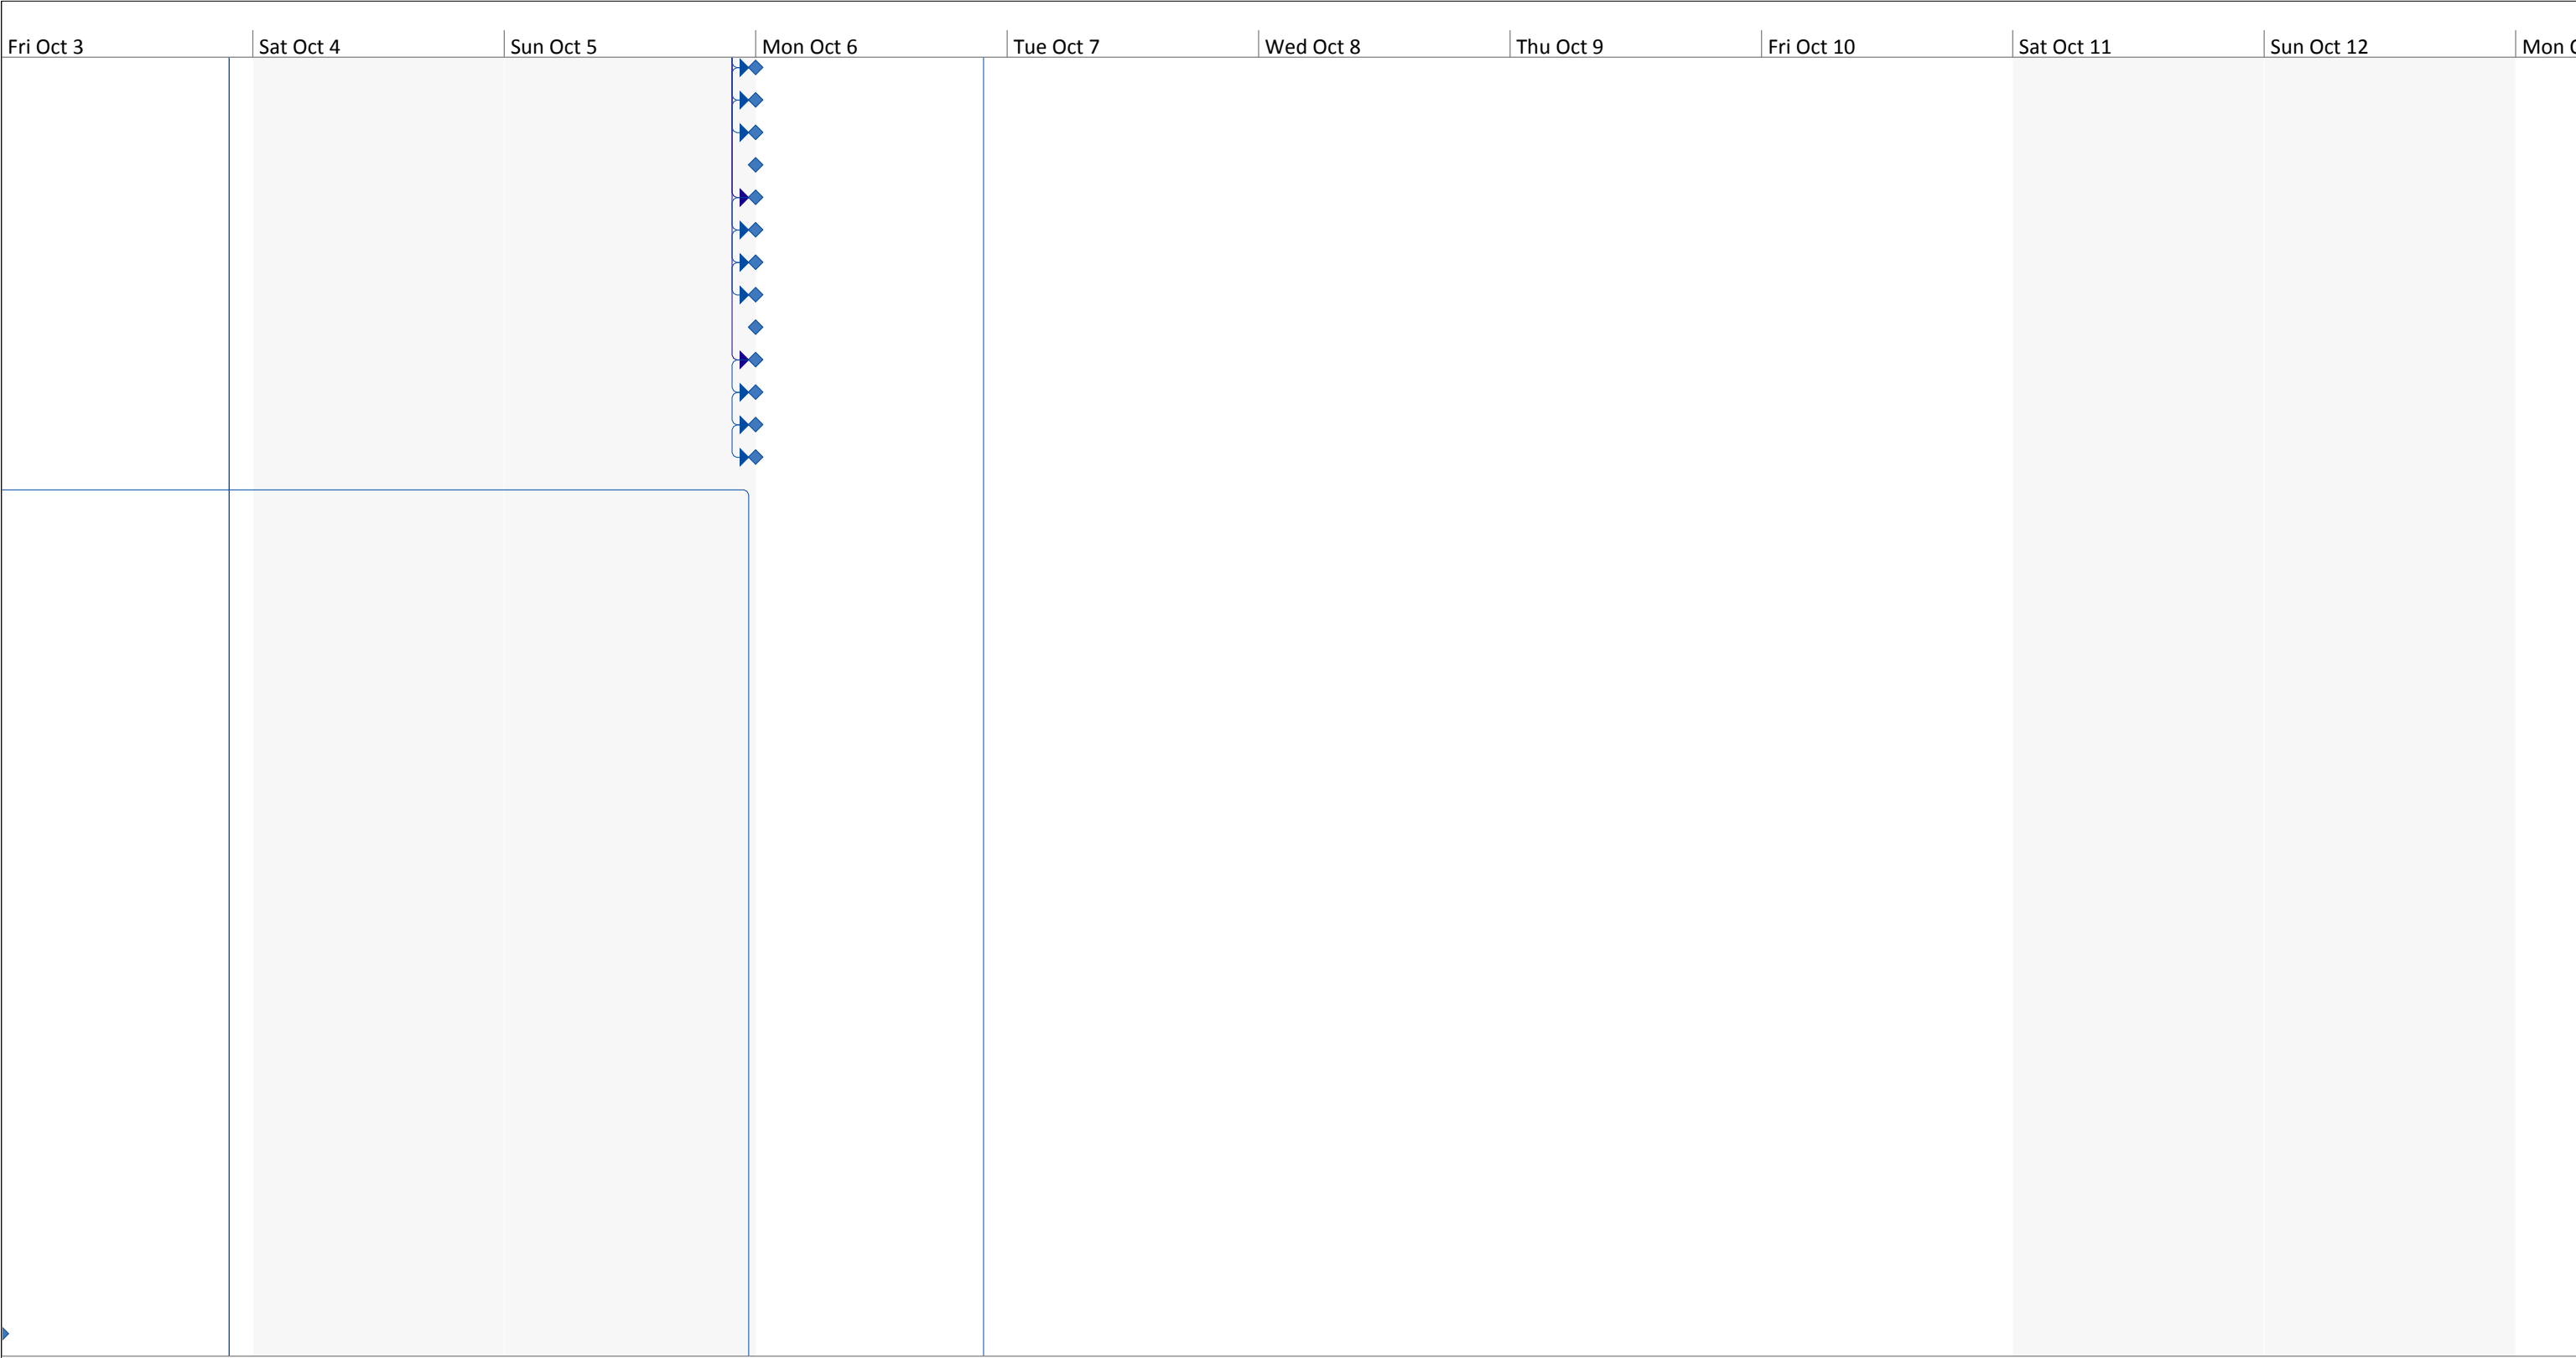











Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone	◆	Summary: Previous	▤	Placeholder Start: Current	▤	Inactive Milestone: Previous	◇
	Task: Previous	▤	Summary: Current	▤	Placeholder Finish: Previous	▤	Inactive Milestone: Current	◇
	Task: Current	▤	Placeholder Duration: Previous	▤	Placeholder Finish: Current	▤	Inactive Summary: Previous	▤
	Milestone: Previous	◆	Placeholder Duration: Current	▤	Inactive Task: Previous	▤	Inactive Summary: Current	▤
	Milestone: Current	◆	Placeholder Start: Previous	▤	Inactive Task: Current	▤	Manual Progress	▤












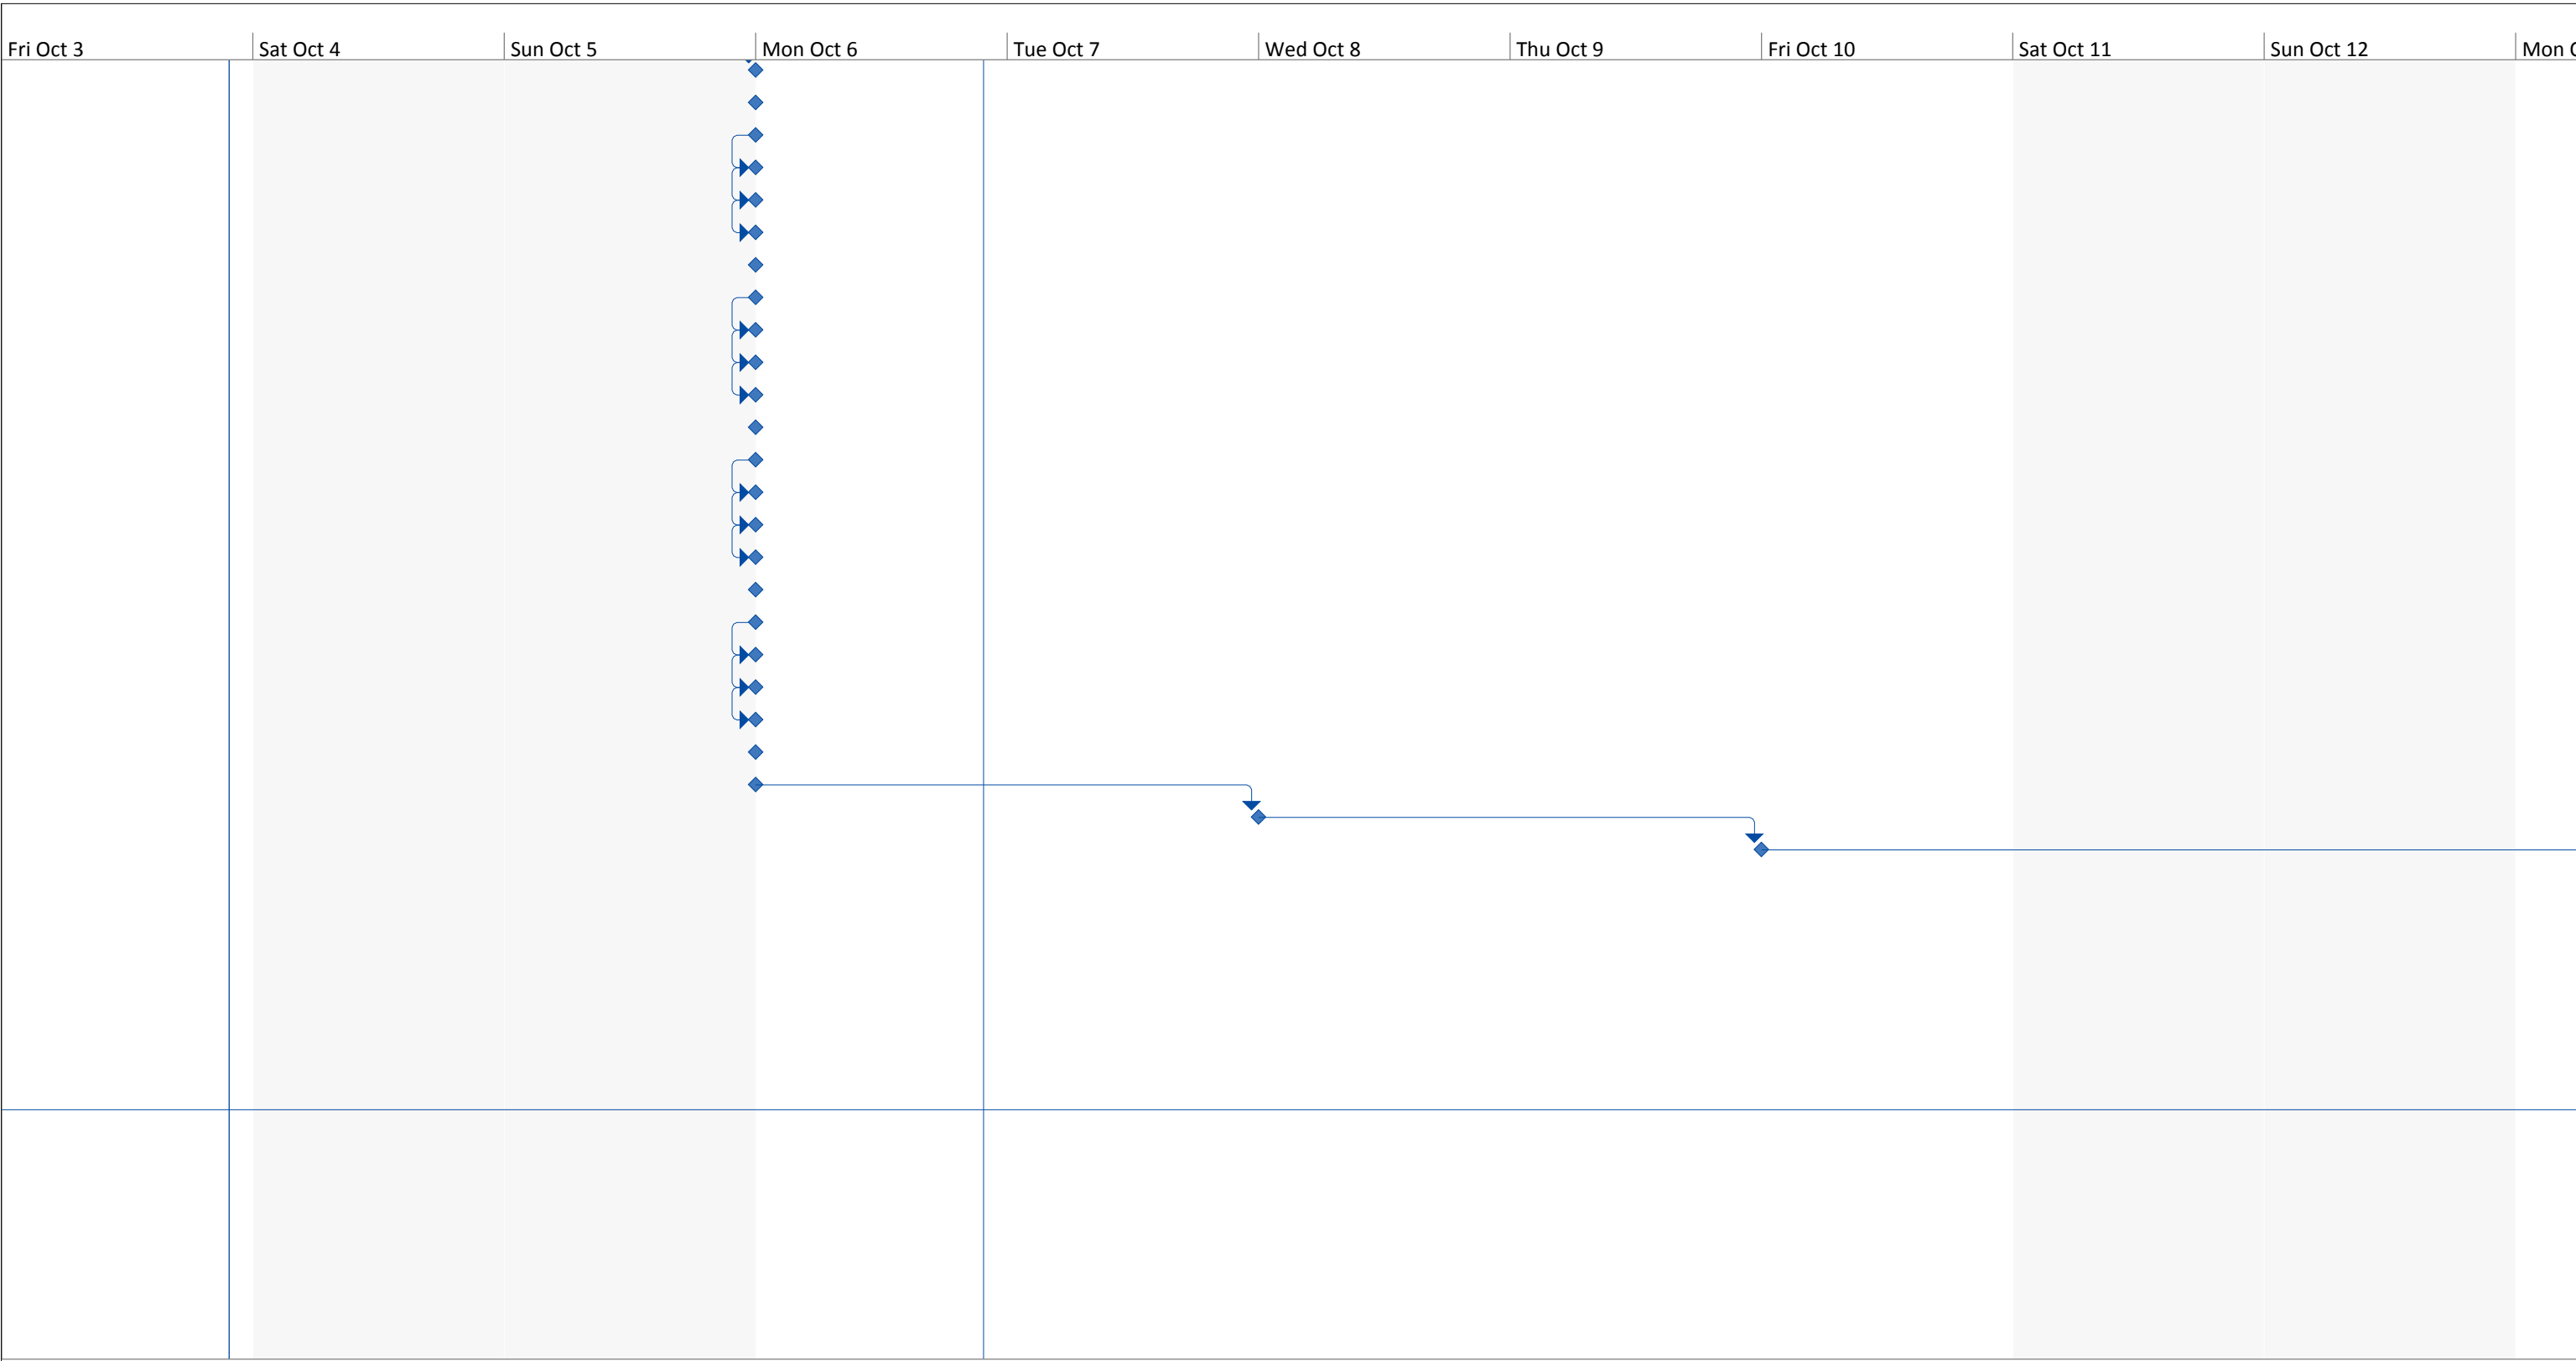



















Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	





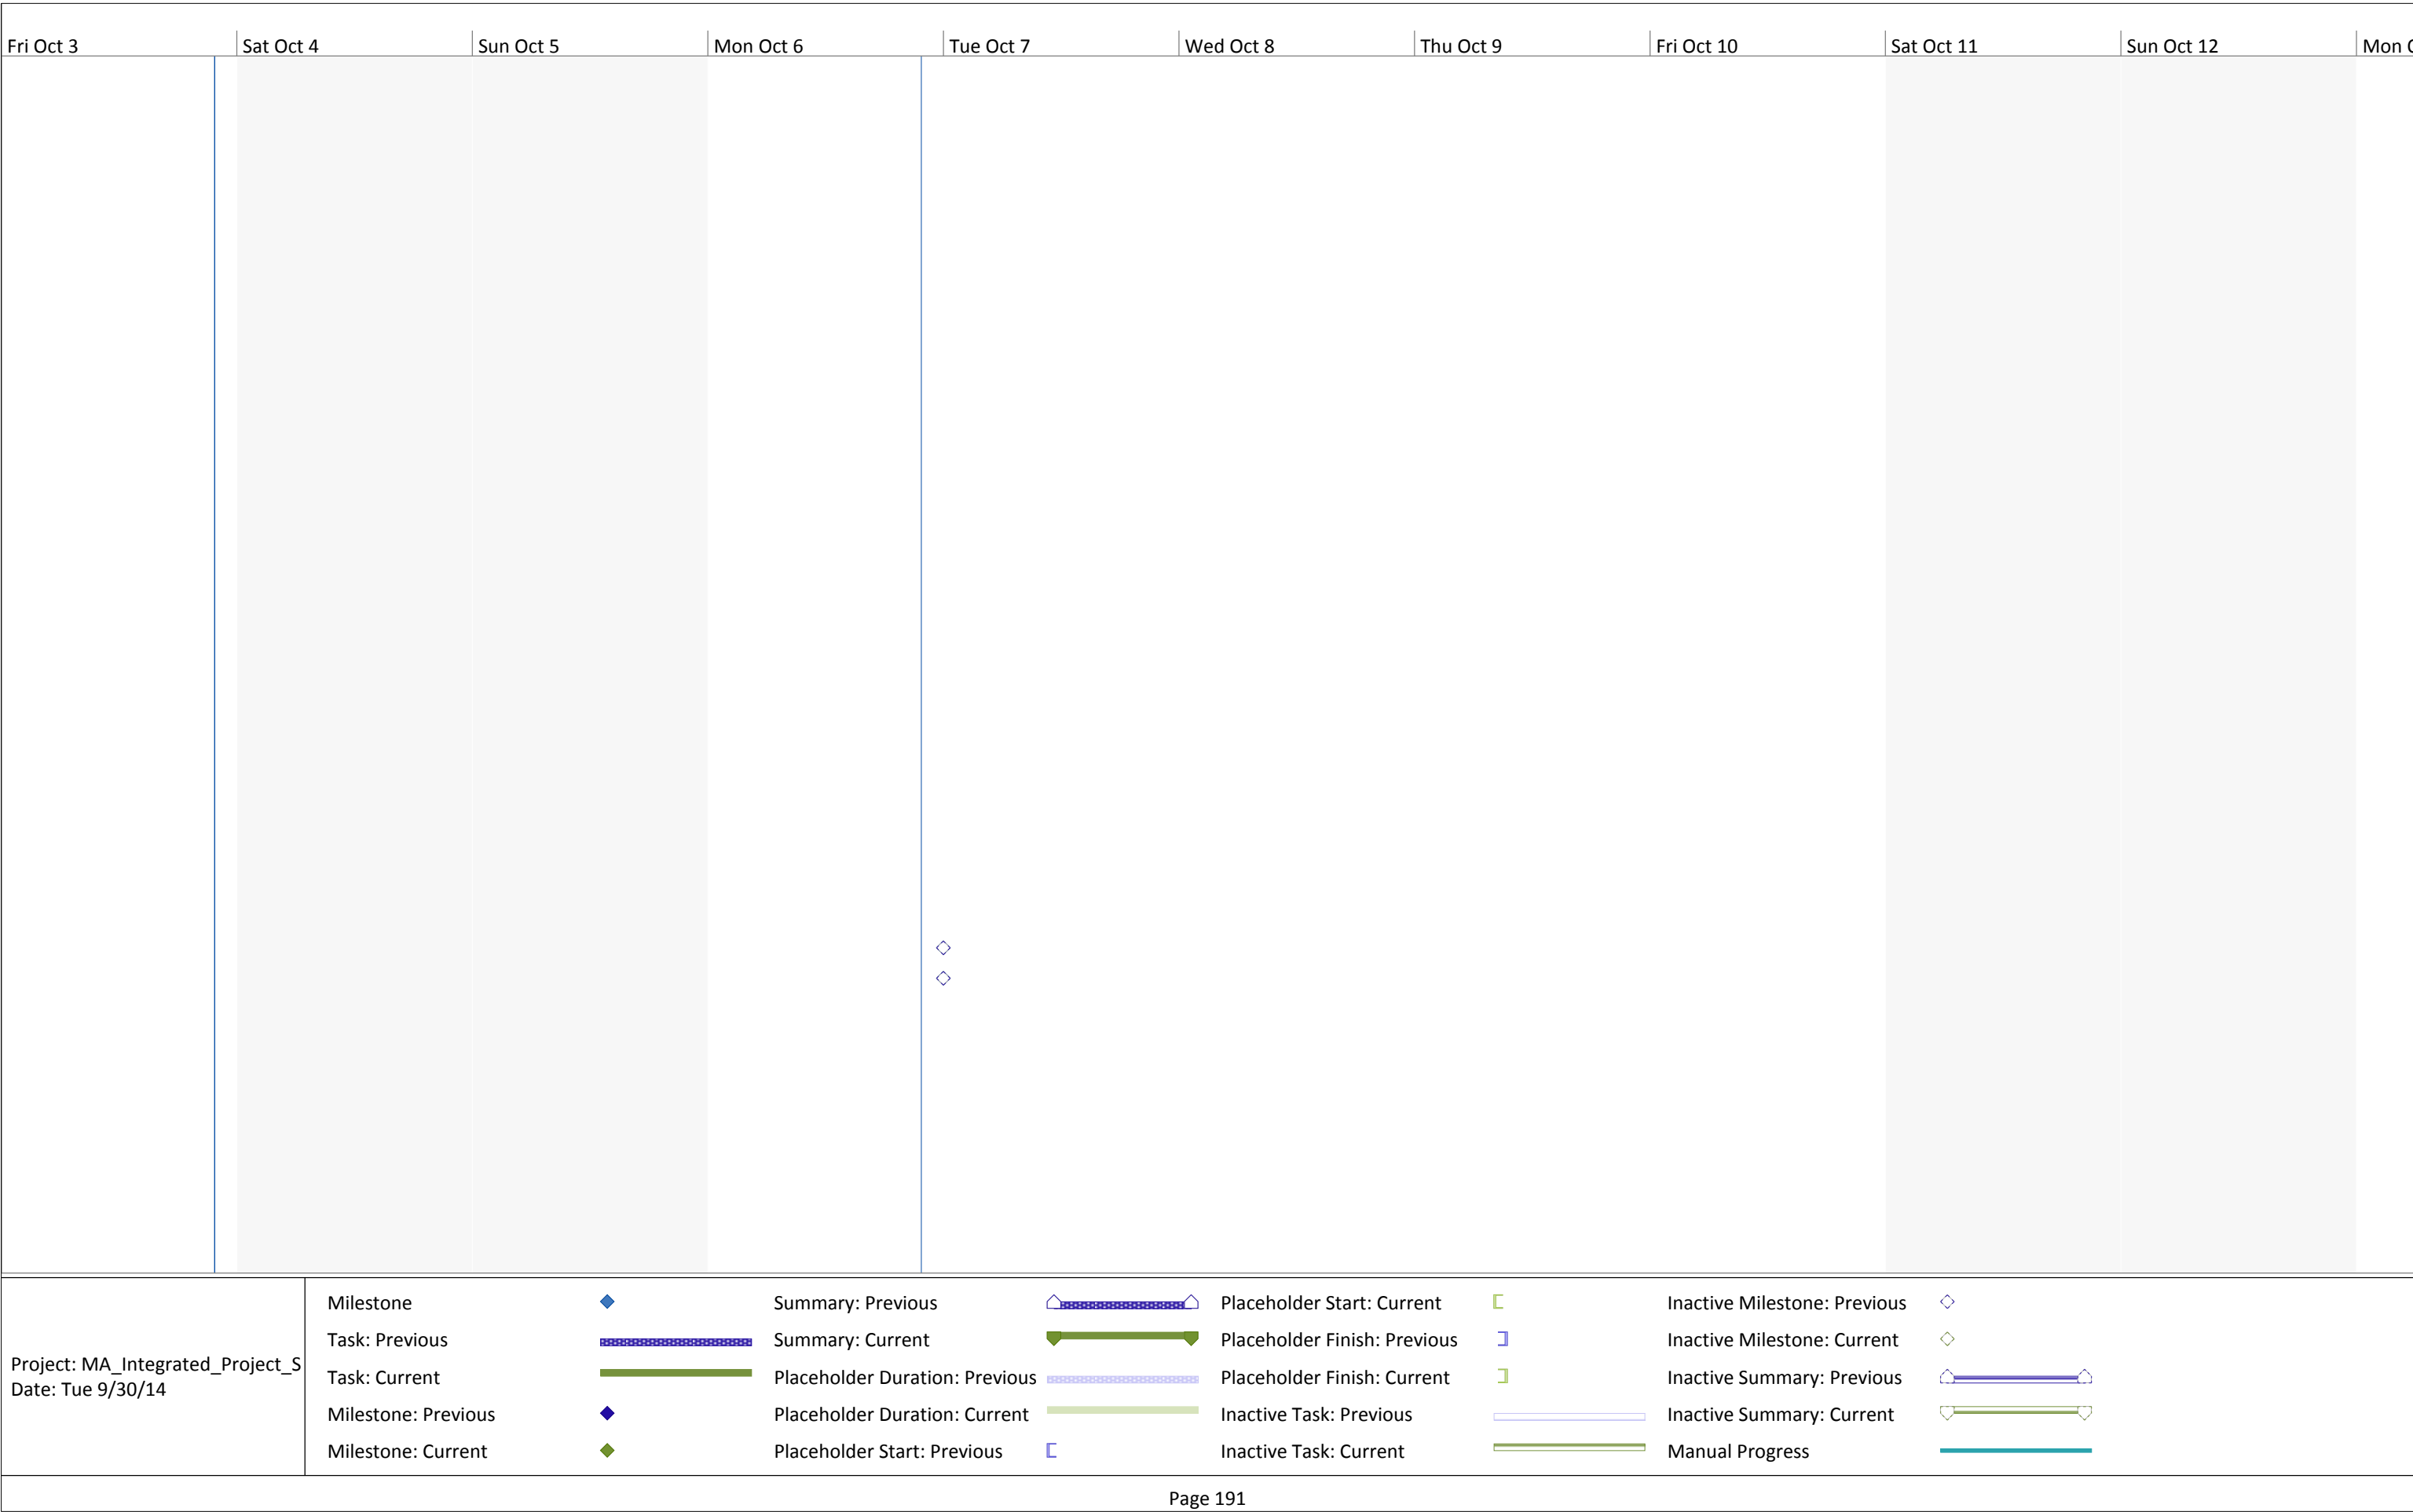



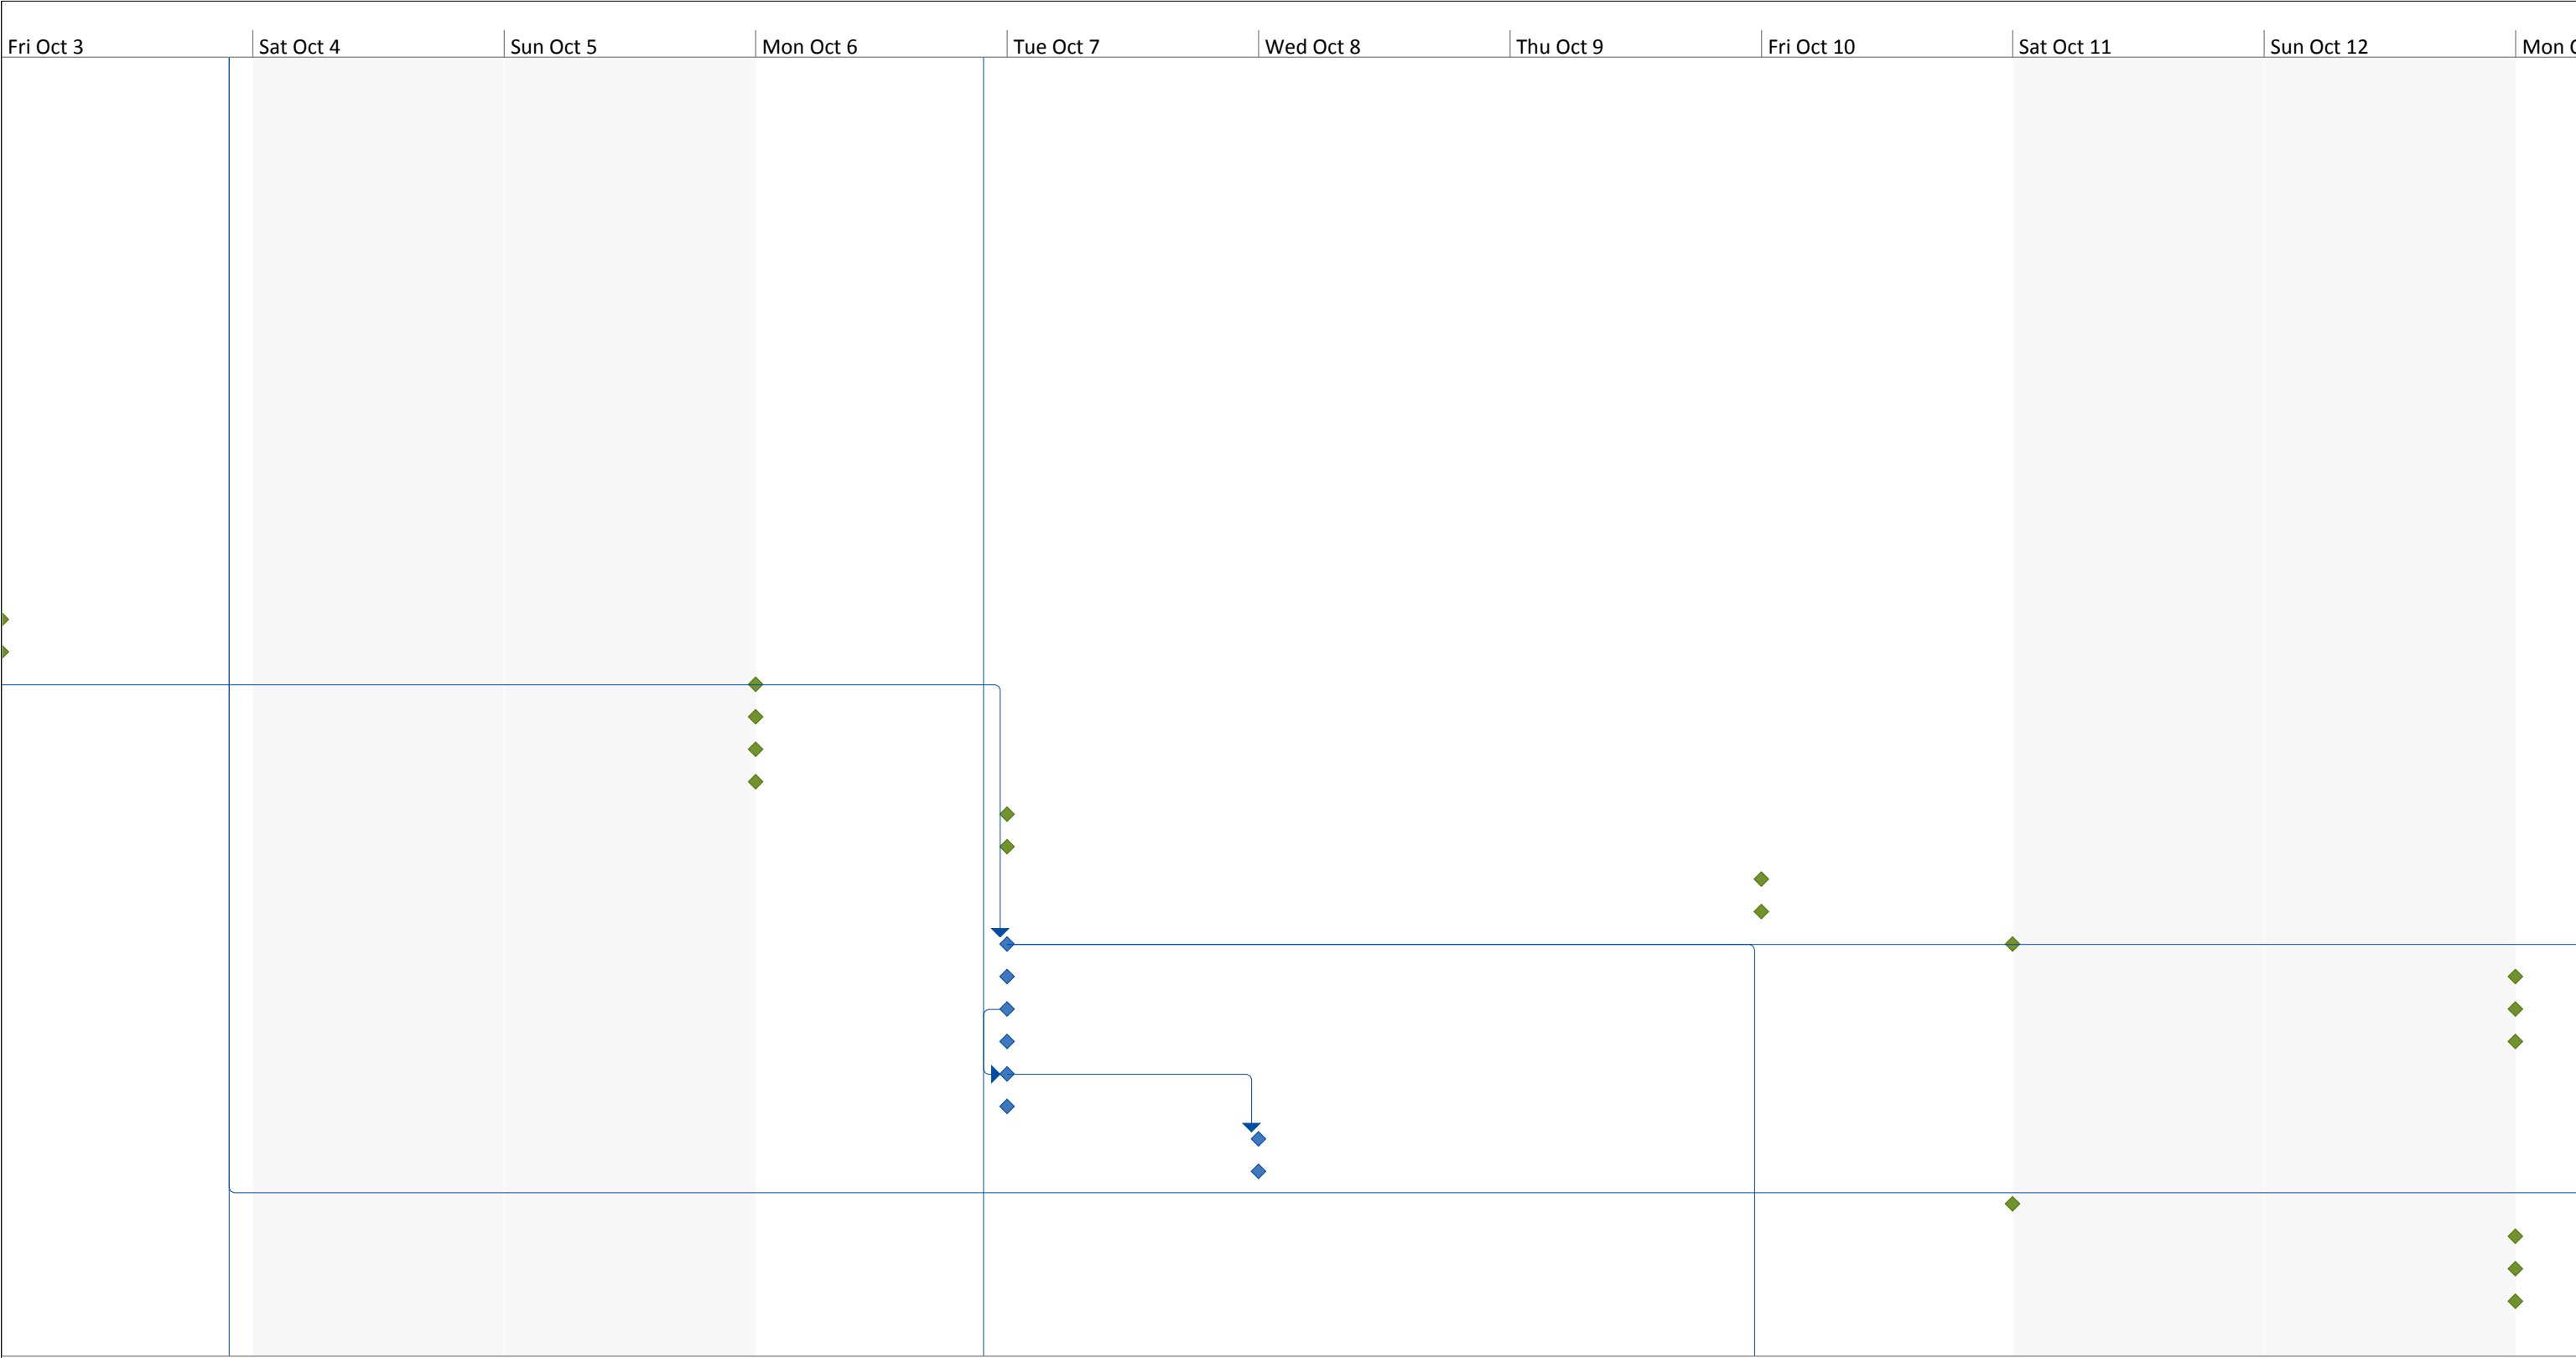













Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	
























Fri Oct 3		Sat Oct 4		Sun Oct 5		Mon Oct 6		Tue Oct 7		Wed Oct 8		Thu Oct 9		Fri Oct 10		Sat Oct 11		Sun Oct 12		Mon Oct 13	




Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	




Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

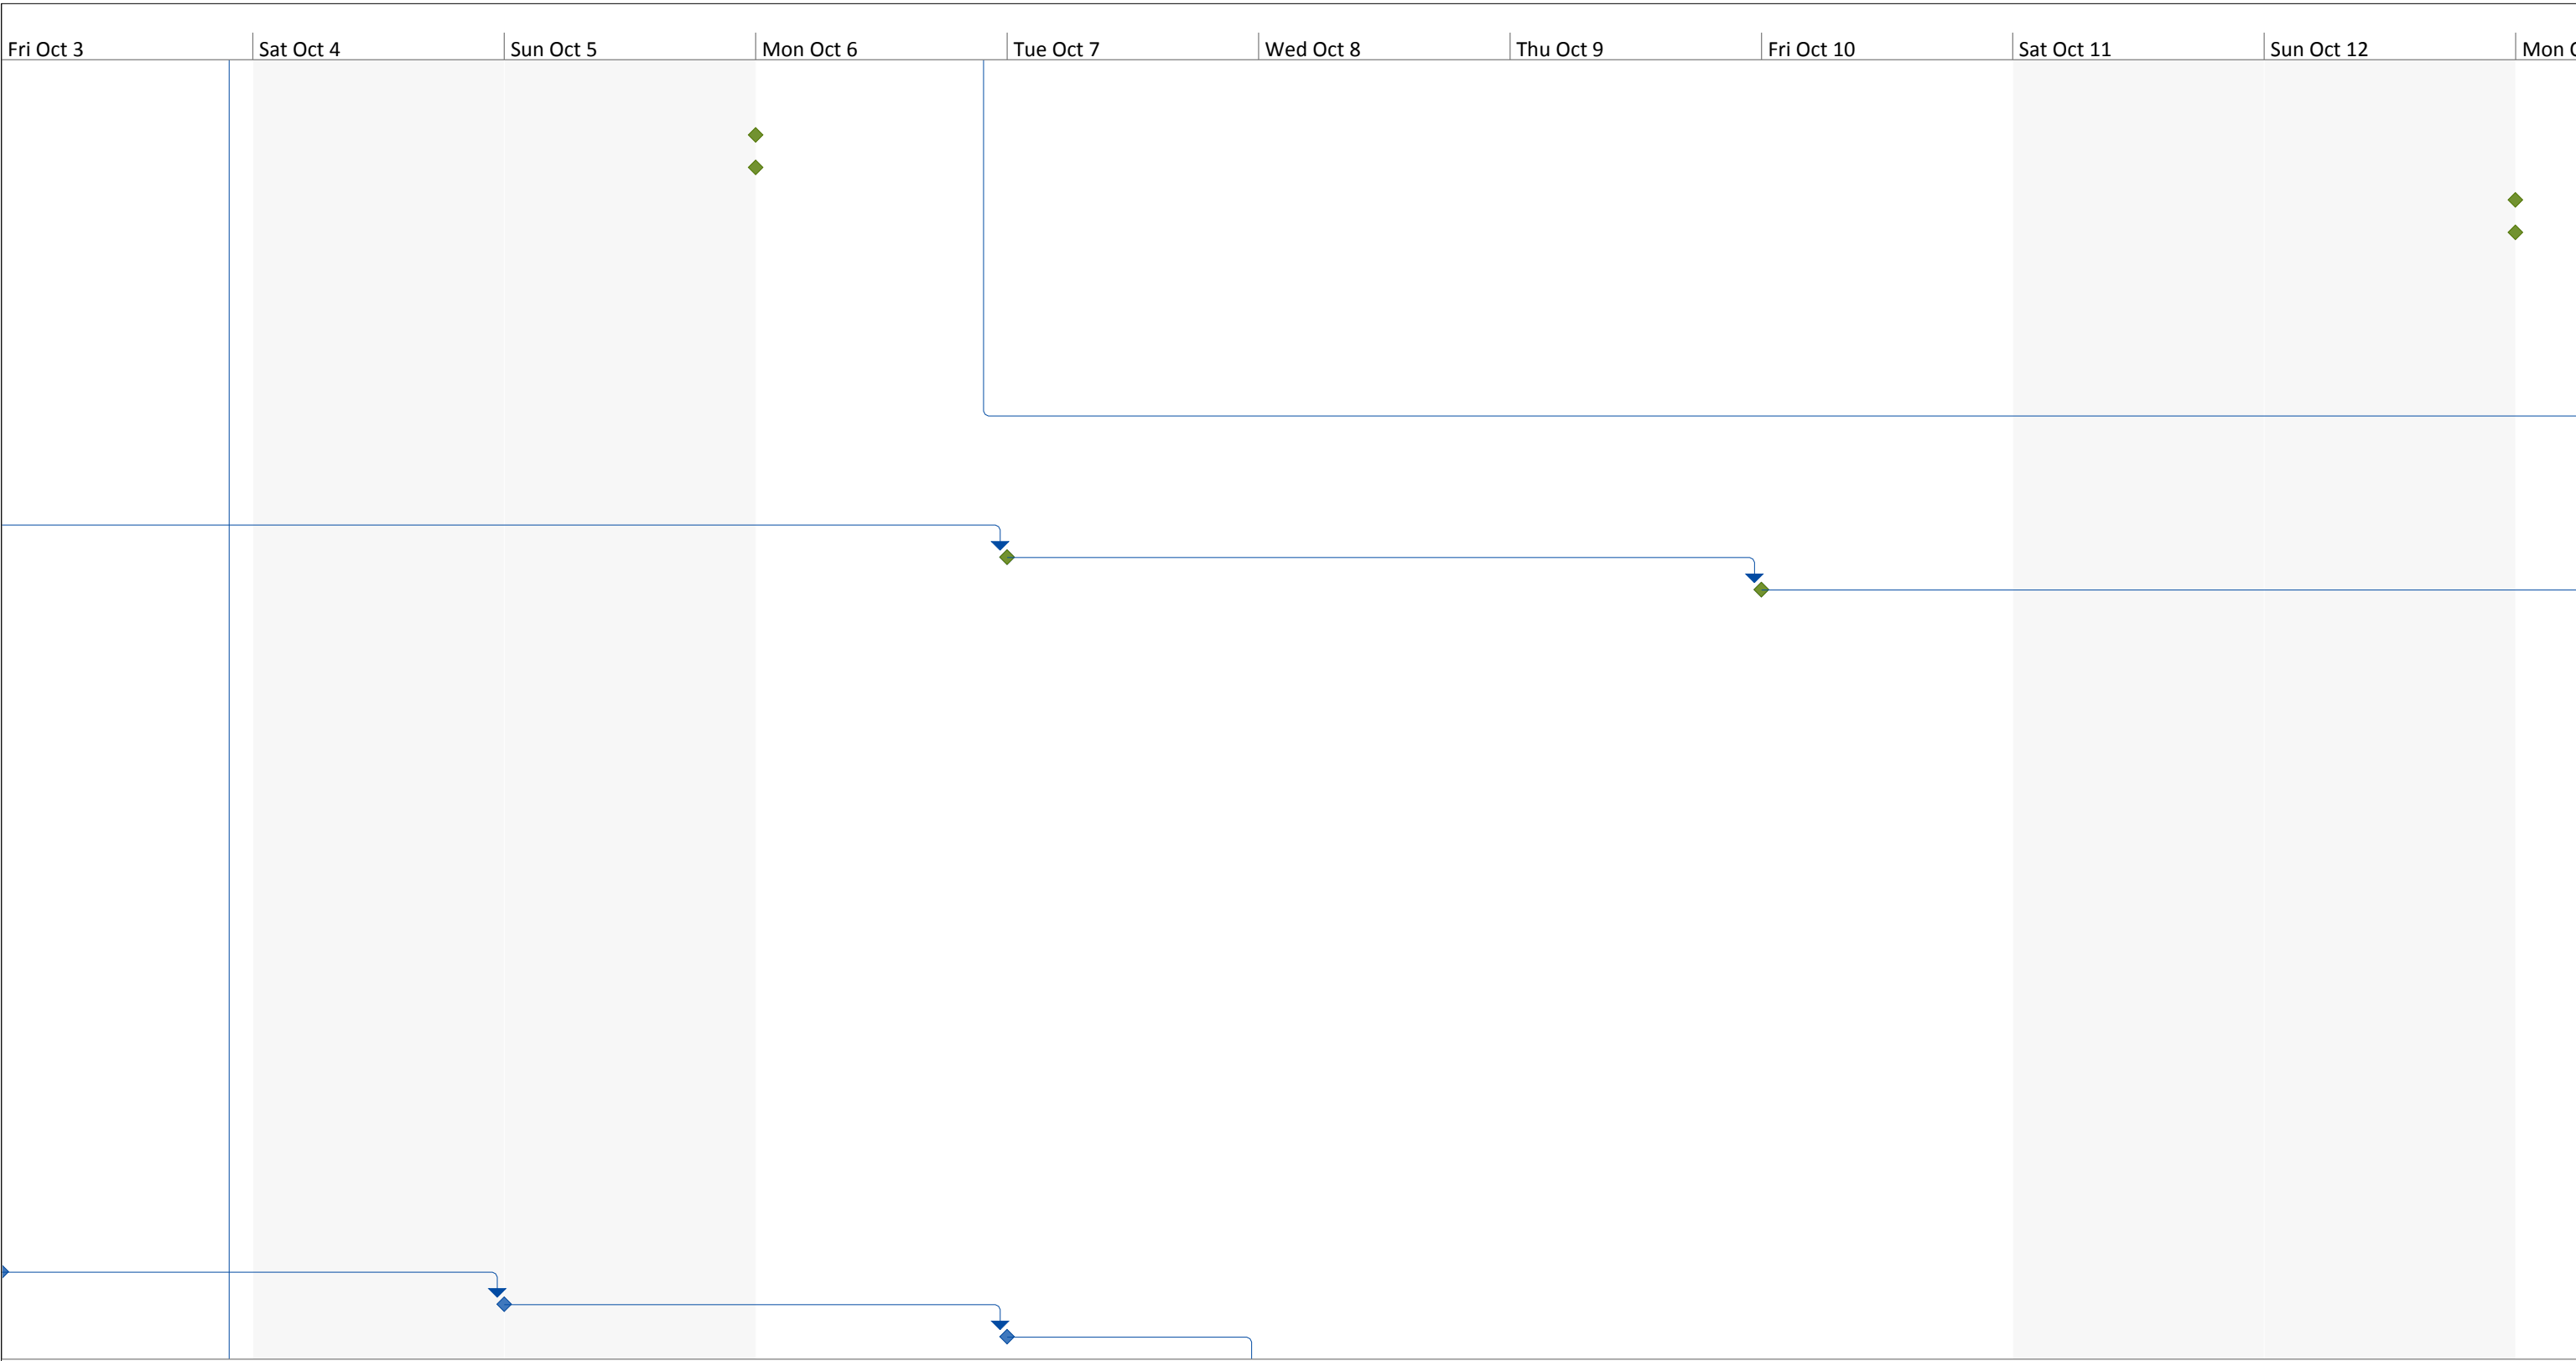


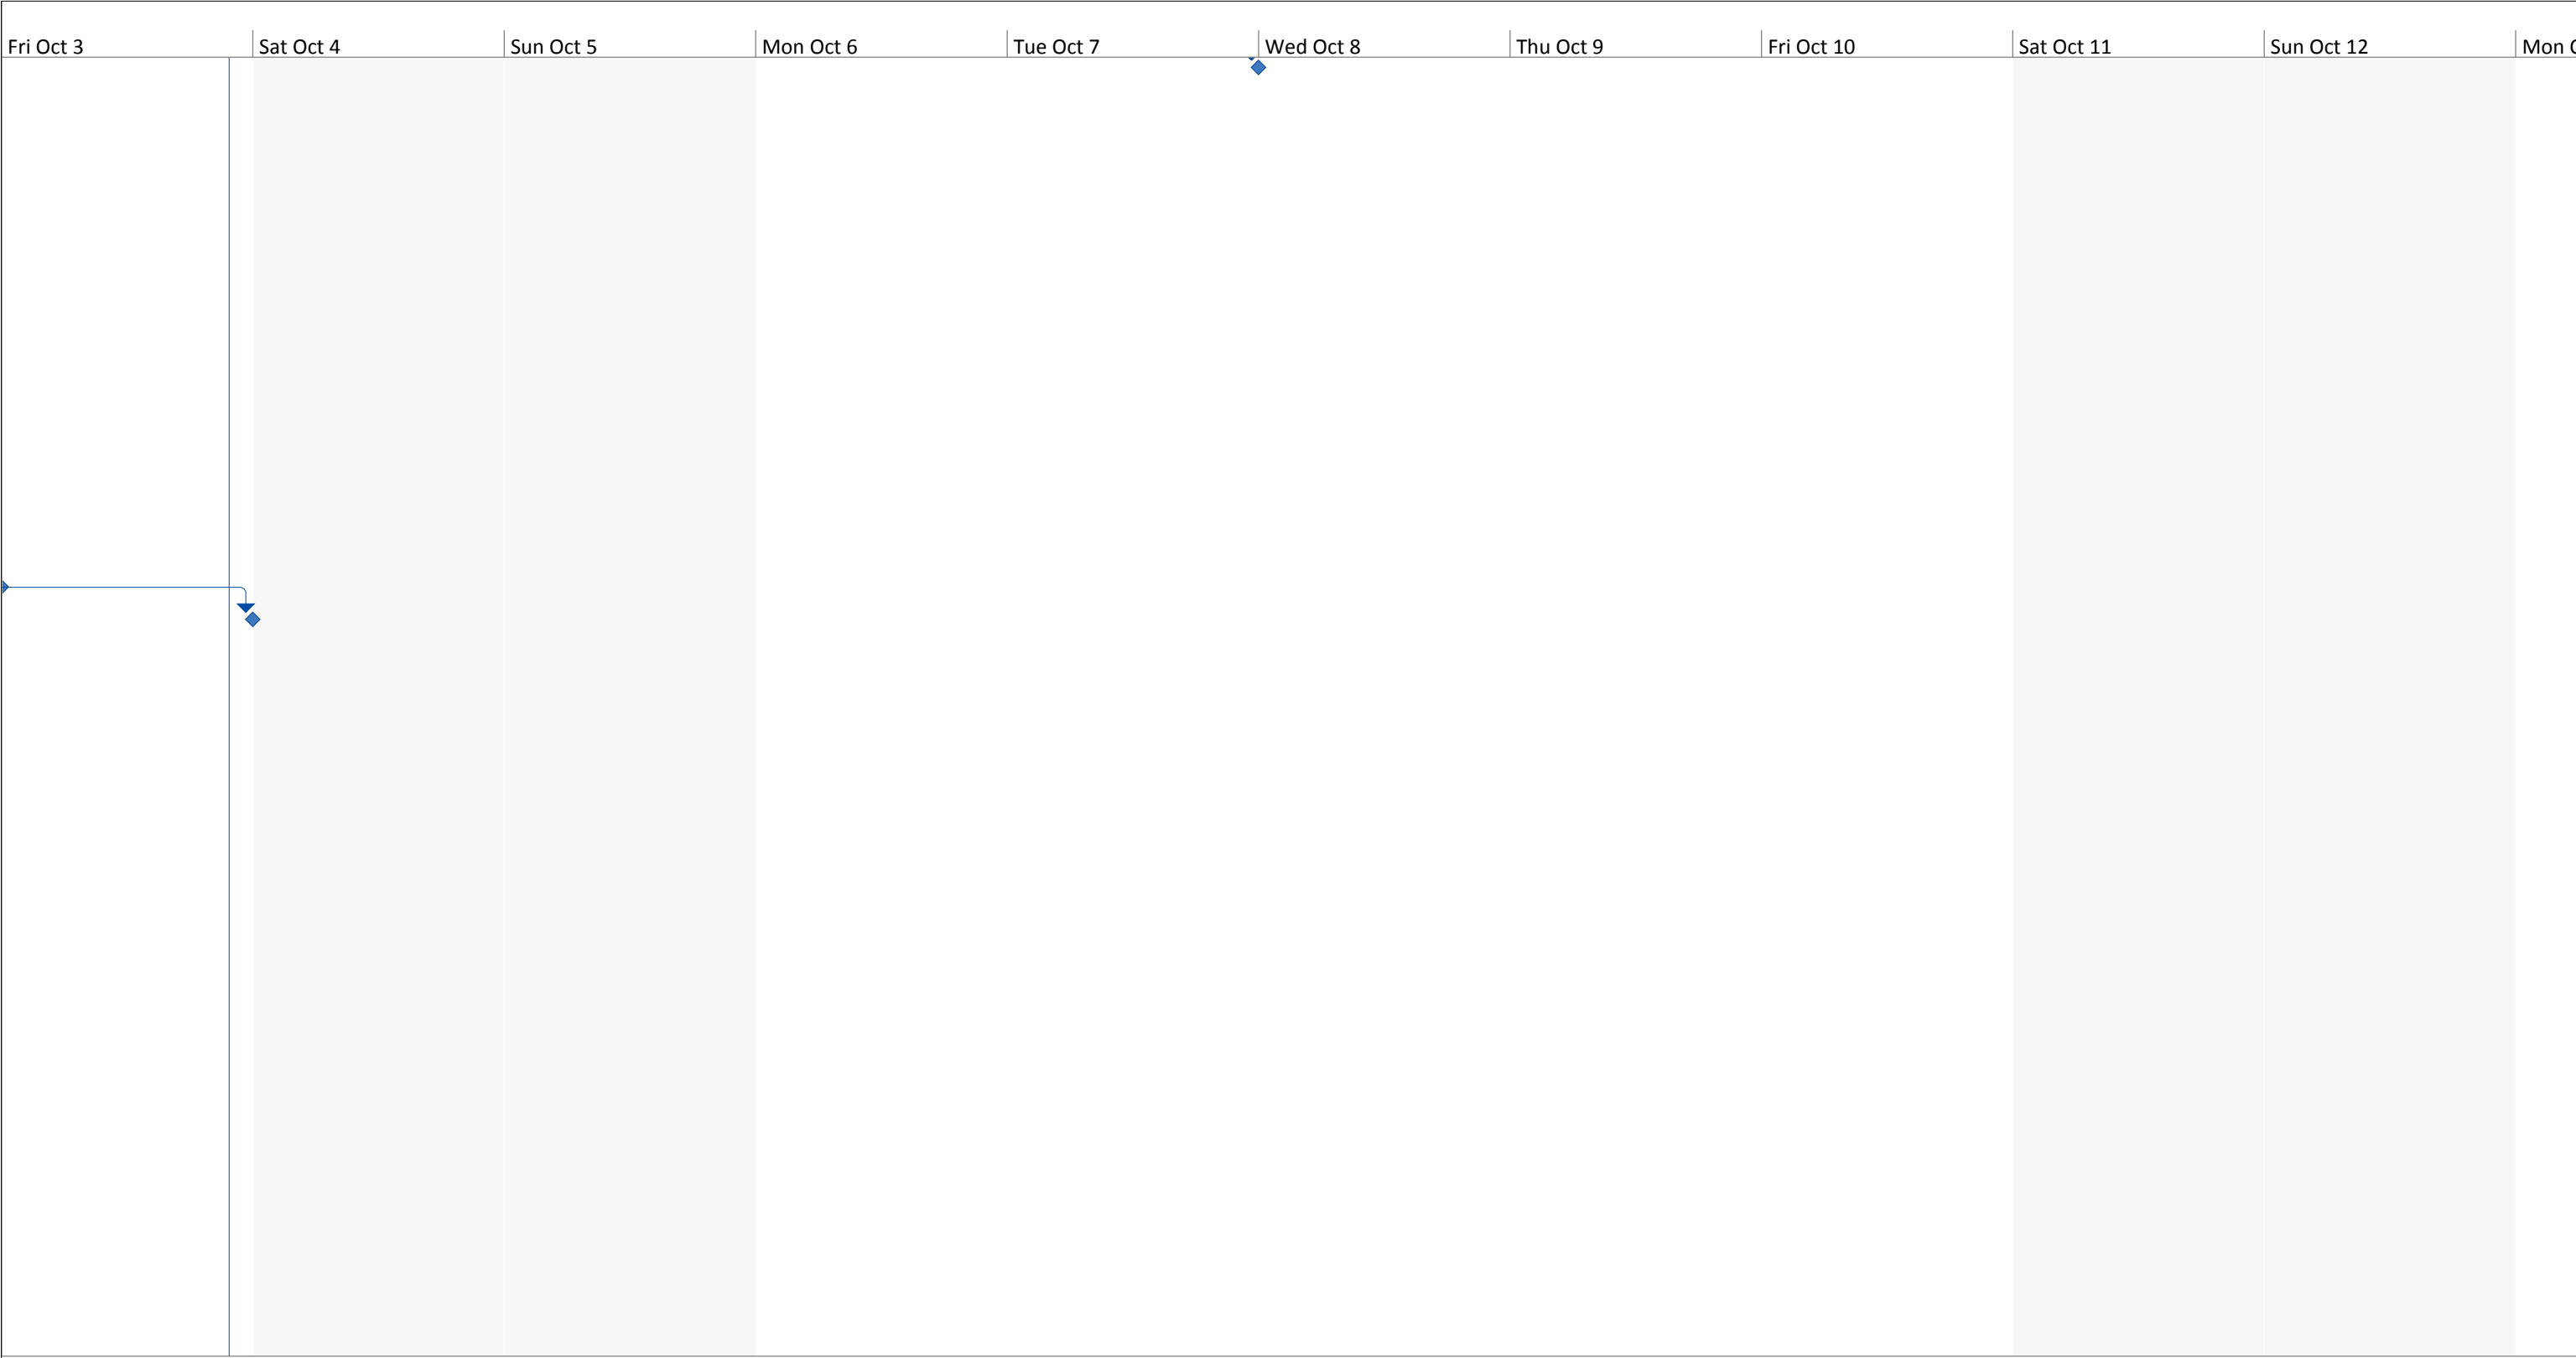



Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	




Fri Oct 3		Sat Oct 4	Sun Oct 5	Mon Oct 6	Tue Oct 7	Wed Oct 8	Thu Oct 9	Fri Oct 10	Sat Oct 11	Sun Oct 12	Mon Oct 13

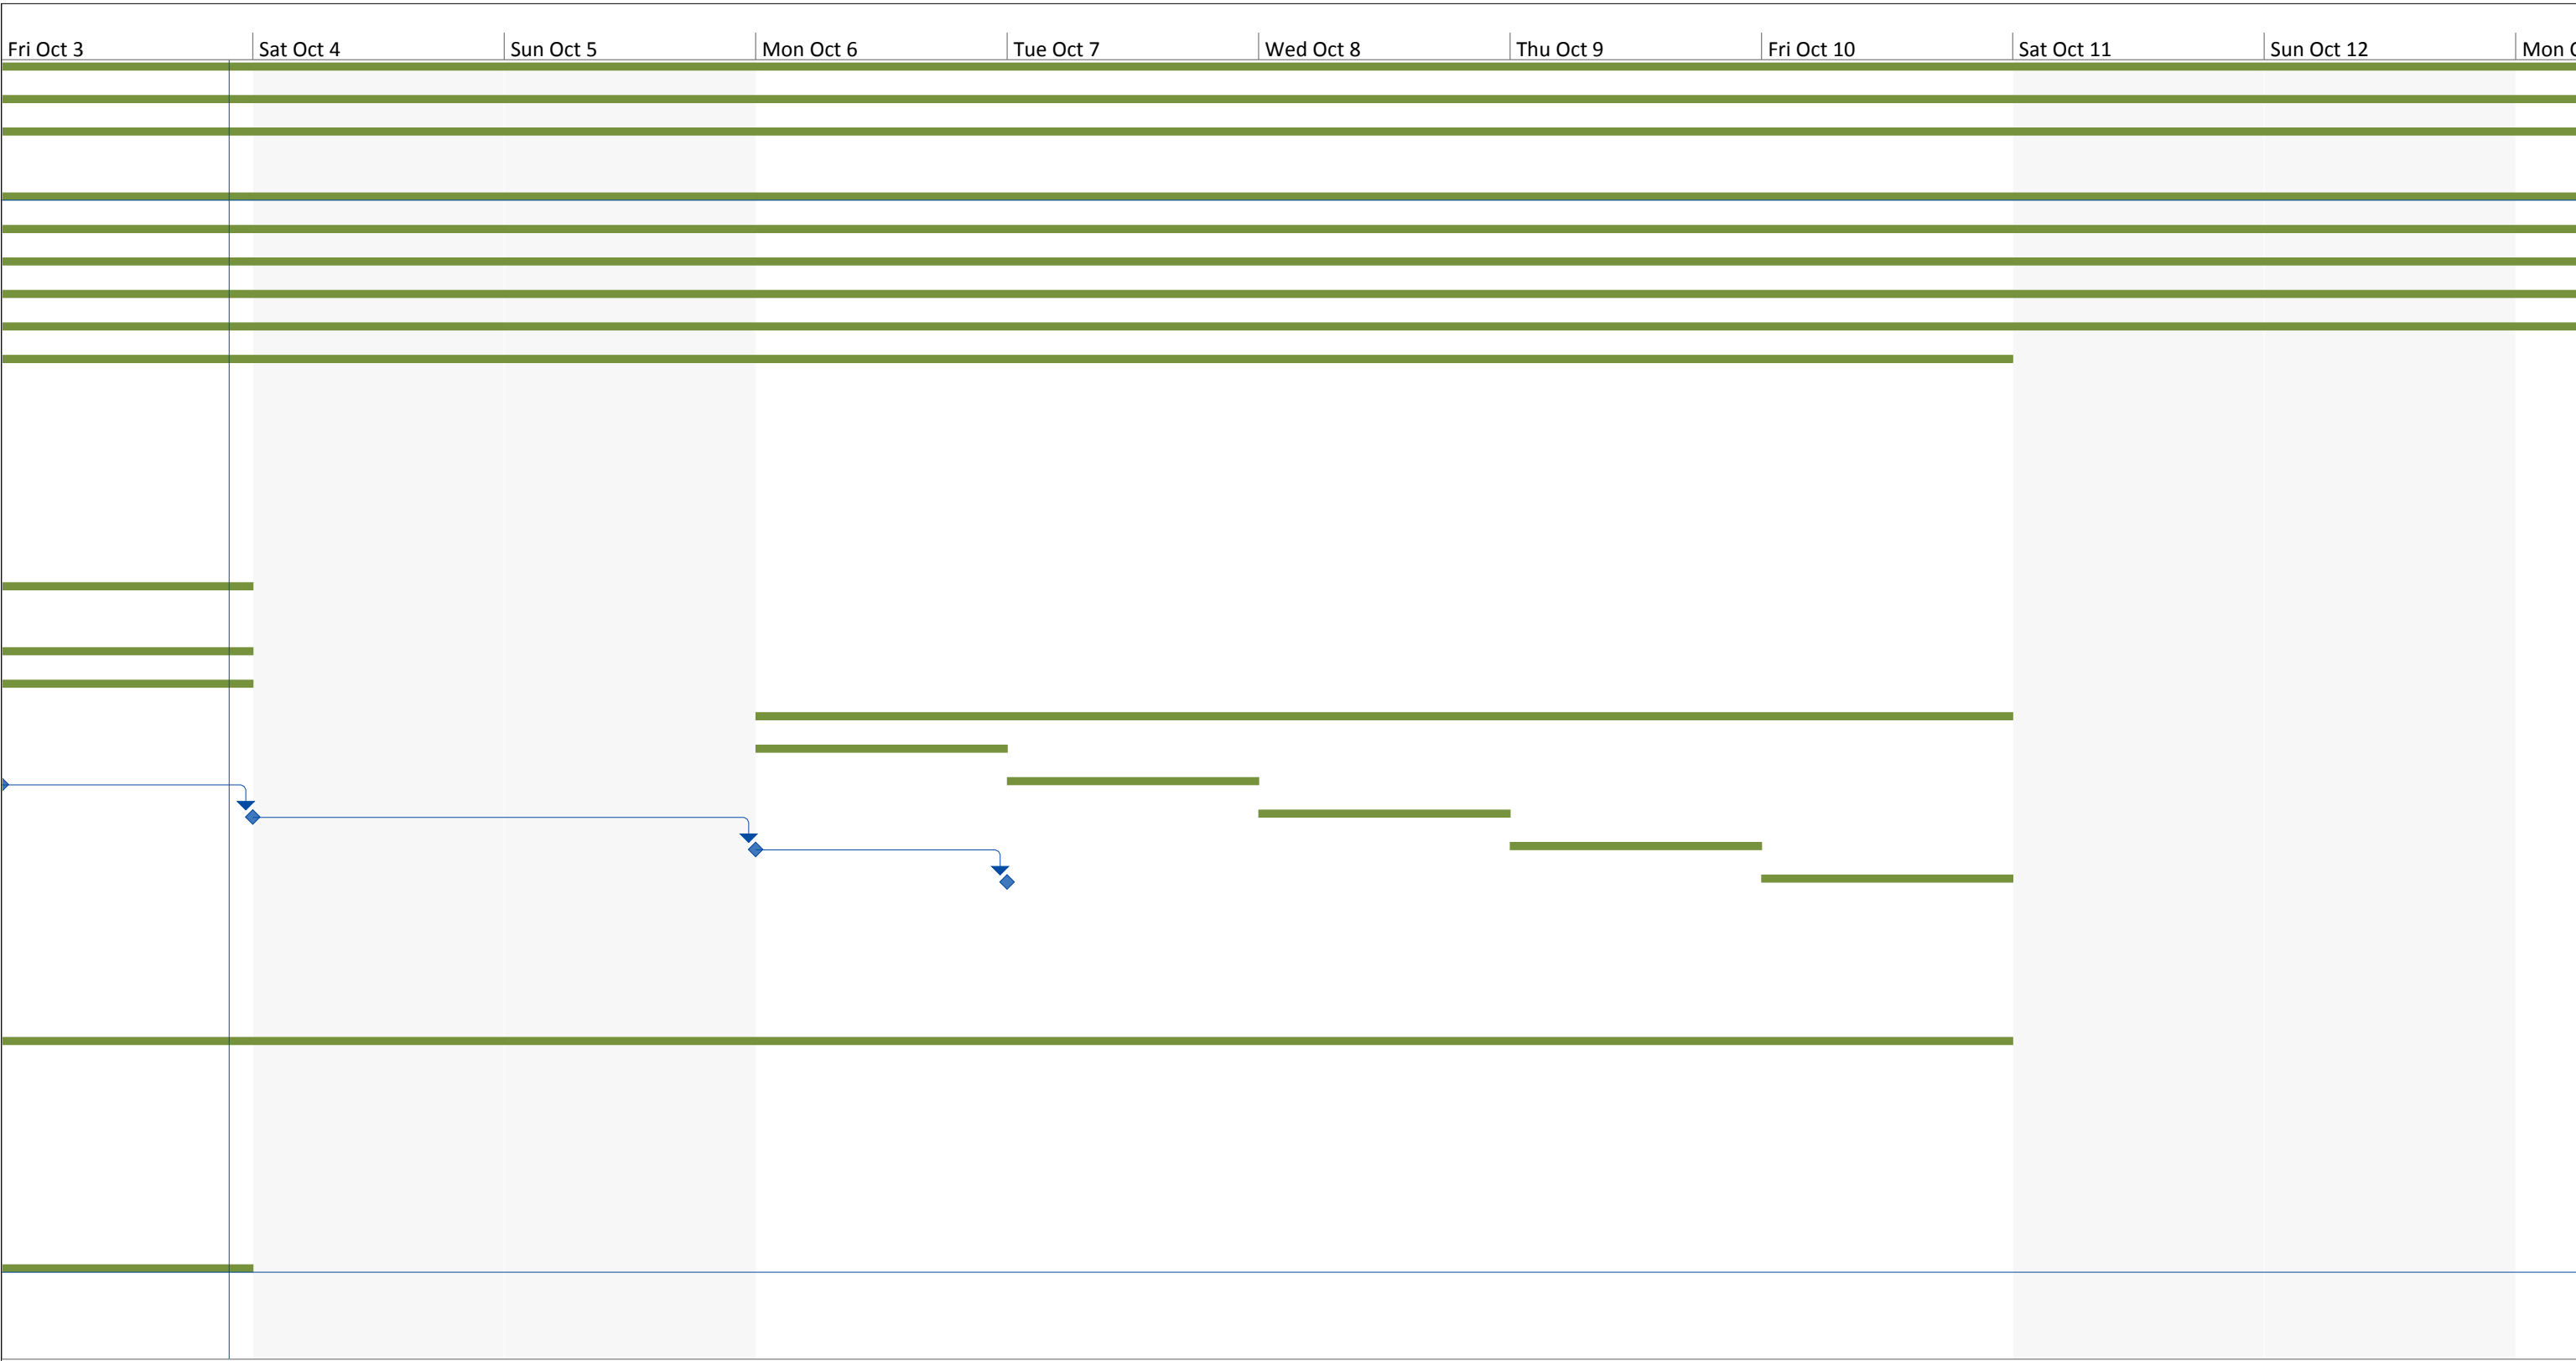

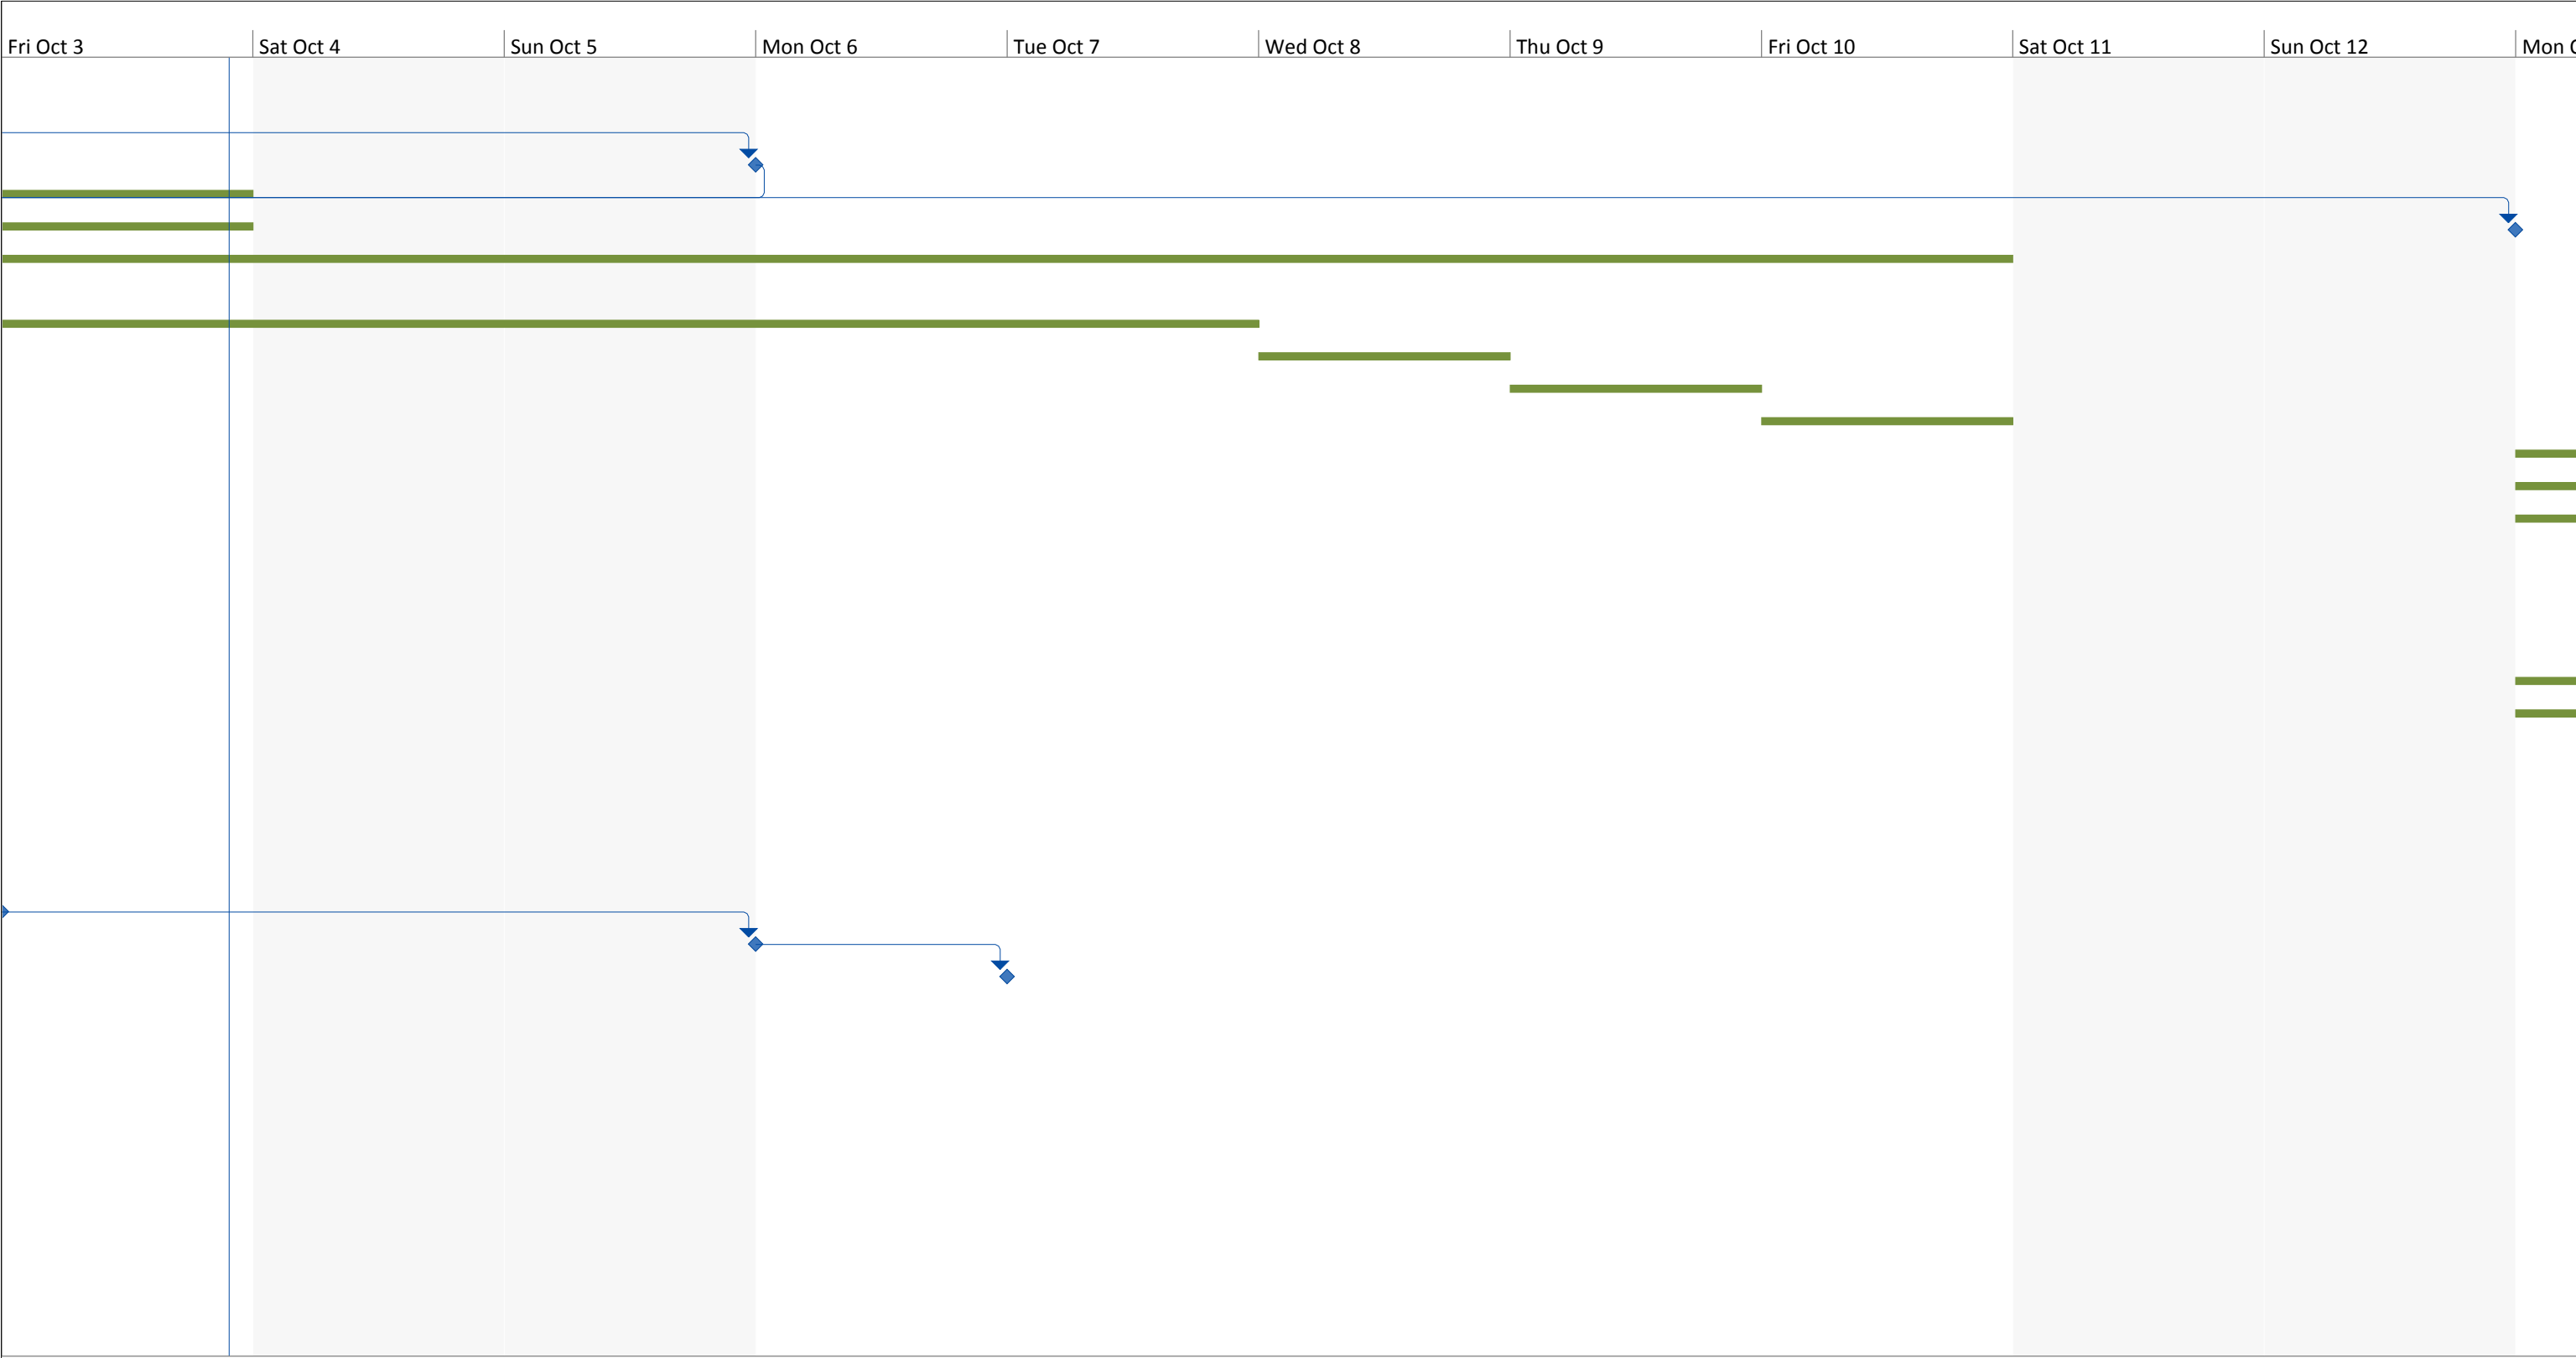

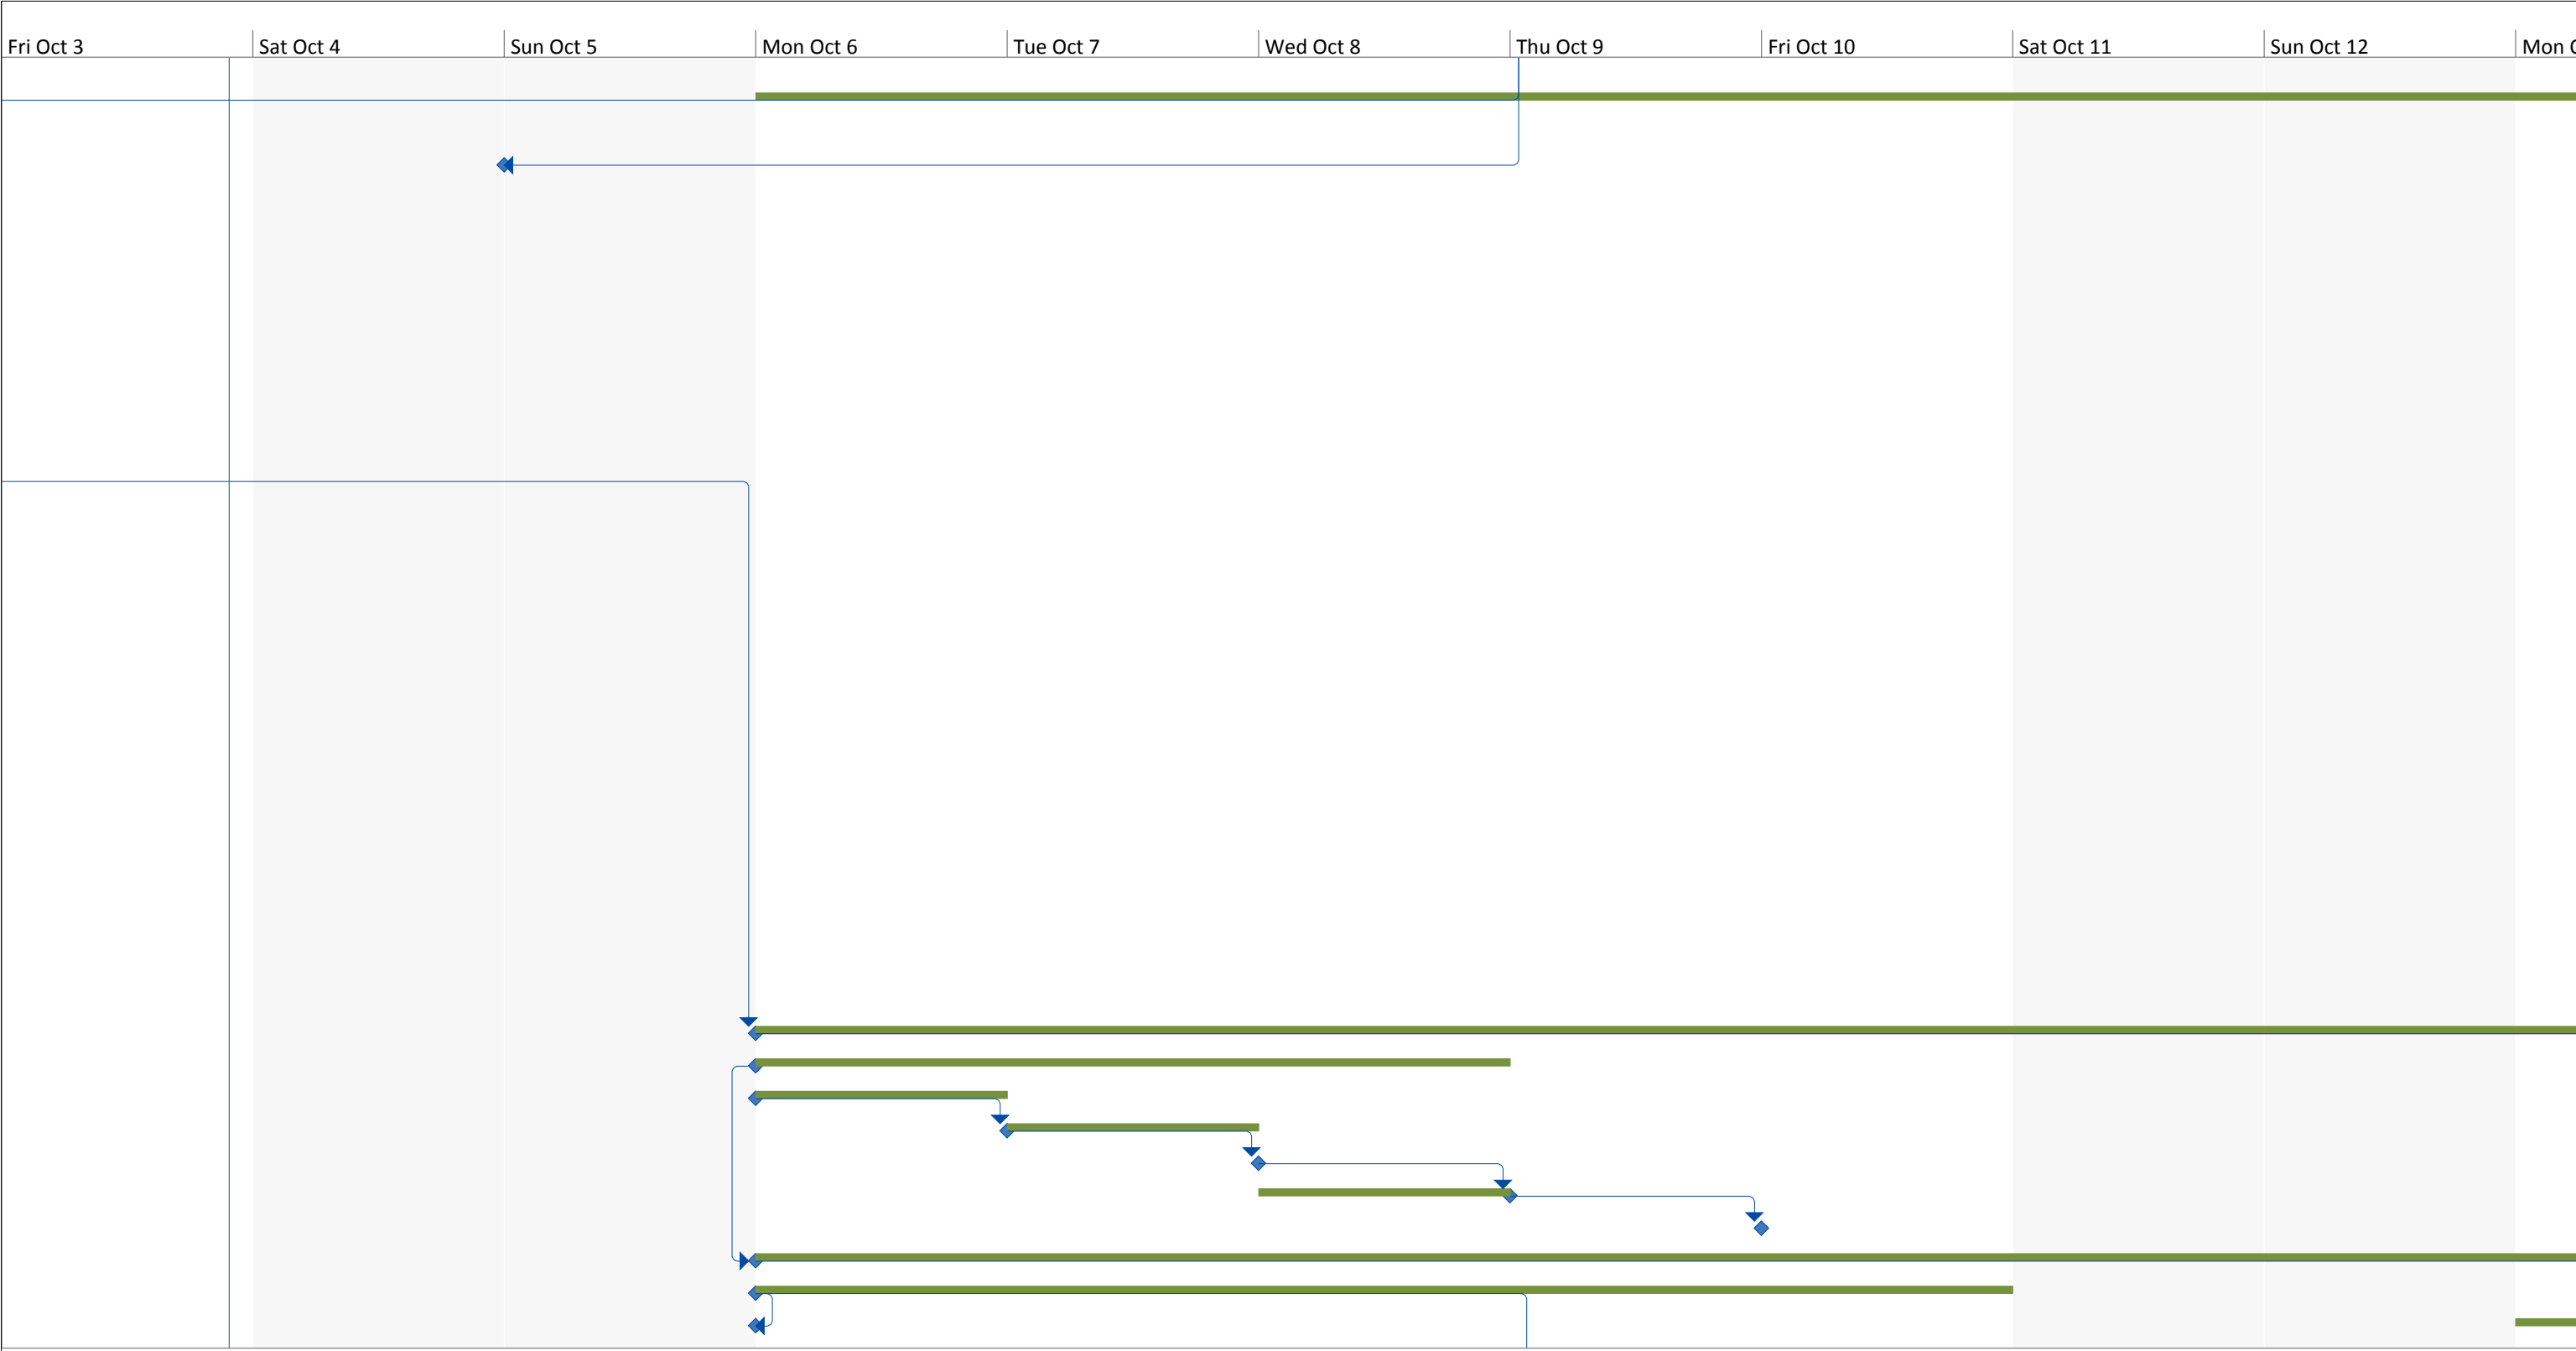



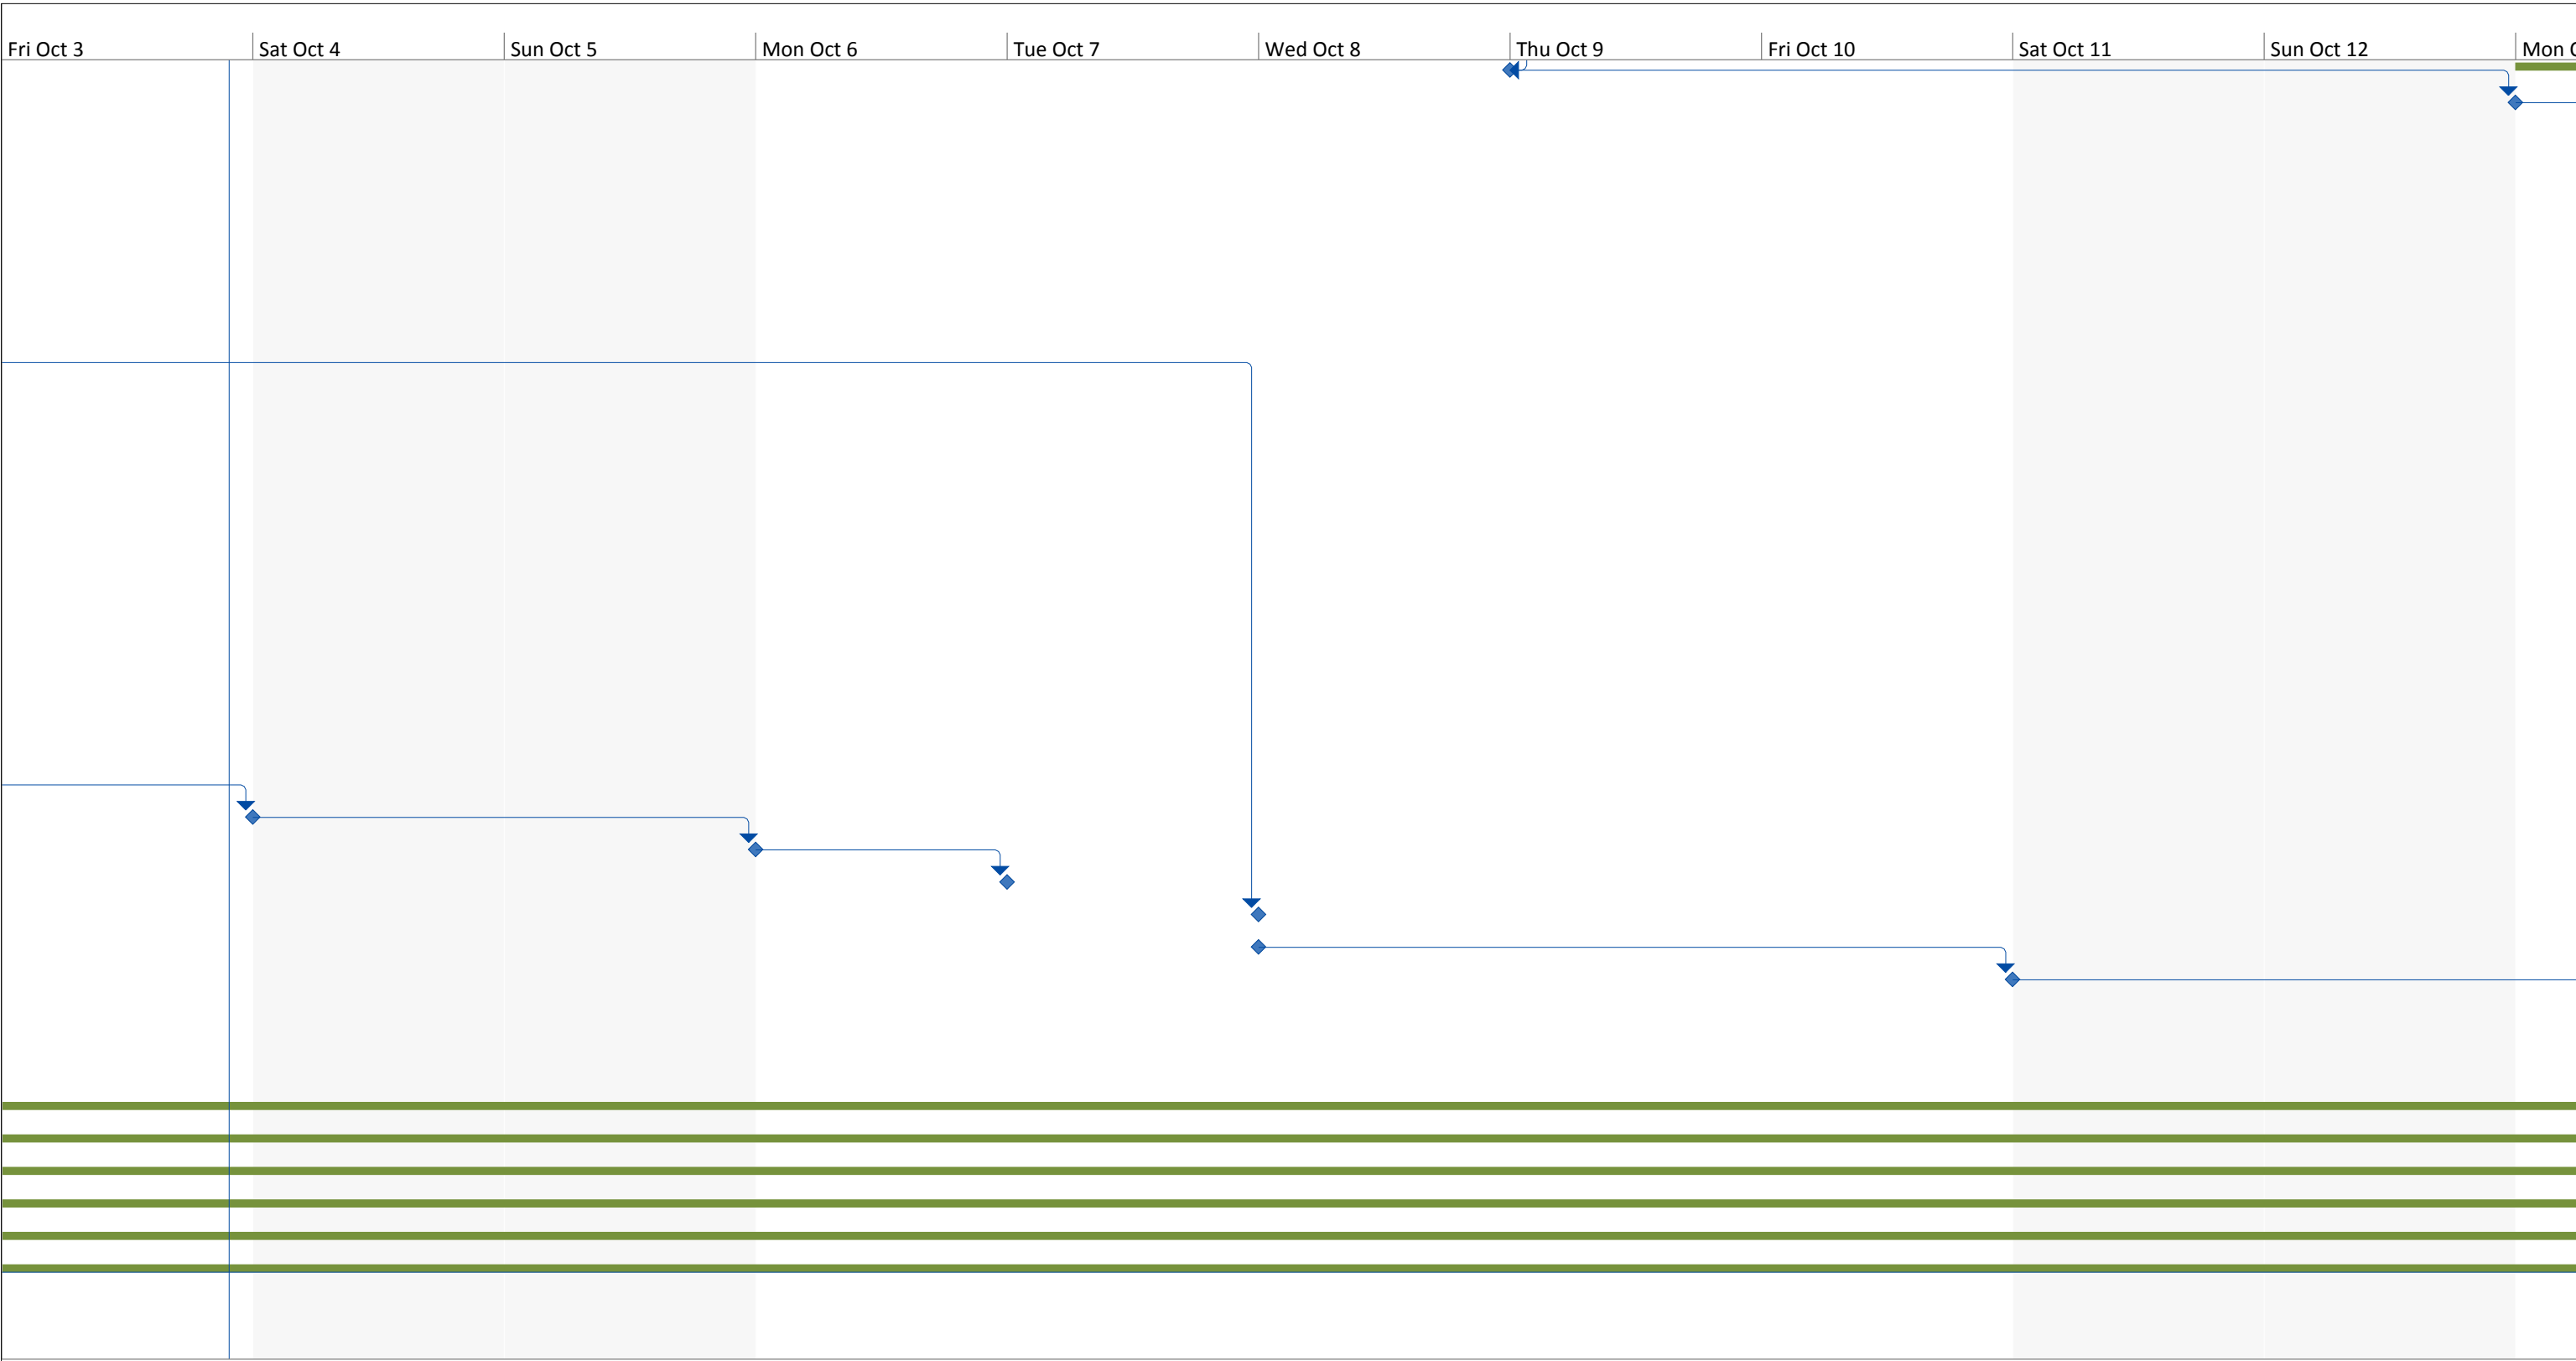
























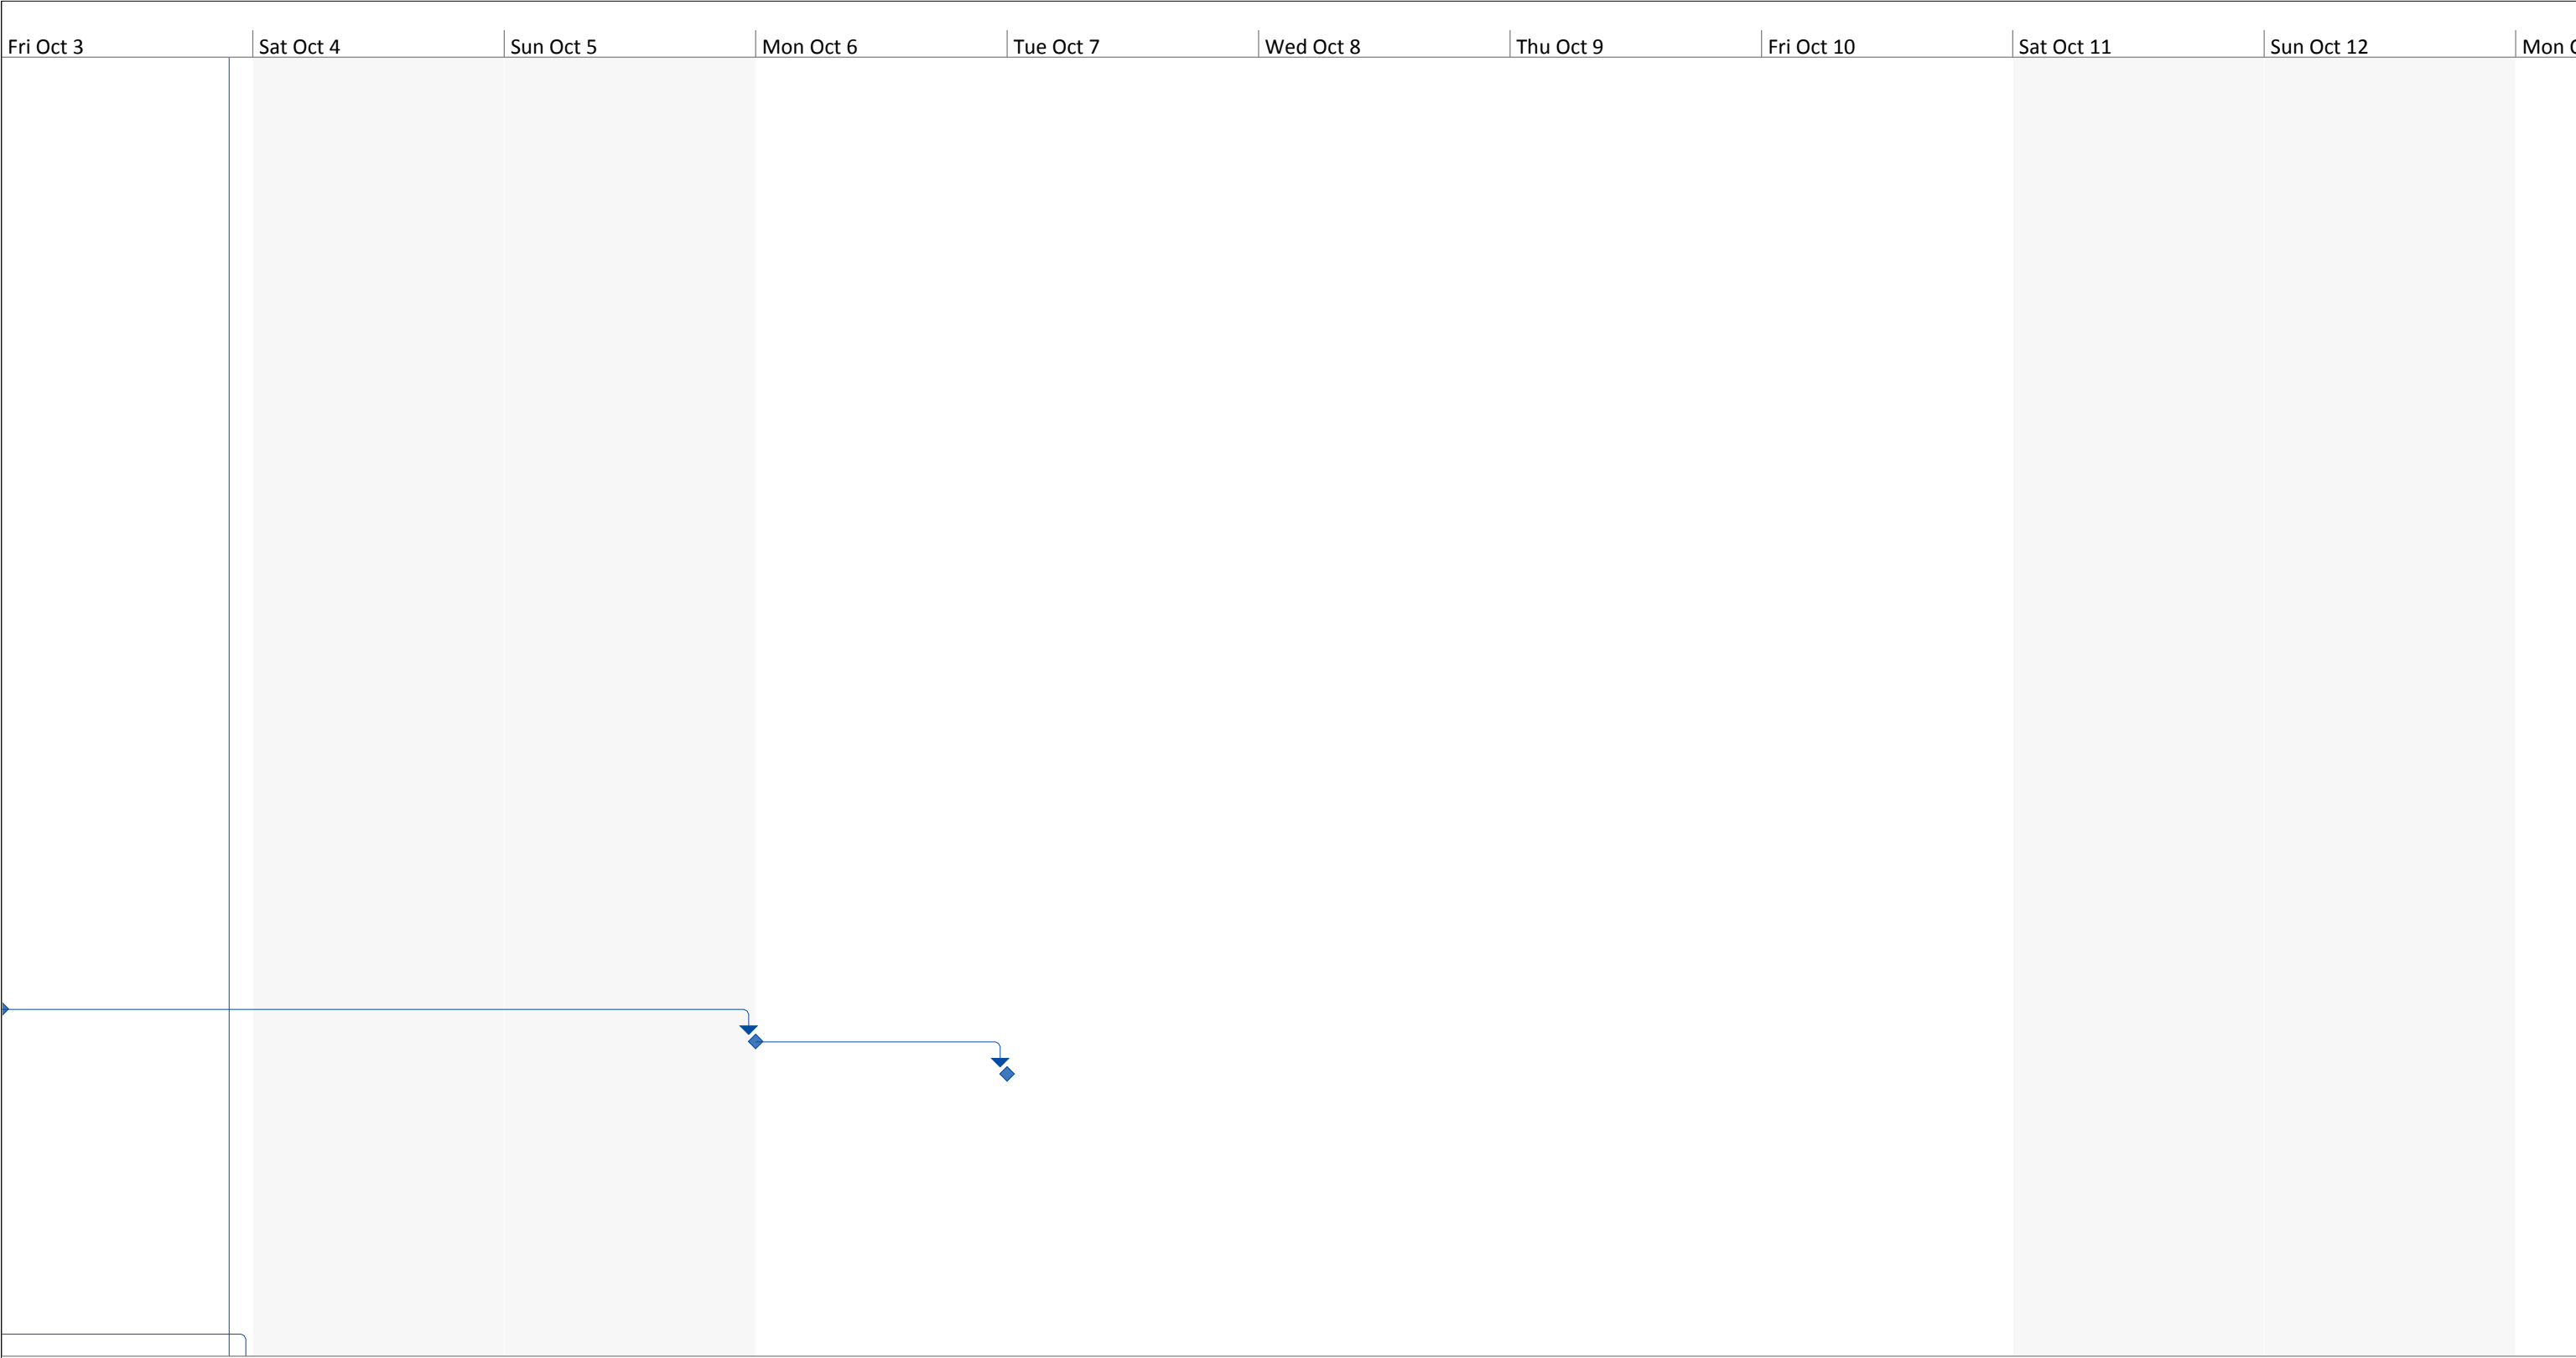














Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone	◆	Summary: Previous	▬	Placeholder Start: Current	▬	Inactive Milestone: Previous	◆
	Task: Previous	▬	Summary: Current	▬	Placeholder Finish: Previous	▬	Inactive Milestone: Current	◆
	Task: Current	▬	Placeholder Duration: Previous	▬	Placeholder Finish: Current	▬	Inactive Summary: Previous	▬
	Milestone: Previous	◆	Placeholder Duration: Current	▬	Inactive Task: Previous	▬	Inactive Summary: Current	▬
	Milestone: Current	◆	Placeholder Start: Previous	▬	Inactive Task: Current	▬	Manual Progress	▬





Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	





Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

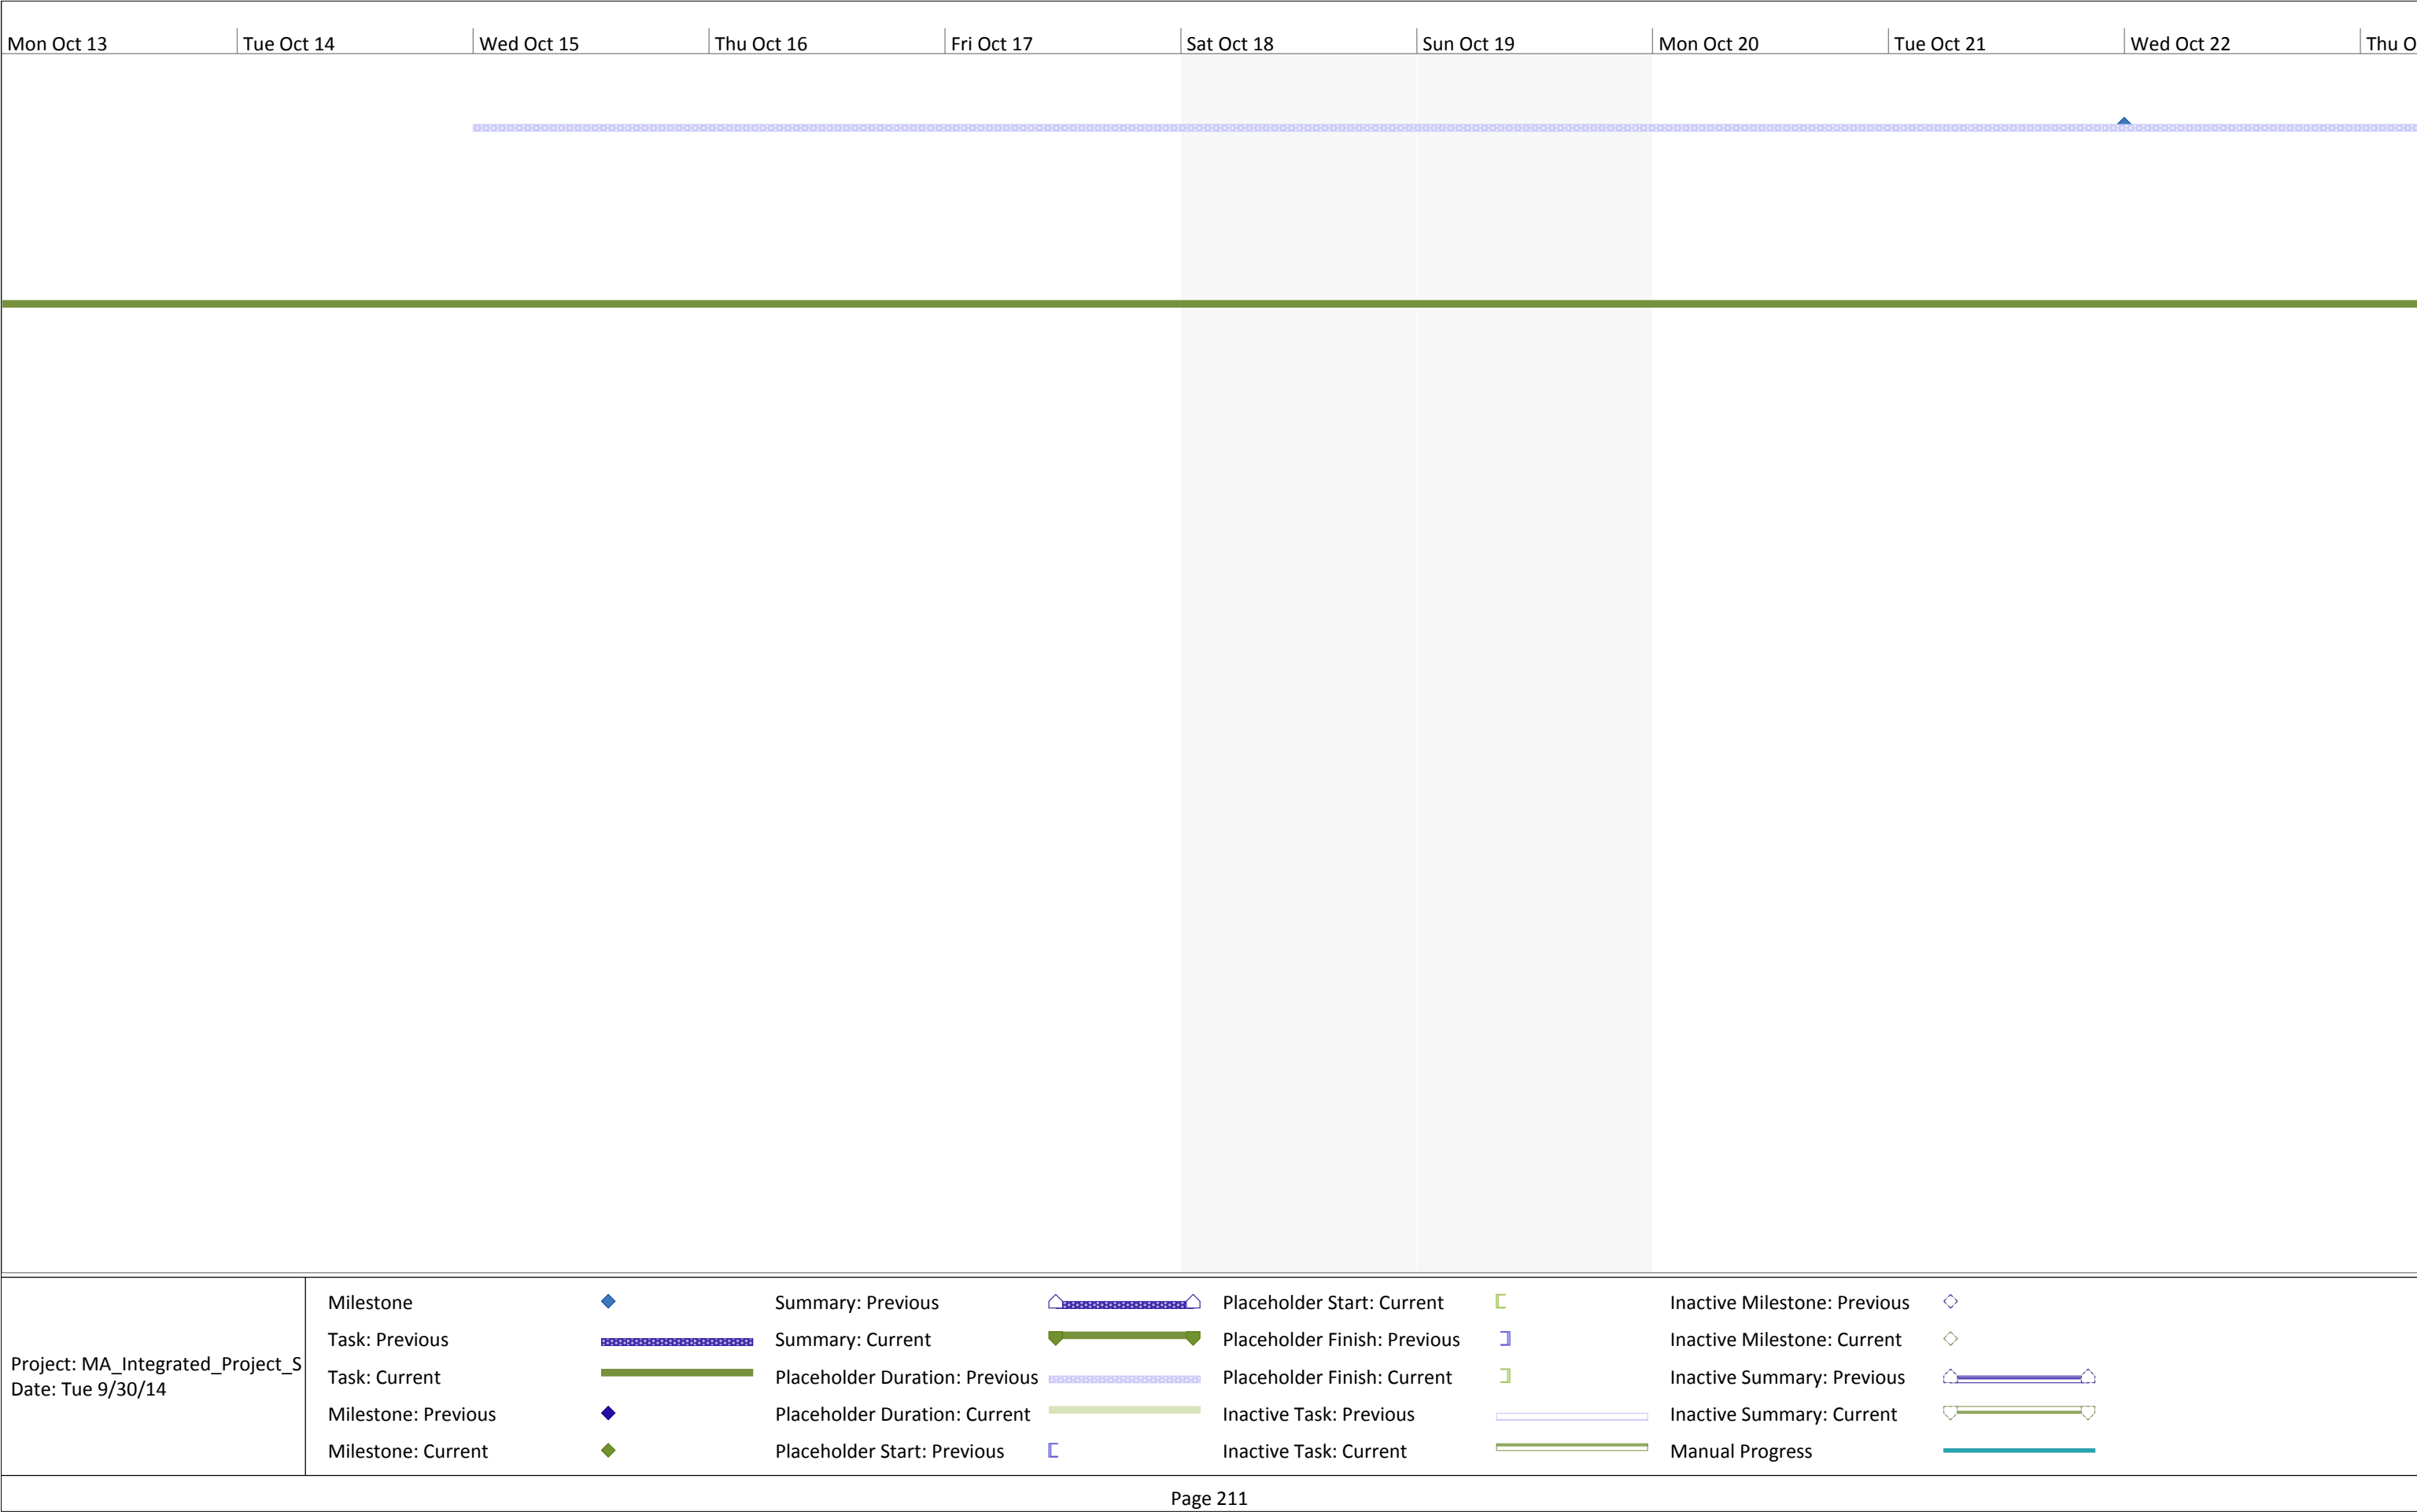


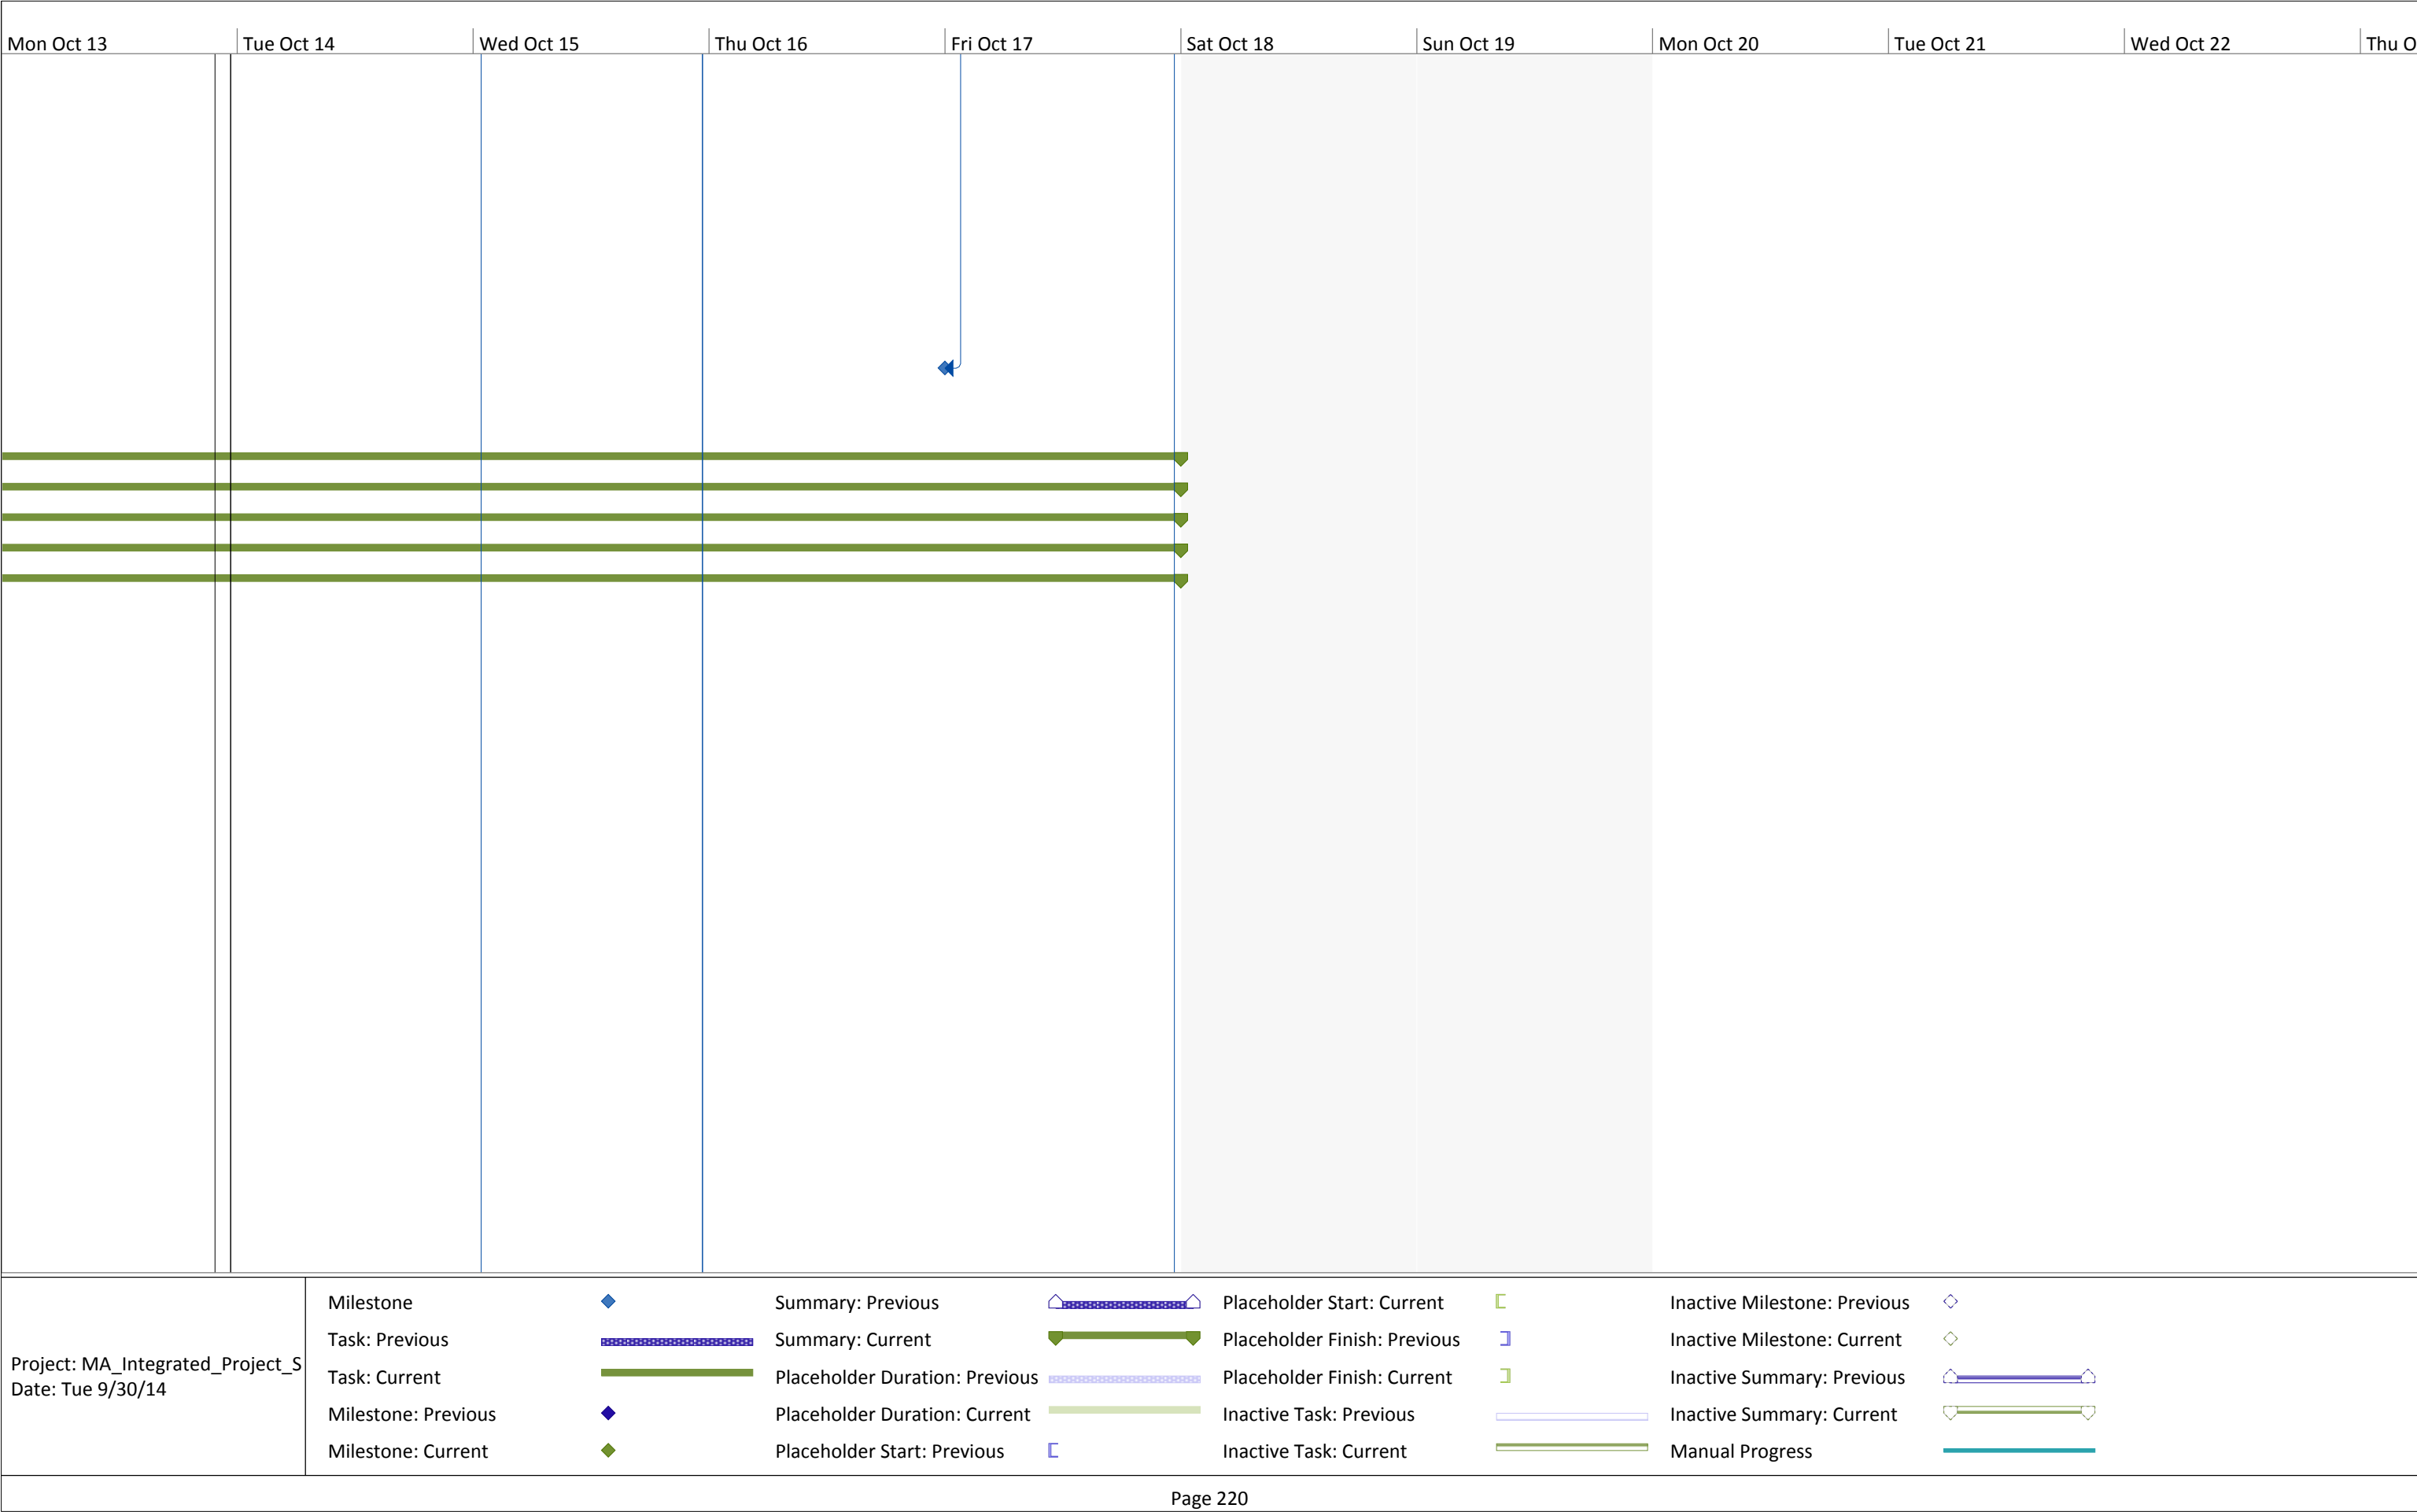

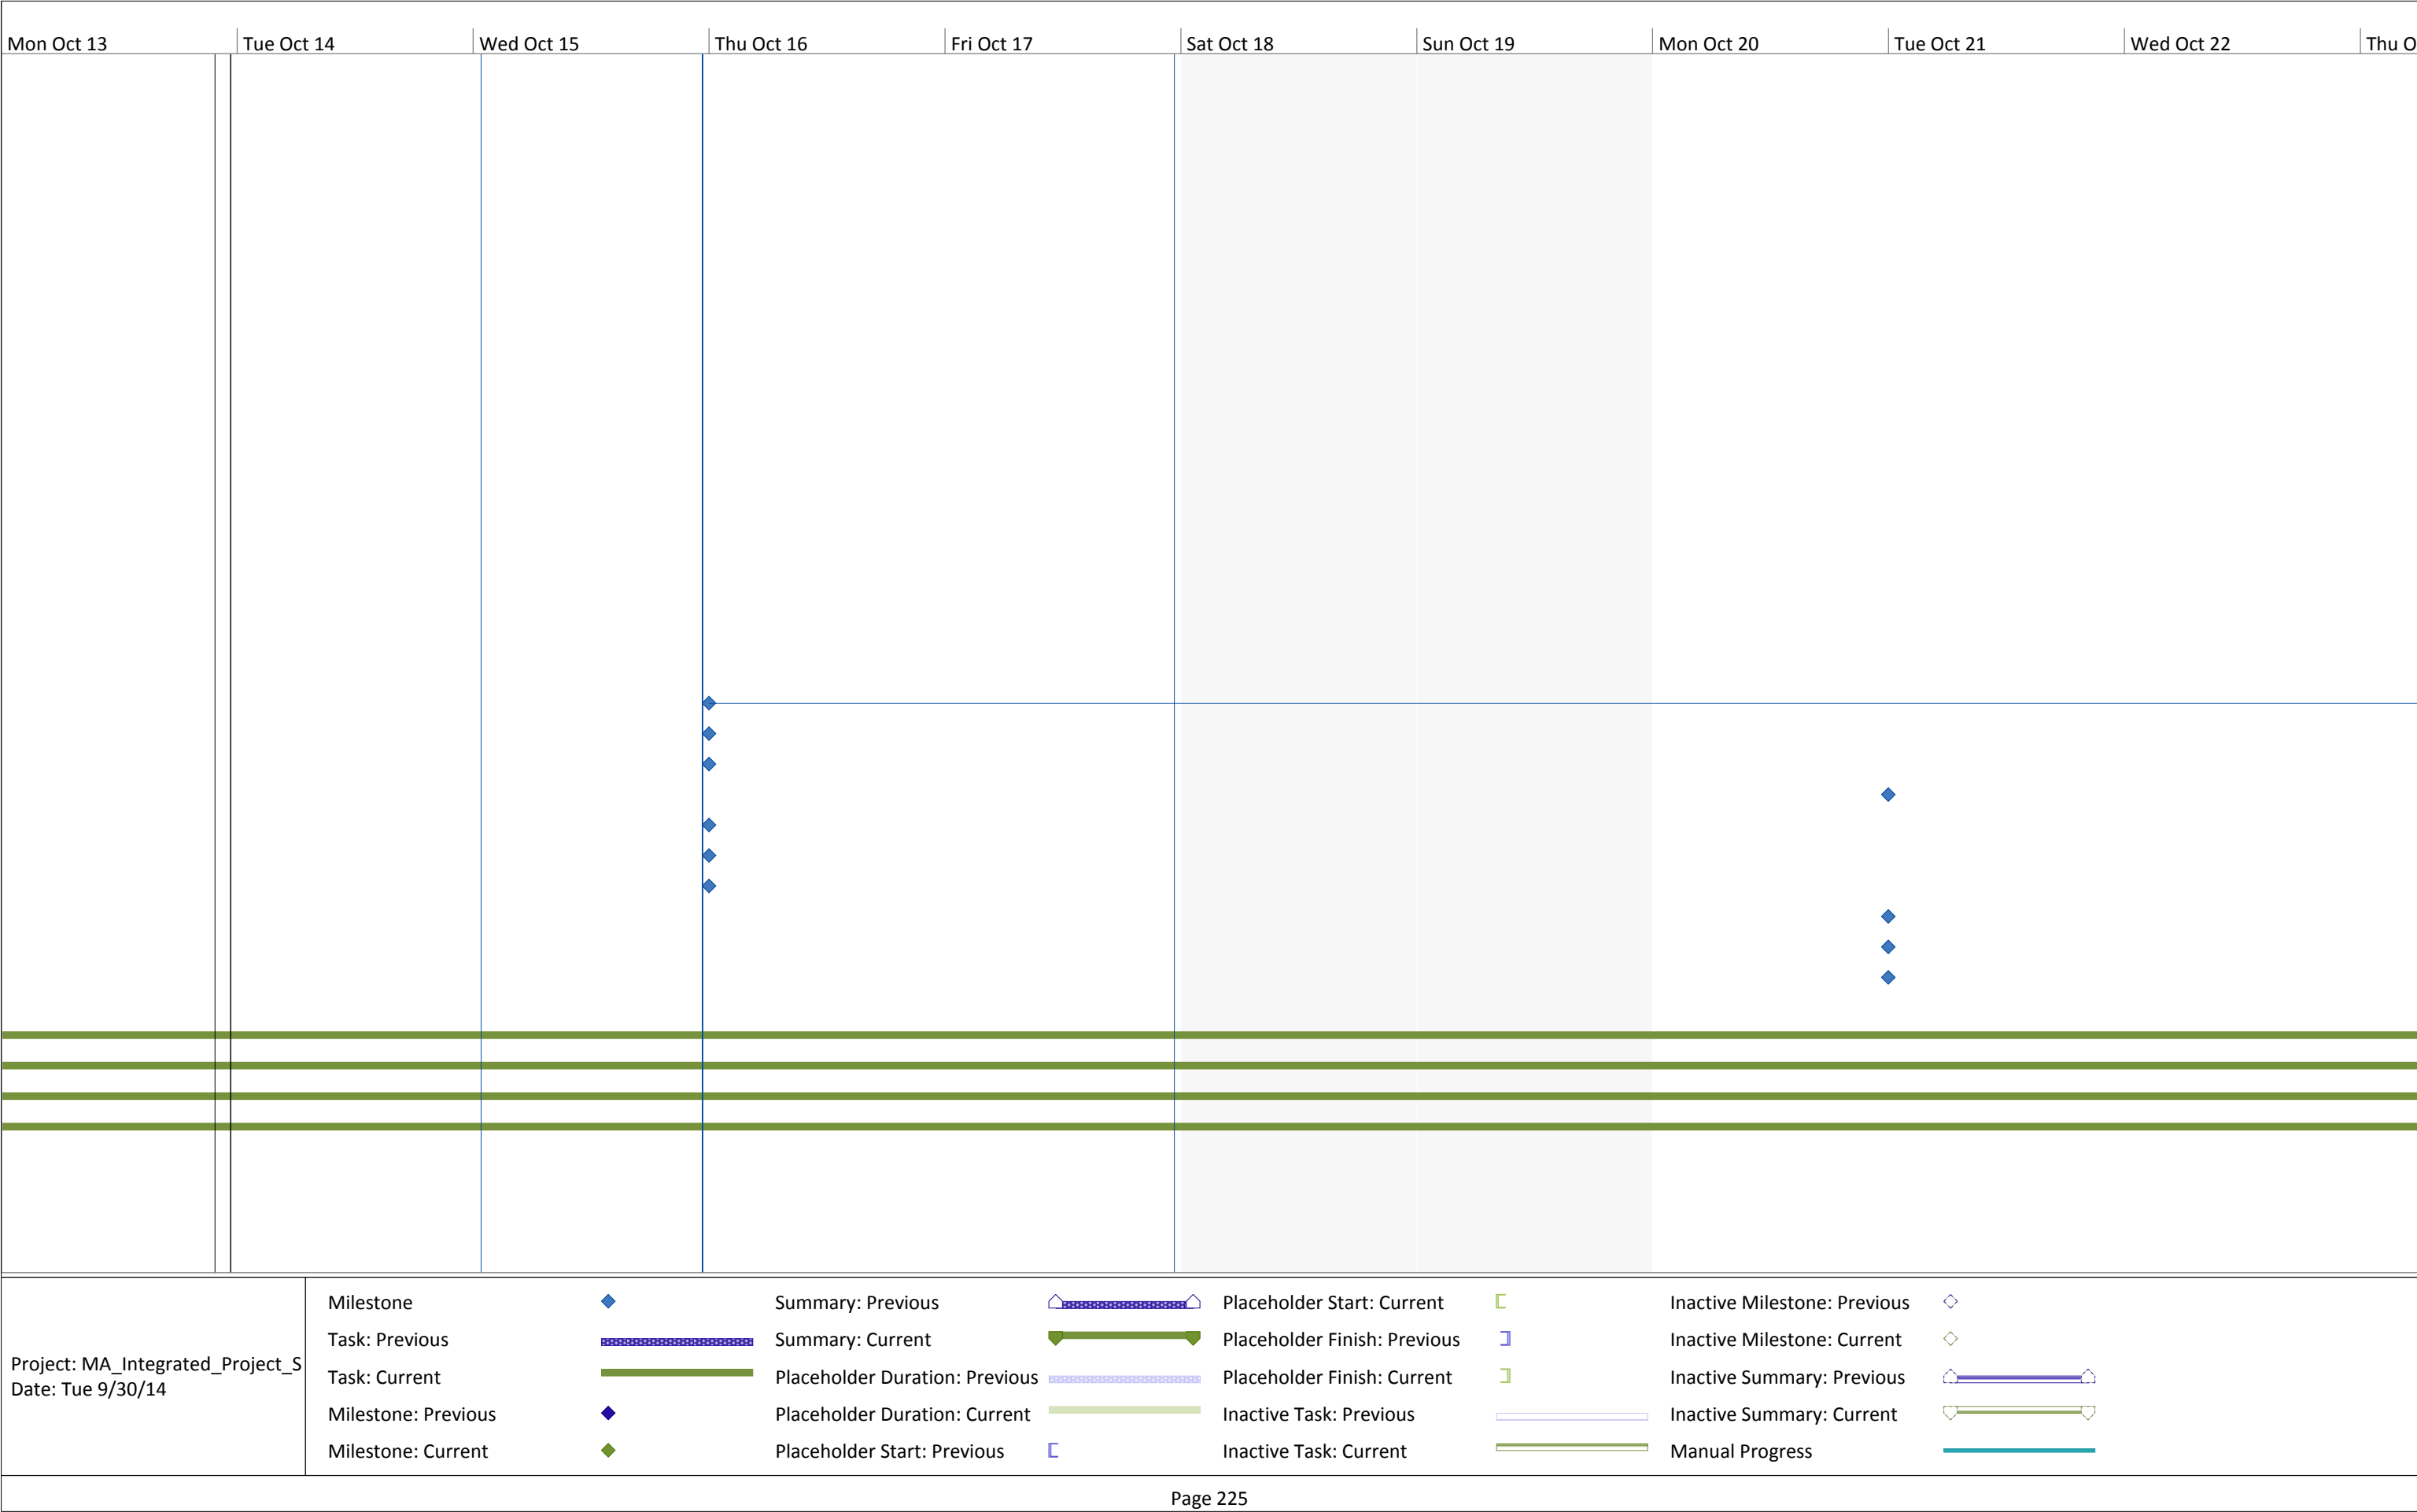


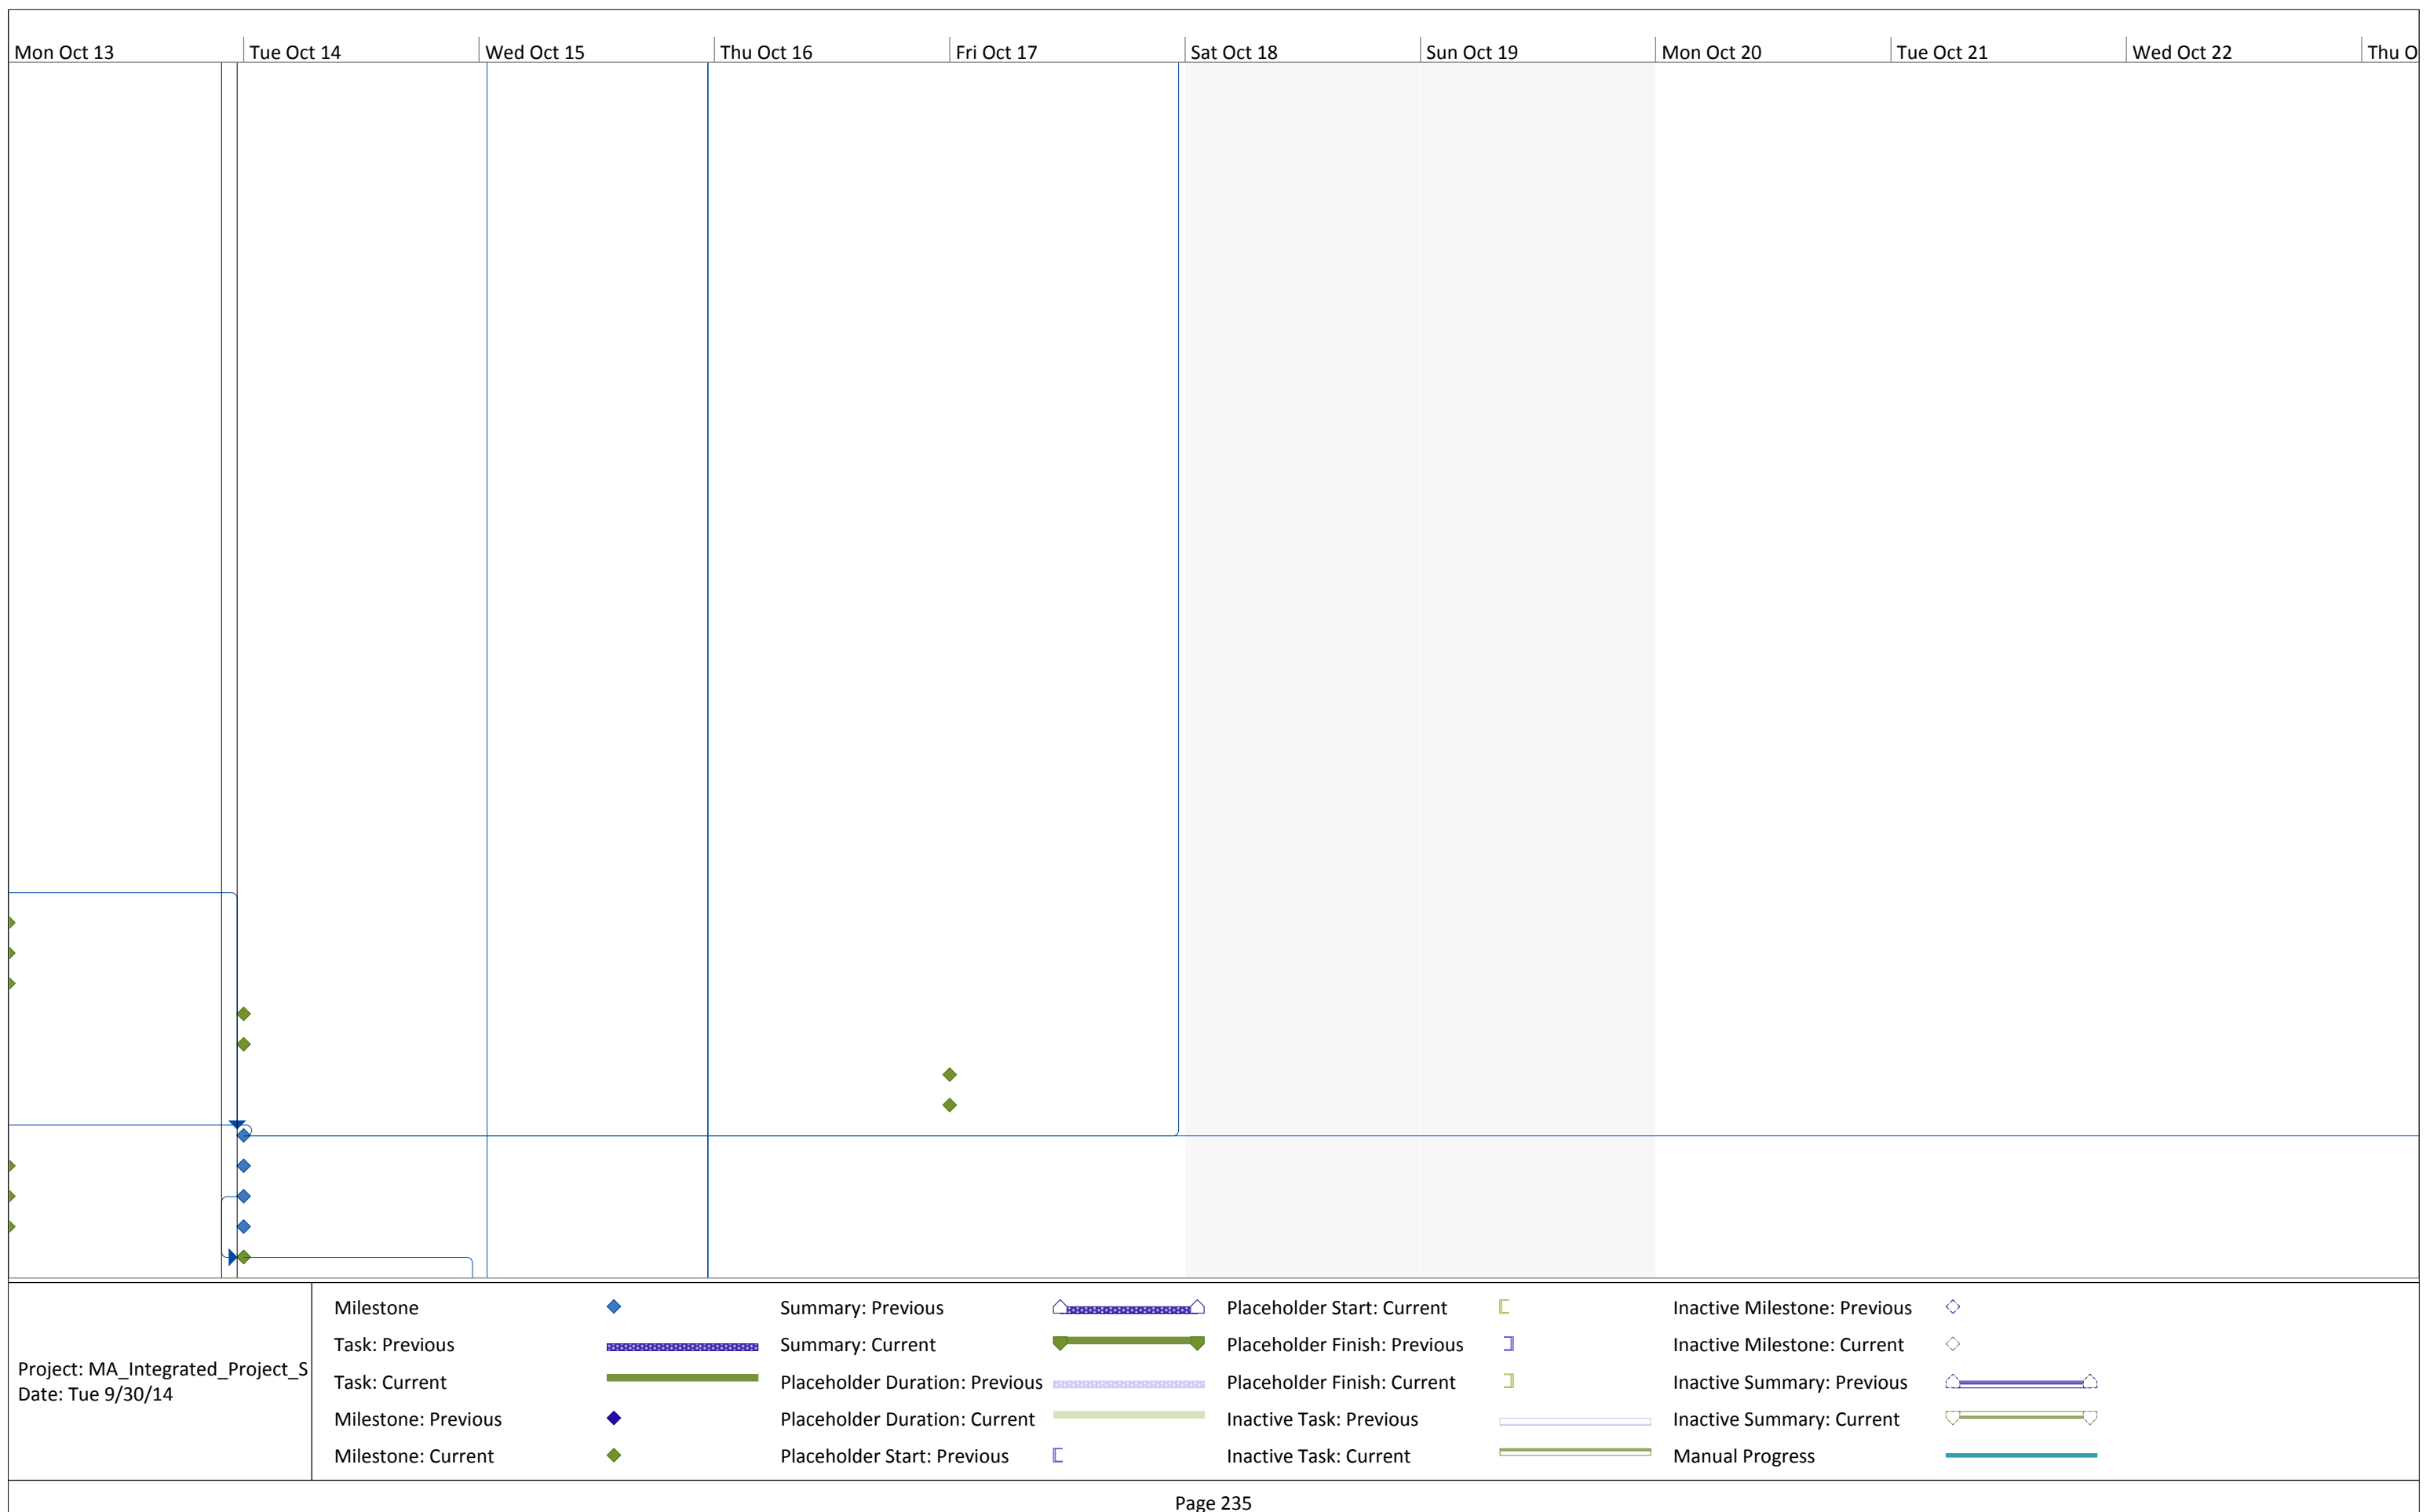

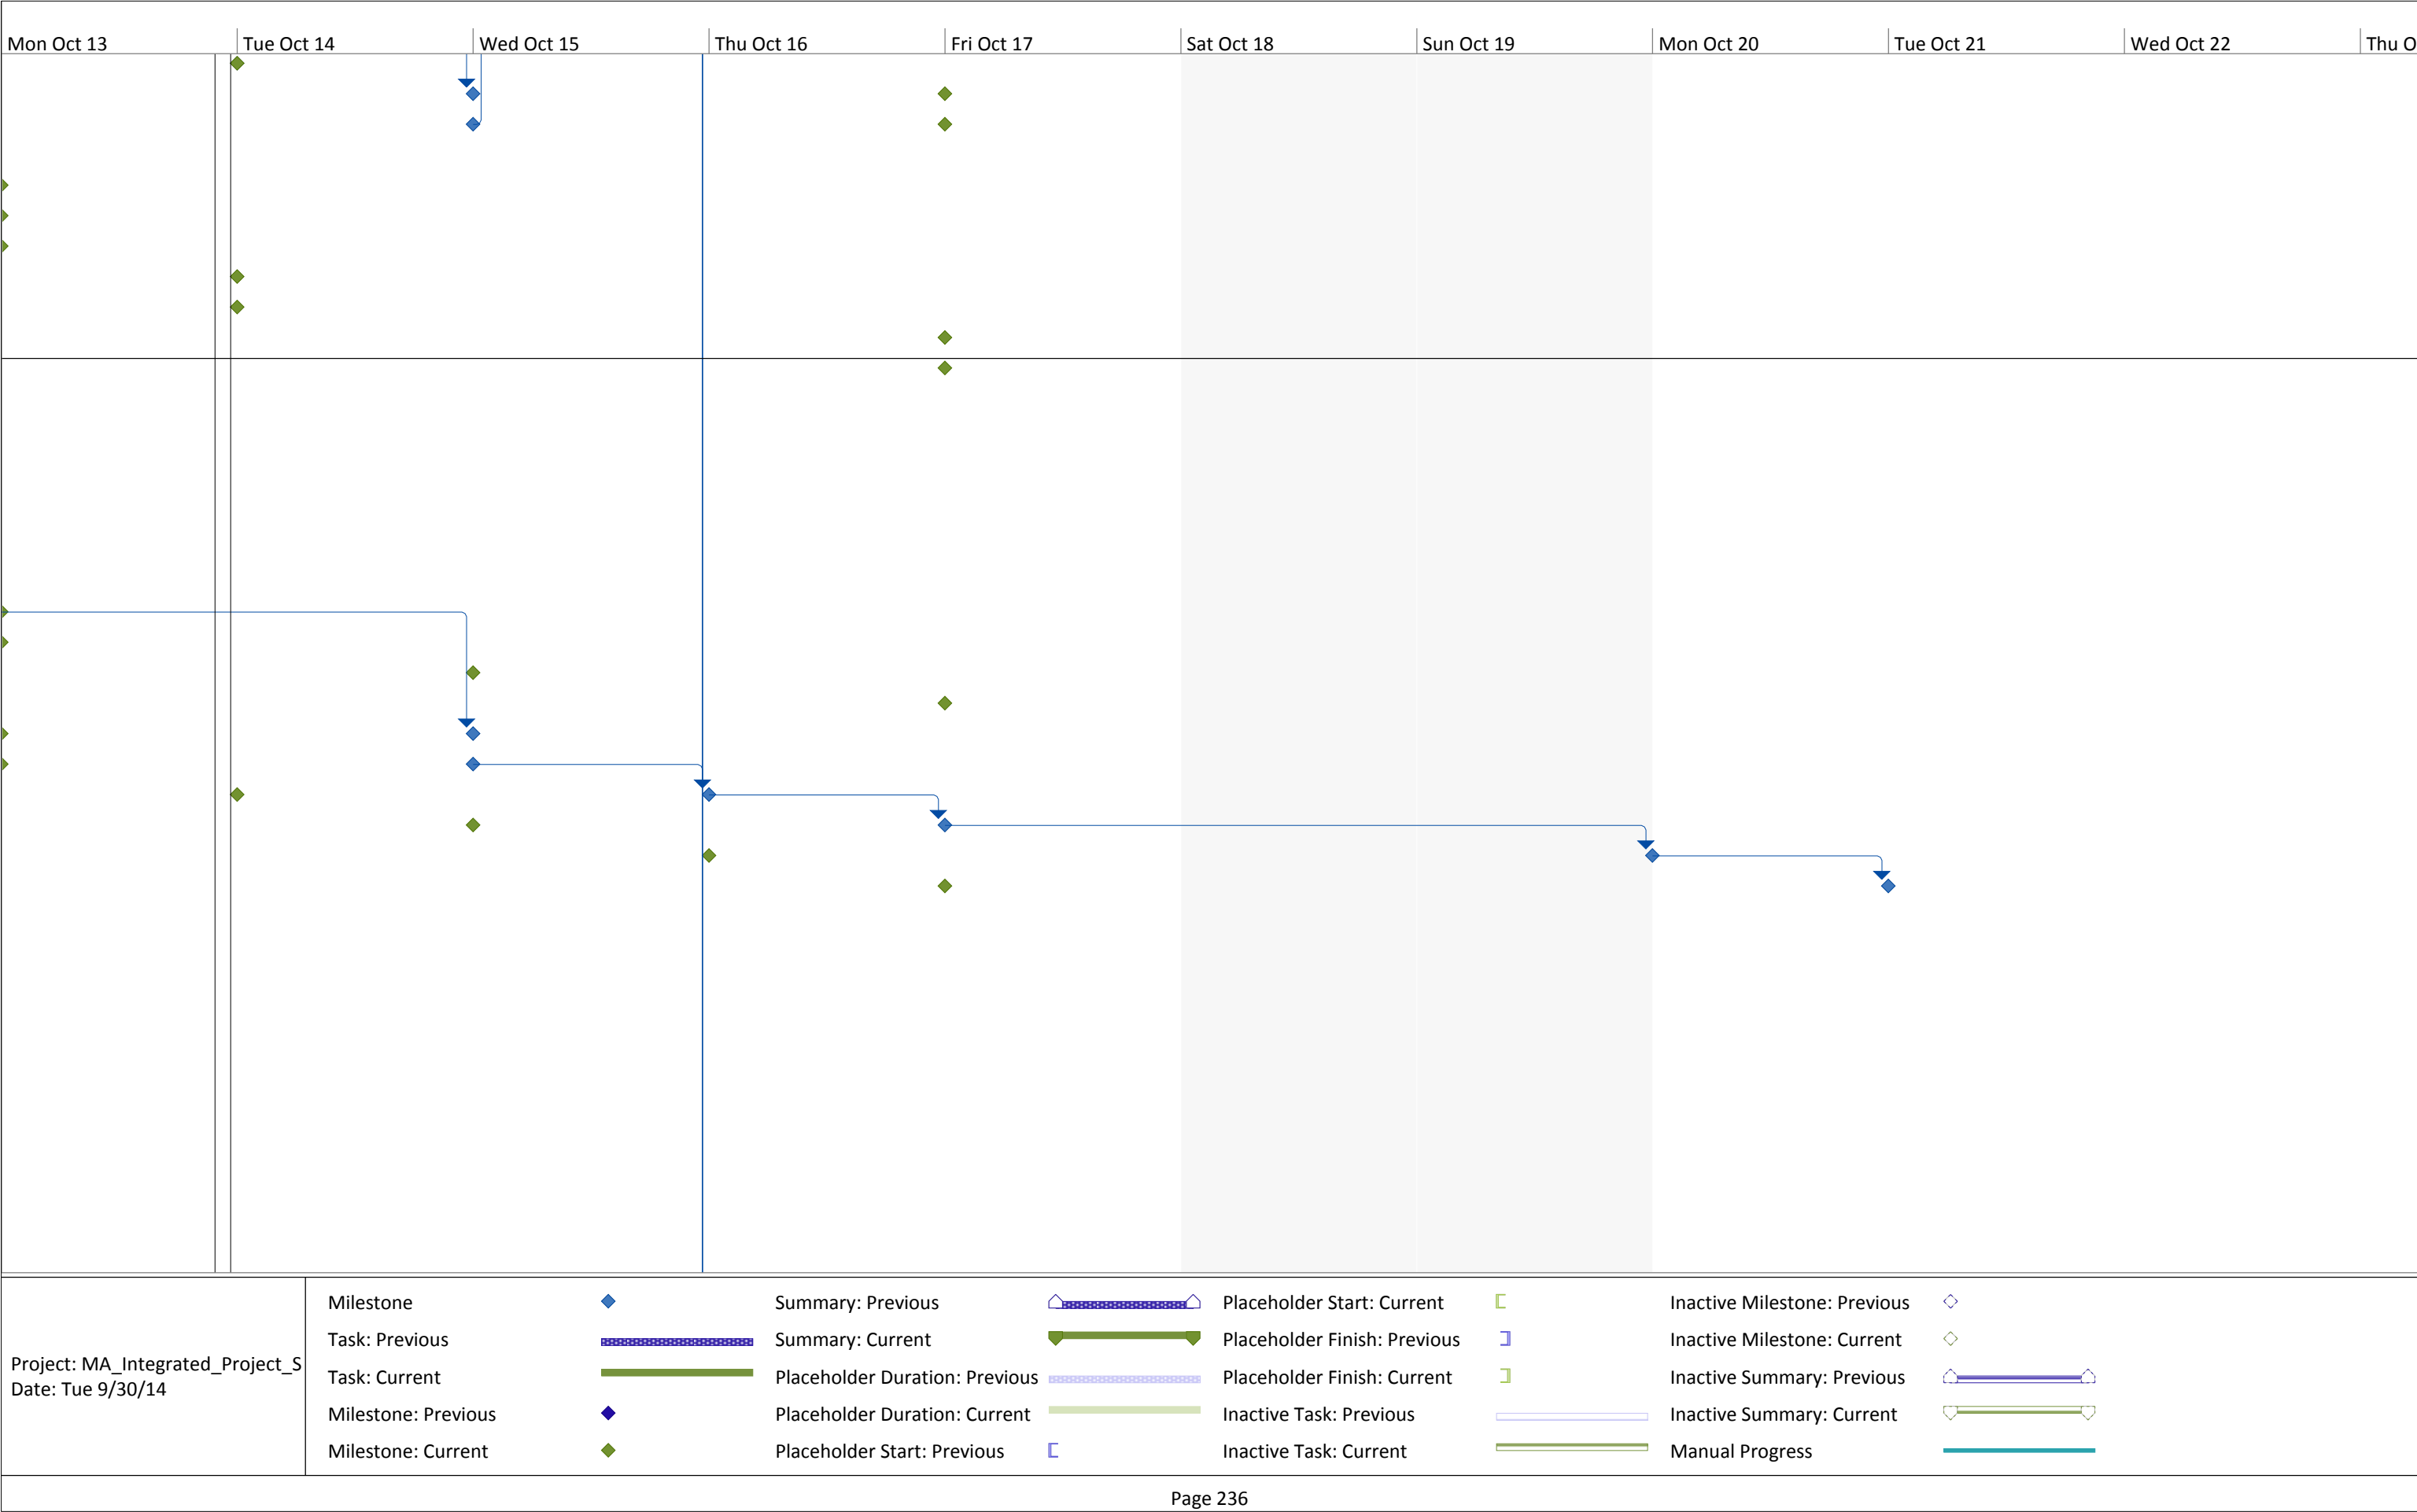


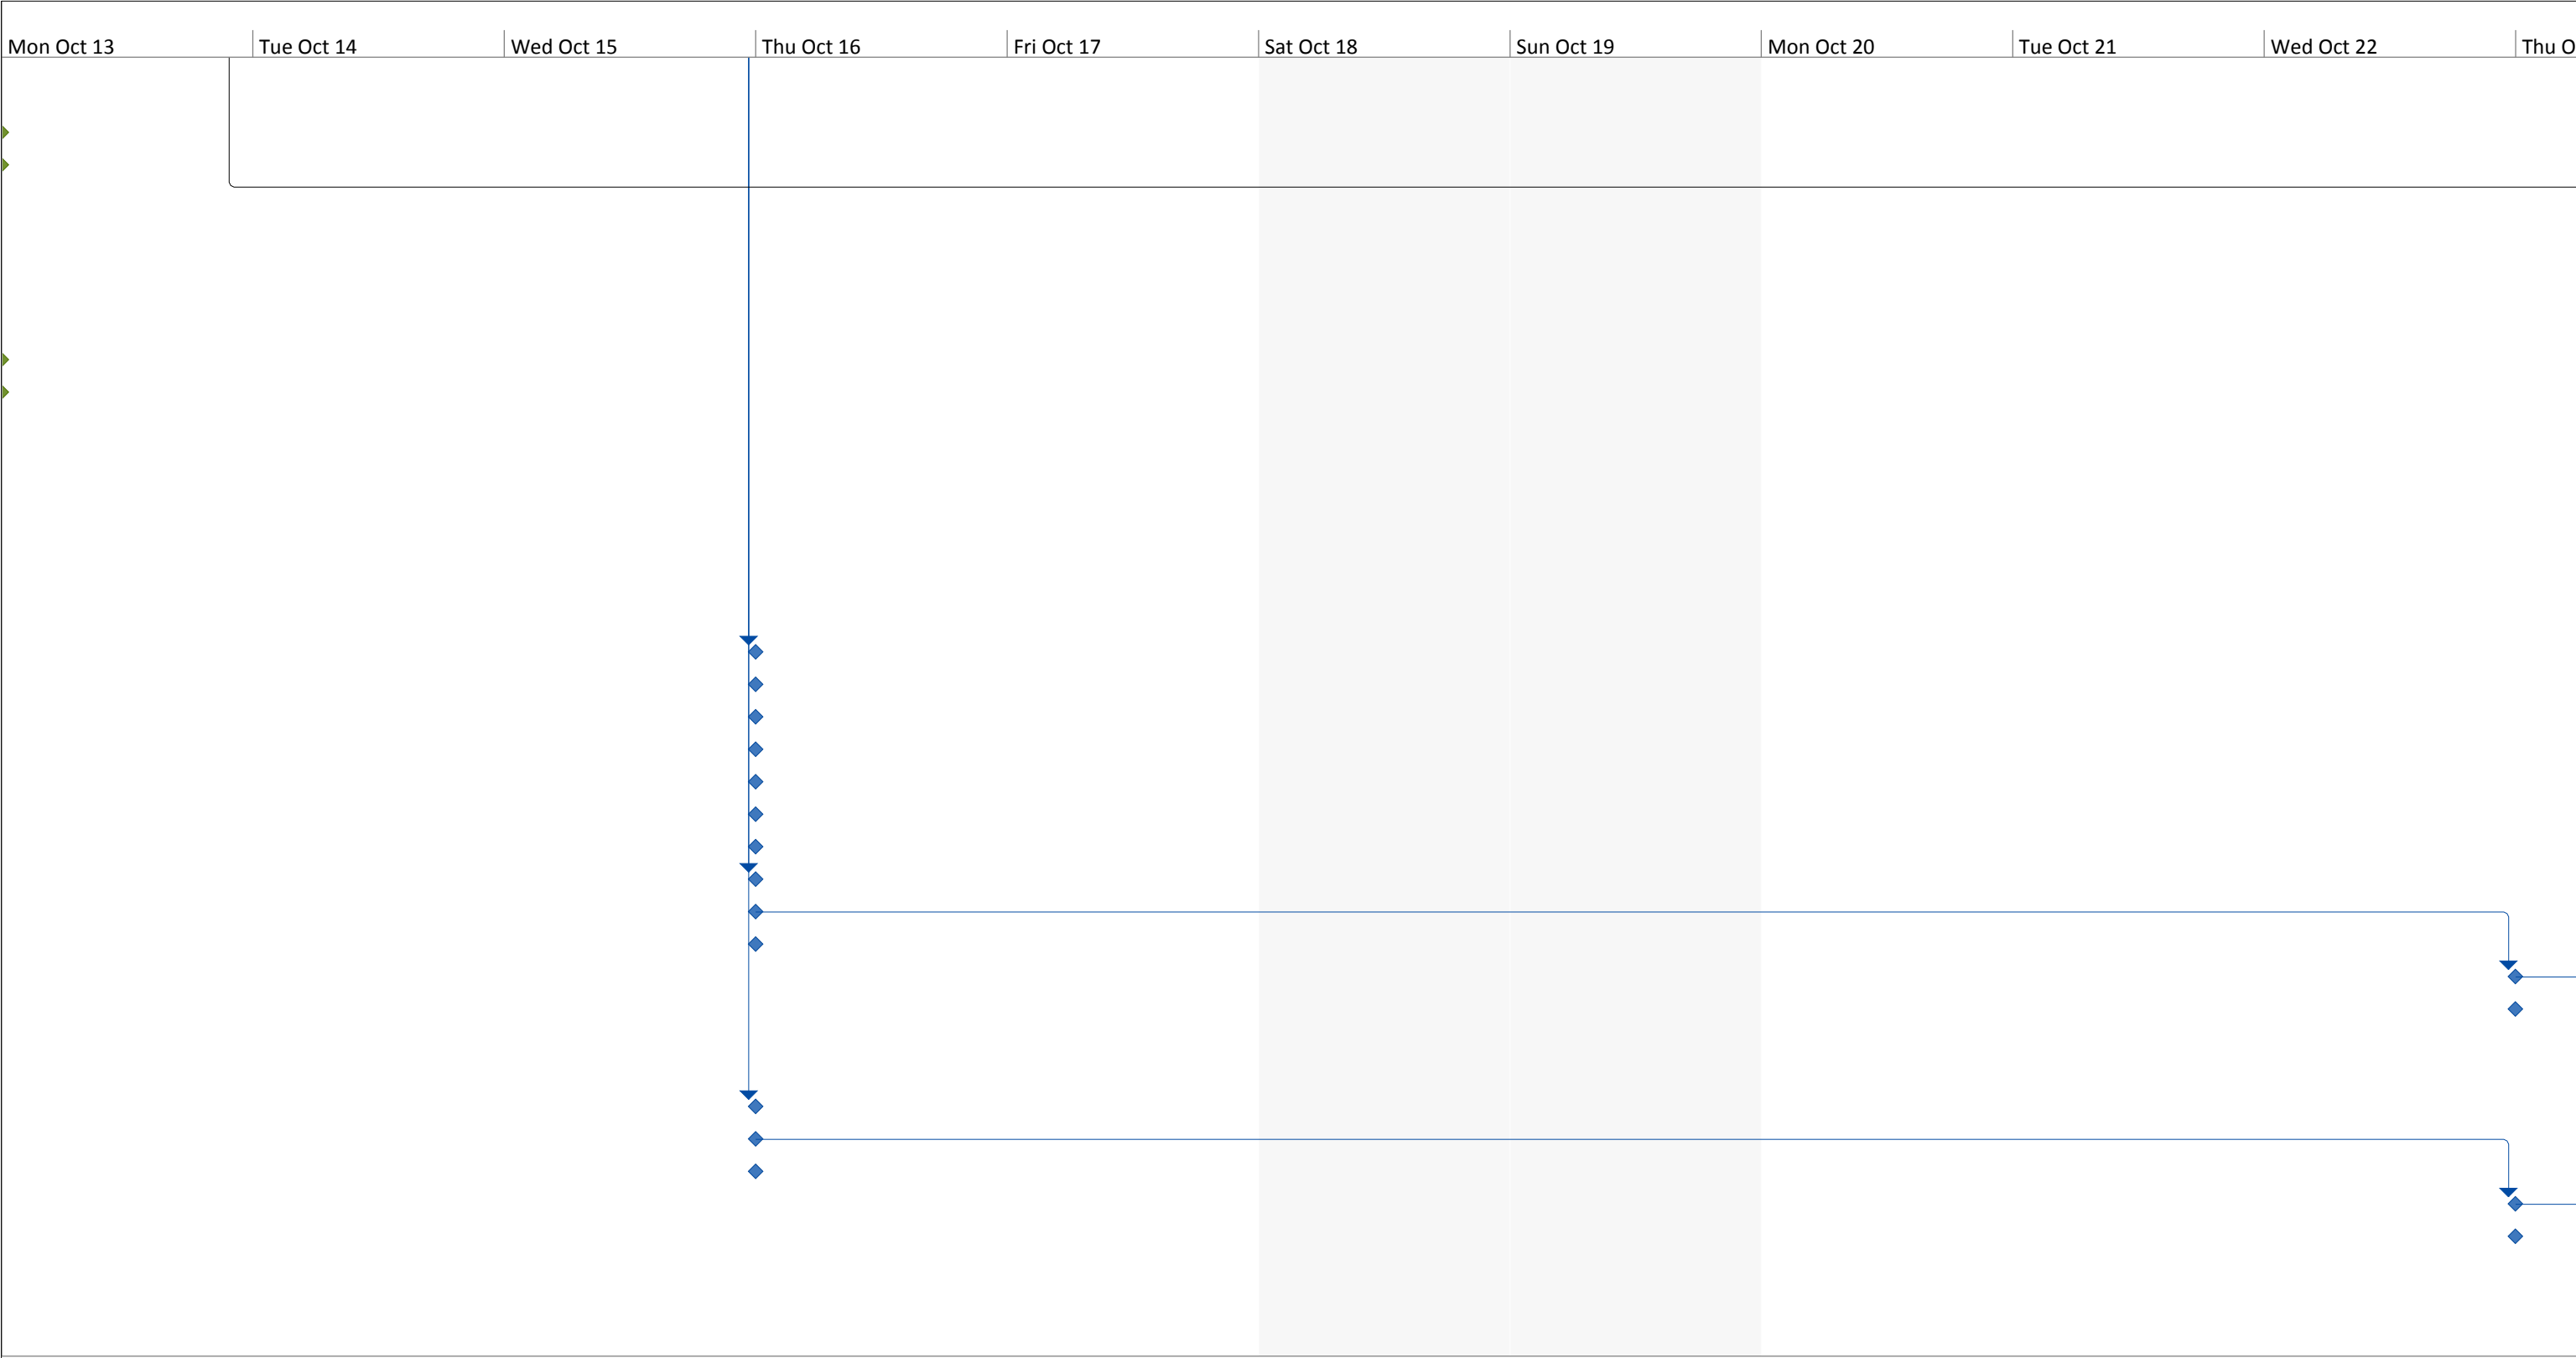



Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	





Mon Oct 13		Tue Oct 14		Wed Oct 15		Thu Oct 16		Fri Oct 17		Sat Oct 18		Sun Oct 19		Mon Oct 20		Tue Oct 21		Wed Oct 22		Thu Oct 23	

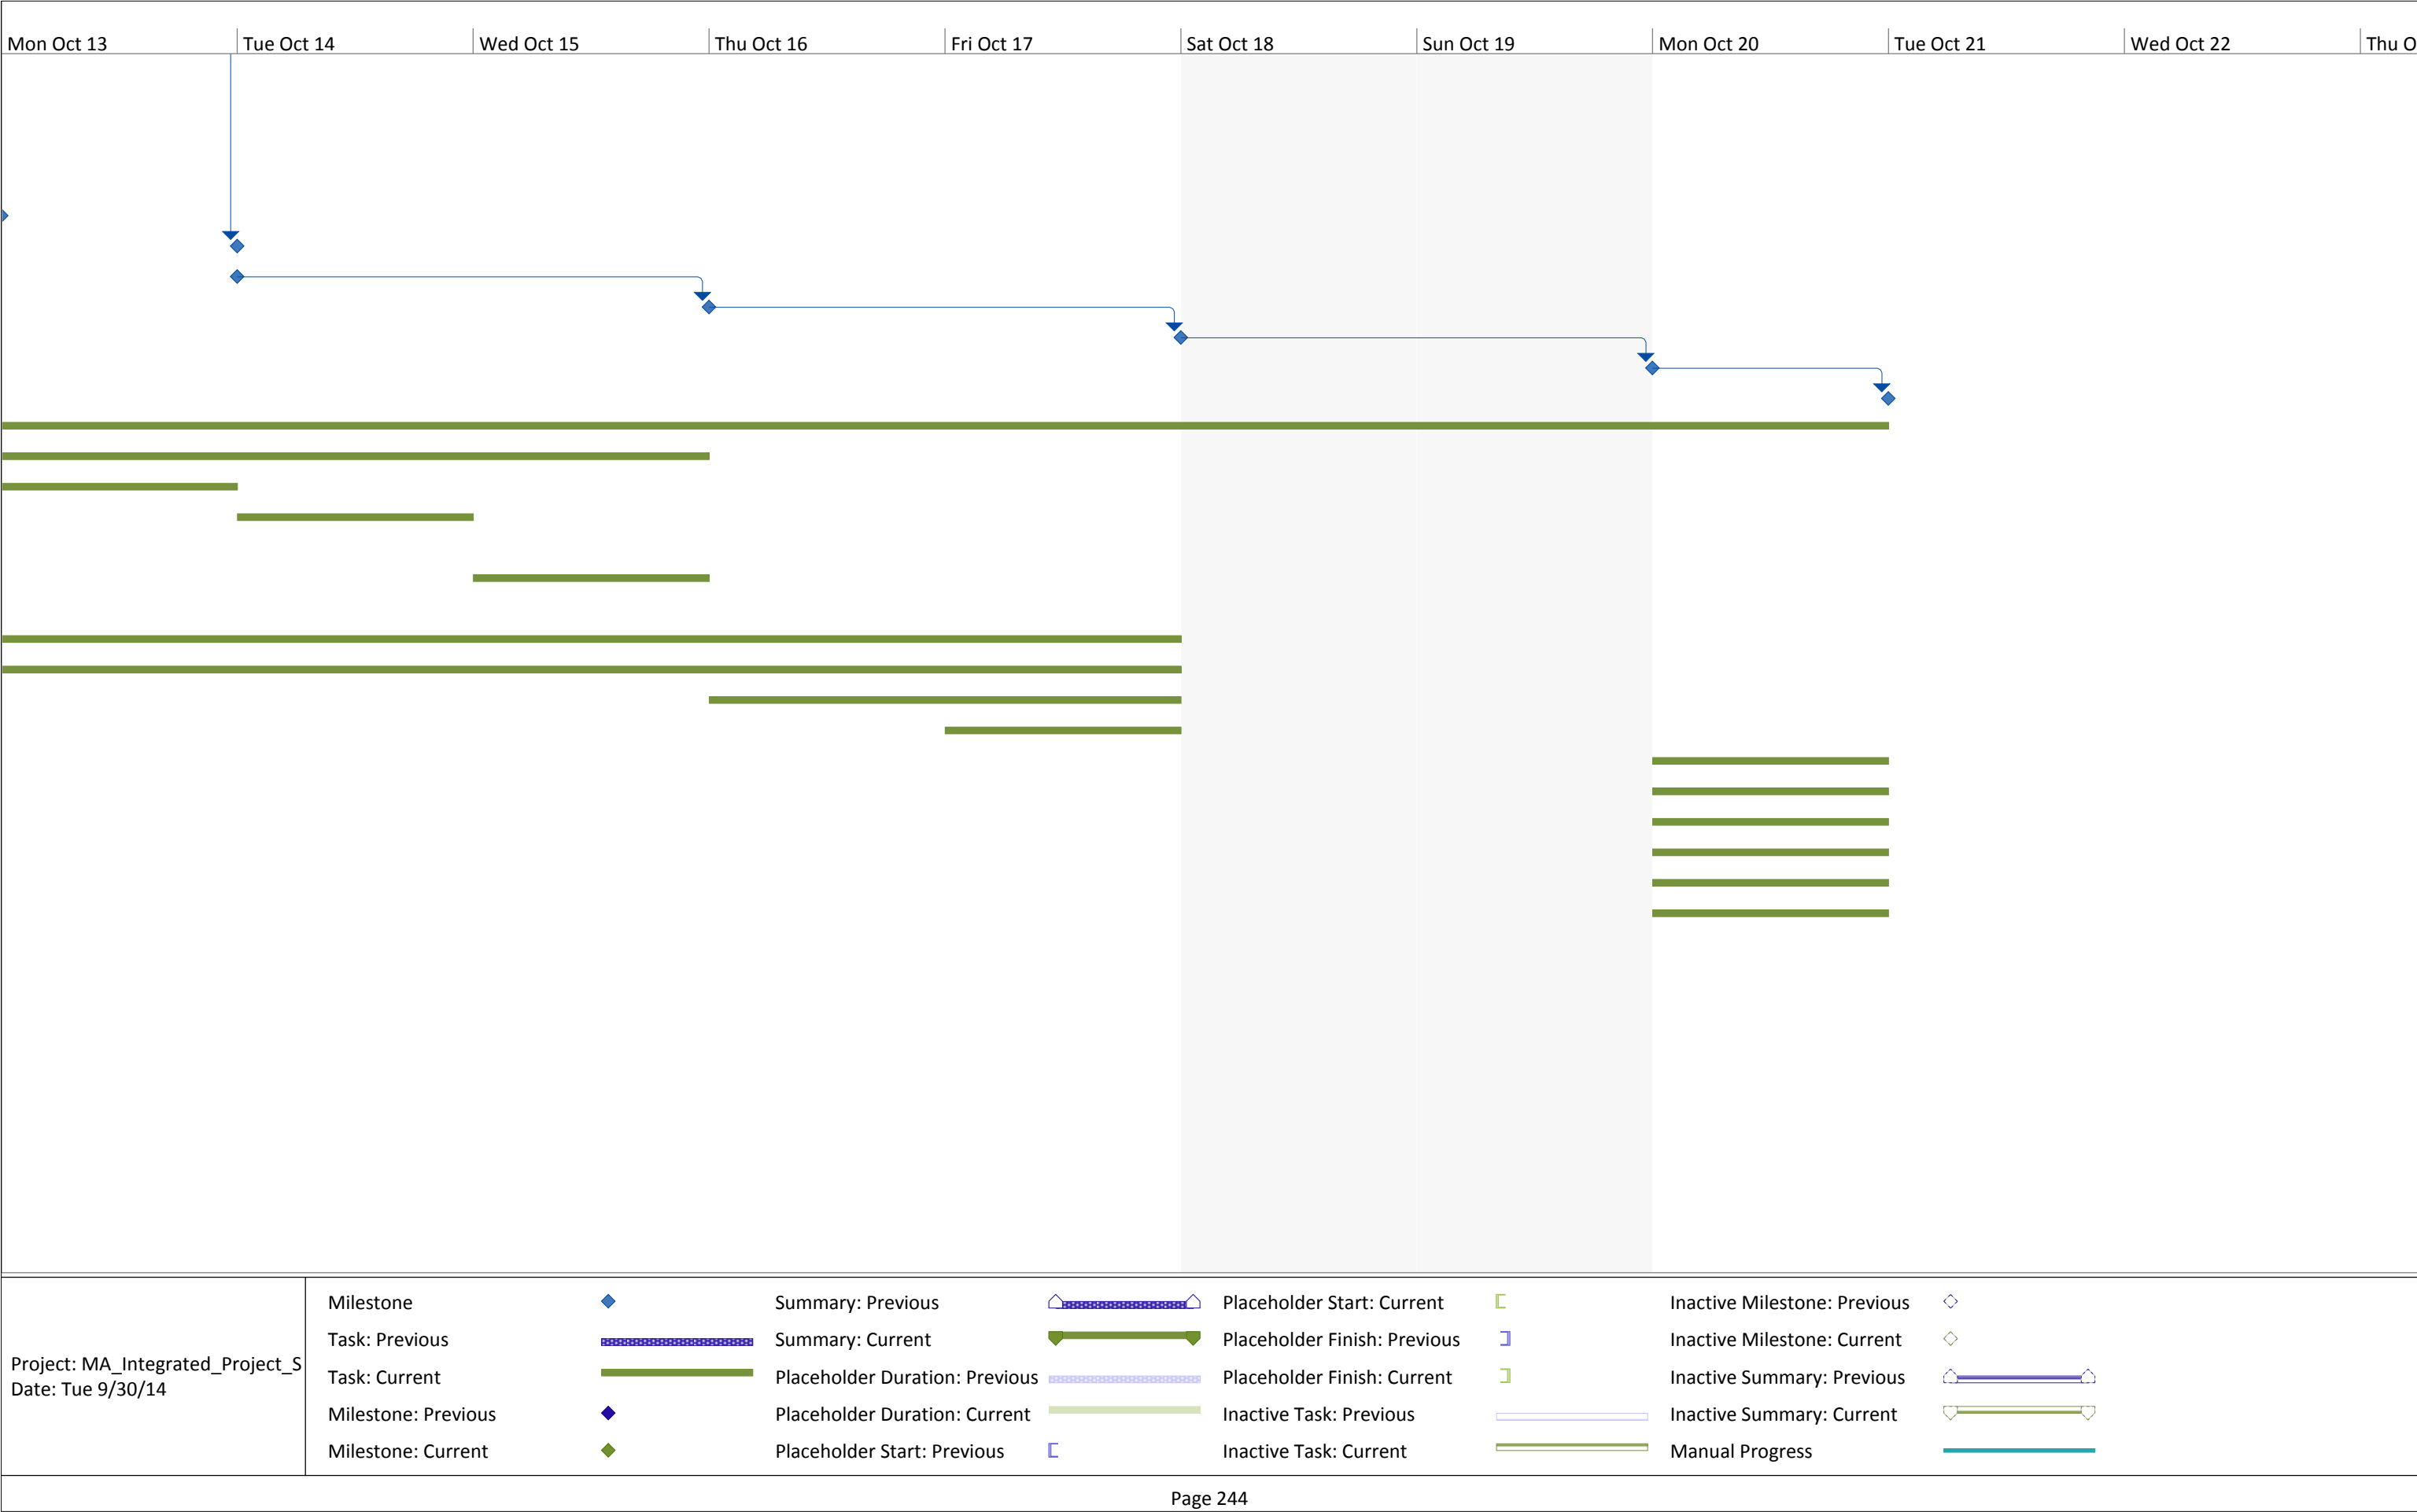


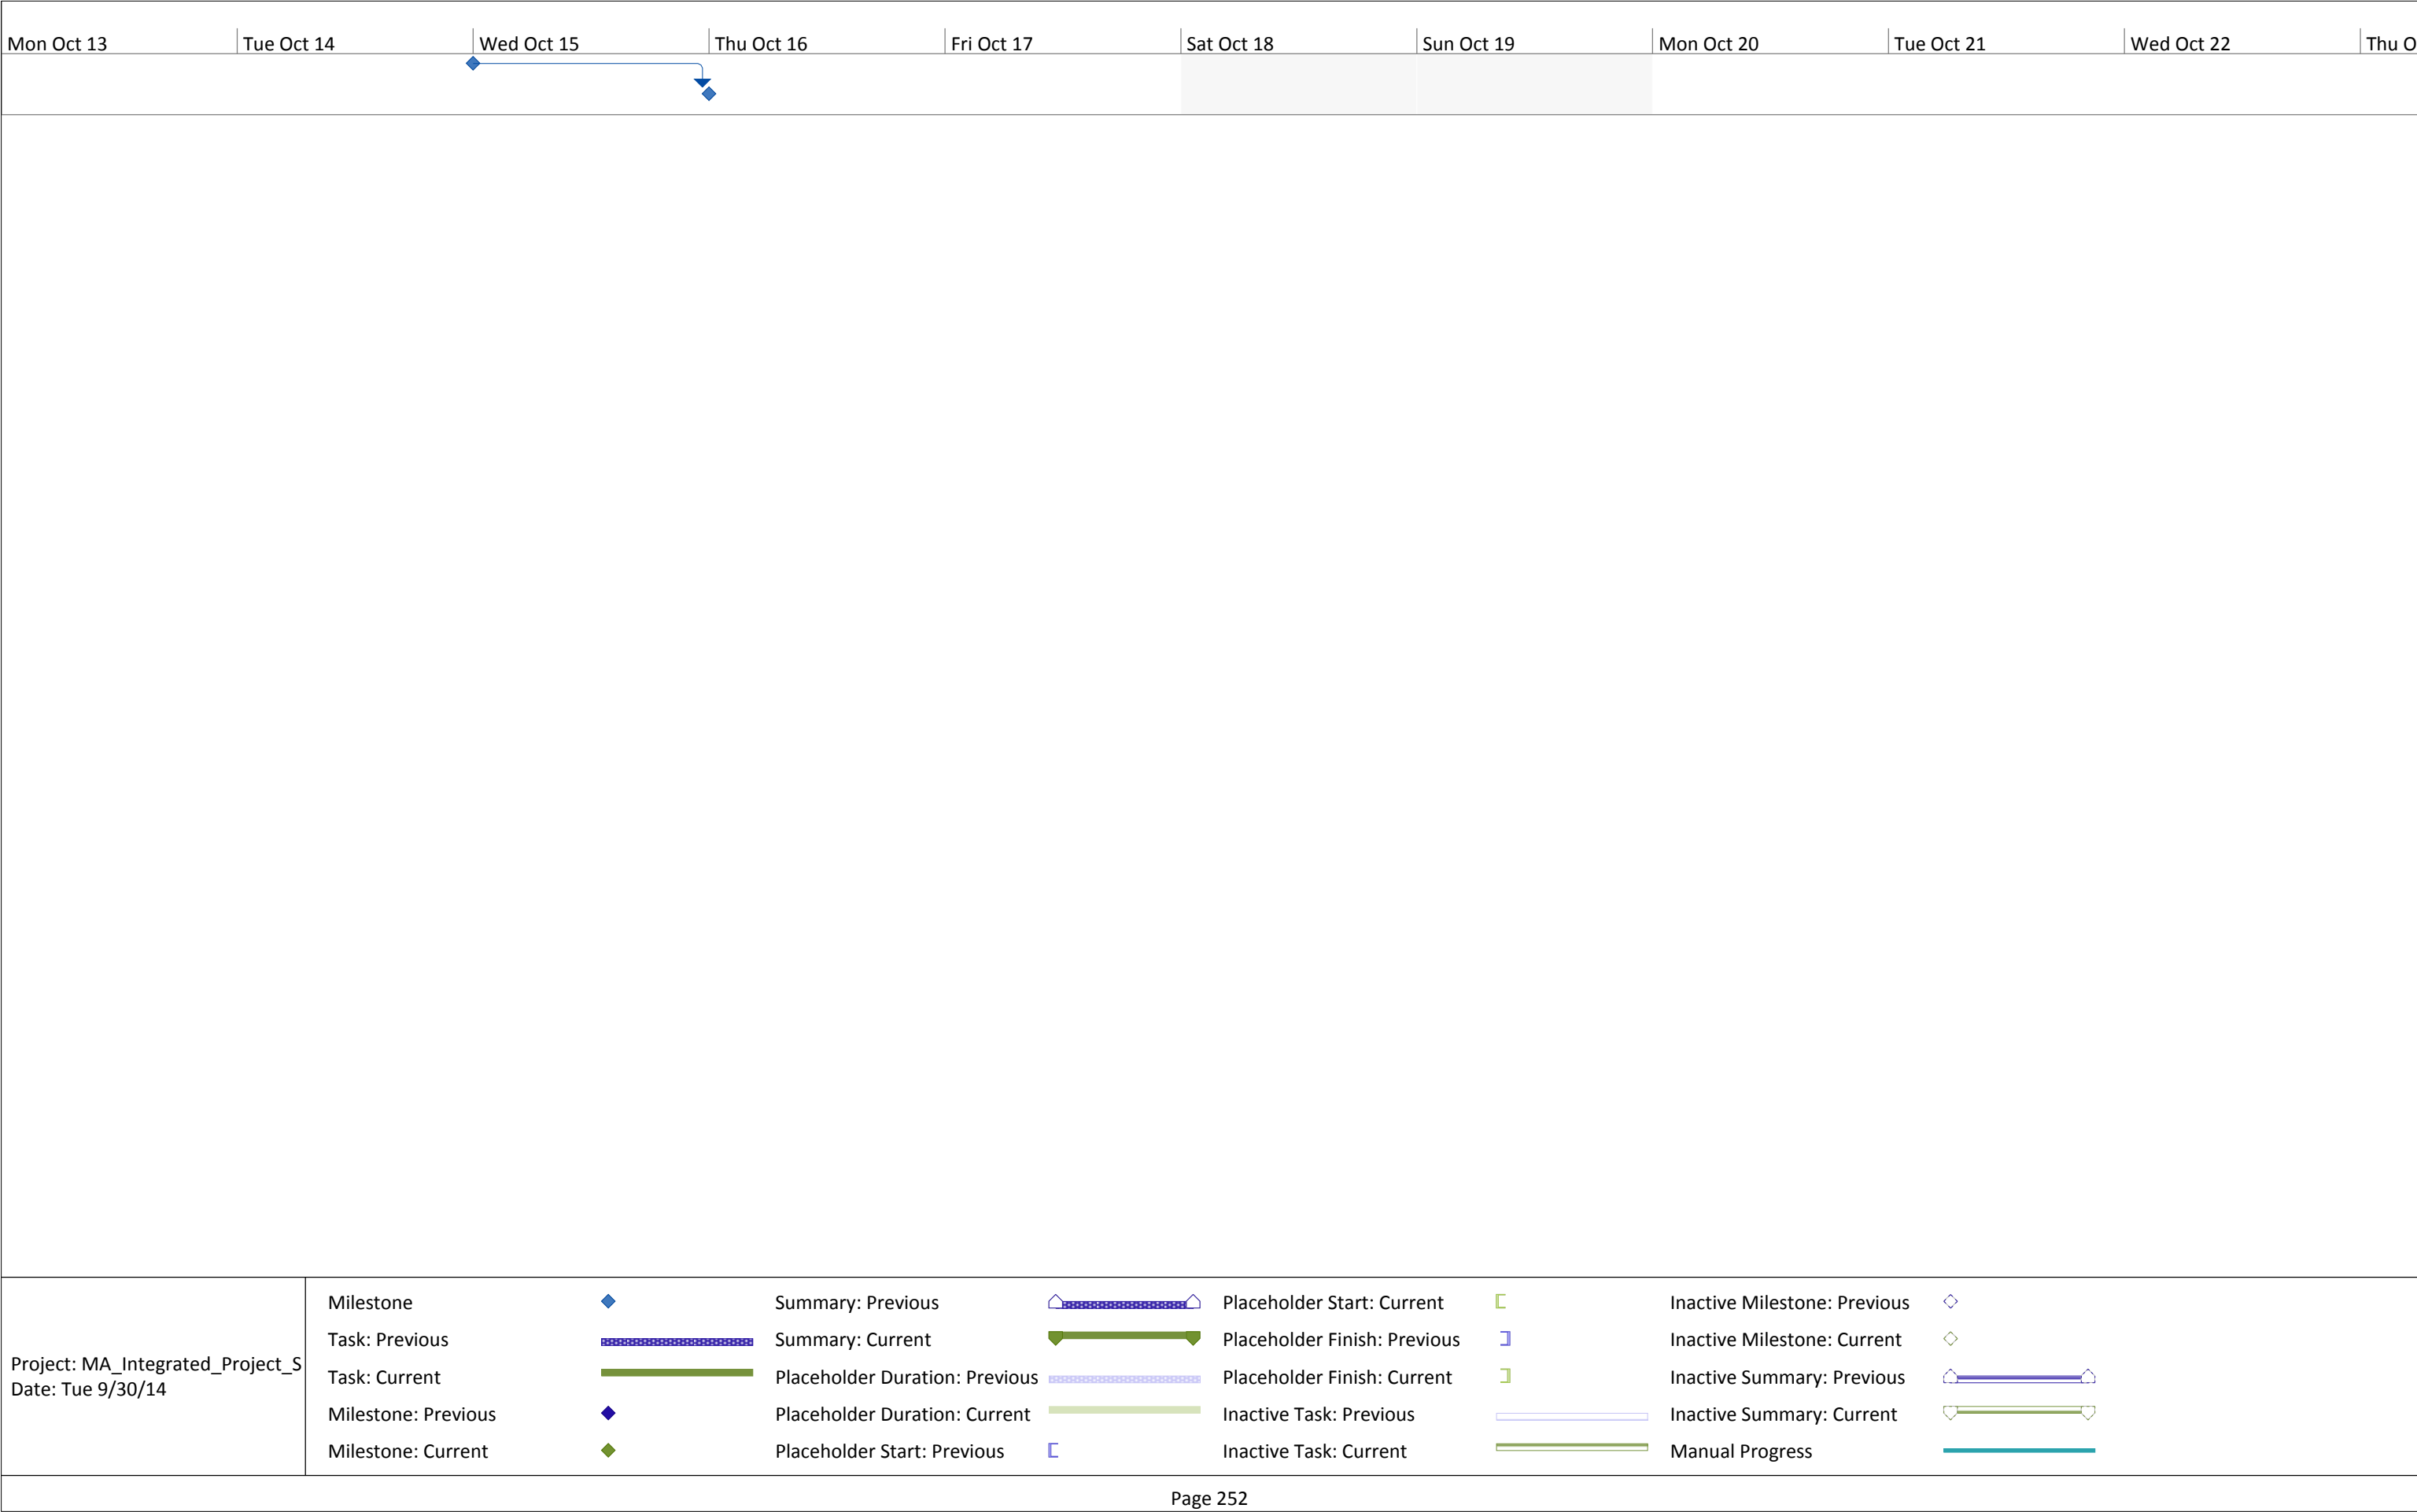

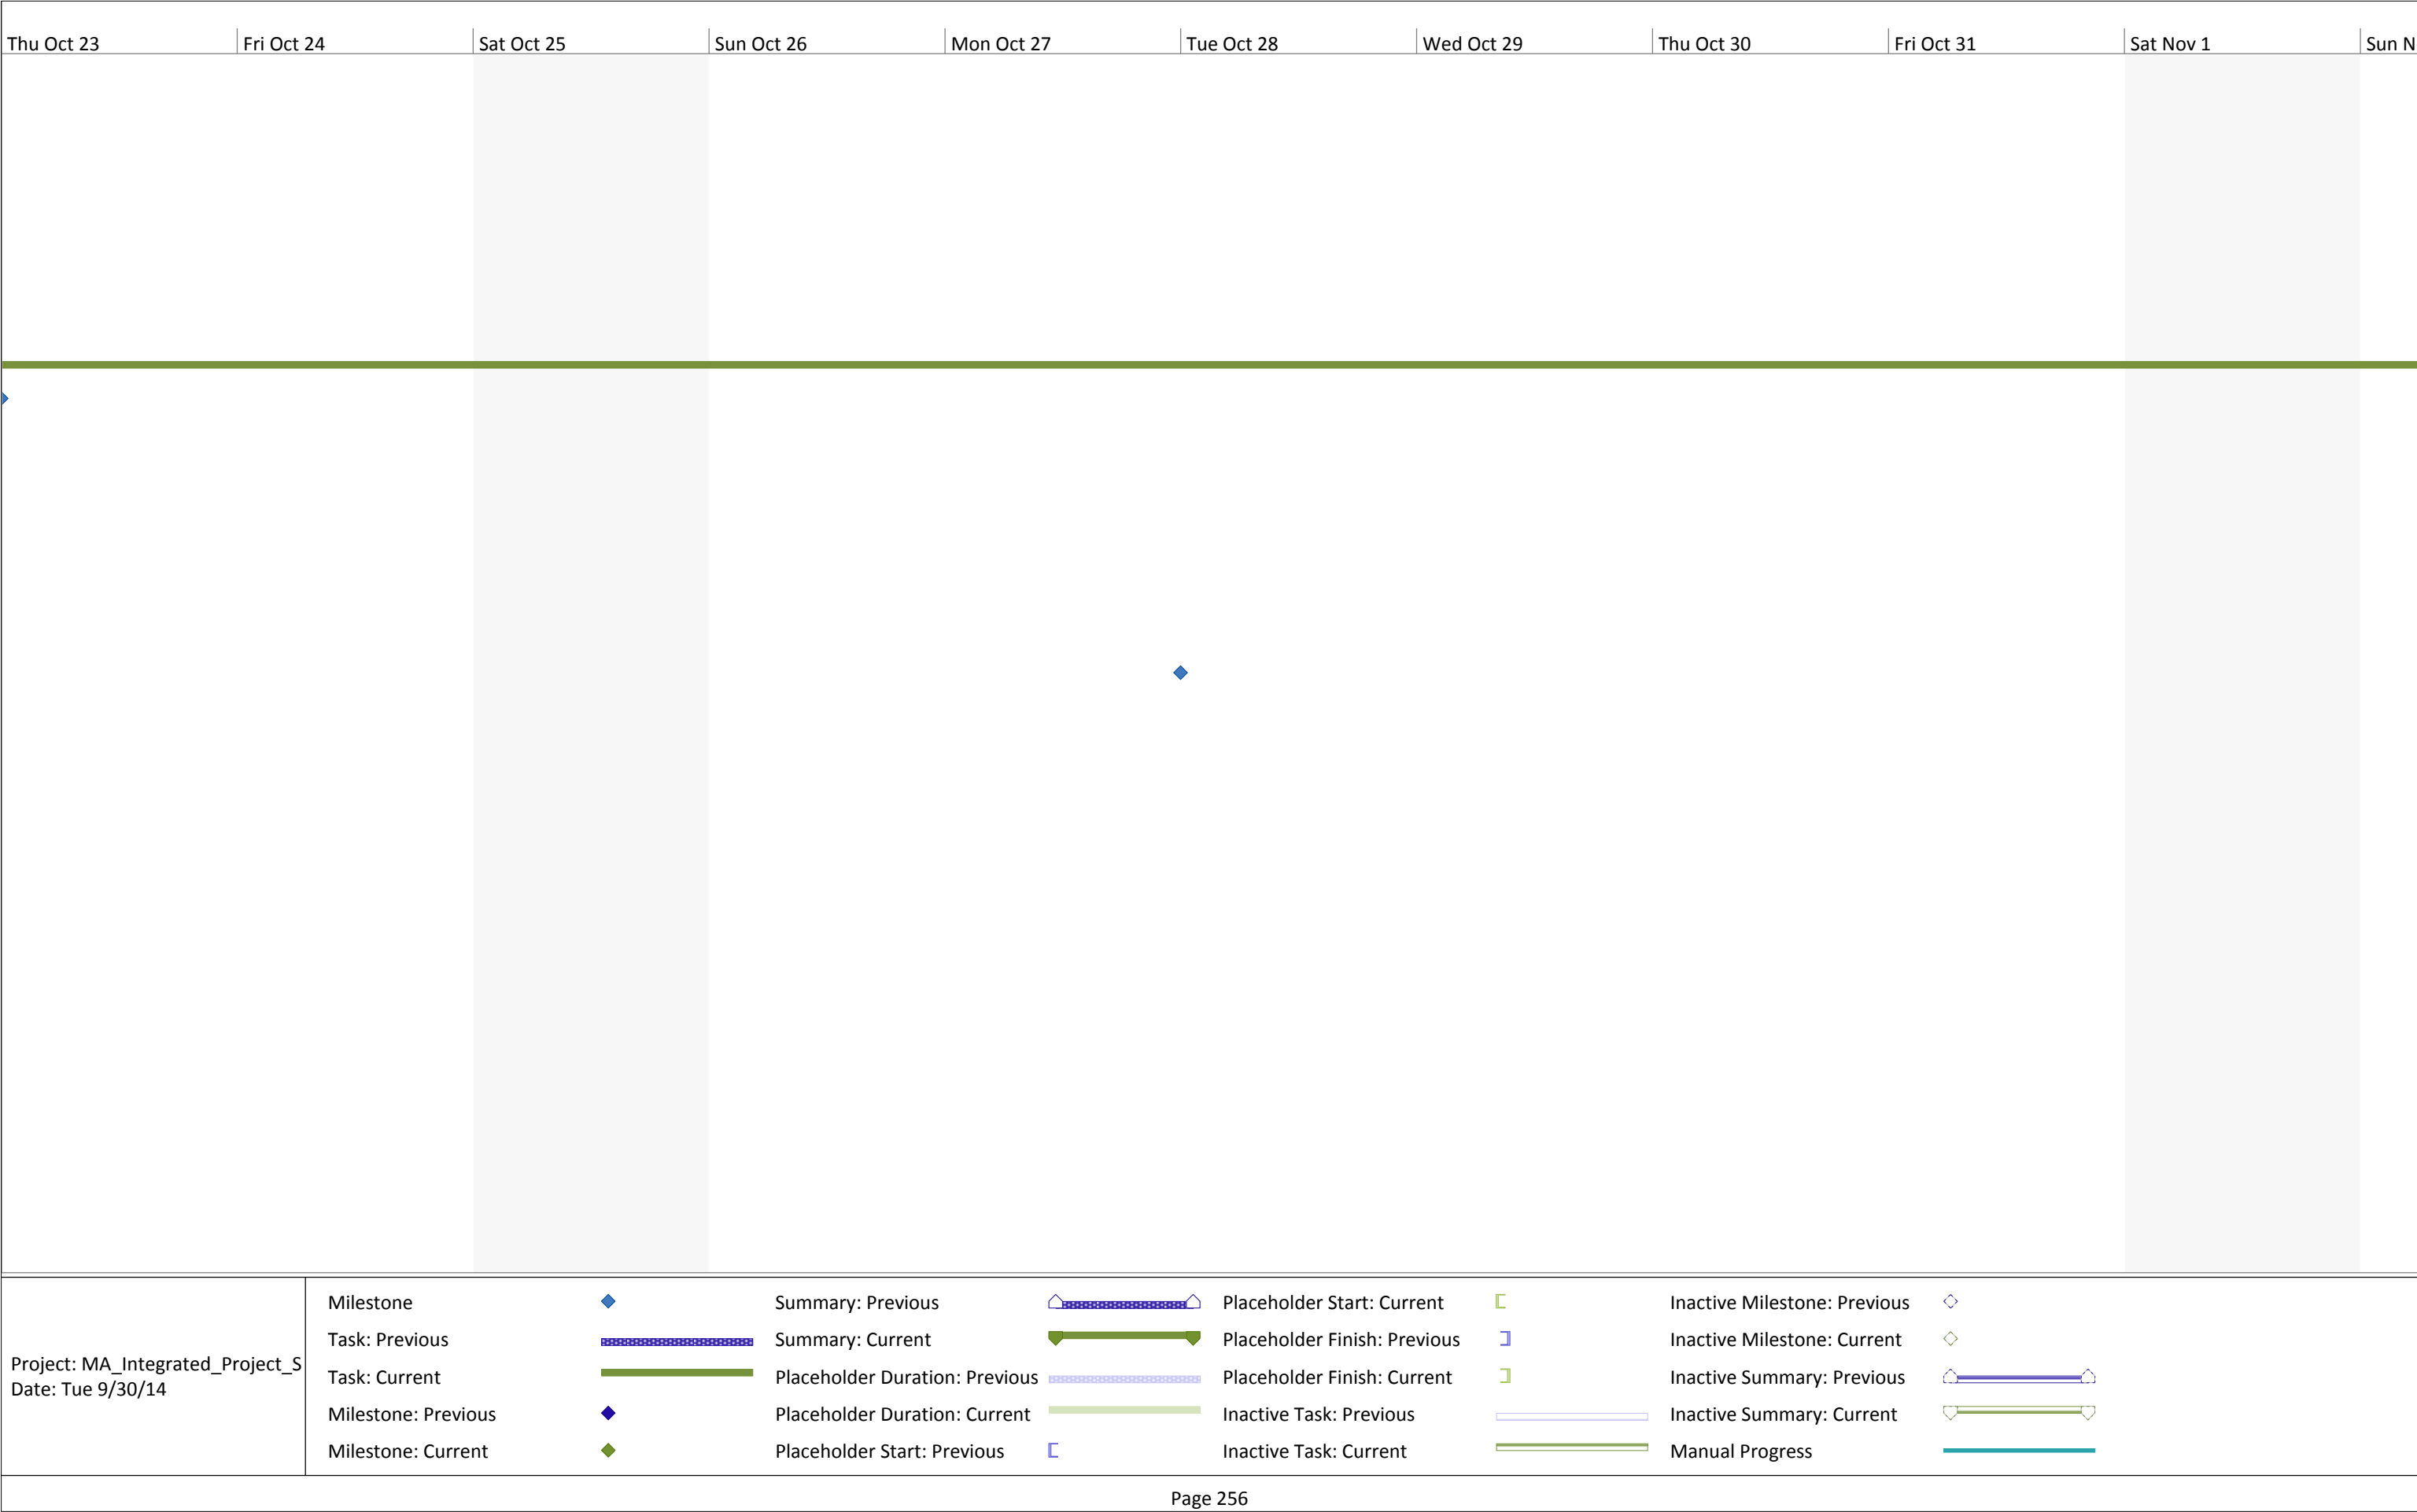



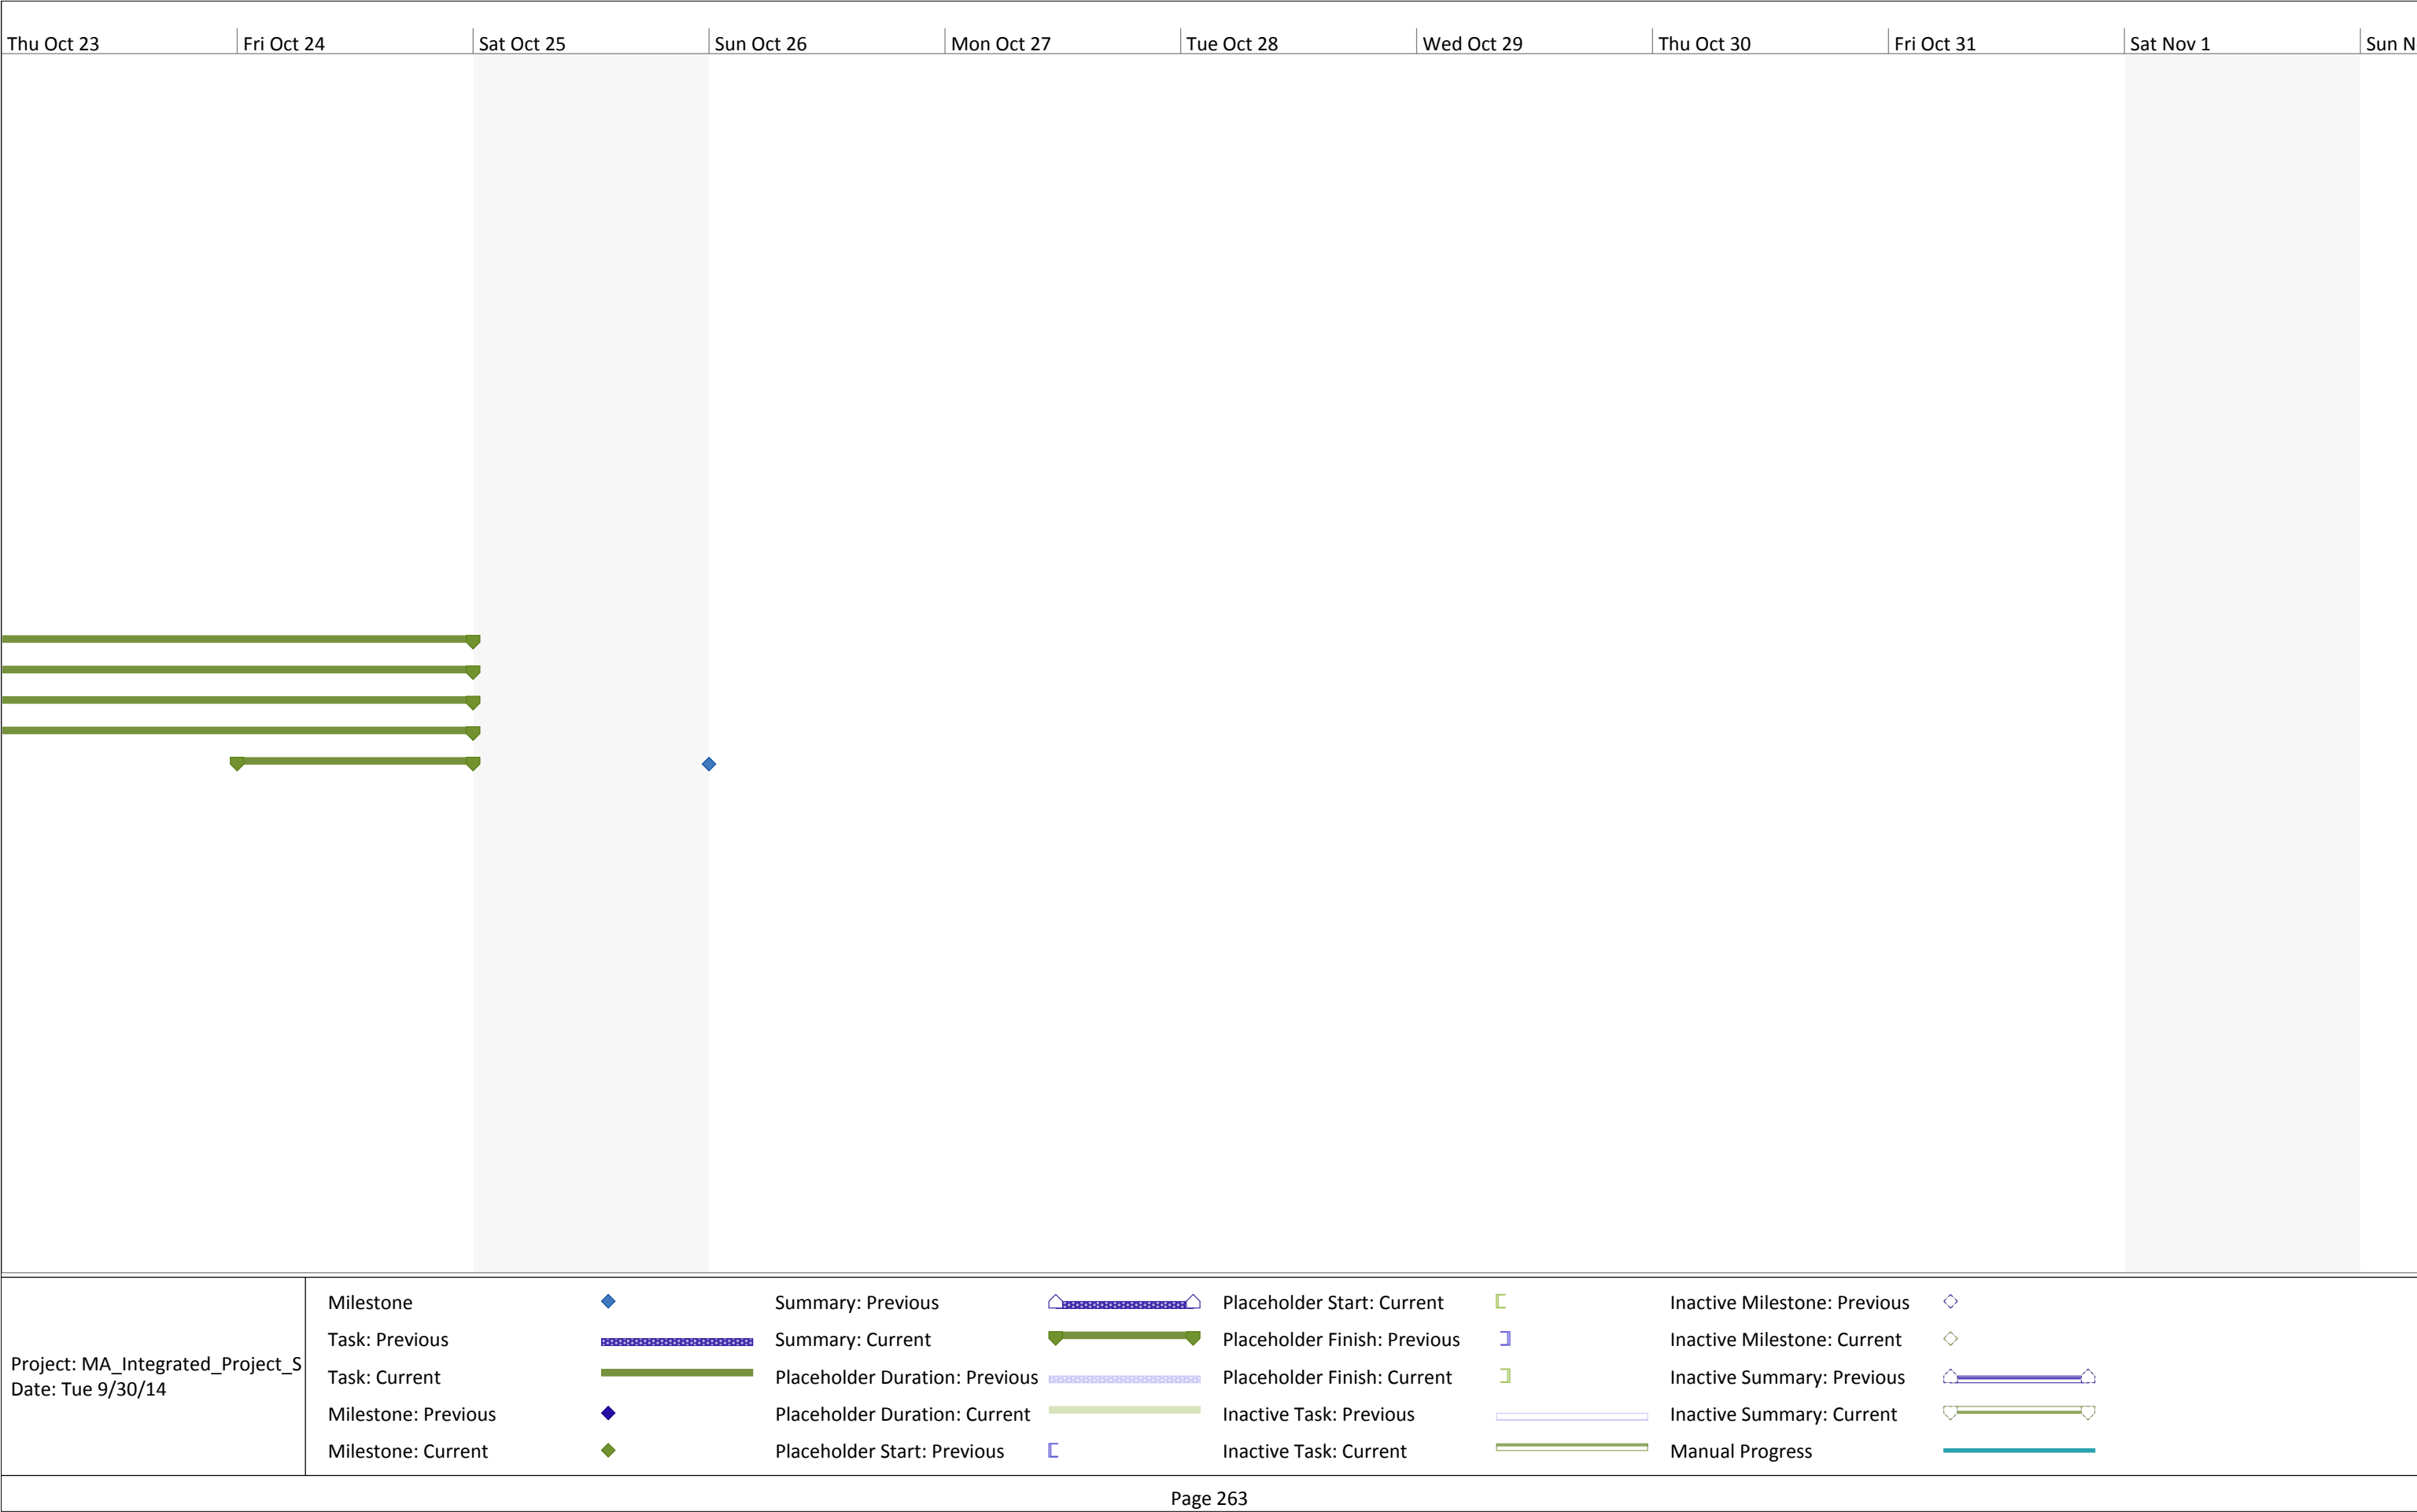

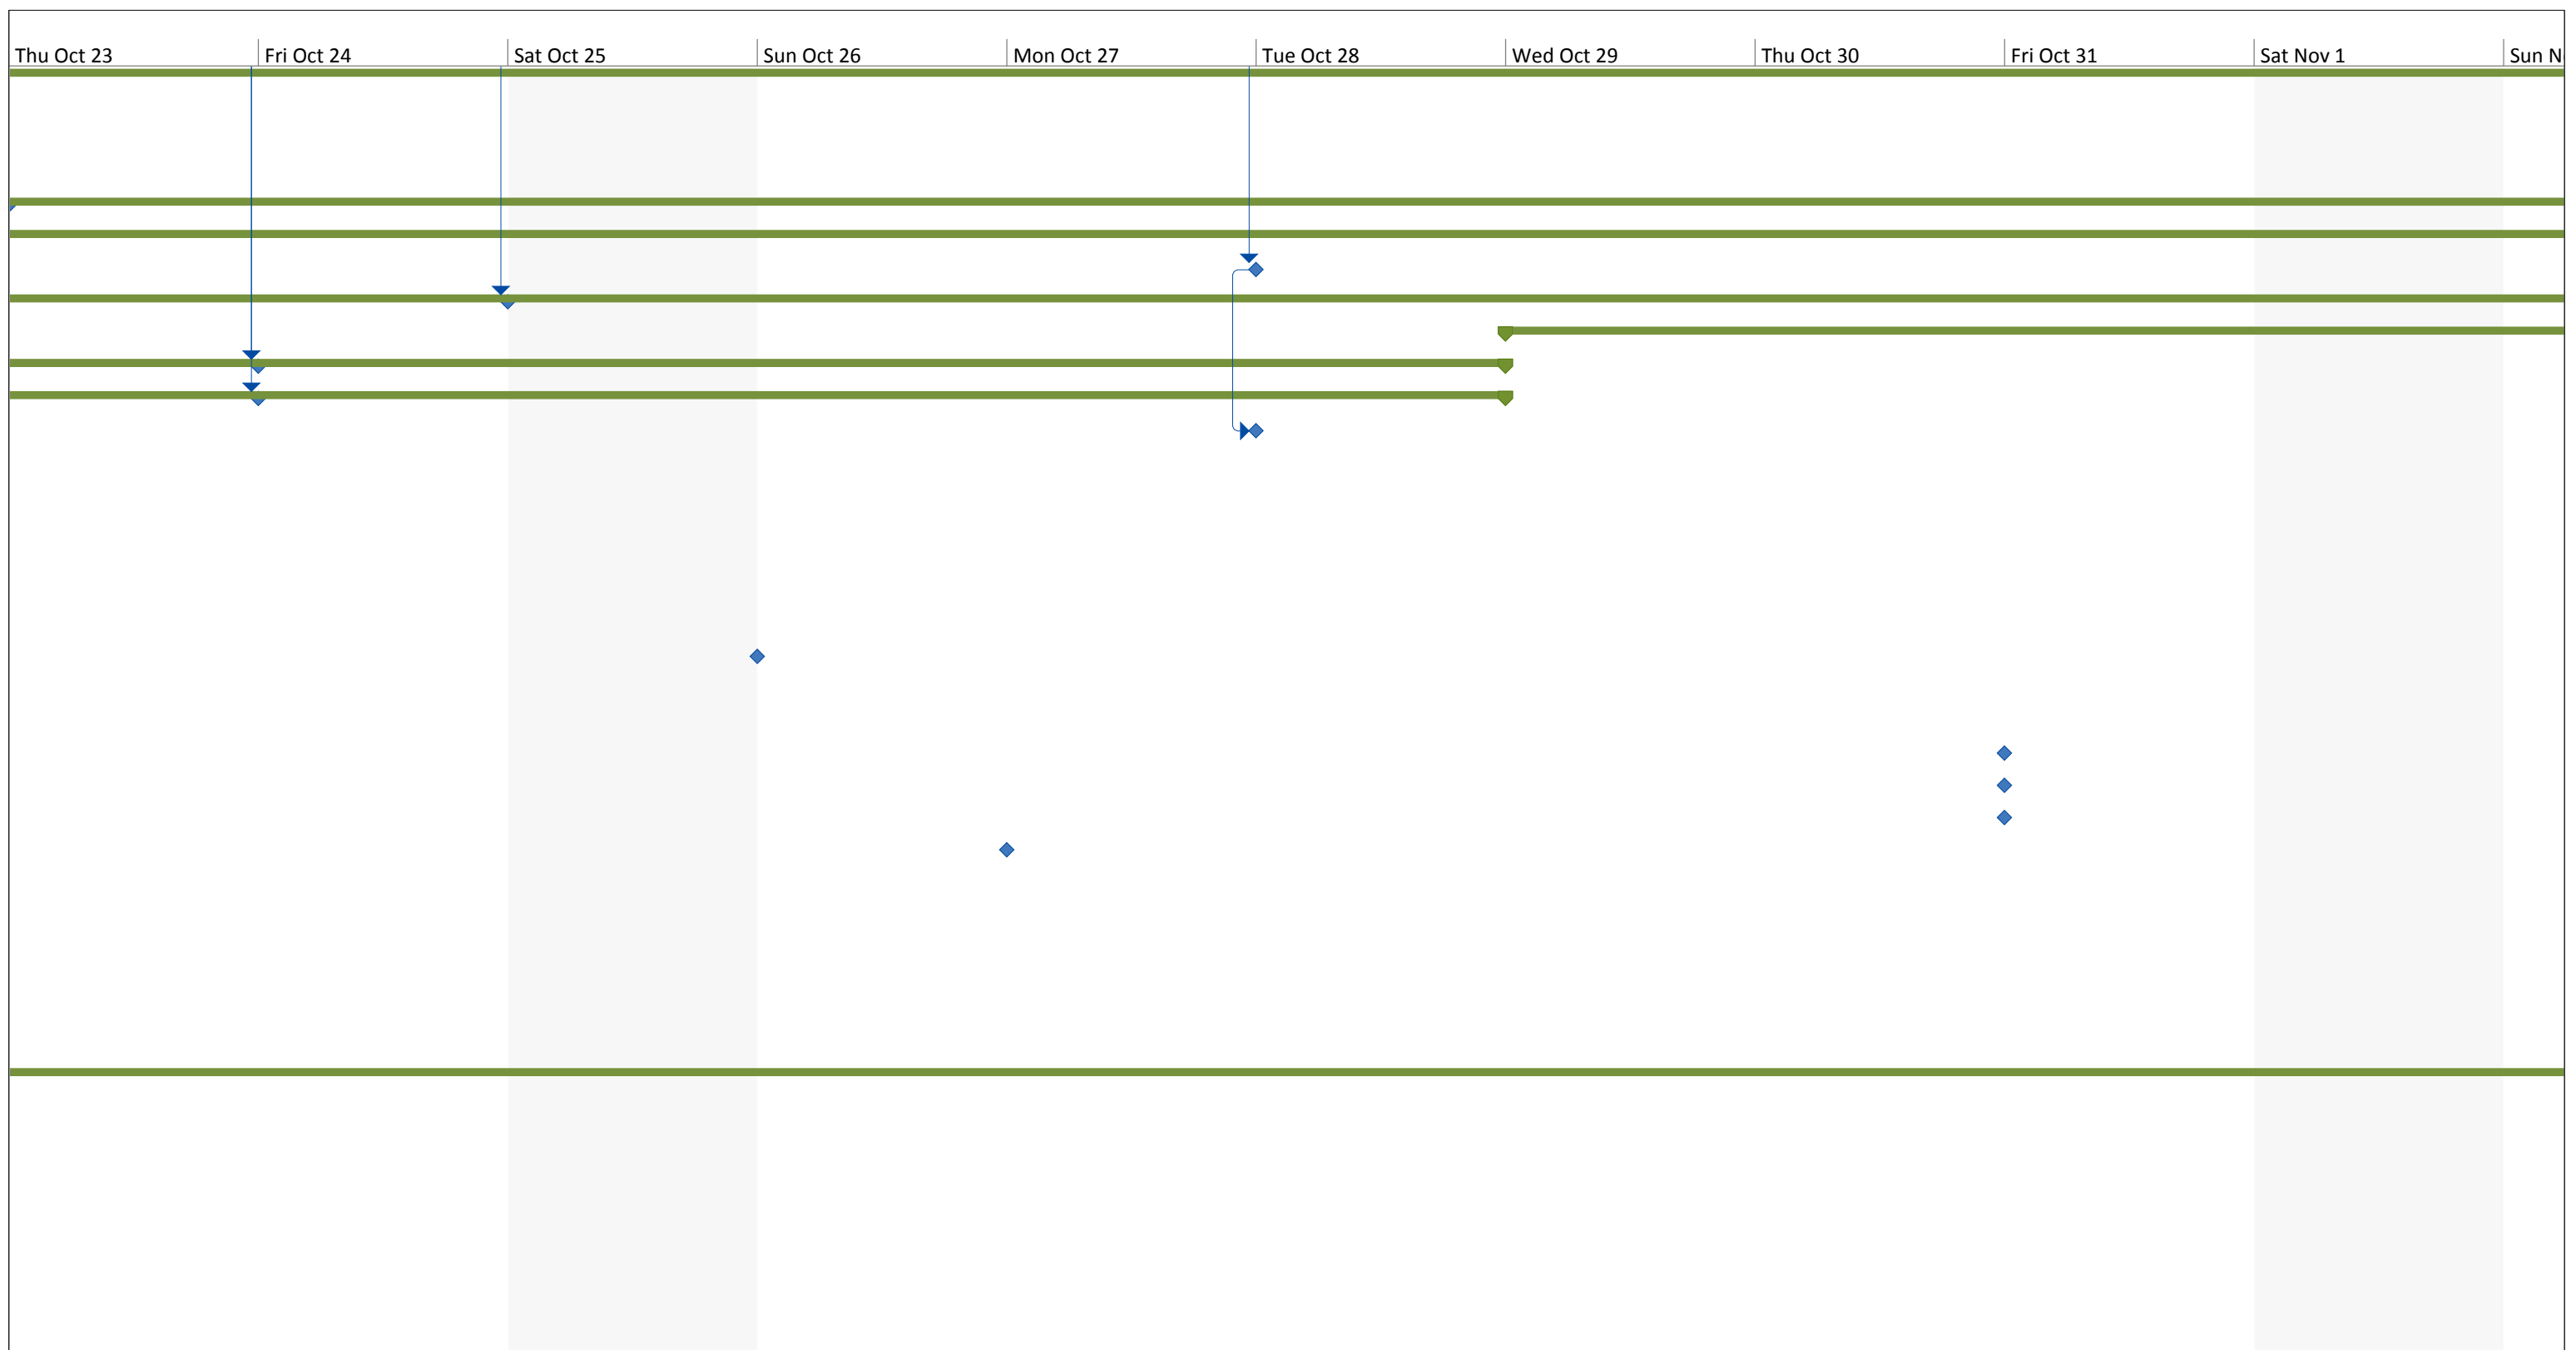





















Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	

Thu Oct 23

Fri Oct 24

Sat Oct 25

Sun Oct 26

Mon Oct 27

Tue Oct 28

Wed Oct 29

Thu Oct 30

Fri Oct 31

Sat Nov 1

Sun Nov 2

Project: MA_Integrated_Project_S

Date: Tue 9/30/14

Milestone

Task: Previous

Task: Current

Milestone: Previous

Milestone: Current

◆

▬

▬

◆

◆

Summary: Previous

Summary: Current

Placeholder Duration: Previous

Placeholder Duration: Current

Placeholder Start: Previous

▬

▬

▬

▬

▬

Placeholder Start: Current

Placeholder Finish: Previous

Placeholder Finish: Current

Inactive Task: Previous

Inactive Task: Current

▬

▬

▬

▬

▬

Inactive Milestone: Previous


Inactive Milestone: Current


Inactive Summary: Previous


Inactive Summary: Current


Manual Progress


Page 269














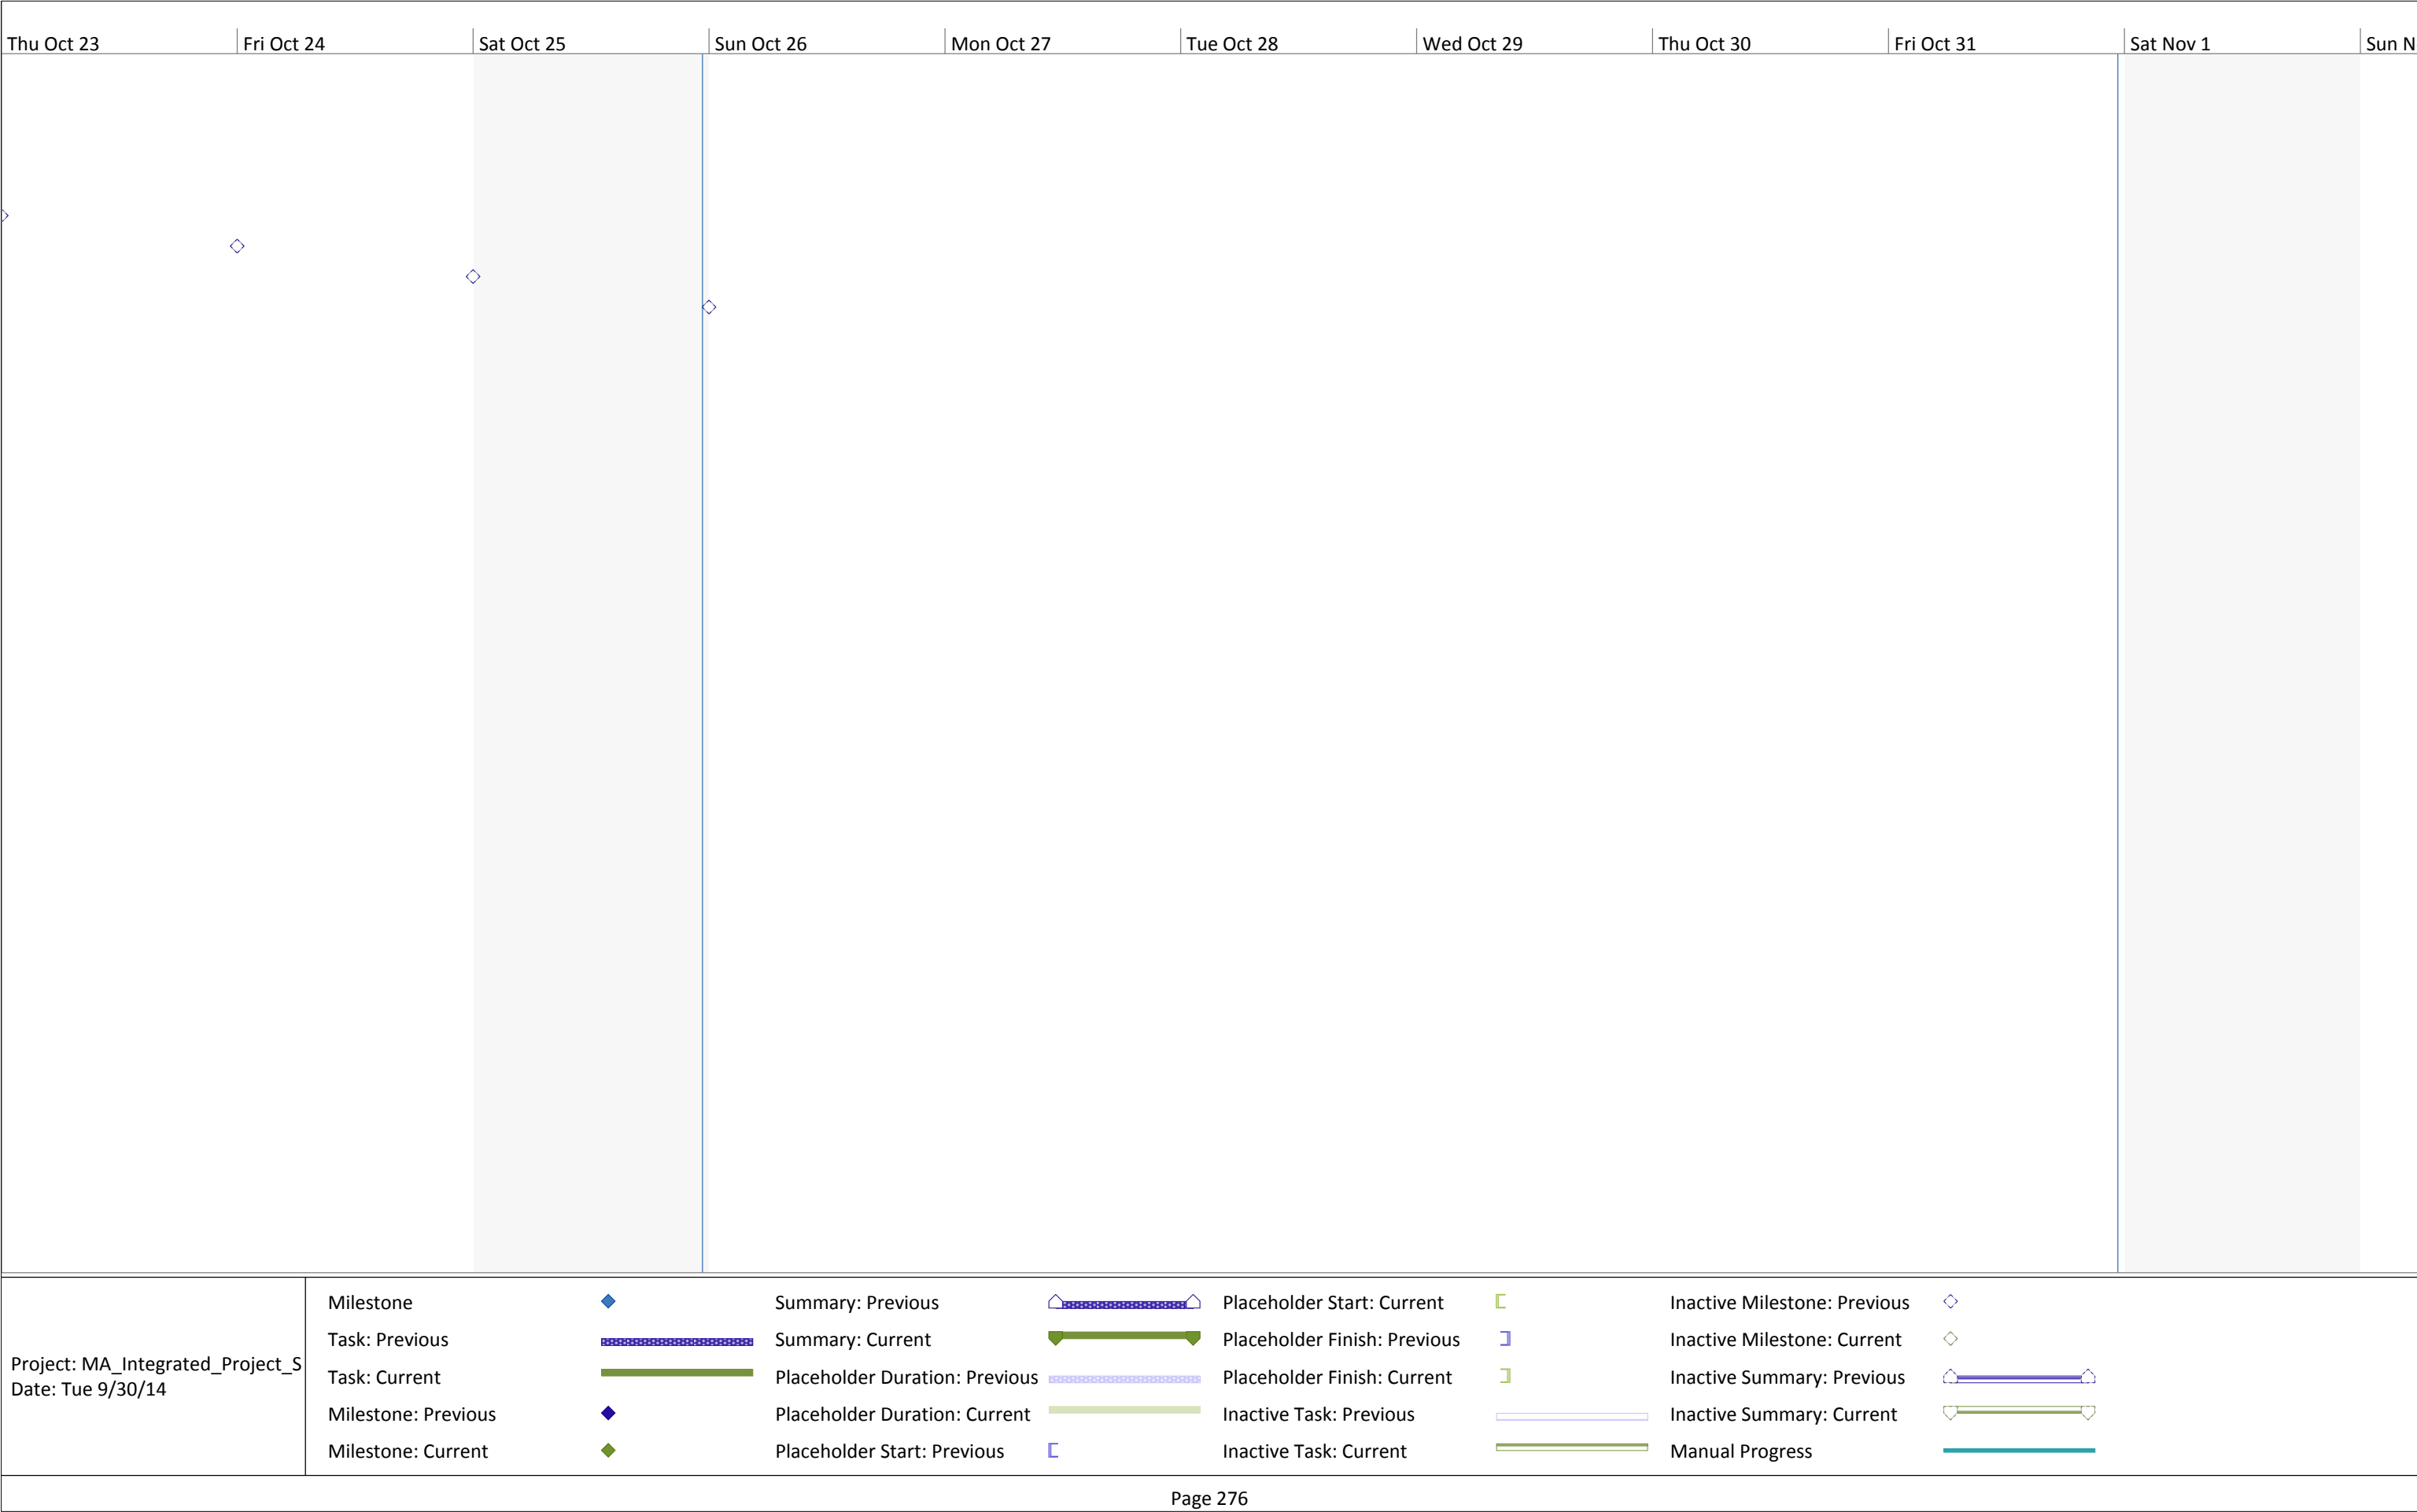

Thu Oct 23		Fri Oct 24		Sat Oct 25		Sun Oct 26		Mon Oct 27		Tue Oct 28		Wed Oct 29		Thu Oct 30		Fri Oct 31		Sat Nov 1		Sun Nov 2	


Thu Oct 23		Fri Oct 24		Sat Oct 25		Sun Oct 26		Mon Oct 27		Tue Oct 28		Wed Oct 29		Thu Oct 30		Fri Oct 31		Sat Nov 1		Sun Nov 2	








Thu Oct 23		Fri Oct 24		Sat Oct 25		Sun Oct 26		Mon Oct 27		Tue Oct 28		Wed Oct 29		Thu Oct 30		Fri Oct 31		Sat Nov 1		Sun Nov 2	


Thu Oct 23		Fri Oct 24		Sat Oct 25		Sun Oct 26		Mon Oct 27		Tue Oct 28		Wed Oct 29		Thu Oct 30		Fri Oct 31		Sat Nov 1		Sun Nov 2	




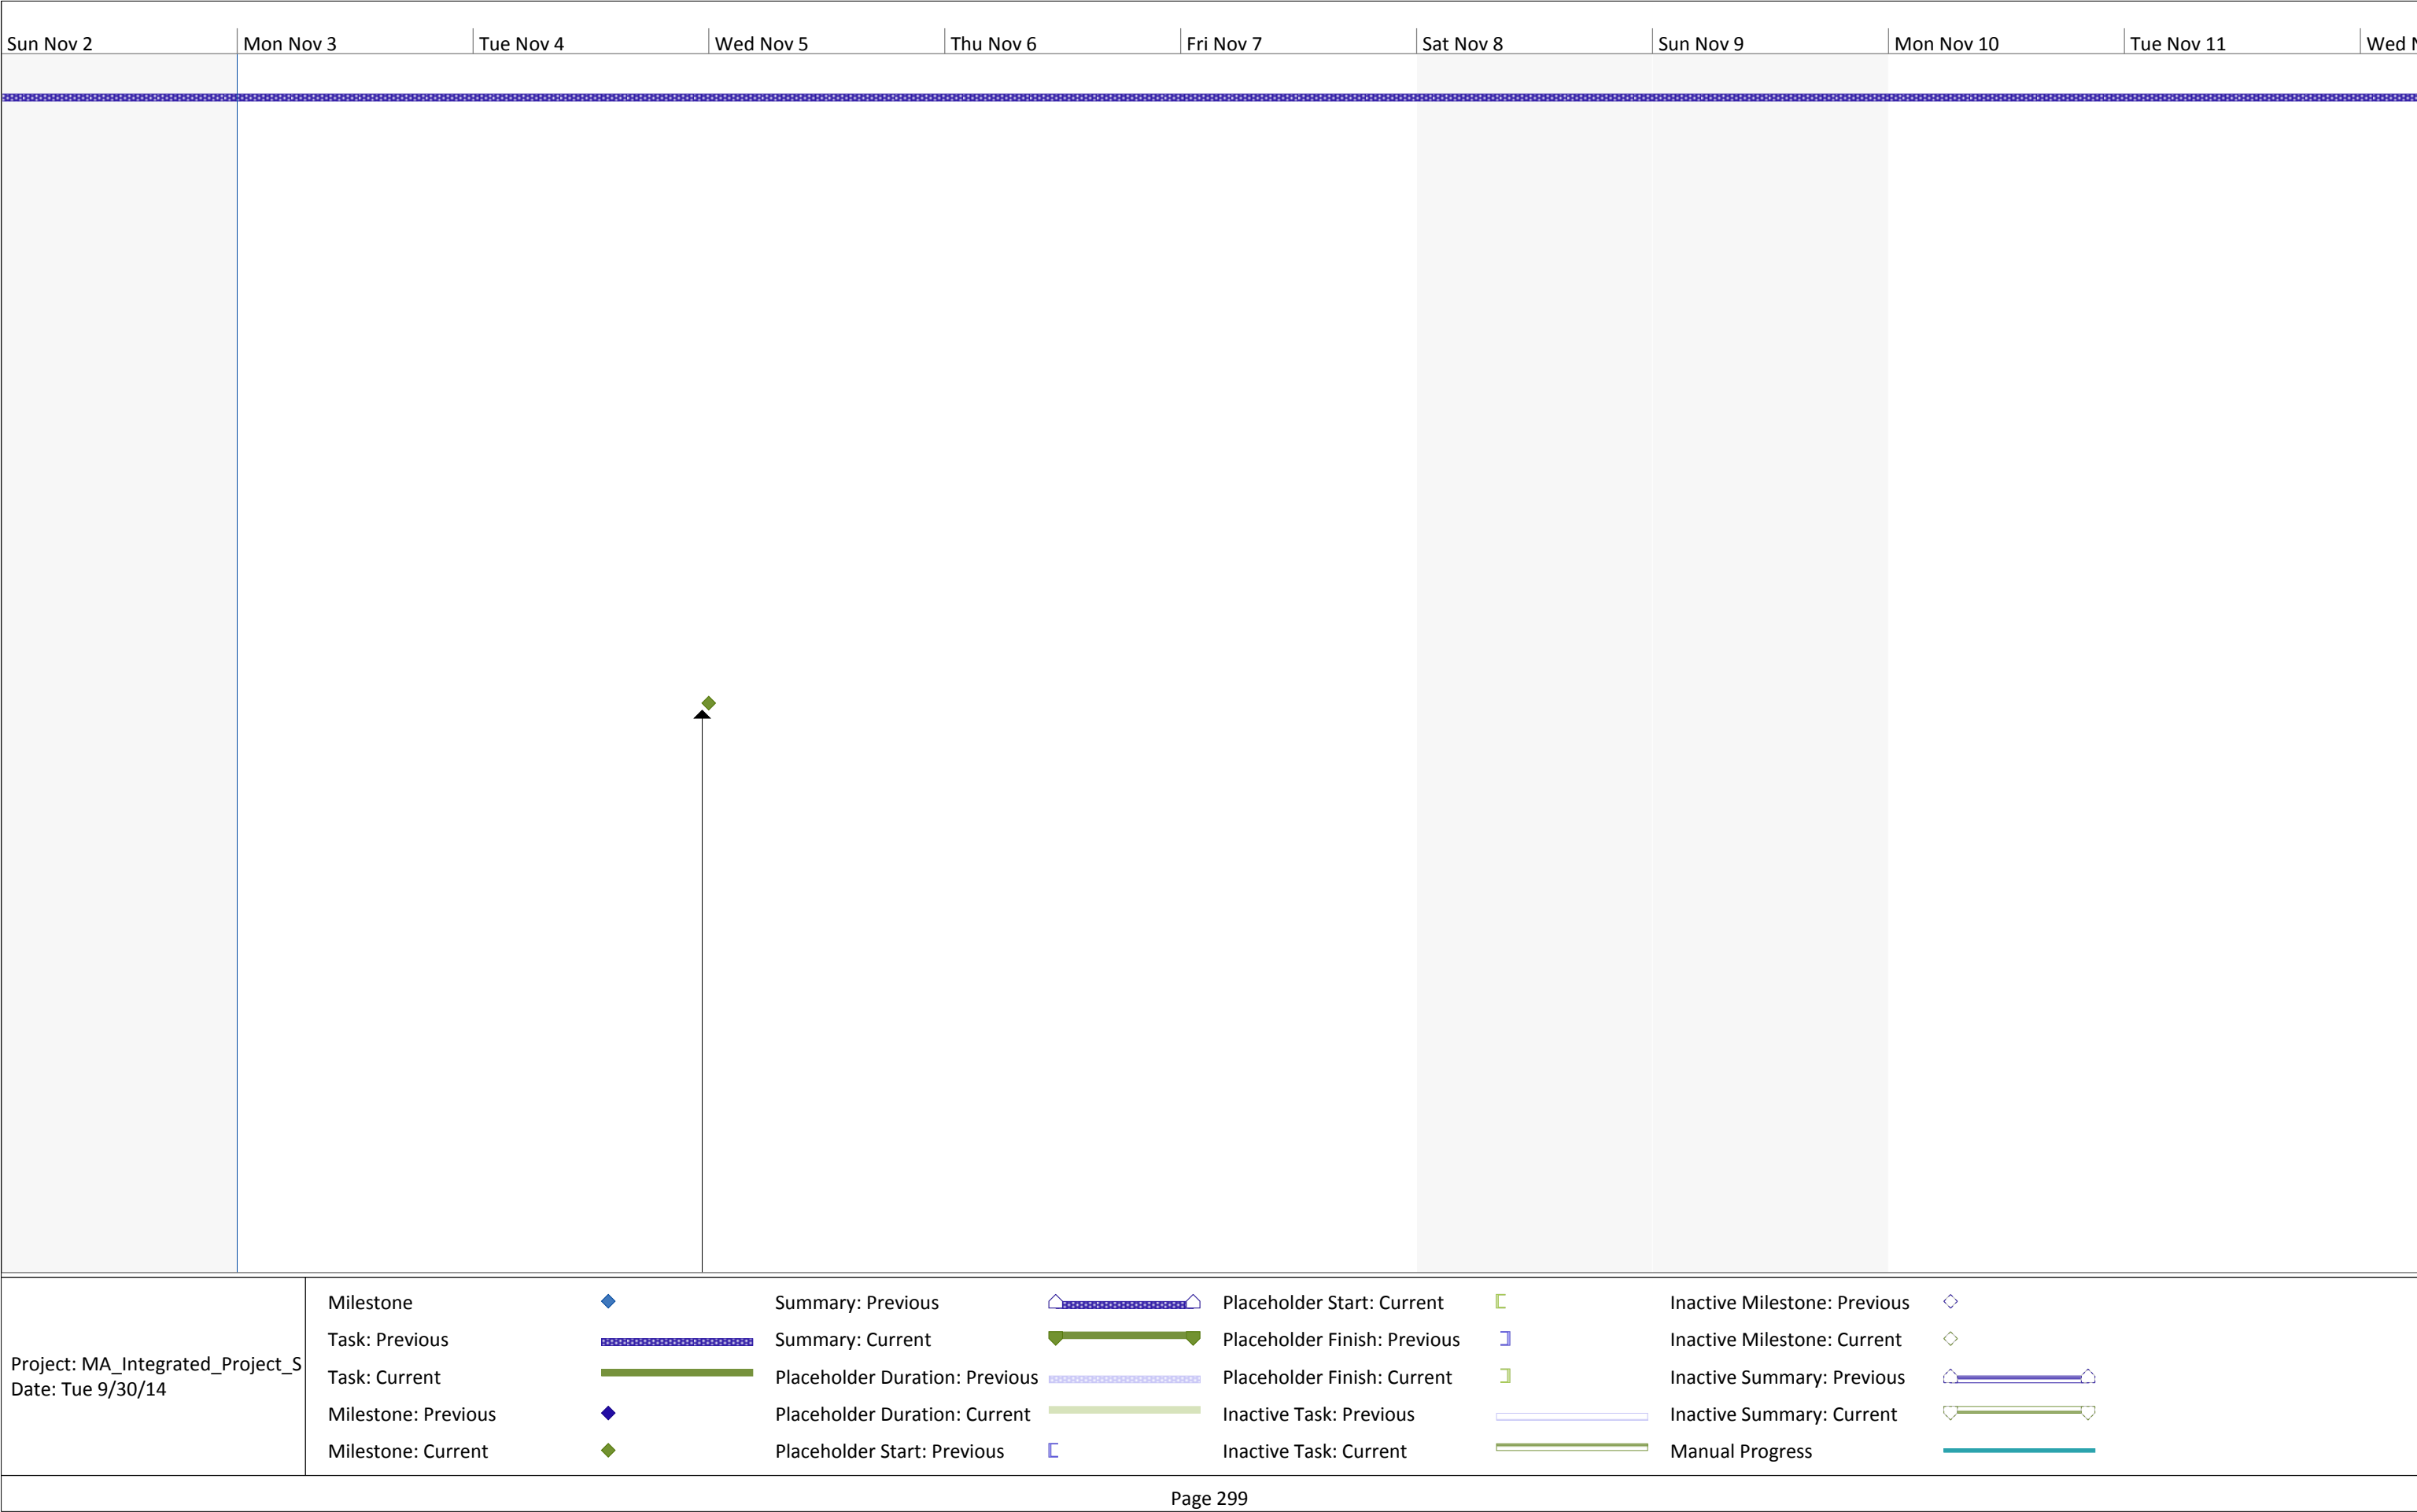



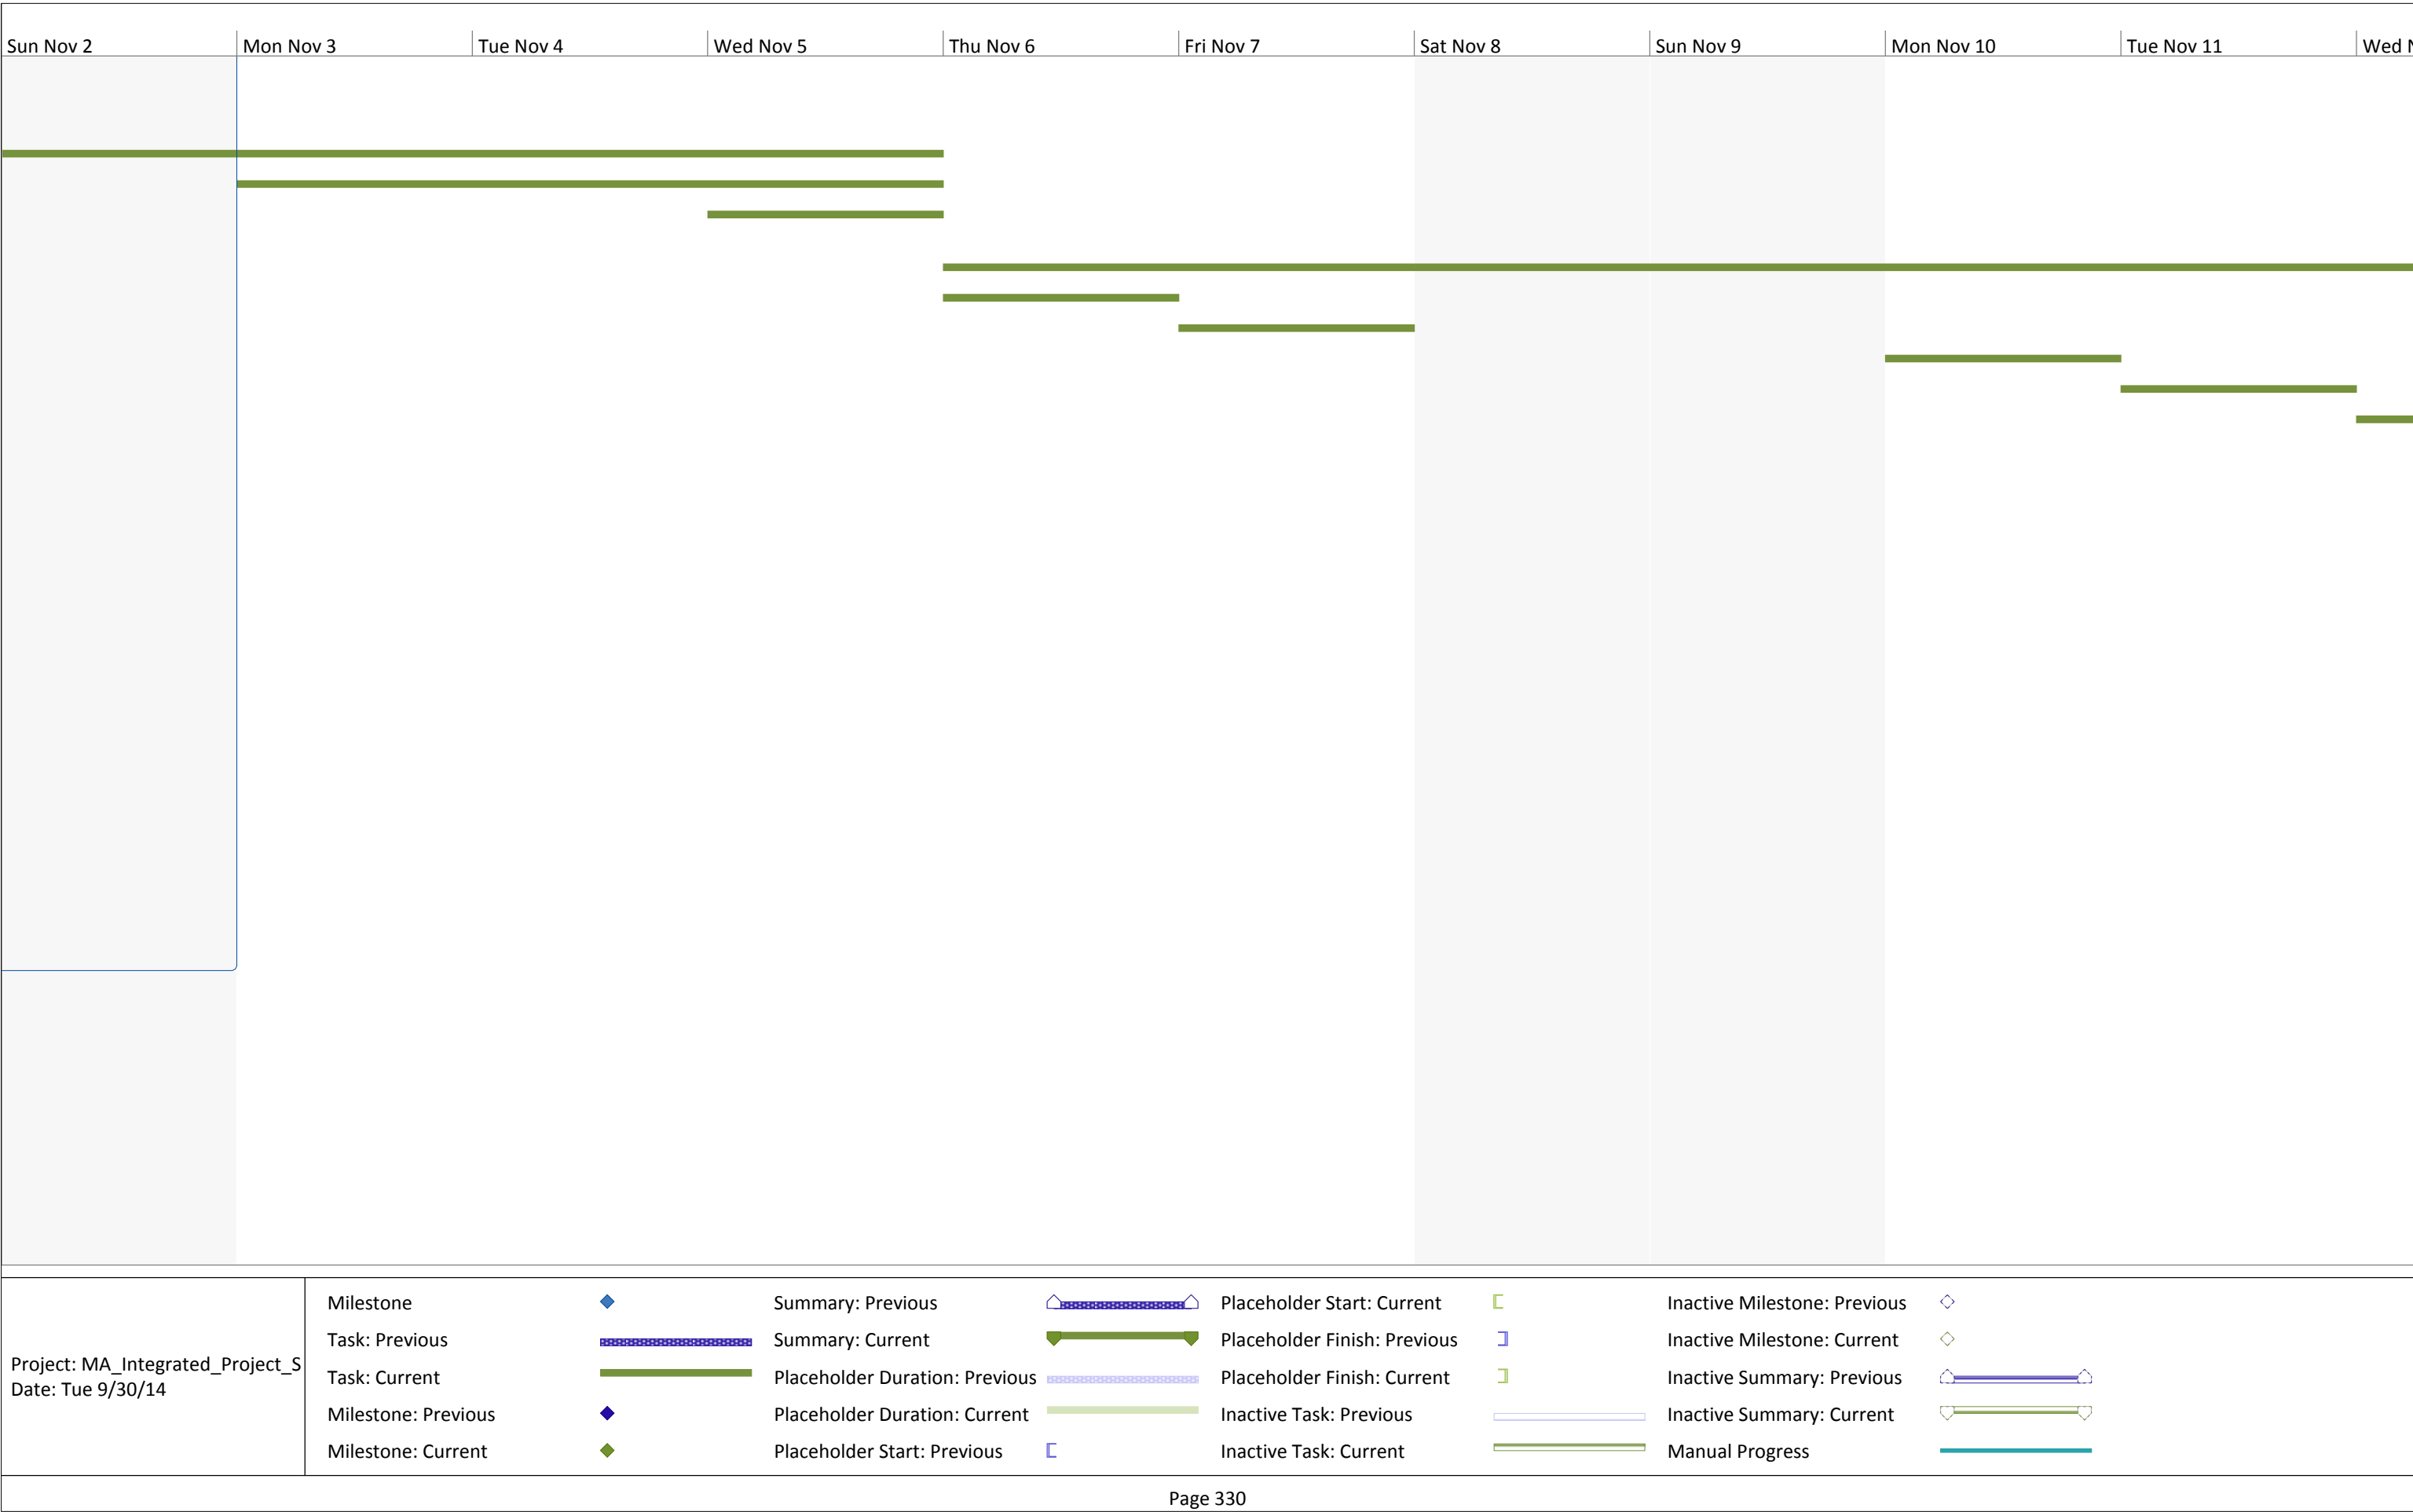

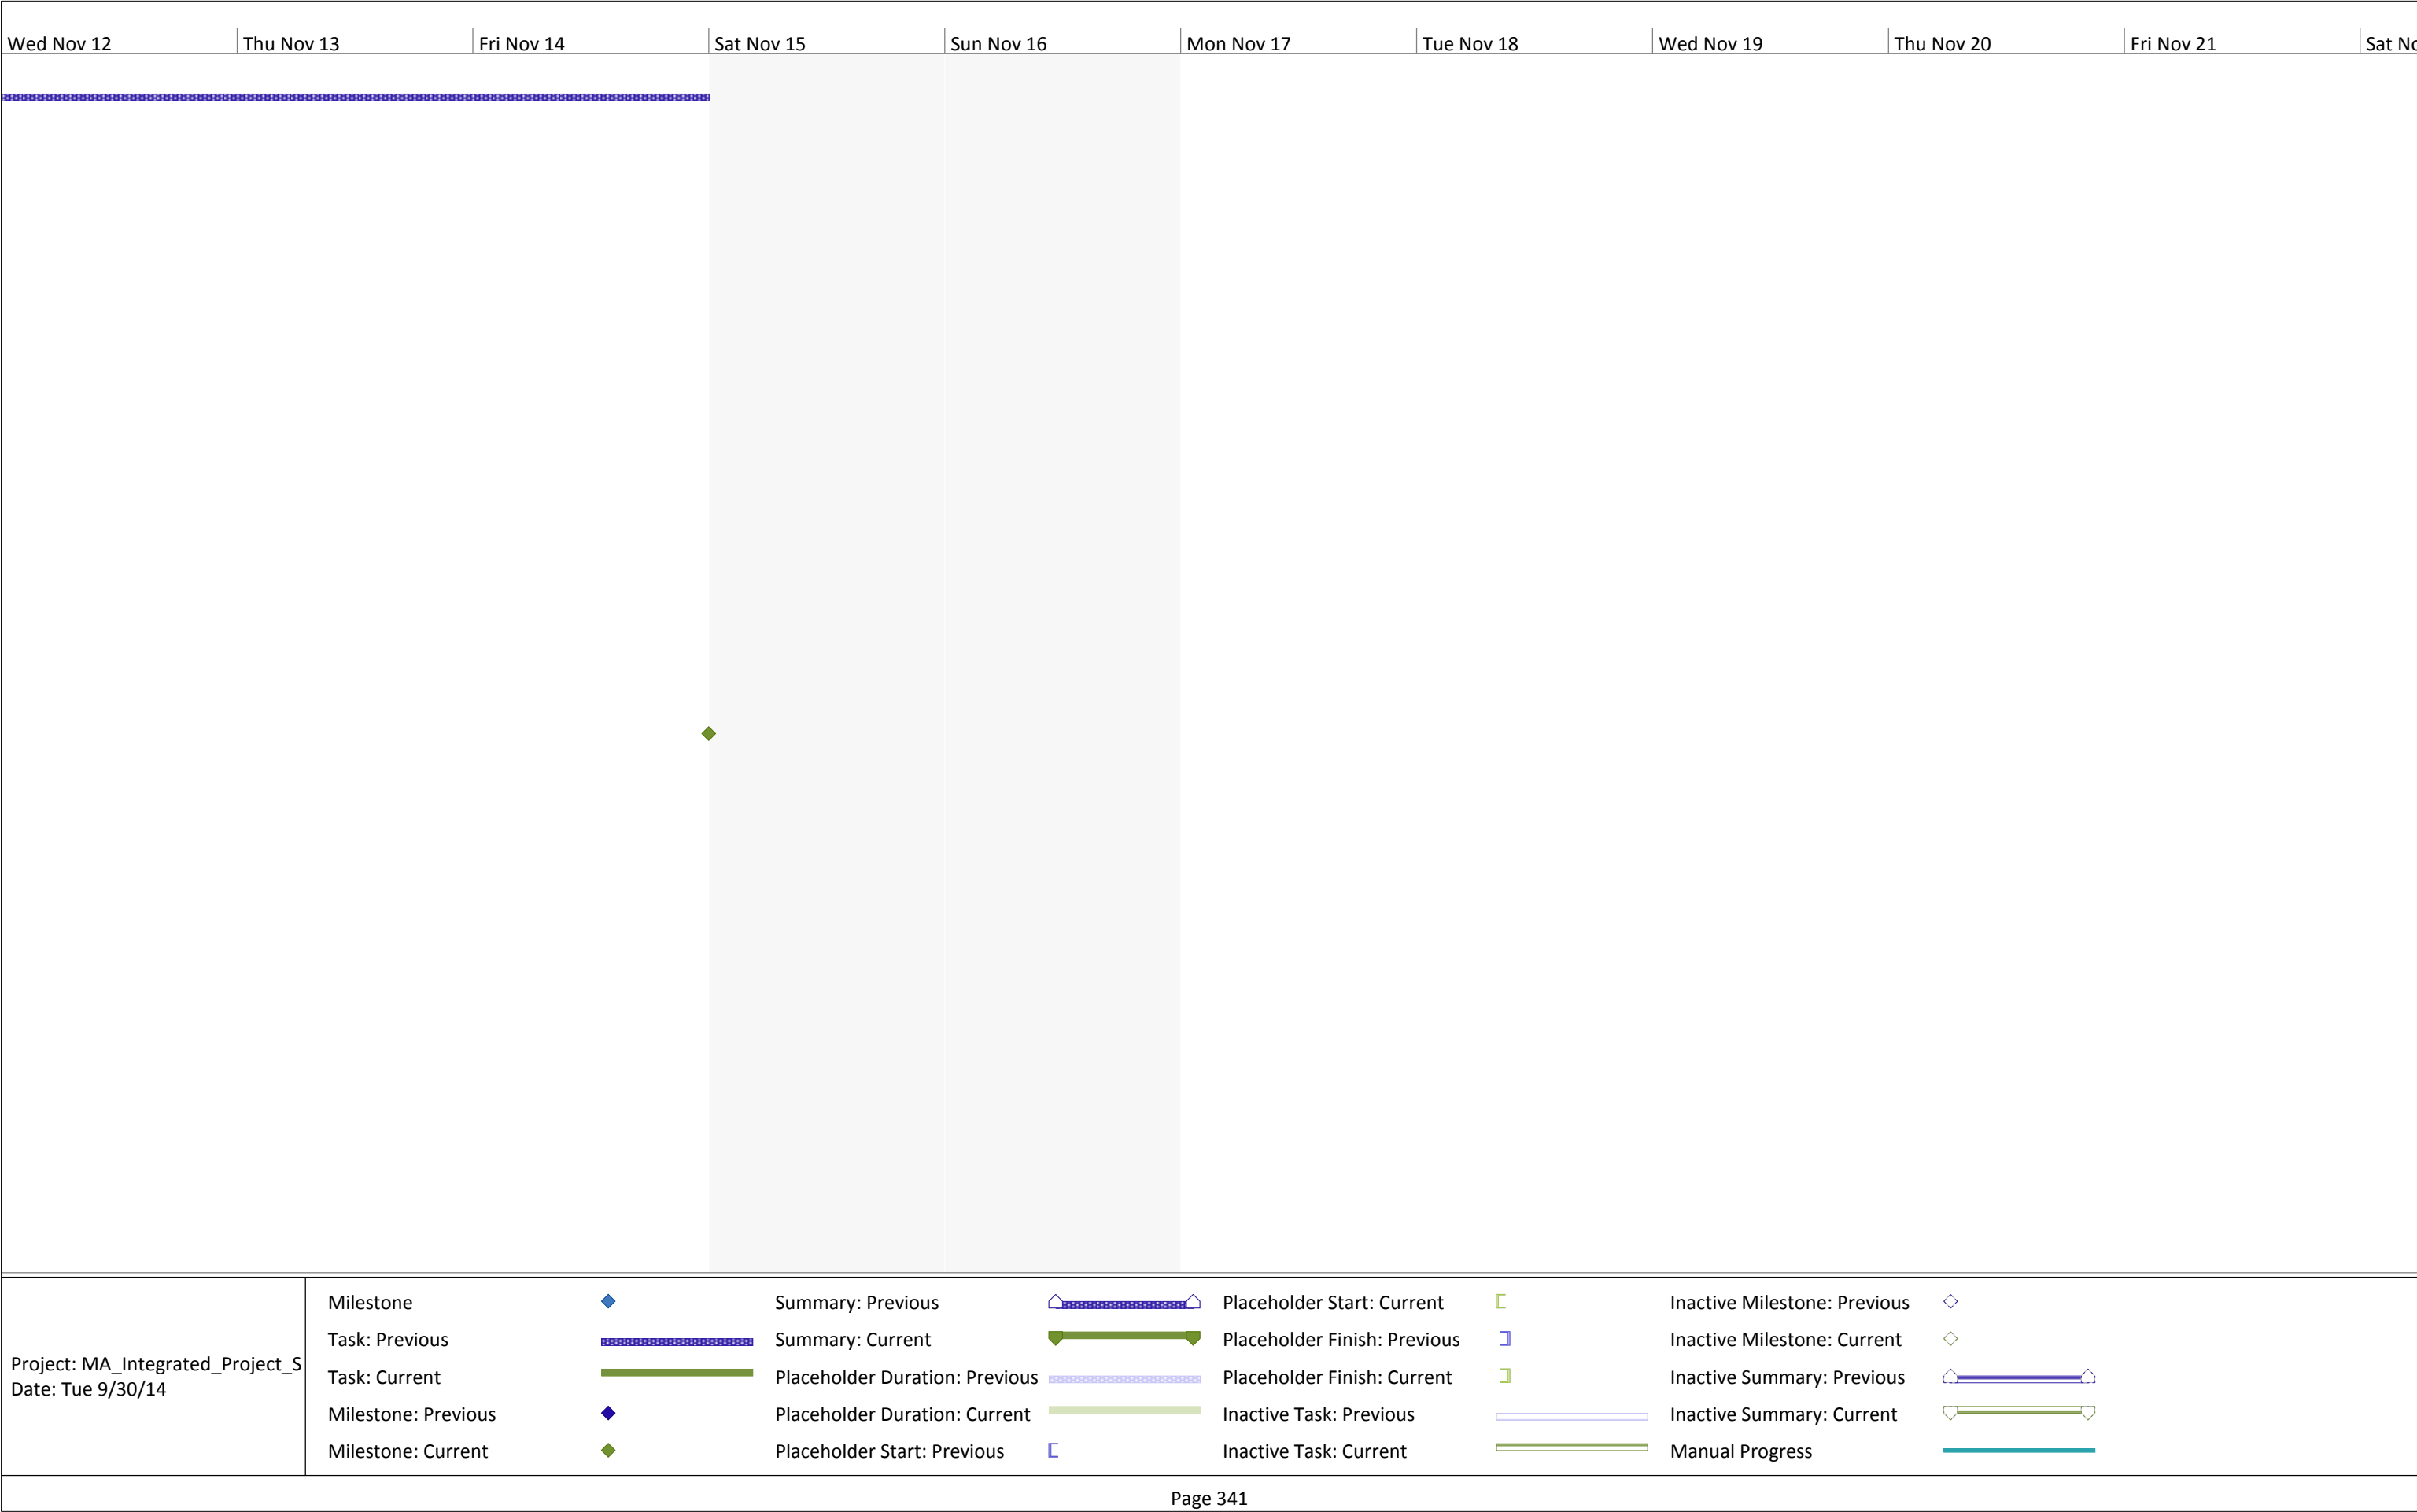

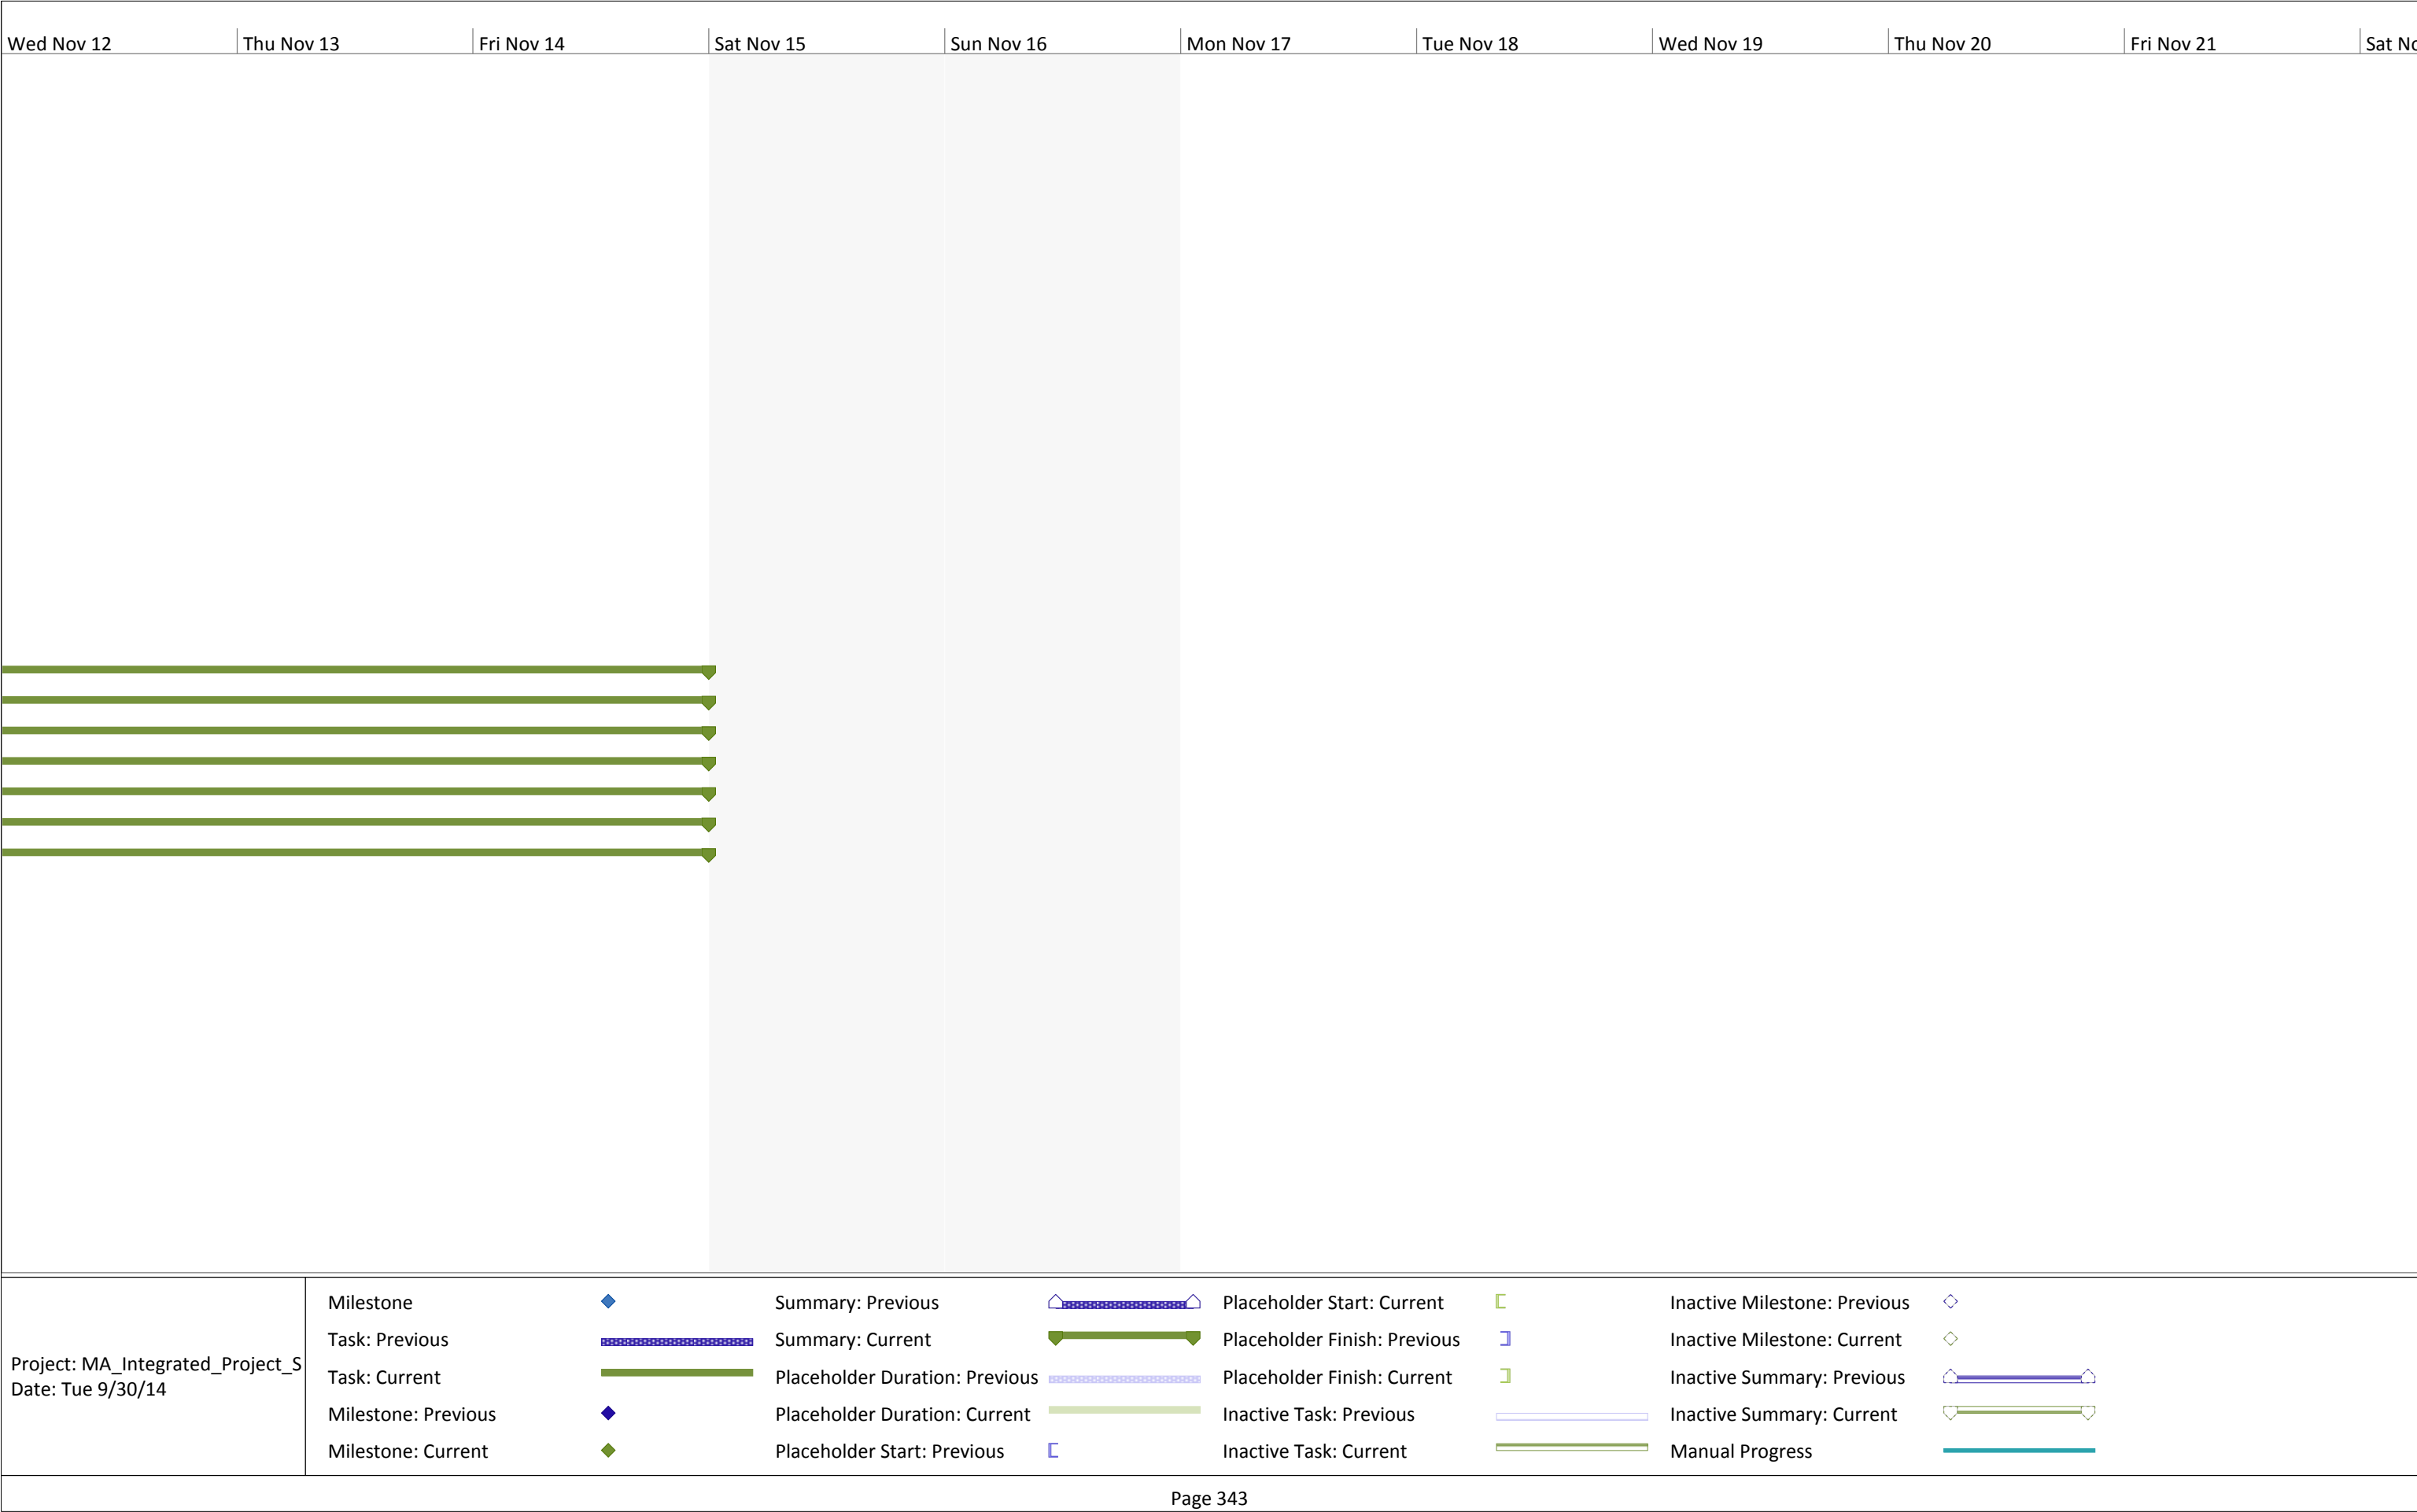

Wed Nov 12

Thu Nov 13

Fri Nov 14

Sat Nov 15

Sun Nov 16

Mon Nov 17

Tue Nov 18

Wed Nov 19

Thu Nov 20

Fri Nov 21

Sat Nov 22

Project: MA_Integrated_Project_S
Date: Tue 9/30/14






Milestone

Task: Previous

Task: Current

Milestone: Previous

Milestone: Current








Summary: Previous

Summary: Current

Placeholder Duration: Previous

Placeholder Duration: Current

Placeholder Start: Previous








Placeholder Start: Current

Placeholder Finish: Previous

Placeholder Finish: Current

Inactive Task: Previous

Inactive Task: Current








Inactive Milestone: Previous

Inactive Milestone: Current

Inactive Summary: Previous

Inactive Summary: Current


Manual Progress





Page 354

Wed Nov 12		Thu Nov 13		Fri Nov 14		Sat Nov 15		Sun Nov 16		Mon Nov 17		Tue Nov 18		Wed Nov 19		Thu Nov 20		Fri Nov 21		Sat Nov 22	
Project: MA_Integrated_Project_S Date: Tue 9/30/14		Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous													
		Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current													
		Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous													
		Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current													
		Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress													

Page 367

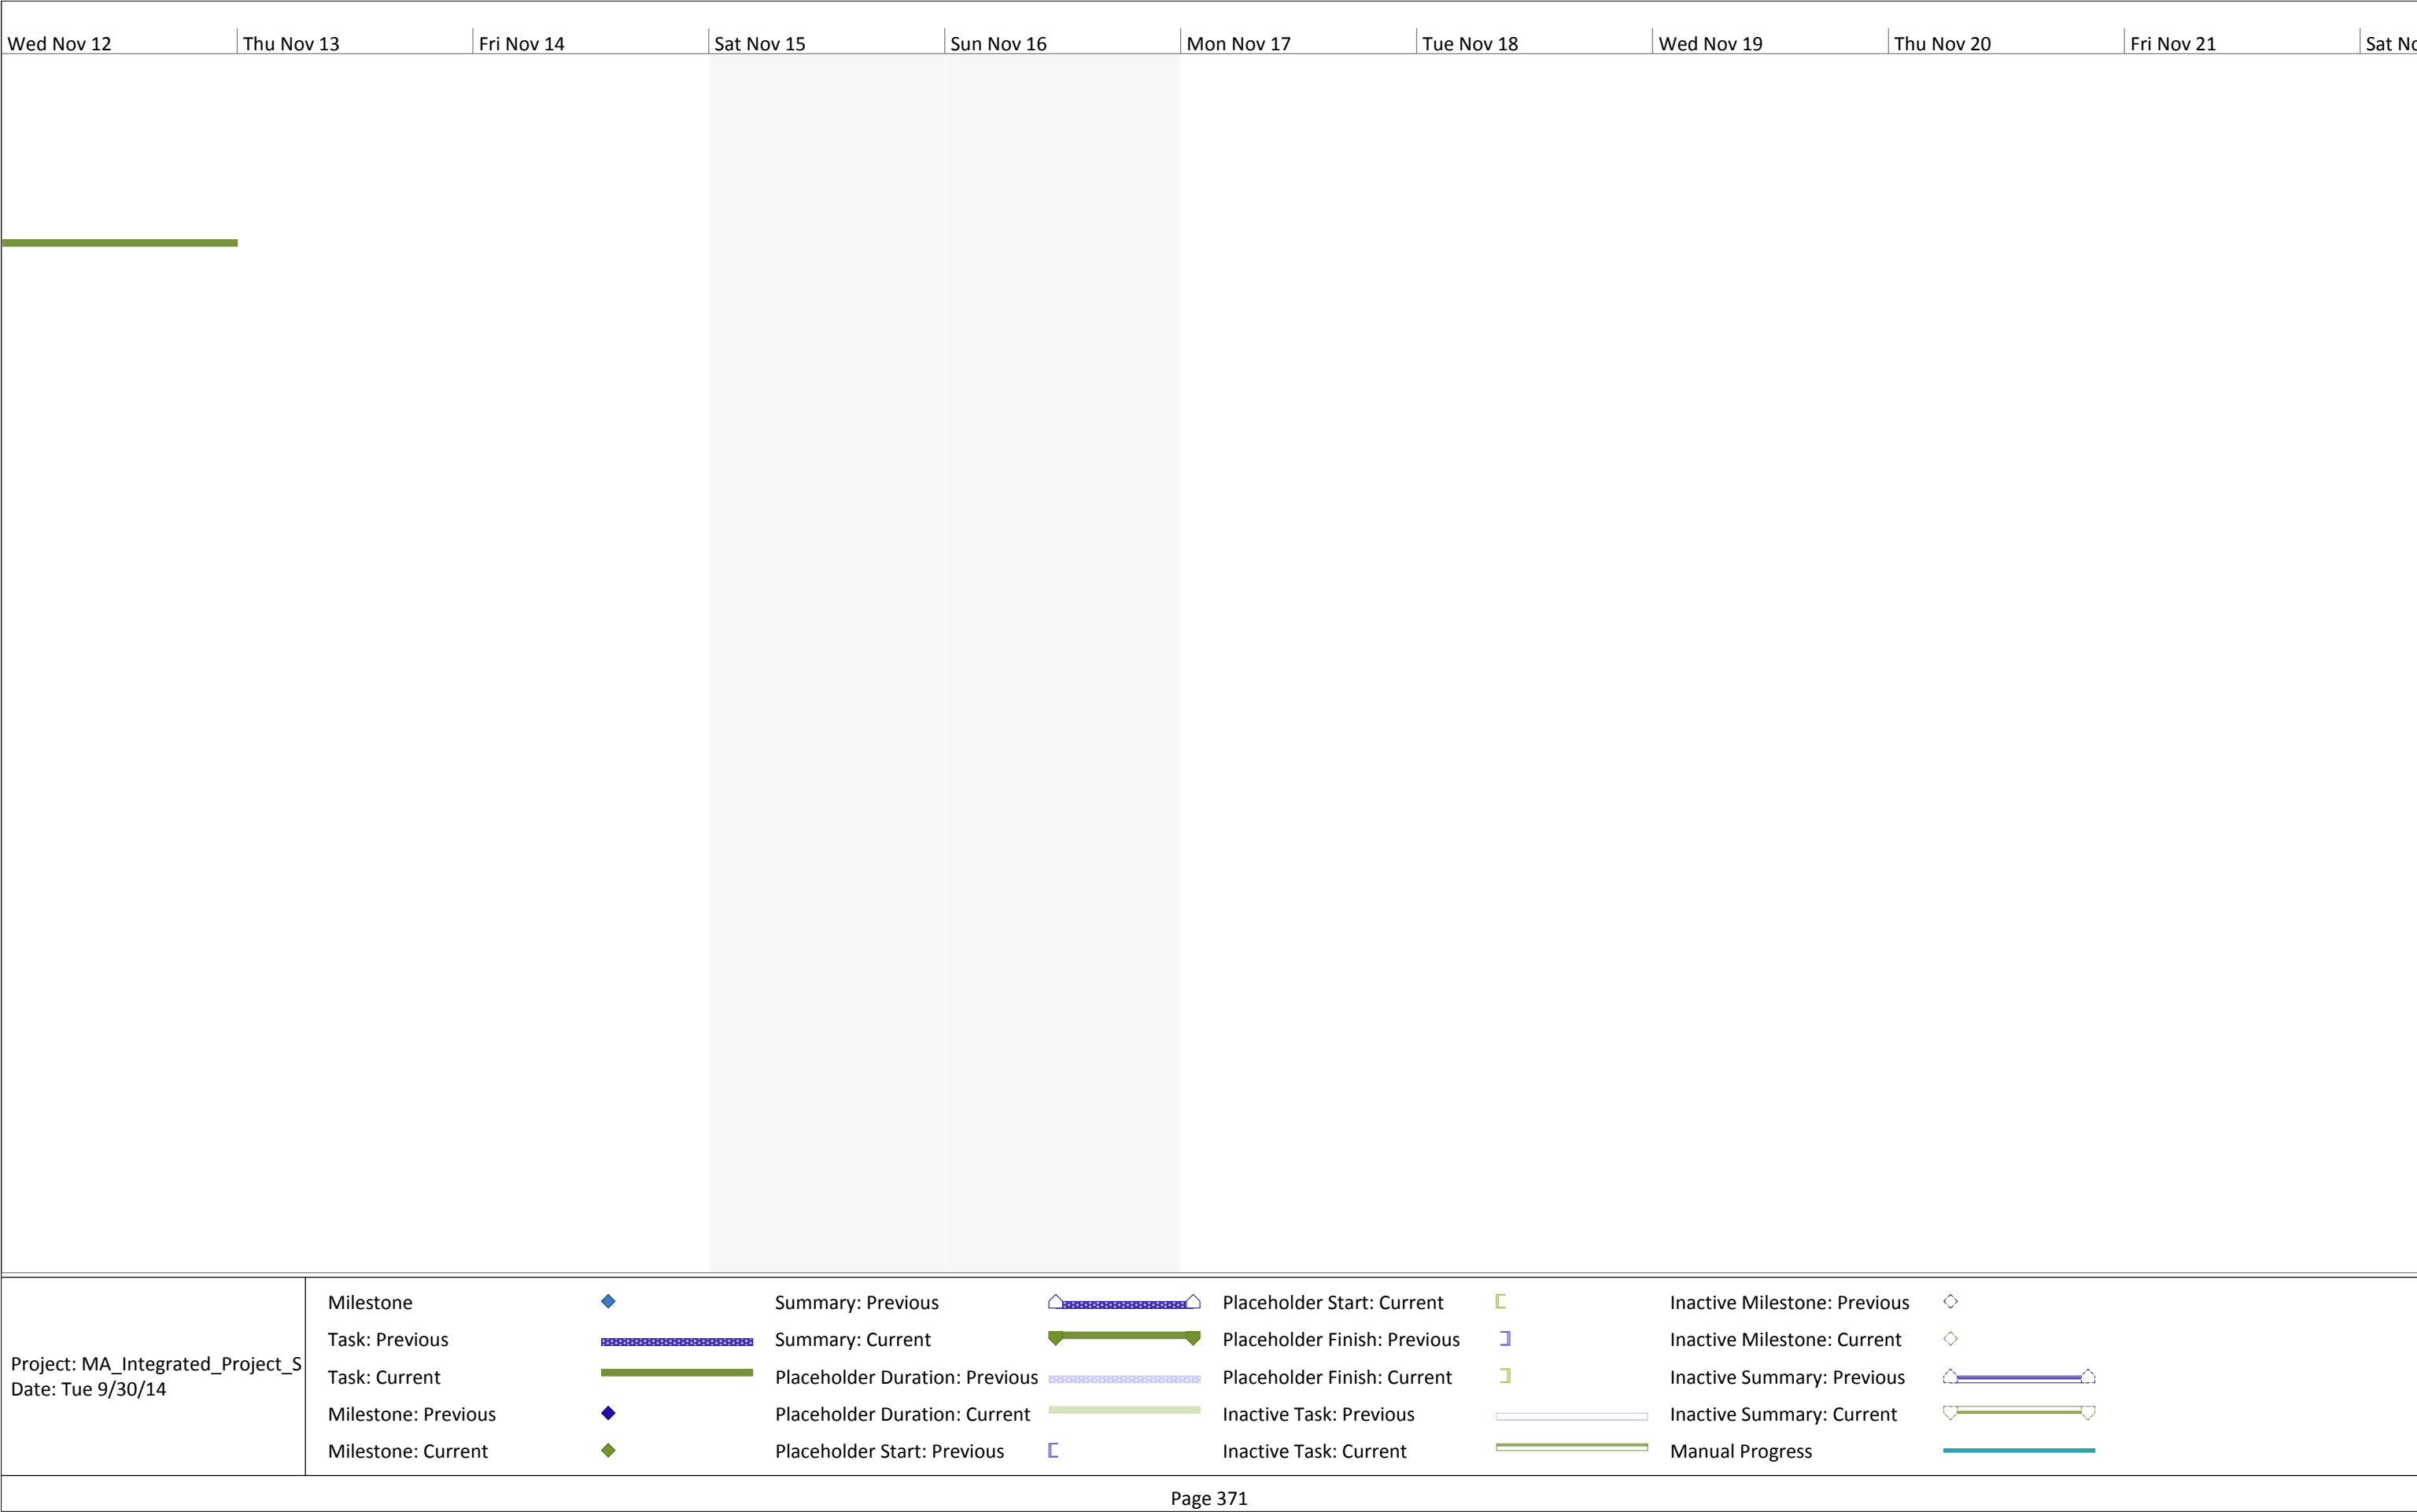

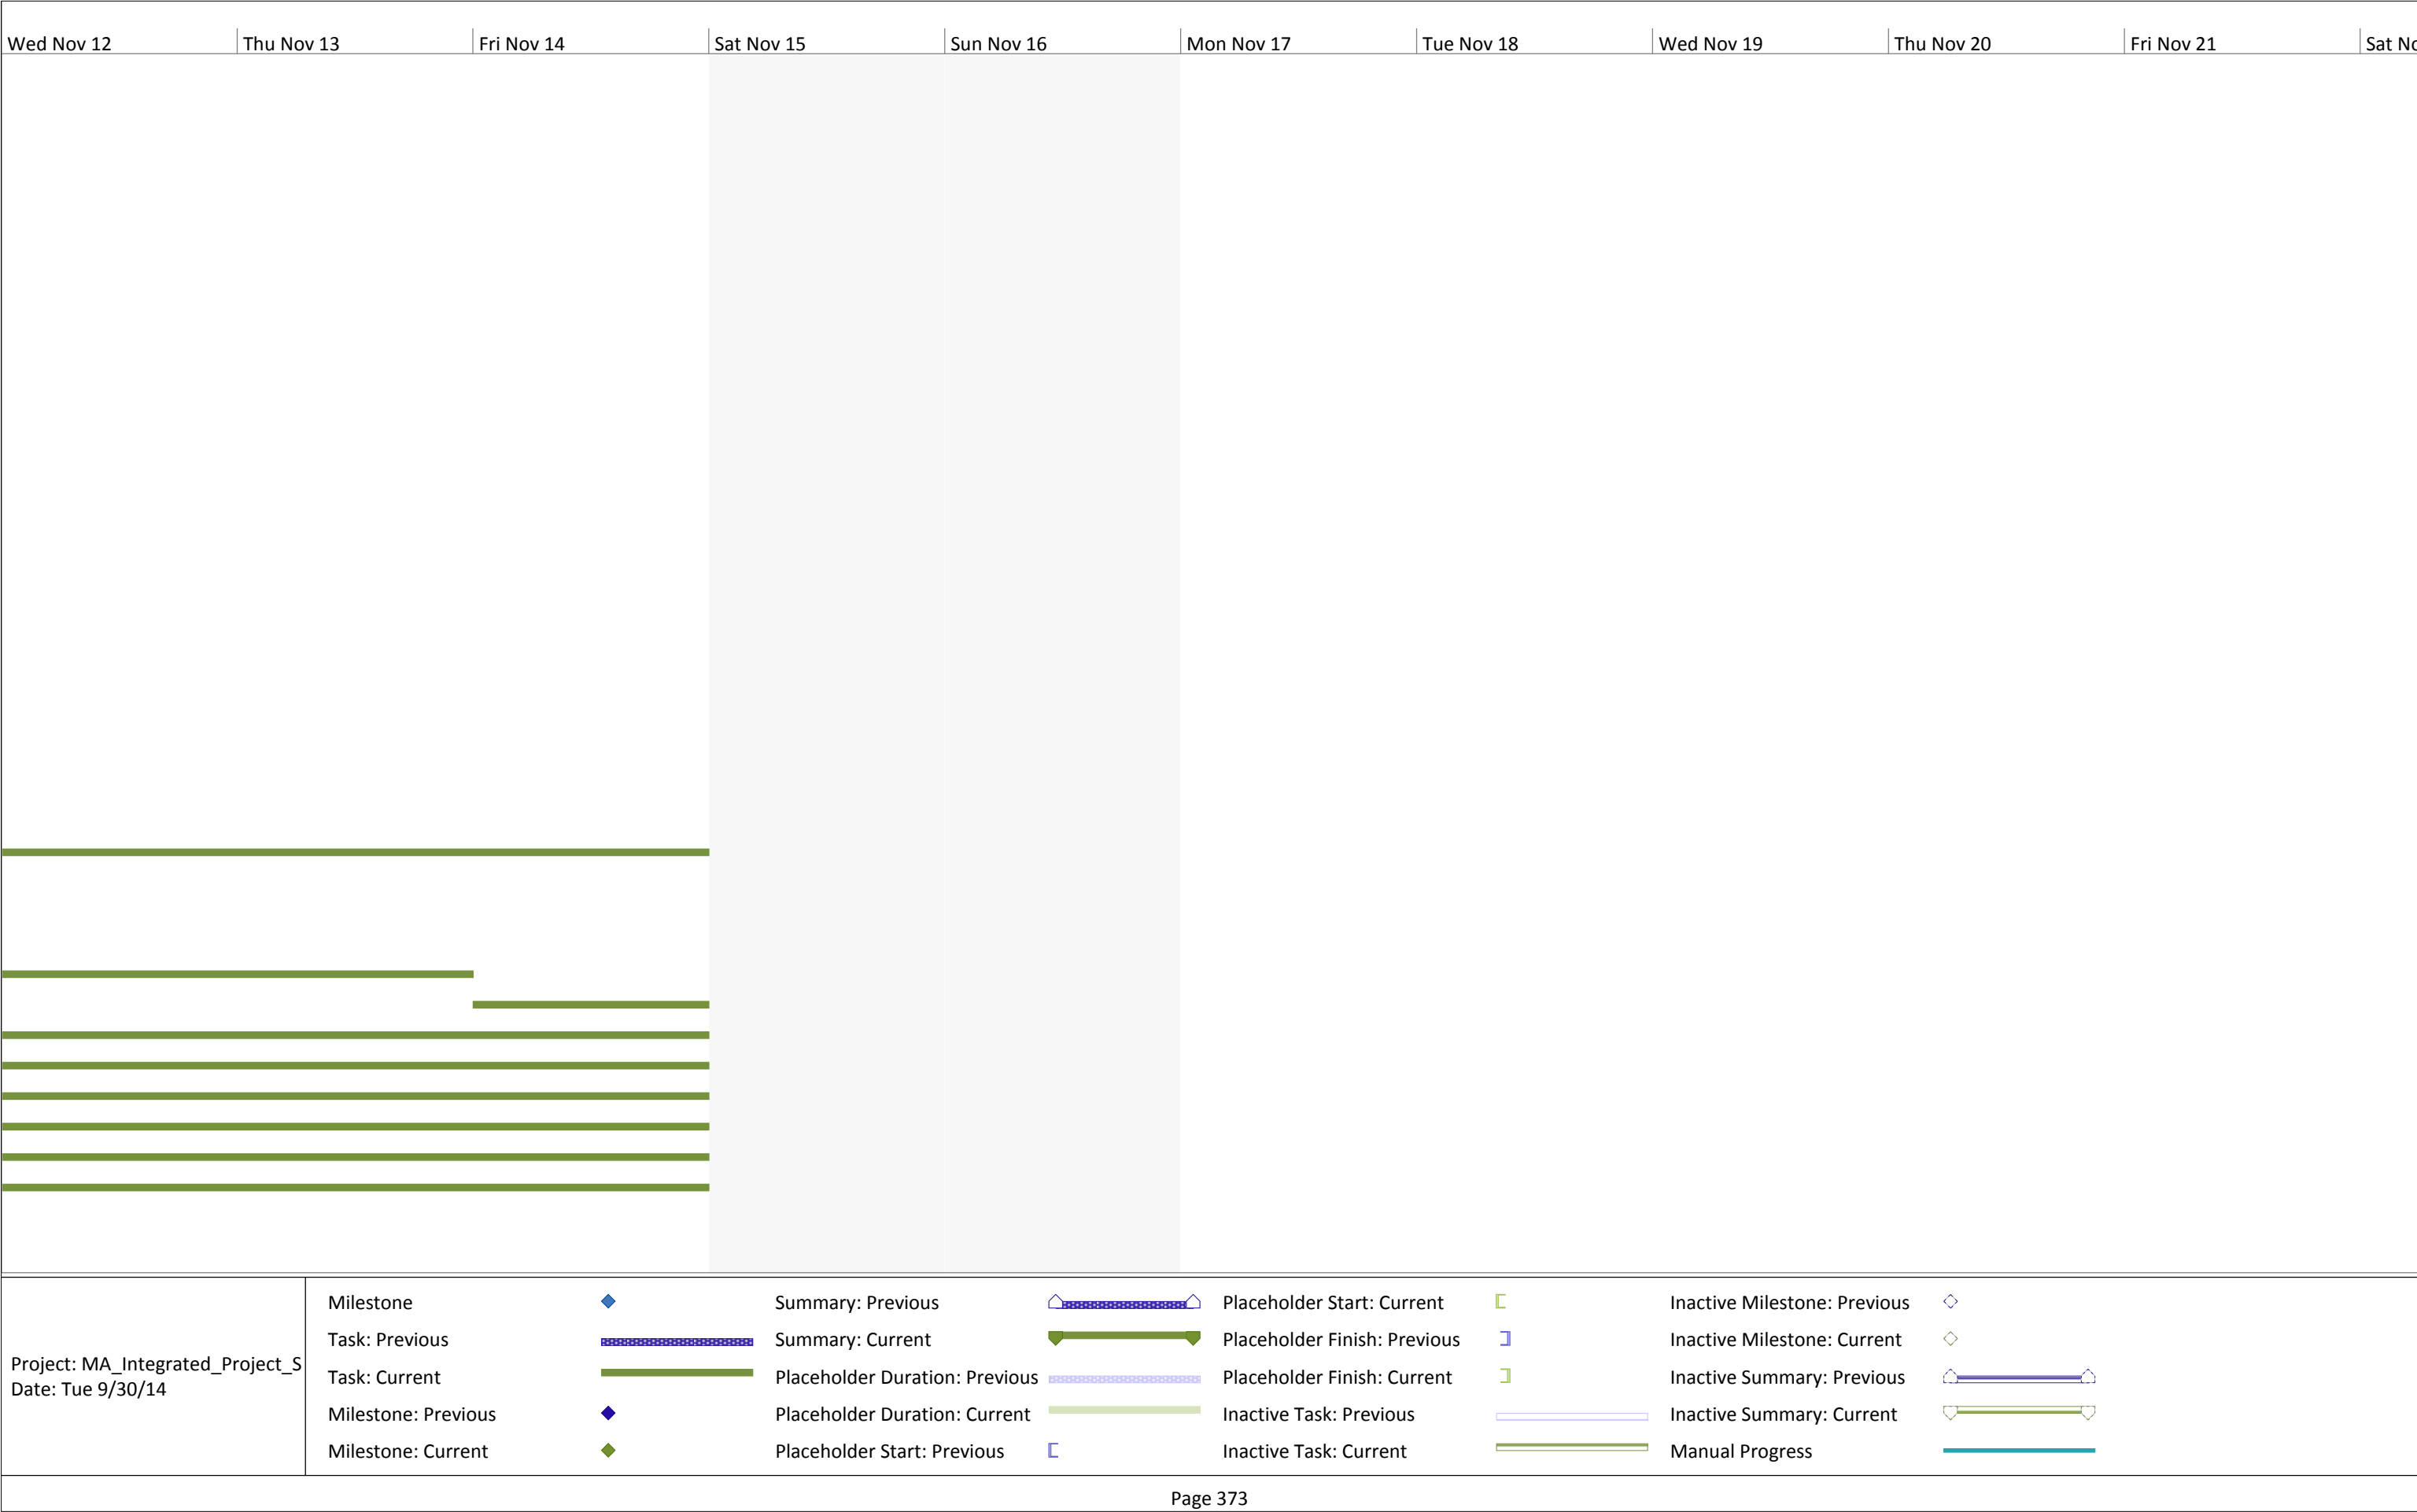

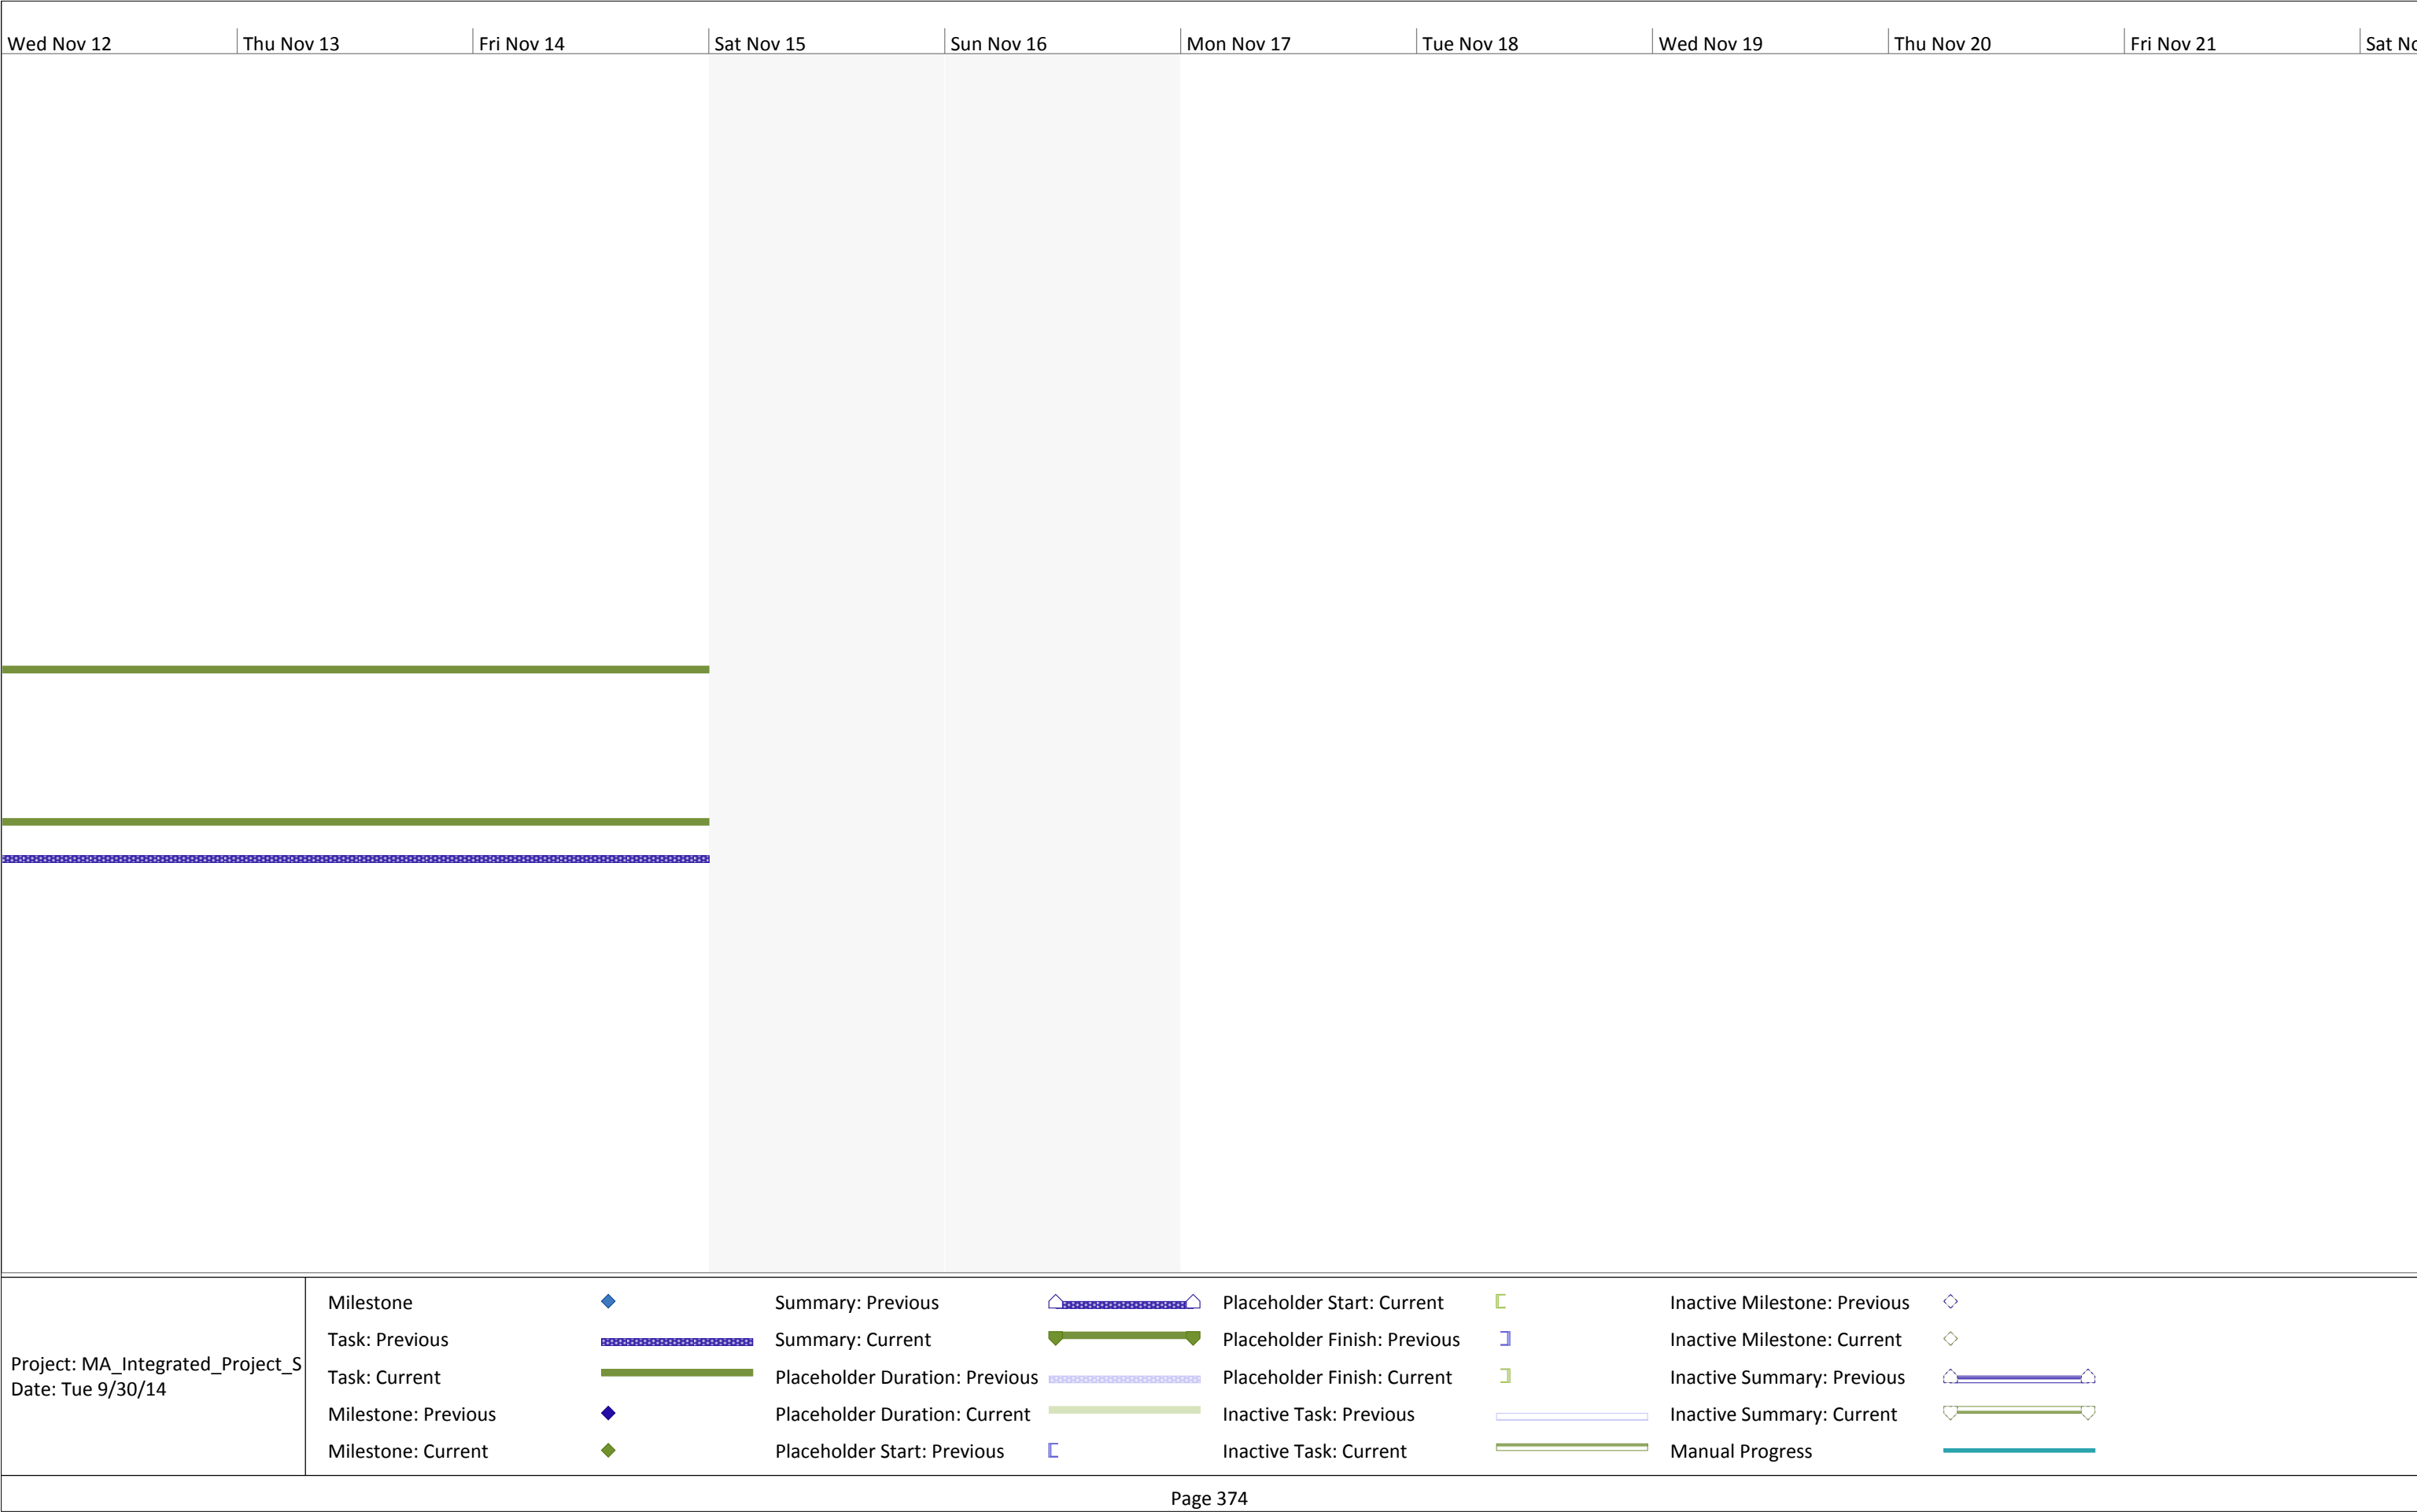

Sat Nov 22	Sun Nov 23	Mon Nov 24	Tue Nov 25	Wed Nov 26	Thu Nov 27	Fri Nov 28	Sat Nov 29	Sun Nov 30	Mon Dec 1	Tue D
<div><div><div>Project: MA_Integrated_Project_S</div><div>Date: Tue 9/30/14</div></div><div><div>Milestone</div><div>Task: Previous</div><div>Task: Current</div><div>Milestone: Previous</div><div>Milestone: Current</div></div><div><div>◆</div><div>▤</div><div>▬</div><div>◆</div><div>◆</div></div><div><div>Summary: Previous</div><div>Summary: Current</div><div>Placeholder Duration: Previous</div><div>Placeholder Duration: Current</div><div>Placeholder Start: Previous</div></div><div><div>▤</div><div>▬</div><div>▤</div><div>▬</div><div>▤</div></div><div><div>Placeholder Start: Current</div><div>Placeholder Finish: Previous</div><div>Placeholder Finish: Current</div><div>Inactive Task: Previous</div><div>Inactive Task: Current</div></div><div><div>▤</div><div>▤</div><div>▤</div><div>▤</div><div>▬</div></div><div><div>Inactive Milestone: Previous</div><div>Inactive Milestone: Current</div><div>Inactive Summary: Previous</div><div>Inactive Summary: Current</div><div>Manual Progress</div></div><div><div>◆</div><div>◆</div><div>▤</div><div>▤</div><div>▬</div></div></div>										

Page 386

Sat Nov 22	Sun Nov 23	Mon Nov 24	Tue Nov 25	Wed Nov 26	Thu Nov 27	Fri Nov 28	Sat Nov 29	Sun Nov 30	Mon Dec 1	Tue D
<div><div><div>Project: MA_Integrated_Project_S</div><div>Date: Tue 9/30/14</div></div><div><div>Milestone</div><div>Task: Previous</div><div>Task: Current</div><div>Milestone: Previous</div><div>Milestone: Current</div></div><div><div>◆</div><div>▤</div><div>▬</div><div>◆</div><div>◆</div></div><div><div>Summary: Previous</div><div>Summary: Current</div><div>Placeholder Duration: Previous</div><div>Placeholder Duration: Current</div><div>Placeholder Start: Previous</div></div><div><div>▤</div><div>▬</div><div>▤</div><div>▬</div><div>▤</div></div><div><div>Placeholder Start: Current</div><div>Placeholder Finish: Previous</div><div>Placeholder Finish: Current</div><div>Inactive Task: Previous</div><div>Inactive Task: Current</div></div><div><div>▤</div><div>▤</div><div>▤</div><div>▤</div><div>▬</div></div><div><div>Inactive Milestone: Previous</div><div>Inactive Milestone: Current</div><div>Inactive Summary: Previous</div><div>Inactive Summary: Current</div><div>Manual Progress</div></div><div><div>◆</div><div>◆</div><div>▤</div><div>▤</div><div>▬</div></div></div>										

Page 394

Sat Nov 22	Sun Nov 23	Mon Nov 24	Tue Nov 25	Wed Nov 26	Thu Nov 27	Fri Nov 28	Sat Nov 29	Sun Nov 30	Mon Dec 1	Tue D
<div><div><div>Project: MA_Integrated_Project_S</div><div>Date: Tue 9/30/14</div></div><div><div>Milestone</div><div>Task: Previous</div><div>Task: Current</div><div>Milestone: Previous</div><div>Milestone: Current</div></div><div><div>◆</div><div>▤</div><div>▬</div><div>◆</div><div>◆</div></div><div><div>Summary: Previous</div><div>Summary: Current</div><div>Placeholder Duration: Previous</div><div>Placeholder Duration: Current</div><div>Placeholder Start: Previous</div></div><div><div>▤</div><div>▬</div><div>▤</div><div>▬</div><div>▤</div></div><div><div>Placeholder Start: Current</div><div>Placeholder Finish: Previous</div><div>Placeholder Finish: Current</div><div>Inactive Task: Previous</div><div>Inactive Task: Current</div></div><div><div>▤</div><div>▤</div><div>▤</div><div>▤</div><div>▬</div></div><div><div>Inactive Milestone: Previous</div><div>Inactive Milestone: Current</div><div>Inactive Summary: Previous</div><div>Inactive Summary: Current</div><div>Manual Progress</div></div><div><div>◆</div><div>◆</div><div>▤</div><div>▤</div><div>▬</div></div></div>										

Page 395

Sat Nov 22	Sun Nov 23	Mon Nov 24	Tue Nov 25	Wed Nov 26	Thu Nov 27	Fri Nov 28	Sat Nov 29	Sun Nov 30	Mon Dec 1	Tue D
<div><div><div>Project: MA_Integrated_Project_S</div><div>Date: Tue 9/30/14</div></div><div><div>Milestone</div><div>Task: Previous</div><div>Task: Current</div><div>Milestone: Previous</div><div>Milestone: Current</div></div><div><div>◆</div><div>▤</div><div>▬</div><div>◆</div><div>◆</div></div><div><div>Summary: Previous</div><div>Summary: Current</div><div>Placeholder Duration: Previous</div><div>Placeholder Duration: Current</div><div>Placeholder Start: Previous</div></div><div><div>▤</div><div>▬</div><div>▤</div><div>▬</div><div>▤</div></div><div><div>Placeholder Start: Current</div><div>Placeholder Finish: Previous</div><div>Placeholder Finish: Current</div><div>Inactive Task: Previous</div><div>Inactive Task: Current</div></div><div><div>▤</div><div>▤</div><div>▤</div><div>▤</div><div>▬</div></div><div><div>Inactive Milestone: Previous</div><div>Inactive Milestone: Current</div><div>Inactive Summary: Previous</div><div>Inactive Summary: Current</div><div>Manual Progress</div></div><div><div>◆</div><div>◆</div><div>▤</div><div>▤</div><div>▬</div></div></div>										

Page 396

Sat Nov 22

Sun Nov 23

Mon Nov 24

Tue Nov 25

Wed Nov 26

Thu Nov 27

Fri Nov 28

Sat Nov 29

Sun Nov 30

Mon Dec 1

Tue D

Project: MA_Integrated_Project_S
Date: Tue 9/30/14

Milestone

Task: Previous

Task: Current

Milestone: Previous

Milestone: Current

◆

▤

▬

◆

◆

Summary: Previous

Summary: Current

Placeholder Duration: Previous

Placeholder Duration: Current

Placeholder Start: Previous

▤

▬

▬

▬

▬

Placeholder Start: Current

Placeholder Finish: Previous

Placeholder Finish: Current

Inactive Task: Previous

Inactive Task: Current

▬

▬

▬

▬

▬

Inactive Milestone: Previous

Inactive Milestone: Current

Inactive Summary: Previous

Inactive Summary: Current

Manual Progress

Page 400

Sat Nov 22

Sun Nov 23

Mon Nov 24

Tue Nov 25

Wed Nov 26

Thu Nov 27

Fri Nov 28

Sat Nov 29

Sun Nov 30

Mon Dec 1

Tue D

Project: MA_Integrated_Project_S
Date: Tue 9/30/14

Milestone

Task: Previous

Task: Current

Milestone: Previous

Milestone: Current

Summary: Previous

Summary: Current

Placeholder Duration: Previous

Placeholder Duration: Current

Placeholder Start: Previous

Placeholder Start: Current

Placeholder Finish: Previous

Placeholder Finish: Current

Inactive Task: Previous

Inactive Task: Current

Inactive Milestone: Previous

Inactive Milestone: Current

Inactive Summary: Previous

Inactive Summary: Current

Manual Progress

Page 405

Sat Nov 22	Sun Nov 23	Mon Nov 24	Tue Nov 25	Wed Nov 26	Thu Nov 27	Fri Nov 28	Sat Nov 29	Sun Nov 30	Mon Dec 1	Tue D
<div><div>Project: MA_Integrated_Project_S Date: Tue 9/30/14</div><div><div>Milestone</div><div>Task: Previous</div><div>Task: Current</div><div>Milestone: Previous</div><div>Milestone: Current</div></div><div><div>◆</div><div>▤</div><div>▬</div><div>◆</div><div>◆</div></div><div><div>Summary: Previous</div><div>Summary: Current</div><div>Placeholder Duration: Previous</div><div>Placeholder Duration: Current</div><div>Placeholder Start: Previous</div></div><div><div>▤</div><div>▬</div><div>▤</div><div>▬</div><div>▤</div></div><div><div>Placeholder Start: Current</div><div>Placeholder Finish: Previous</div><div>Placeholder Finish: Current</div><div>Inactive Task: Previous</div><div>Inactive Task: Current</div></div><div><div>▤</div><div>▤</div><div>▤</div><div>▤</div><div>▬</div></div><div><div>Inactive Milestone: Previous</div><div>Inactive Milestone: Current</div><div>Inactive Summary: Previous</div><div>Inactive Summary: Current</div><div>Manual Progress</div></div><div><div>◆</div><div>◆</div><div>▤</div><div>▤</div><div>▬</div></div></div>										

Page 409

Sat Nov 22	Sun Nov 23	Mon Nov 24	Tue Nov 25	Wed Nov 26	Thu Nov 27	Fri Nov 28	Sat Nov 29	Sun Nov 30	Mon Dec 1	Tue D
<div><div>Project: MA_Integrated_Project_S Date: Tue 9/30/14</div><div><div>Milestone</div><div>Task: Previous</div><div>Task: Current</div><div>Milestone: Previous</div><div>Milestone: Current</div></div><div><div>◆</div><div>▤</div><div>▬</div><div>◆</div><div>◆</div></div><div><div>Summary: Previous</div><div>Summary: Current</div><div>Placeholder Duration: Previous</div><div>Placeholder Duration: Current</div><div>Placeholder Start: Previous</div></div><div><div>▤</div><div>▬</div><div>▤</div><div>▬</div><div>▤</div></div><div><div>Placeholder Start: Current</div><div>Placeholder Finish: Previous</div><div>Placeholder Finish: Current</div><div>Inactive Task: Previous</div><div>Inactive Task: Current</div></div><div><div>▤</div><div>▤</div><div>▤</div><div>▤</div><div>▬</div></div><div><div>Inactive Milestone: Previous</div><div>Inactive Milestone: Current</div><div>Inactive Summary: Previous</div><div>Inactive Summary: Current</div><div>Manual Progress</div></div><div><div>◆</div><div>◆</div><div>▤</div><div>▤</div><div>▬</div></div></div>										

Page 416

Tue Dec 2

Wed Dec 3

Thu Dec 4

Fri Dec 5

Sat Dec 6

Sun Dec 7

Mon Dec 8

Tue Dec 9

Wed Dec 10

Thu Dec 11

Fri Dec 12

Project: MA_Integrated_Project_S
Date: Tue 9/30/14

Milestone

Task: Previous

Task: Current

Milestone: Previous

Milestone: Current

◆

▤

▬

◆

◆

Summary: Previous

Summary: Current

Placeholder Duration: Previous

Placeholder Duration: Current

Placeholder Start: Previous

▤

▬

▤

▬

▤

Placeholder Start: Current

Placeholder Finish: Previous

Placeholder Finish: Current

Inactive Task: Previous

Inactive Task: Current

▤

▤

▤

▤

▬

Inactive Milestone: Previous

Inactive Milestone: Current

Inactive Summary: Previous

Inactive Summary: Current

Manual Progress

◆


◆


▤


▤


▬


Page 422







































































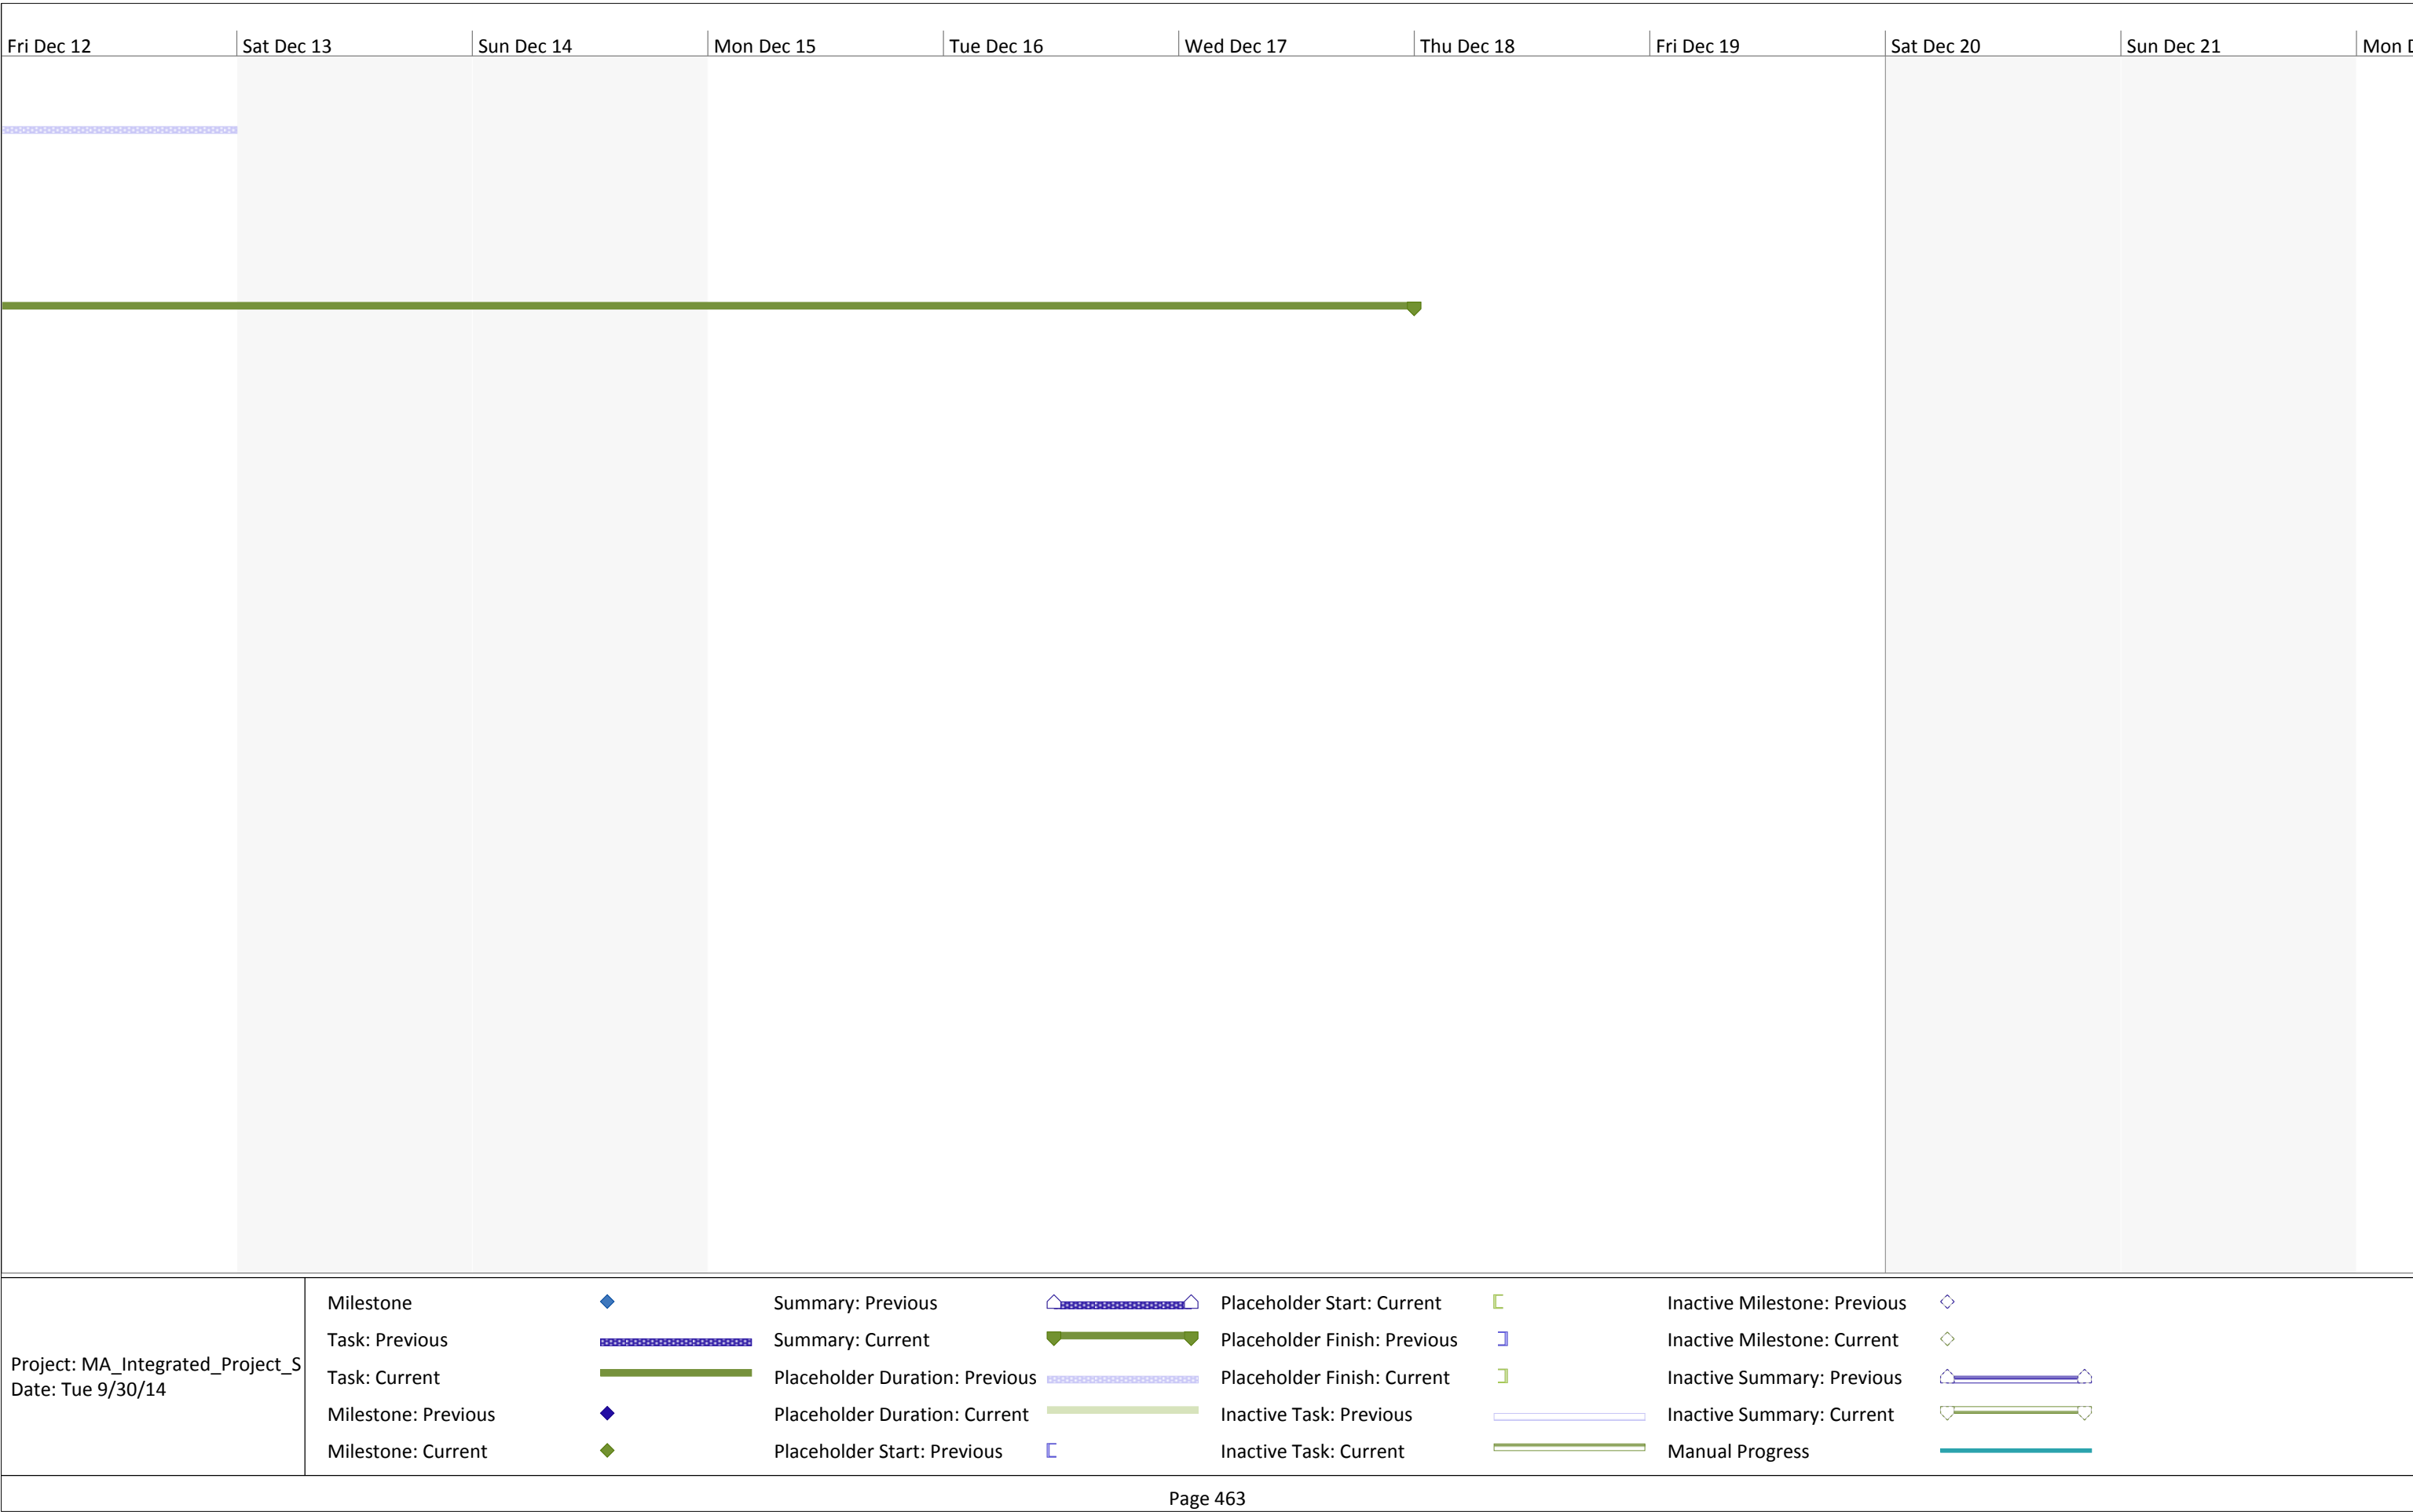





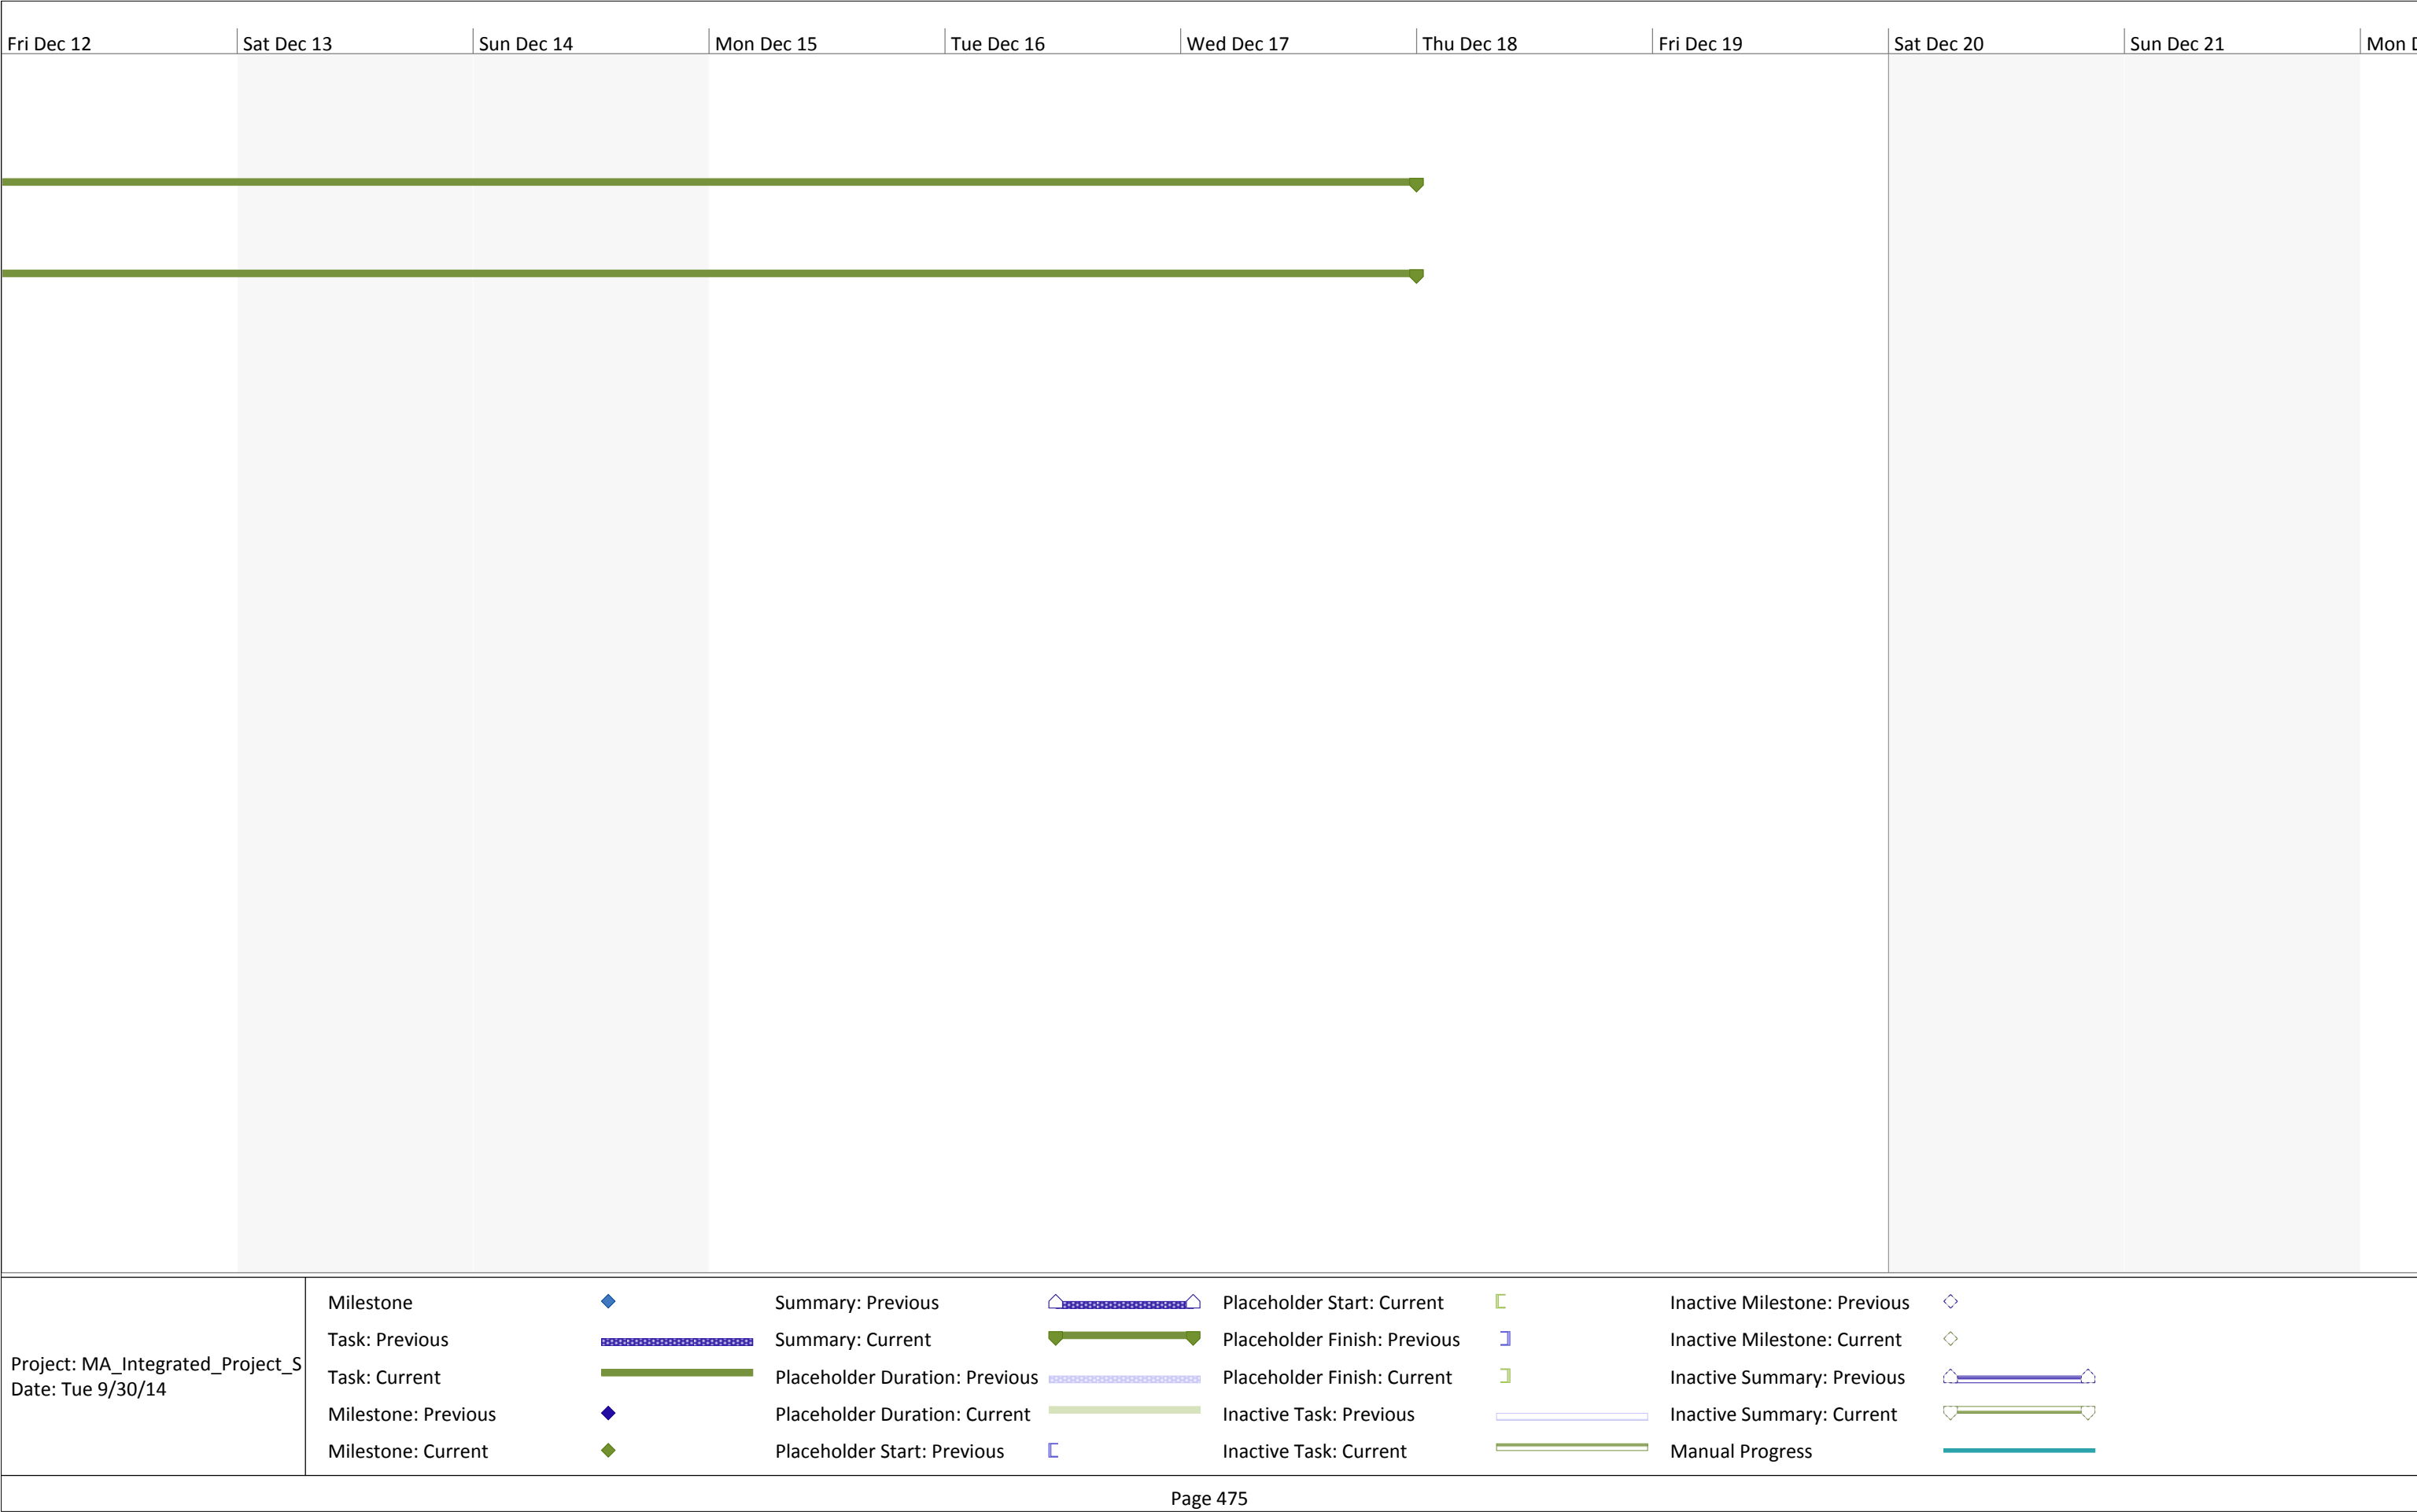














Fri Dec 12		Sat Dec 13		Sun Dec 14		Mon Dec 15		Tue Dec 16		Wed Dec 17		Thu Dec 18		Fri Dec 19		Sat Dec 20		Sun Dec 21		Mon Dec 22	
Project: MA_Integrated_Project_S Date: Tue 9/30/14		Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous													
		Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current													
		Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous													
		Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current													
		Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress													

Page 472







Project: MA_Integrated_Project_S Date: Tue 9/30/14	Milestone		Summary: Previous		Placeholder Start: Current		Inactive Milestone: Previous	
	Task: Previous		Summary: Current		Placeholder Finish: Previous		Inactive Milestone: Current	
	Task: Current		Placeholder Duration: Previous		Placeholder Finish: Current		Inactive Summary: Previous	
	Milestone: Previous		Placeholder Duration: Current		Inactive Task: Previous		Inactive Summary: Current	
	Milestone: Current		Placeholder Start: Previous		Inactive Task: Current		Manual Progress	
