


VOLUME 2

Springfield Regional Justice Center Project

Submitted By:



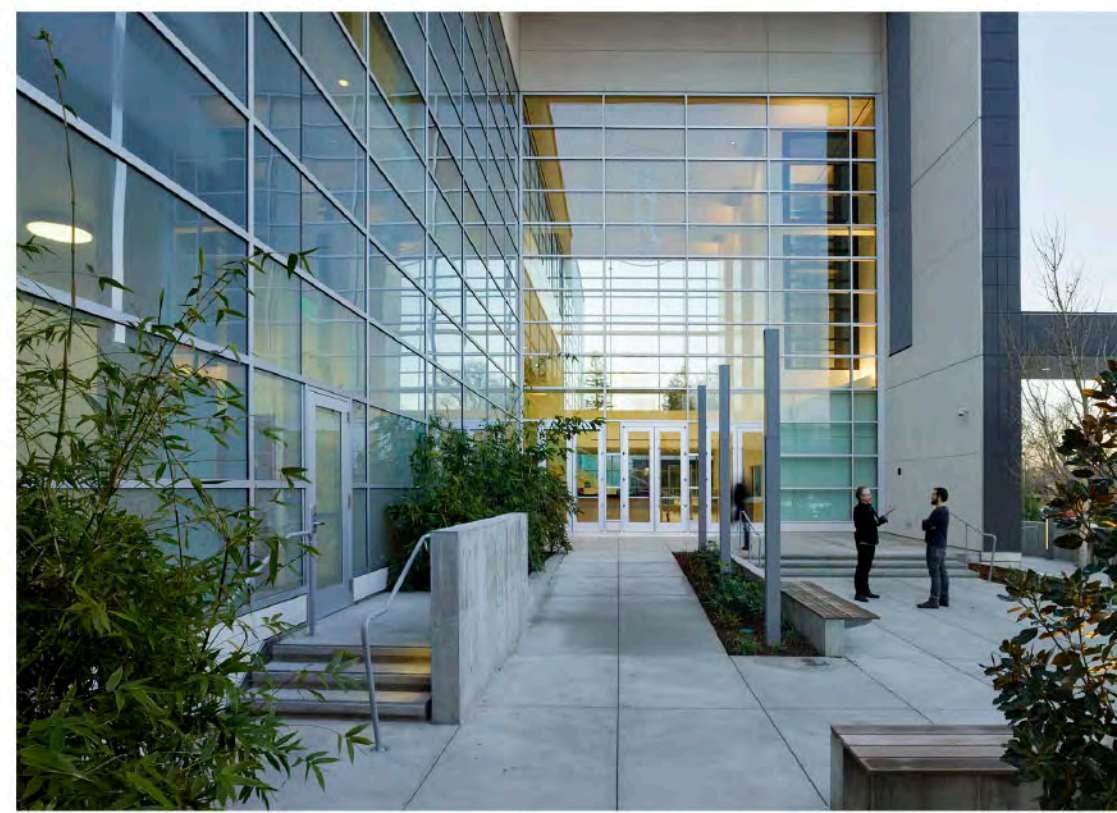

All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

NEW SPRINGFIELD REGIONAL JUSTICE CENTER | R1.01



16 OCT 2025



All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

VIEW FROM HIGHWAY I-91 SOUTH | R1.02



16 OCT 2025



All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

VIEW FROM COURTHOUSE DRIVE | R1.03



16 OCT 2025



All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

VIEW OF MAIN ENTRY PLAZA | R1.04



16 OCT 2025



All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

VIEW OF MAIN ENTRY PLAZA | R1.05



16 OCT 2025



All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

VIEW FROM RIVERFRONT PUBLIC PARK | R1.06



16 OCT 2025



All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

VIEW FROM ACROSS RIVER | R1.07



16 OCT 2025



All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

VIEW FROM ACROSS RIVER | R1.08



16 OCT 2025



All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

VIEW OF TYPICAL COURTROOM CORRIDOR | R1.09



16 OCT 2025




All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

VIEW OF TYPICAL JUDGE LOBBY | R1.10



16 OCT 2025

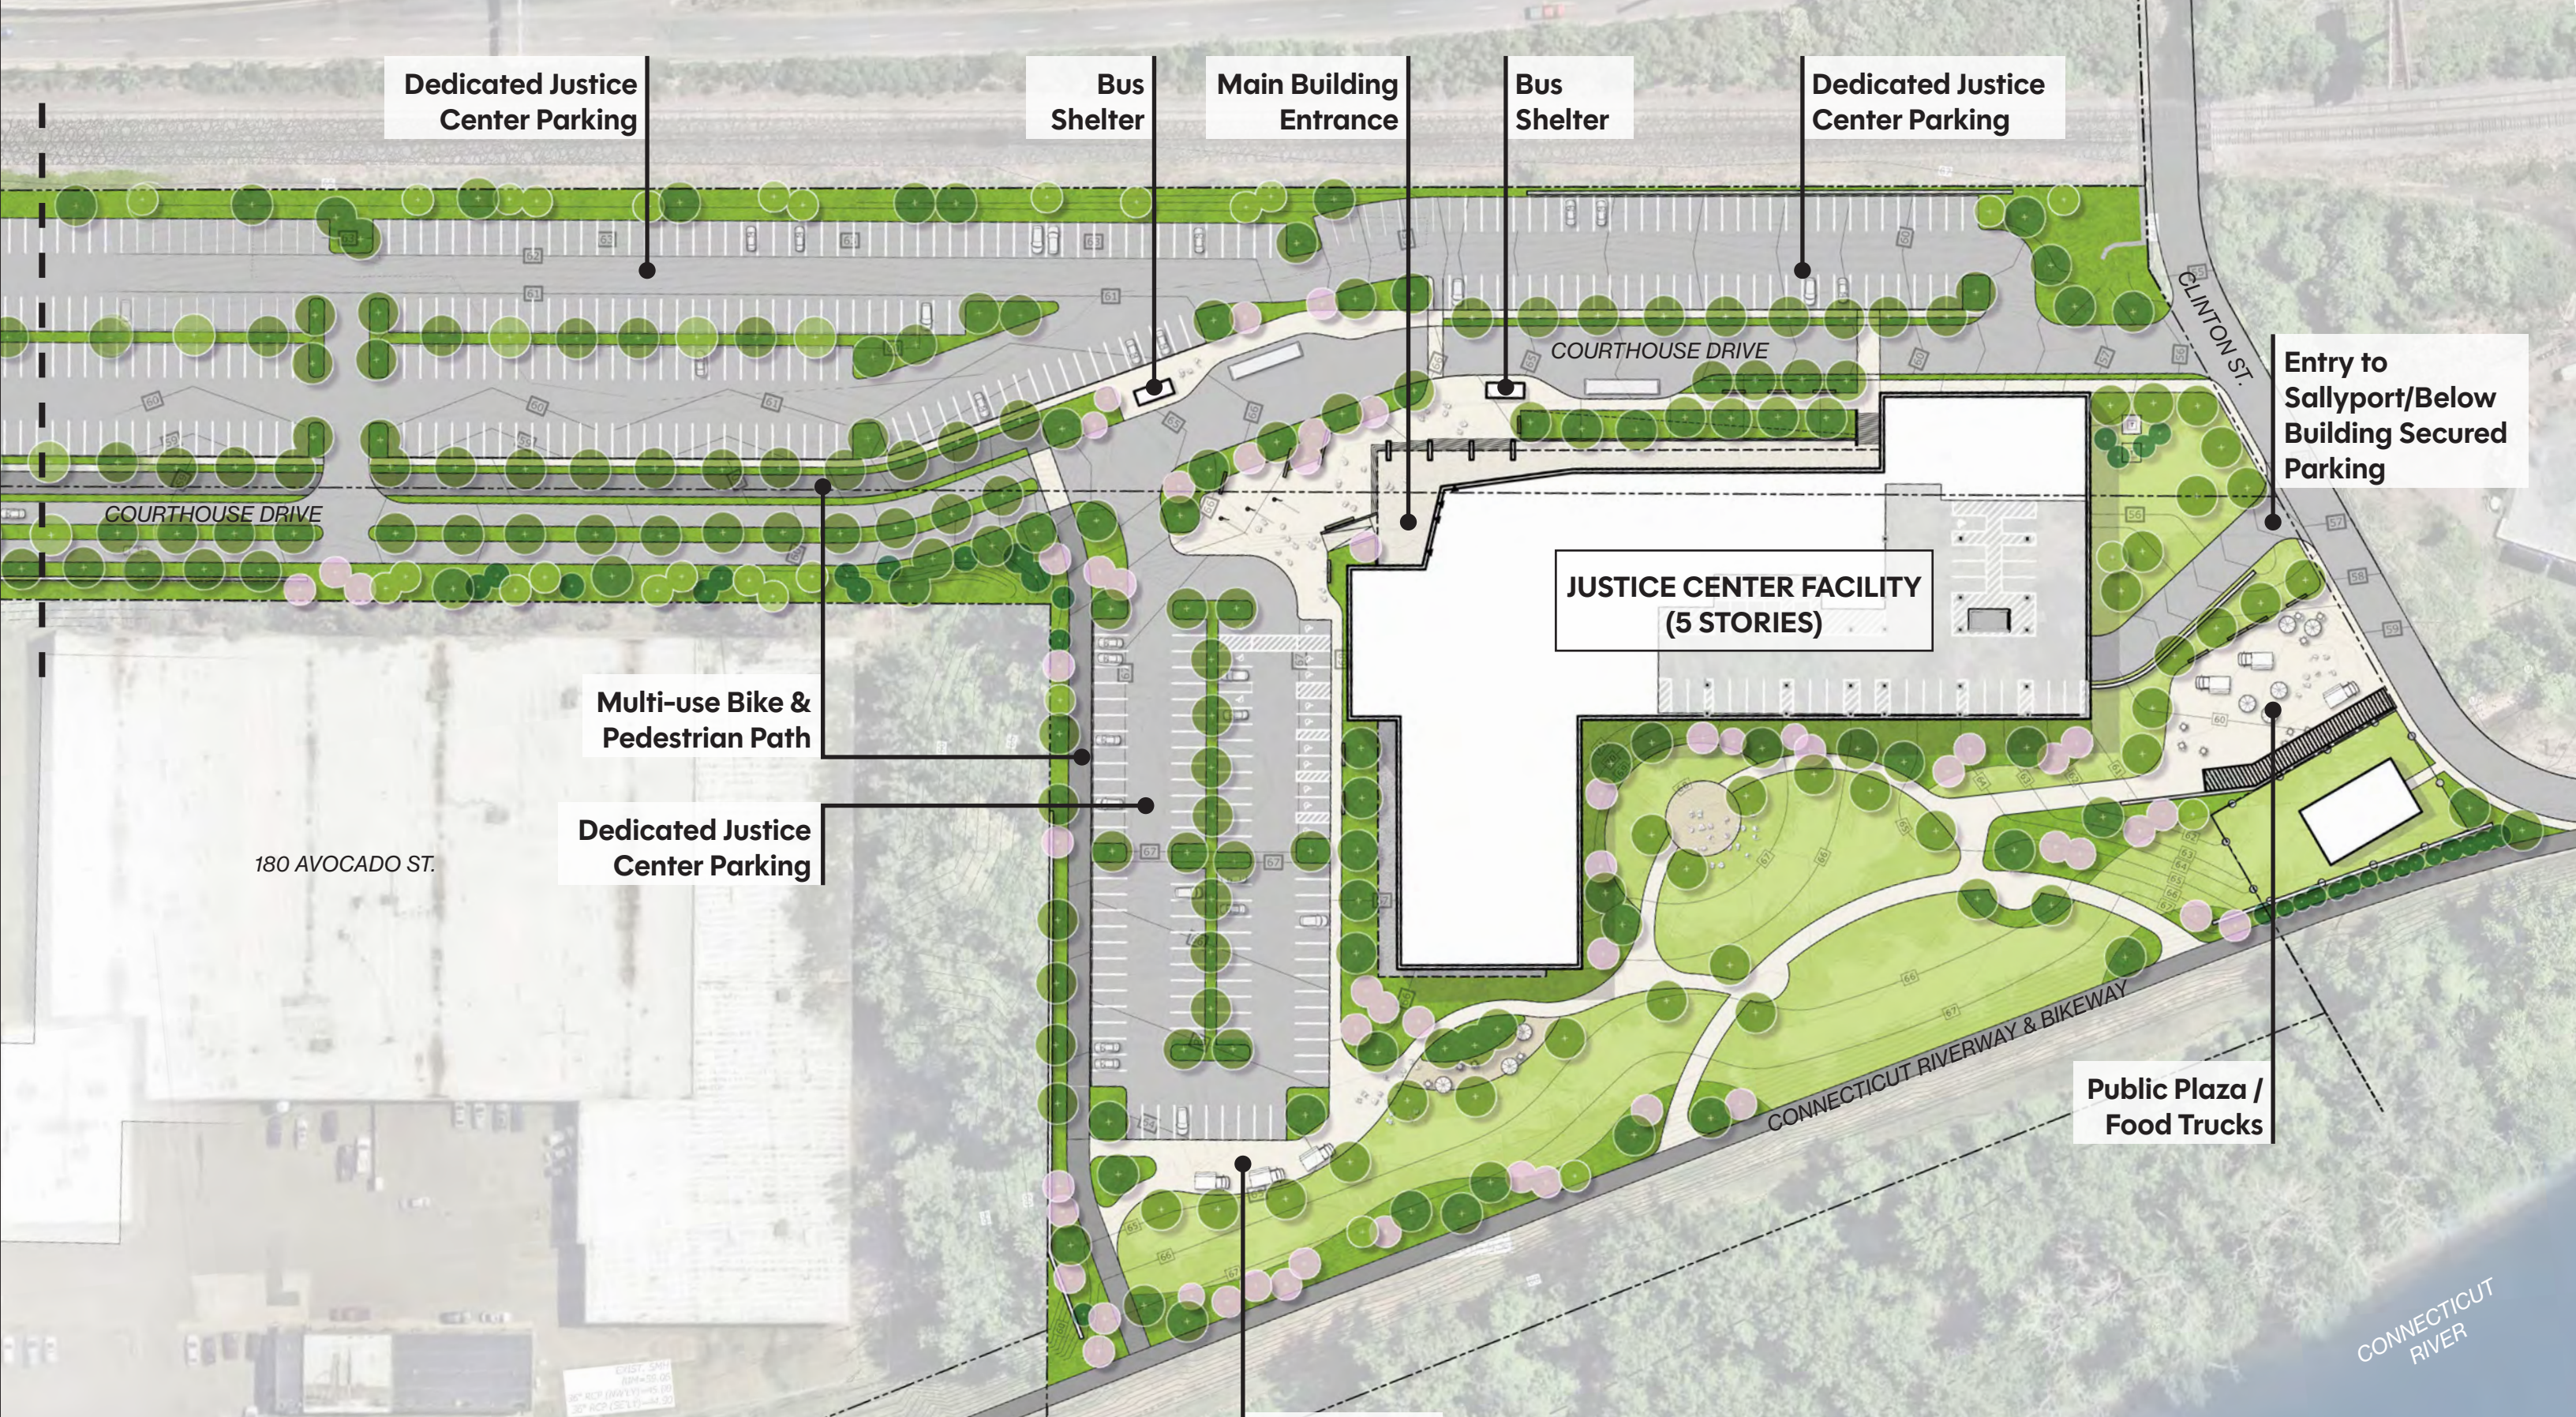

Dedicated Justice Center Parking

Bus Shelter

Main Building Entrance

Bus Shelter

Dedicated Justice Center Parking

Entry to Sallyport/Below Building Secured Parking

JUSTICE CENTER FACILITY (5 STORIES)

Multi-use Bike & Pedestrian Path


Dedicated Justice Center Parking

Public Plaza / Food Trucks


Public Plaza / Food Trucks


PARKING TYPE	LOCATION	STANDARD SPACES	ACCESSIBLE SPACES (VAN)	TOTAL SPACES
PUBLIC PARKING	SURFACE LOTS (WITHIN 1/4 MILE RADIUS)	639	12 (3)	651
RESERVED, SECURED	BENEATH BUILDING	32	1 (1)	33
RESERVED	SURFACE LOT NORTH OF BUILDING	36	2 (1)	38
TOTAL ON-SITE PARKING		707	15 (5)	722

Proposed Landscape Plan | R1.11



CONNECTICUT RIVER



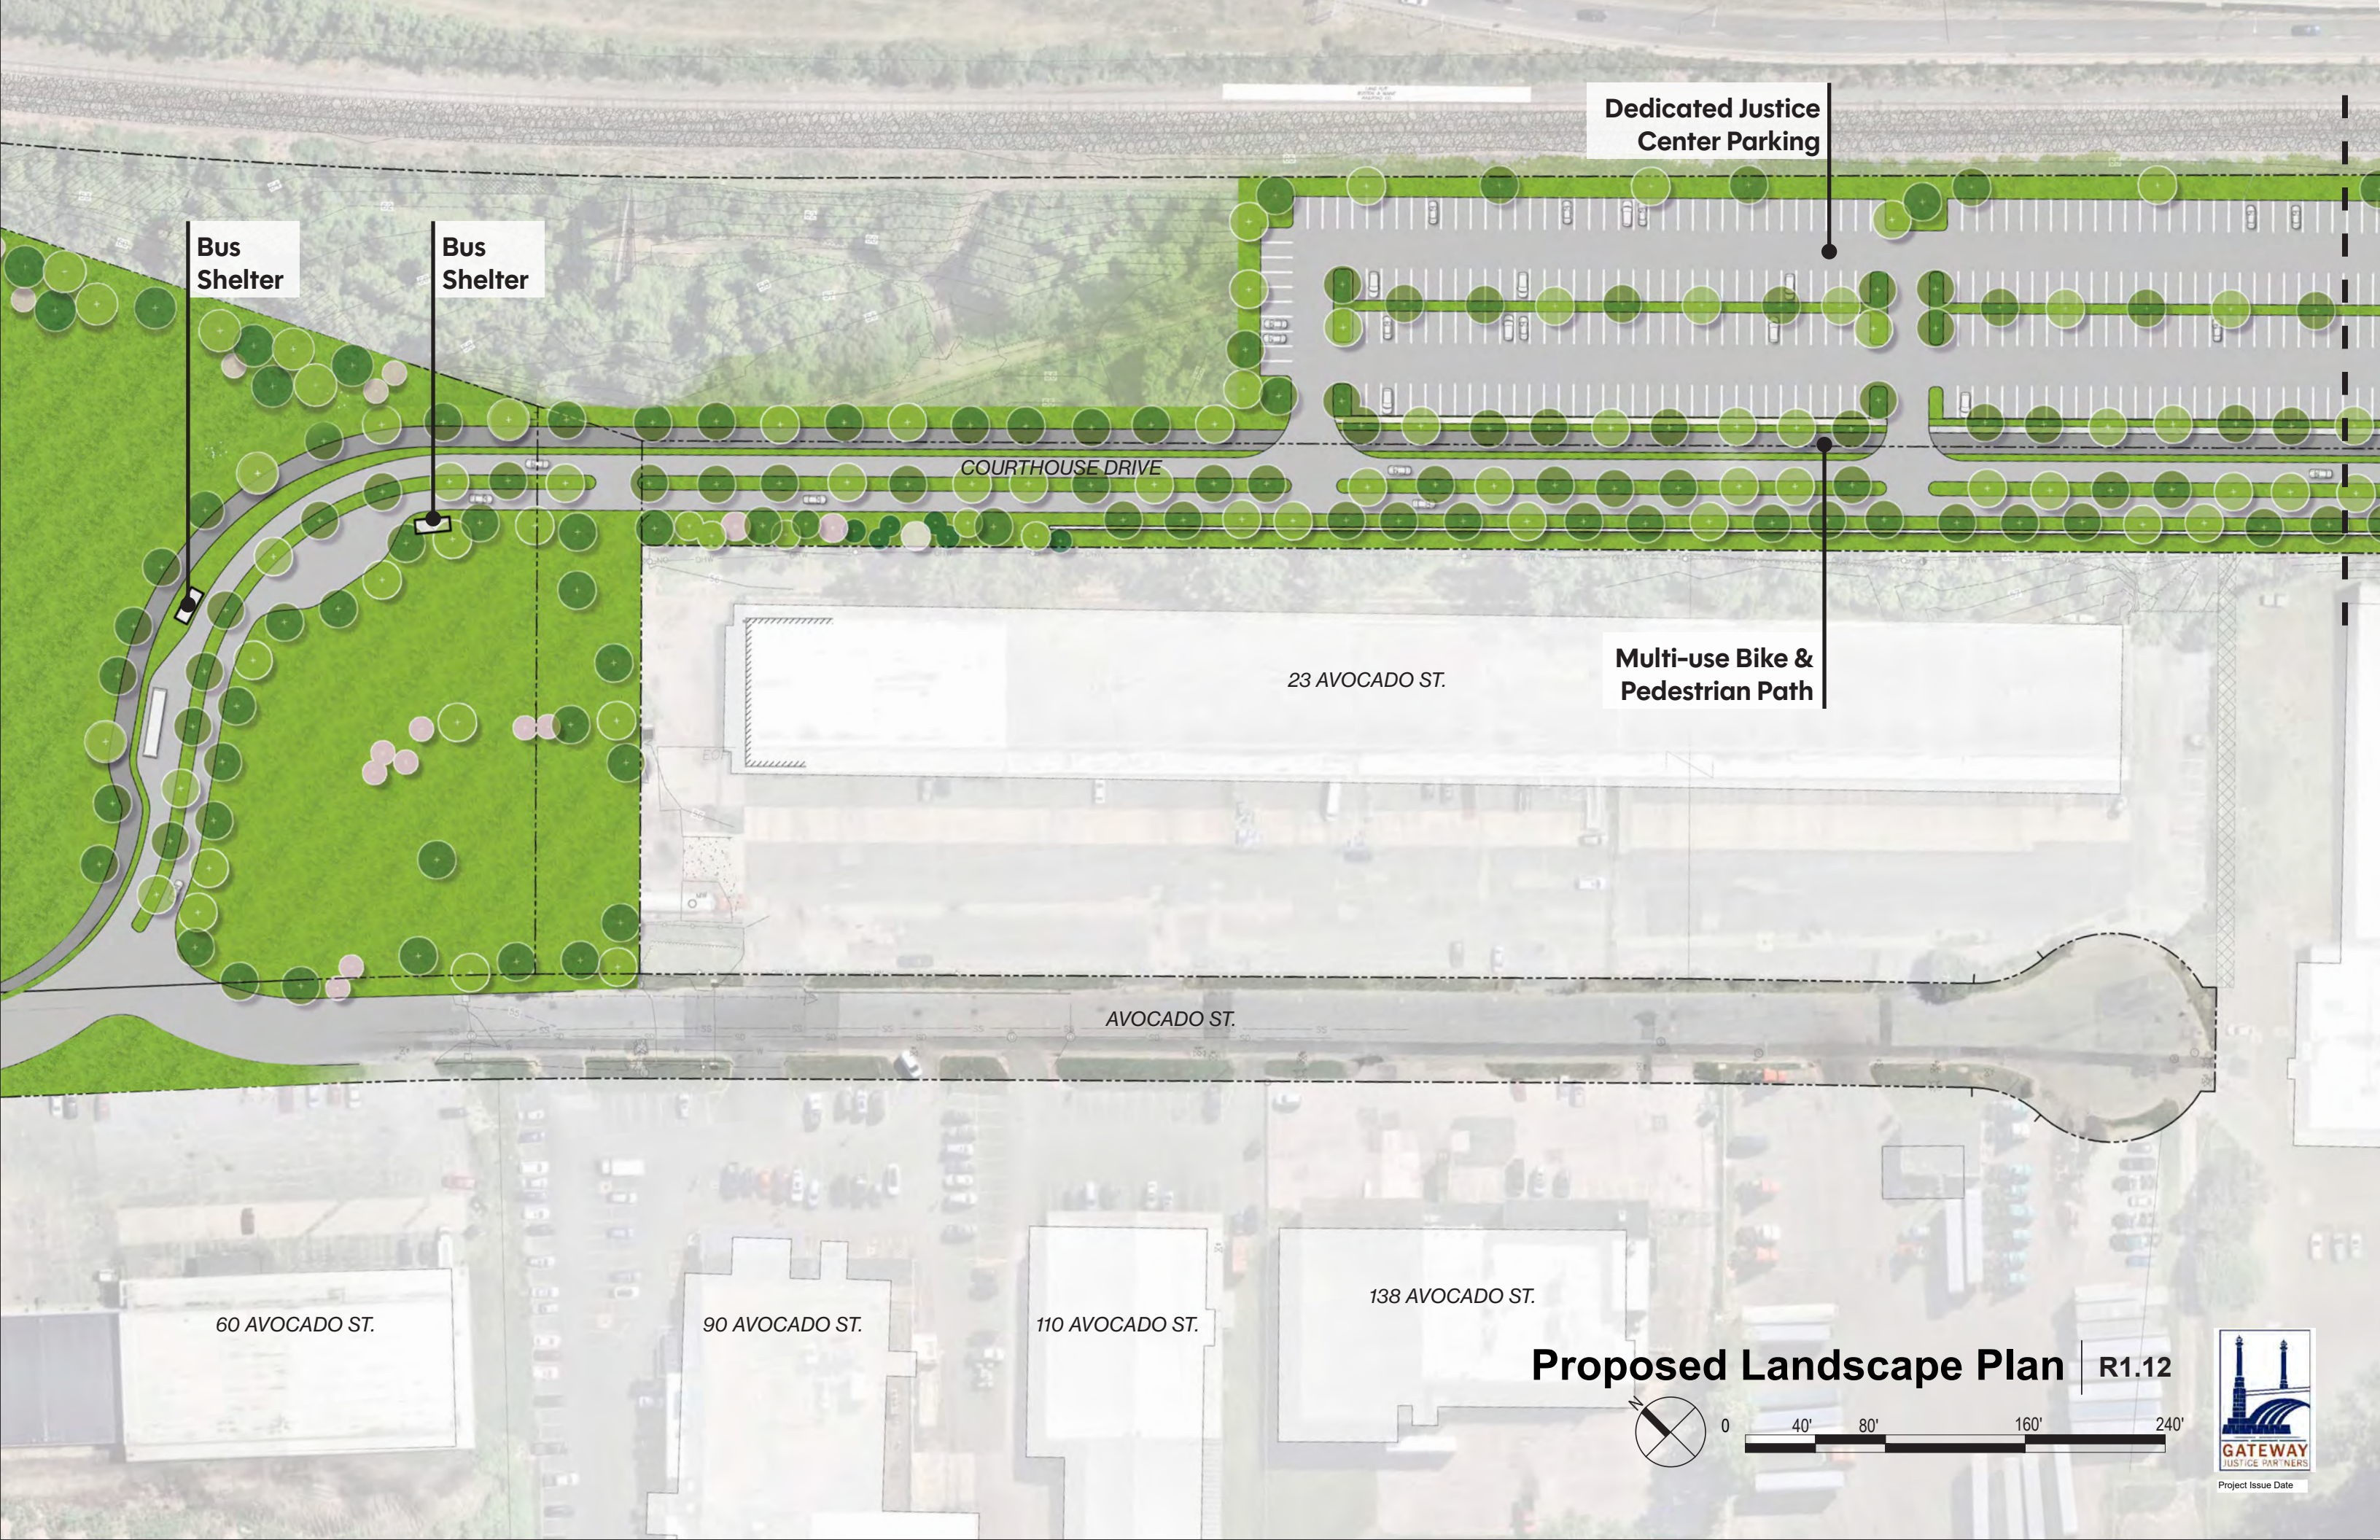

Bus Shelter

Bus Shelter

Dedicated Justice Center Parking

COURTHOUSE DRIVE

23 AVOCADO ST.

Multi-use Bike & Pedestrian Path

AVOCADO ST.


60 AVOCADO ST.


90 AVOCADO ST.

110 AVOCADO ST.

138 AVOCADO ST.

Proposed Landscape Plan | R1.12



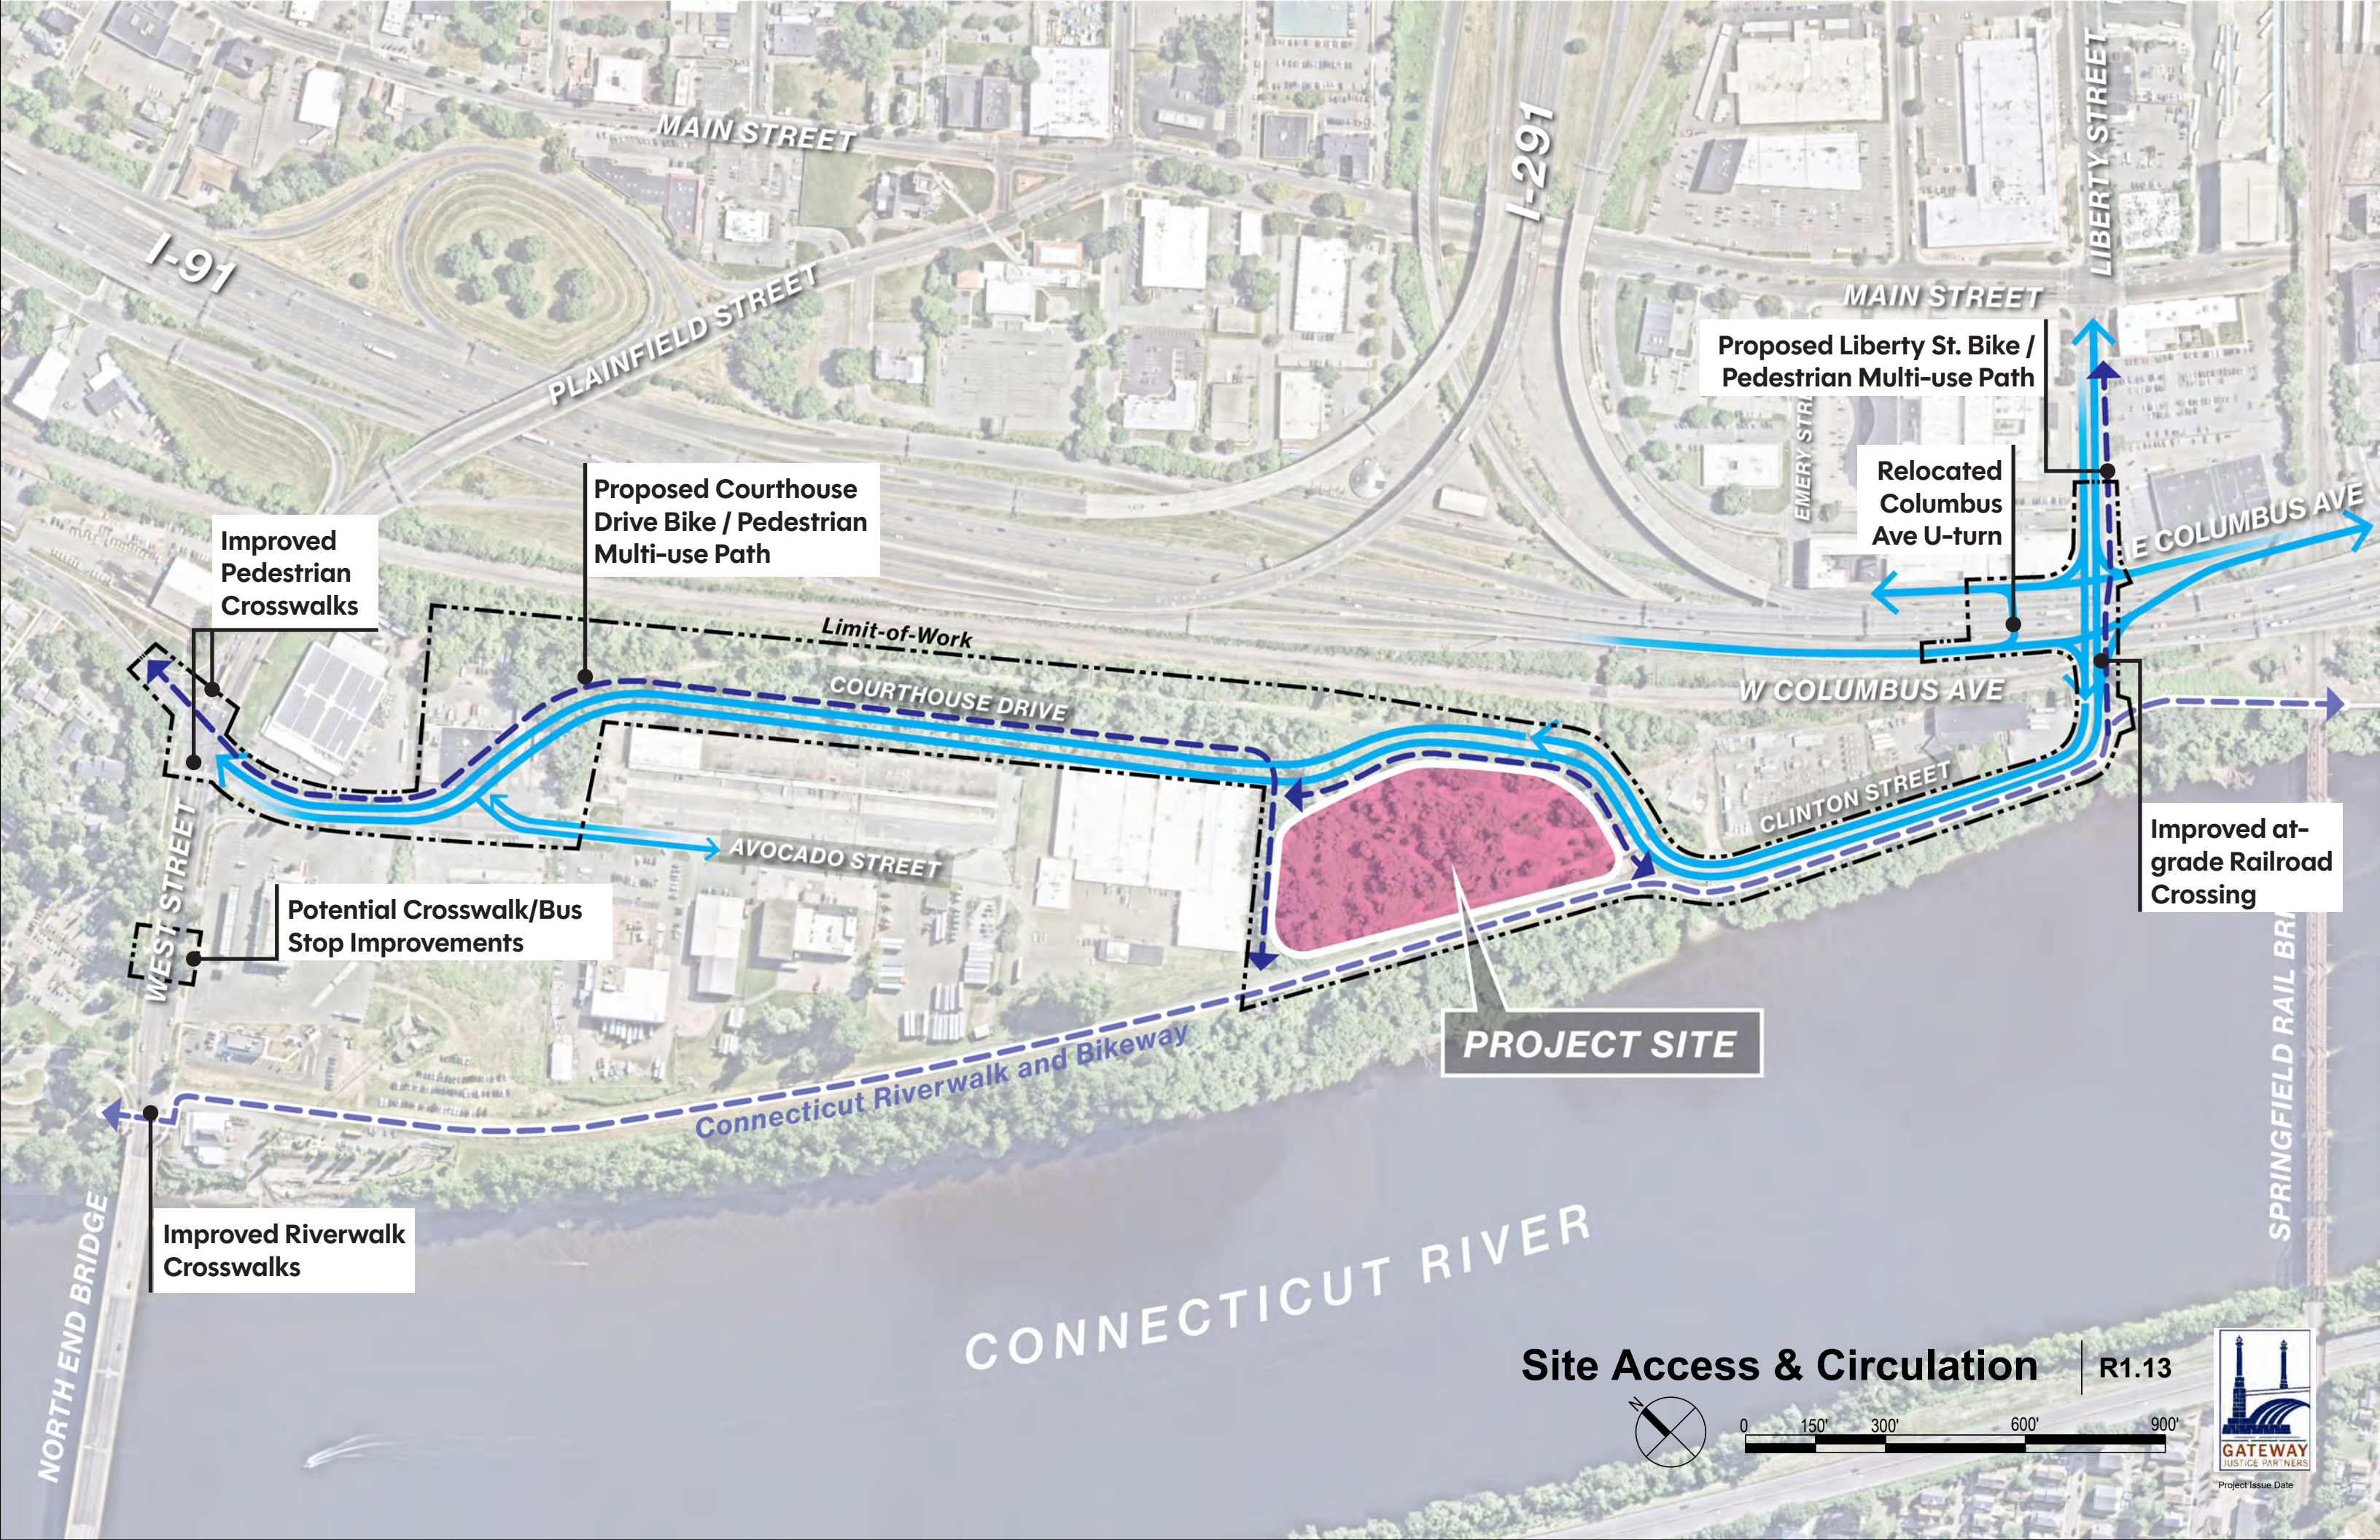

Proposed Courthouse Drive Bike / Pedestrian Multi-use Path

Proposed Liberty St. Bike / Pedestrian Multi-use Path

Relocated Columbus Ave U-turn

Improved Pedestrian Crosswalks



Potential Crosswalk/Bus Stop Improvements


Improved at-grade Railroad Crossing

PROJECT SITE

Site Access & Circulation

R1.13



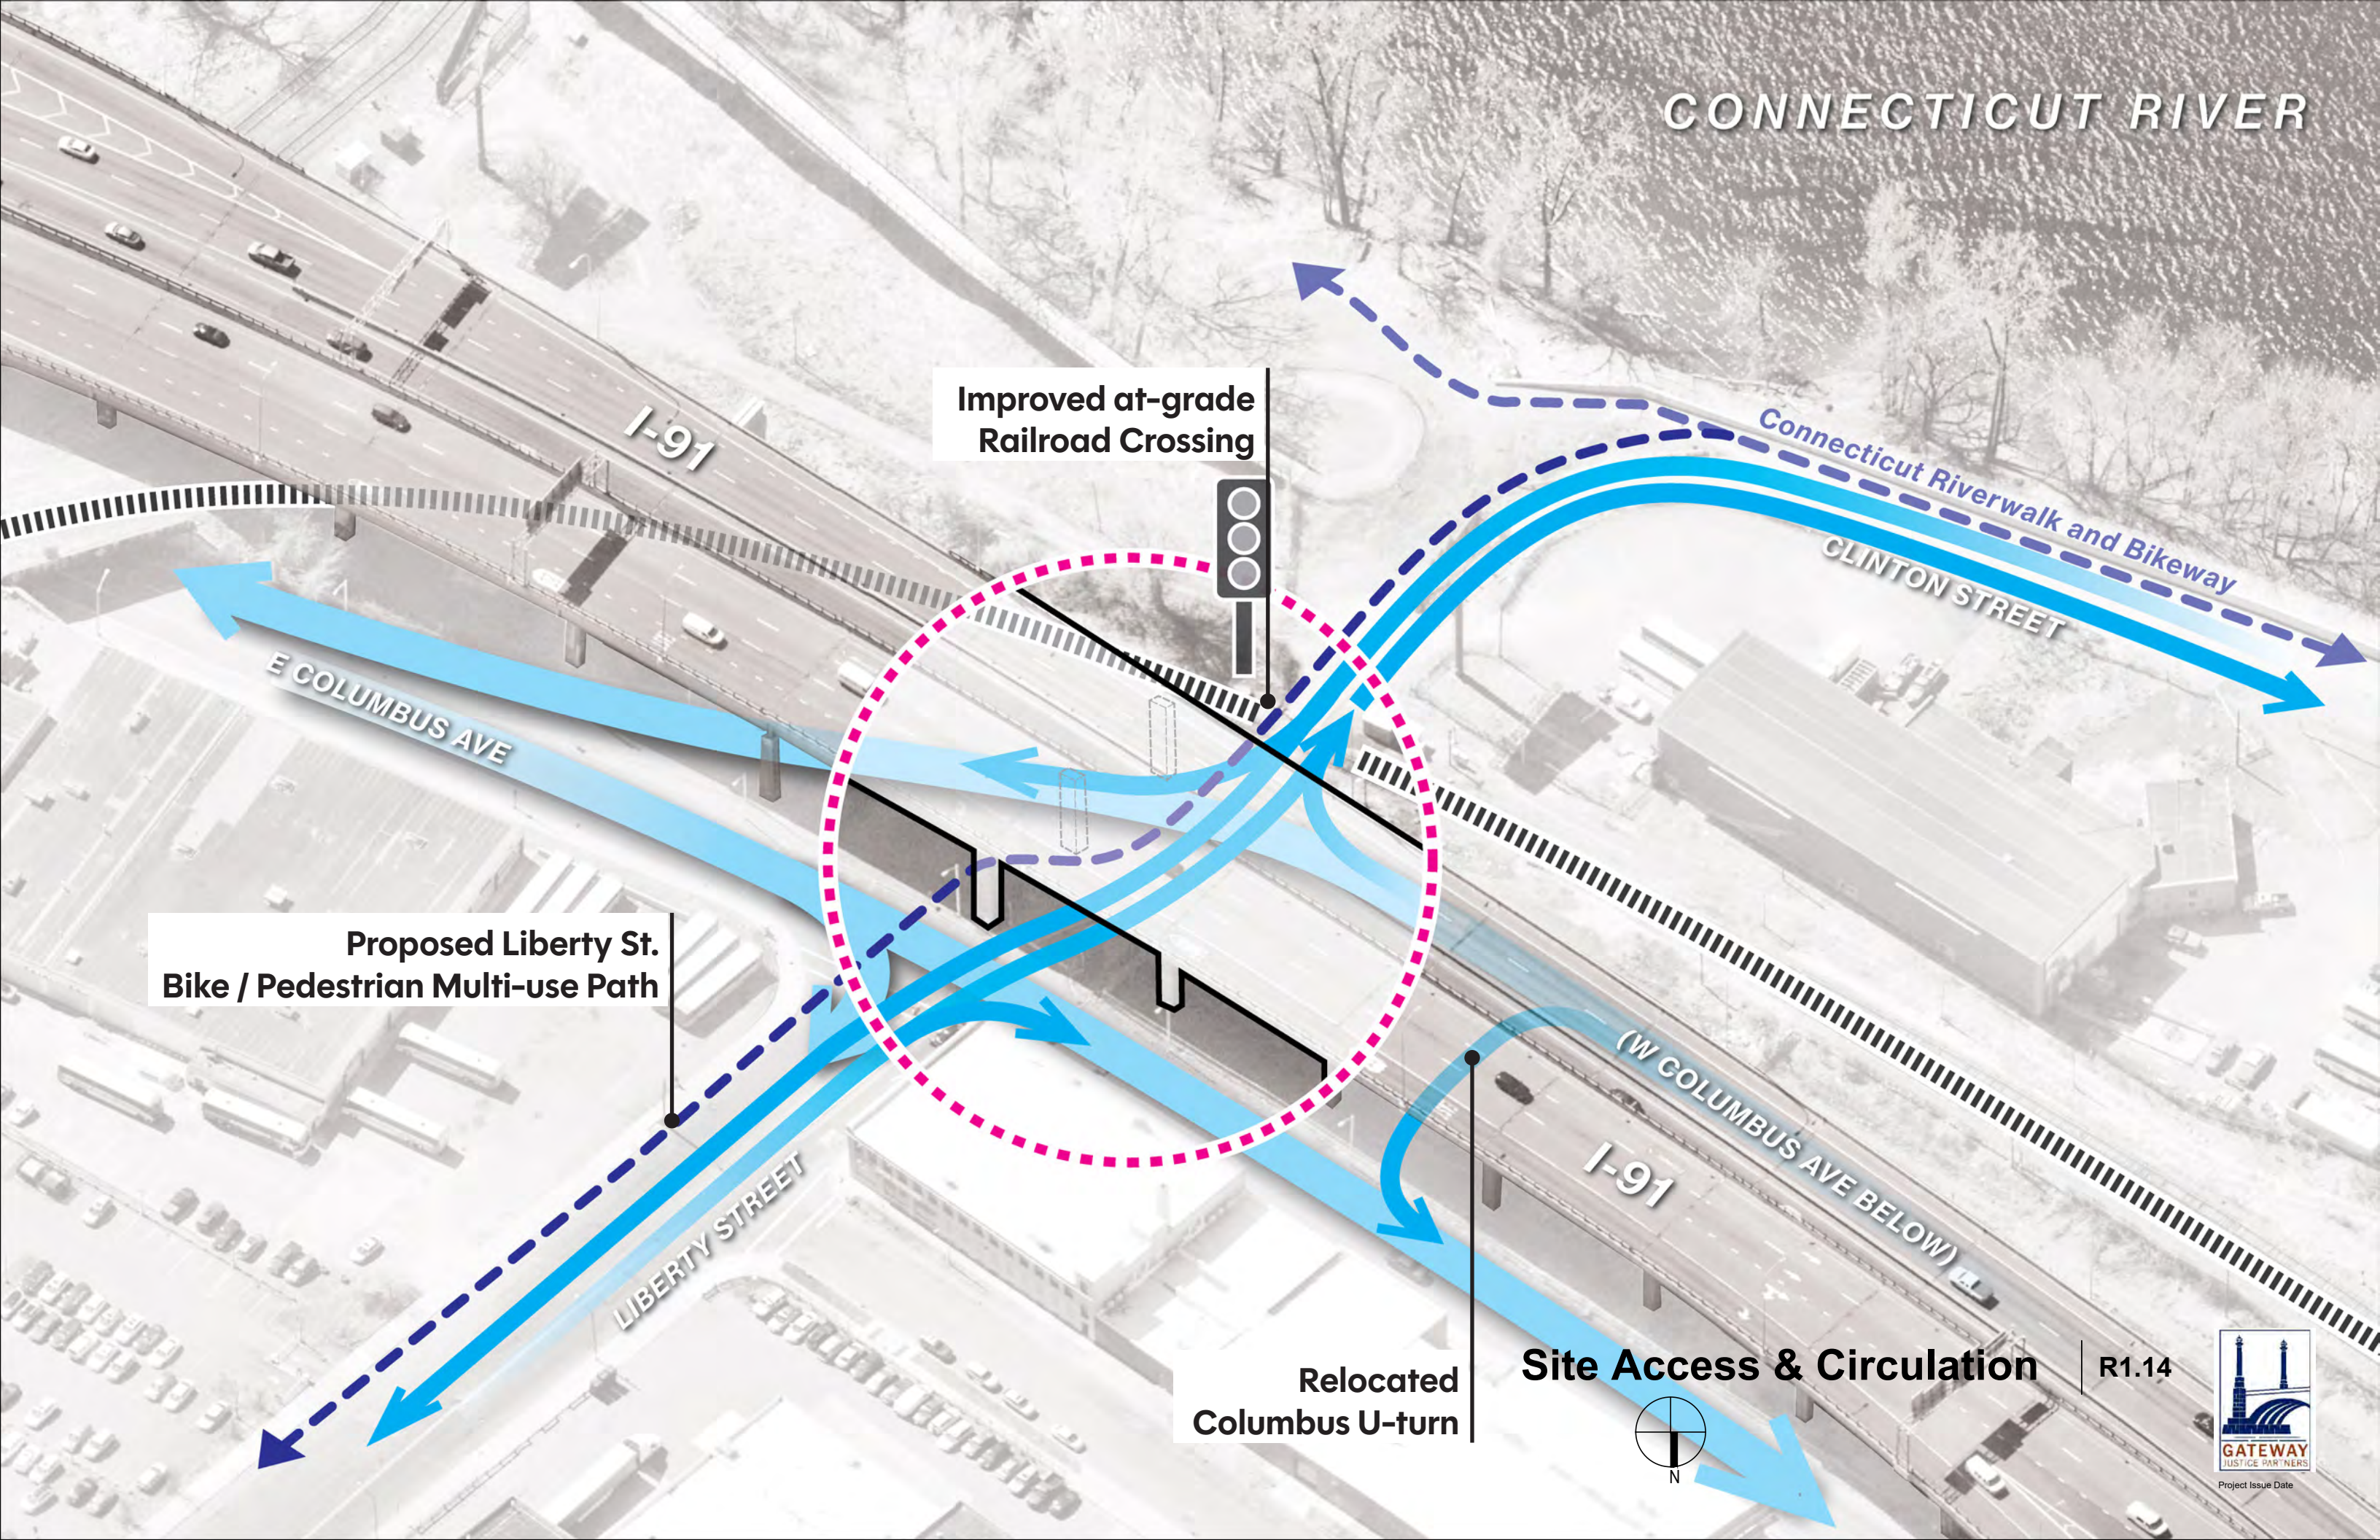

Improved at-grade
Railroad Crossing

Proposed Liberty St.
Bike / Pedestrian Multi-use Path

Relocated
Columbus U-turn

Site Access & Circulation

R1.14




All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

Perspective - Liberty Street Underpass to Clinton Street and Courthouse Drive (Existing Condition)

R1.15



Project Issue Date

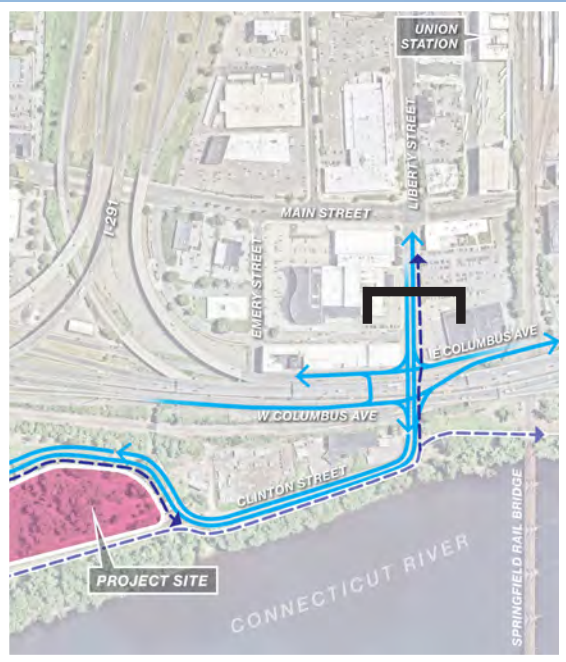

All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

Perspective - Liberty Street Underpass to Clinton Street and Courthouse Drive Proposed Condition

R1.16



Project Issue Date



All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.



Perspective - Liberty Street Underpass to Clinton Street and Courthouse Drive Proposed Condition

R1.17






Project Issue Date

Existing

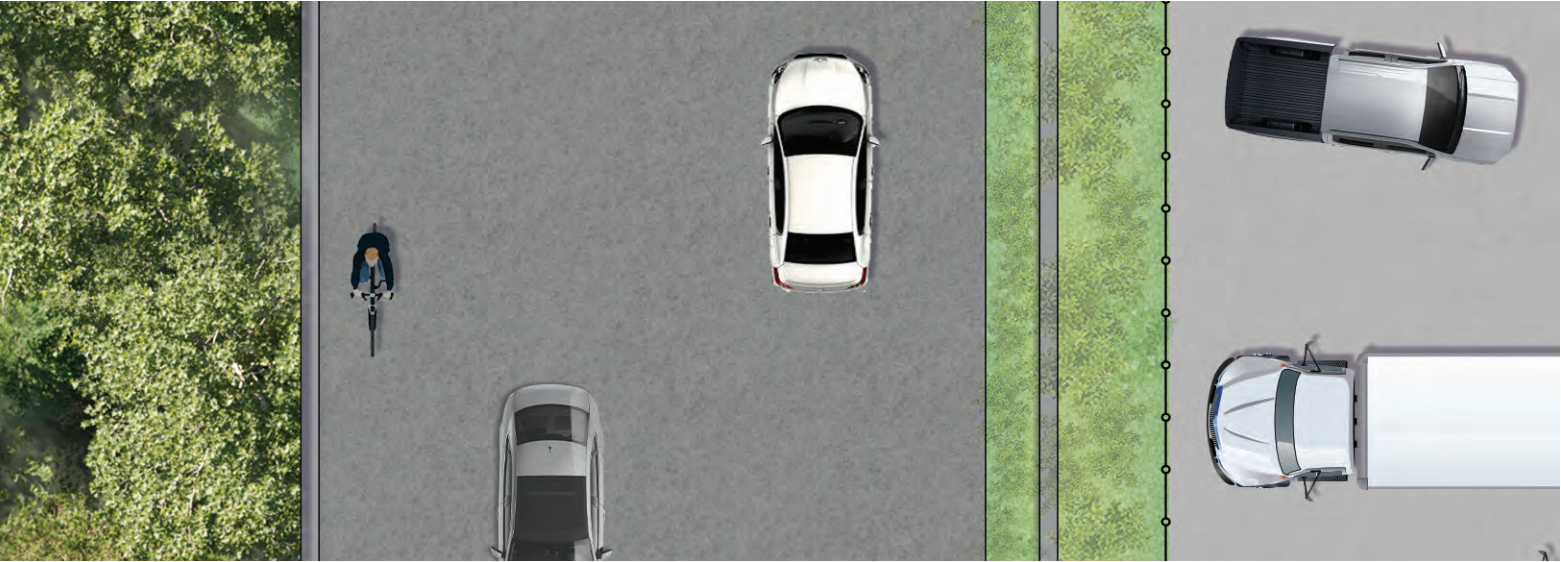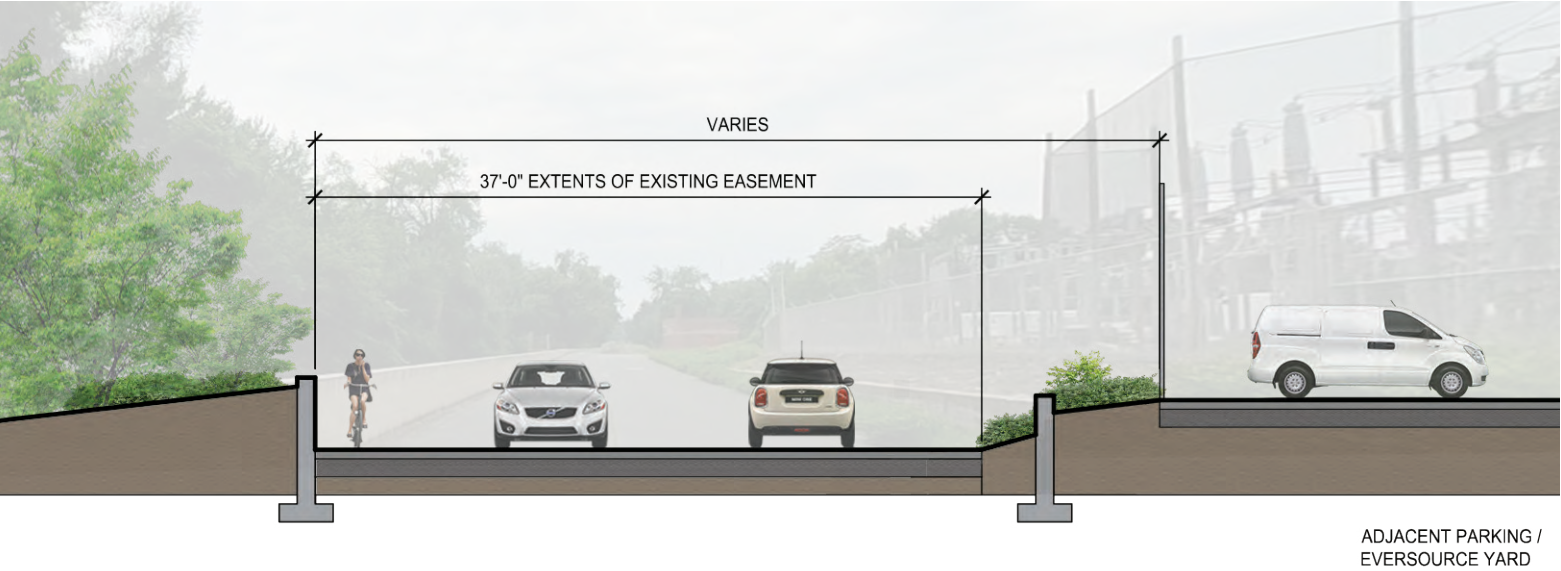

Proposed

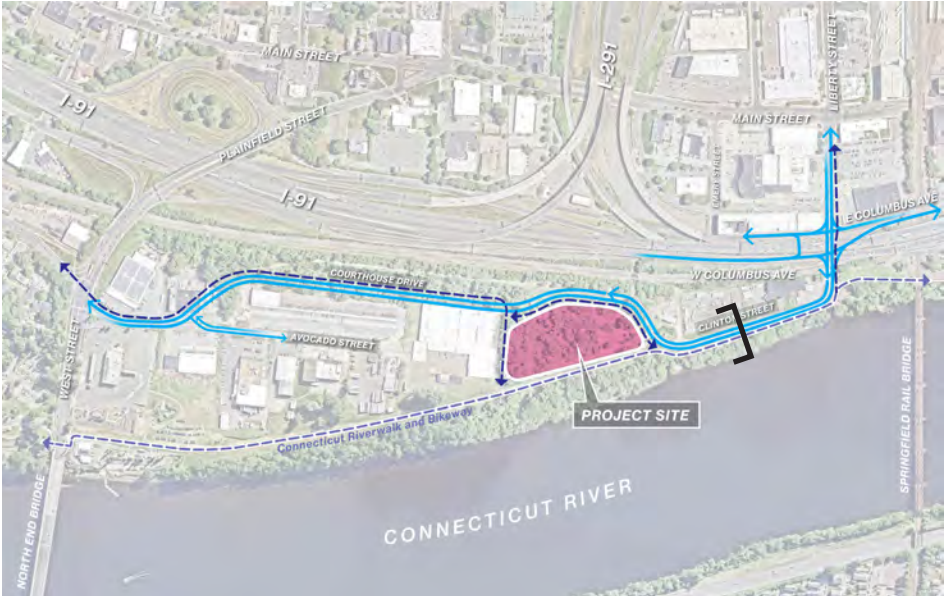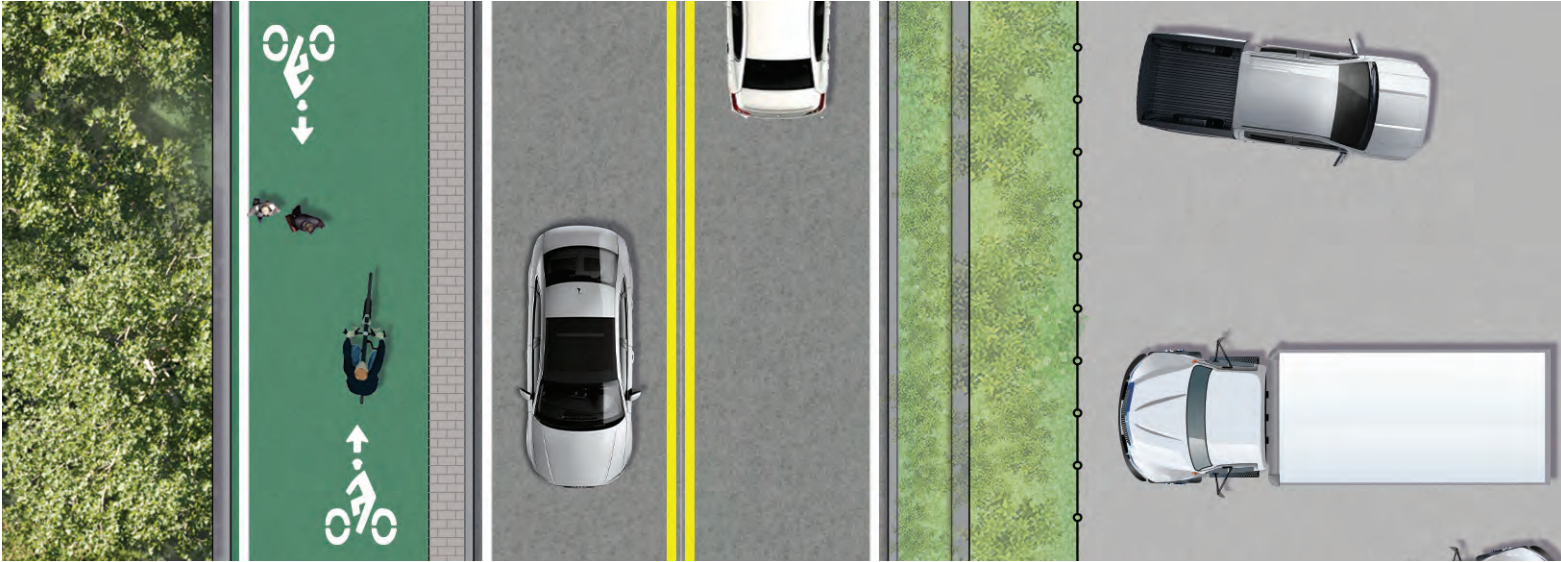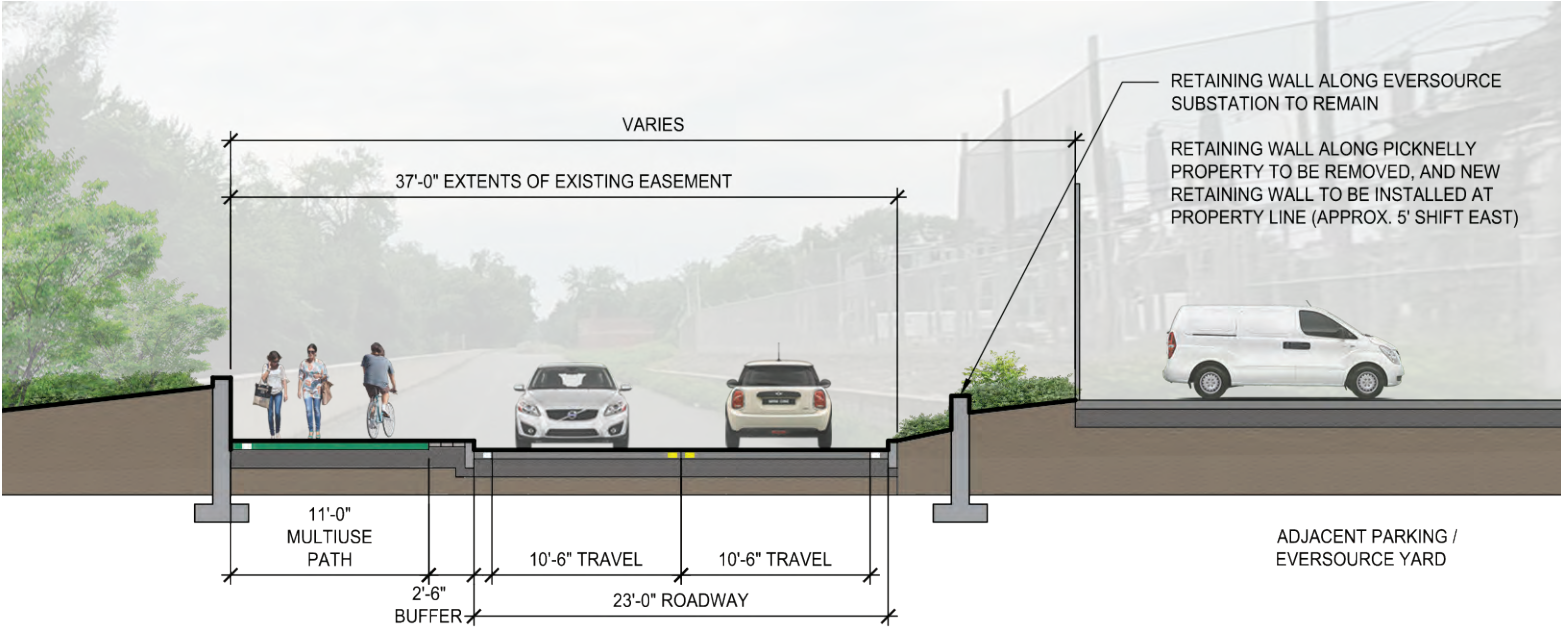


Street Section - Clinton Street | R1.18





Project Issue Date

Existing

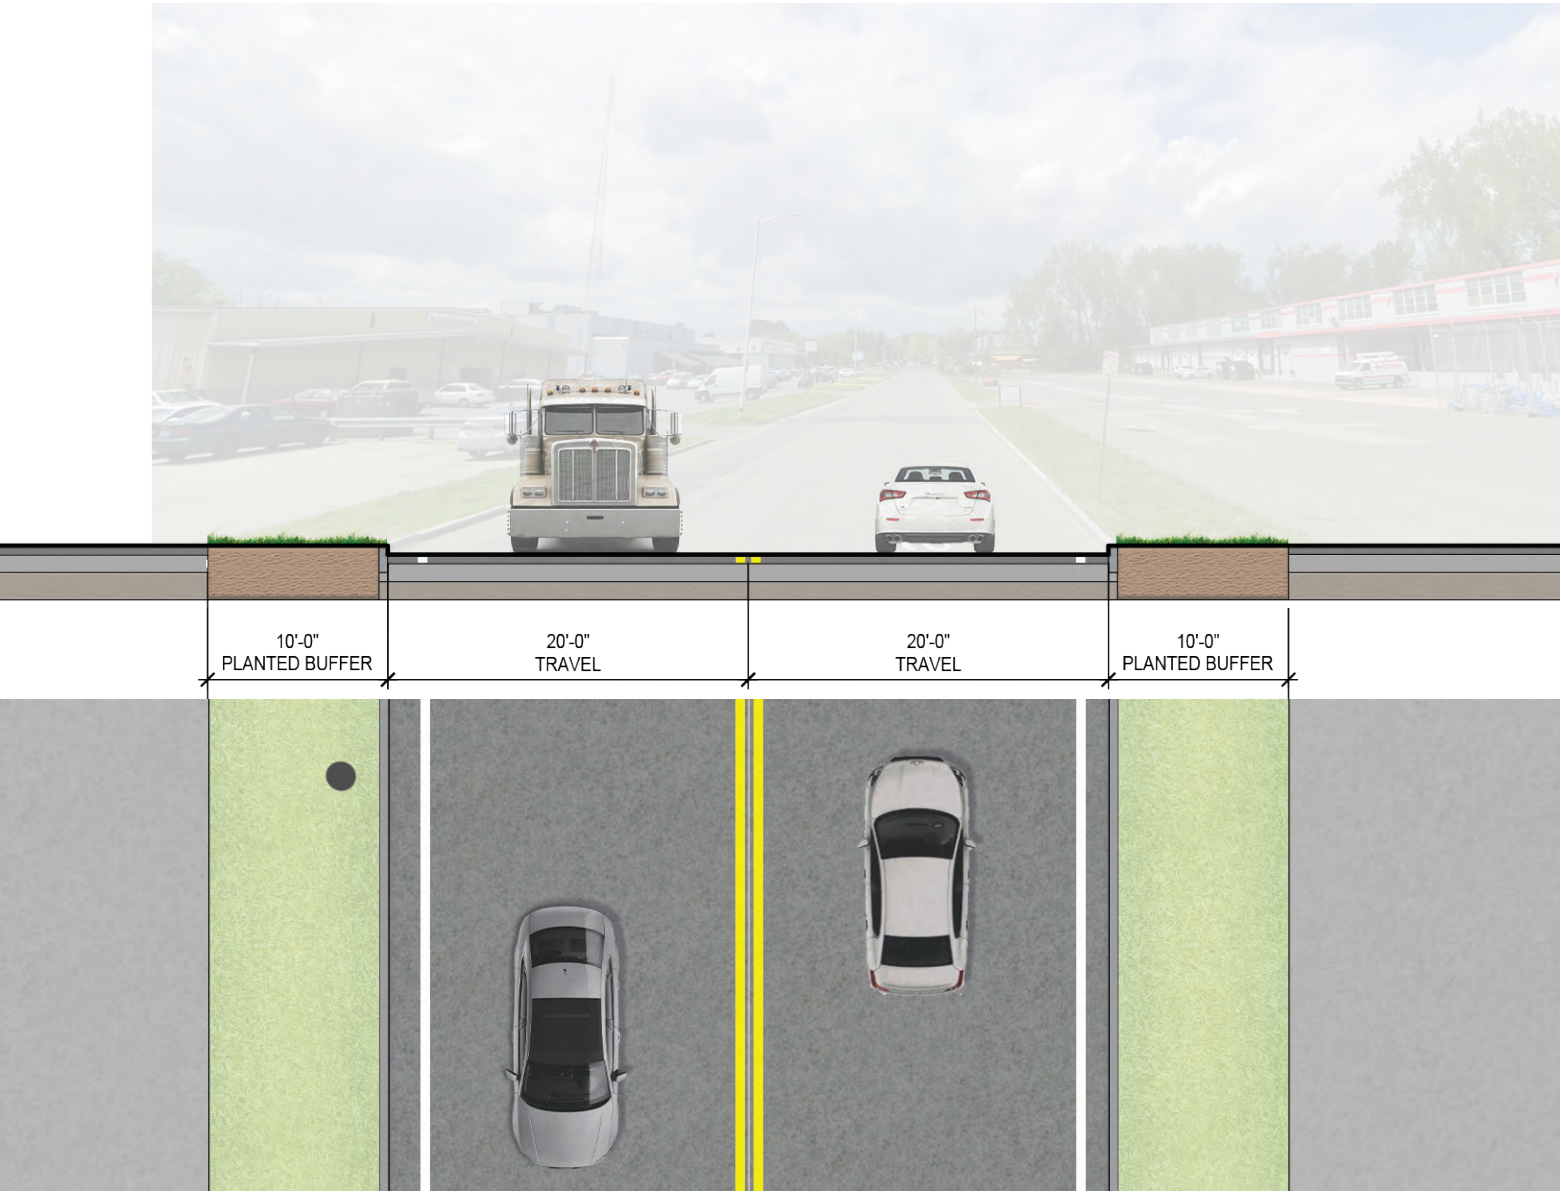


Proposed

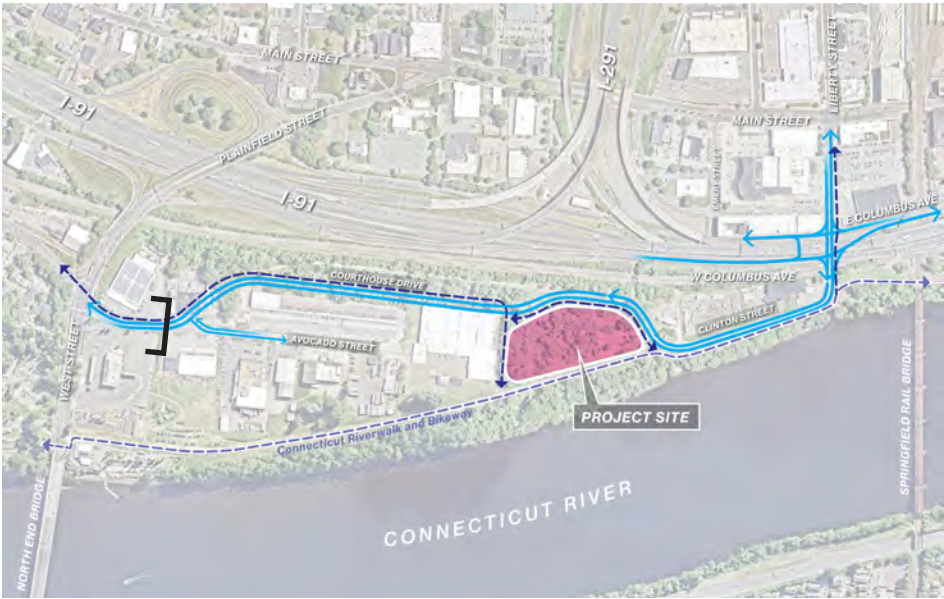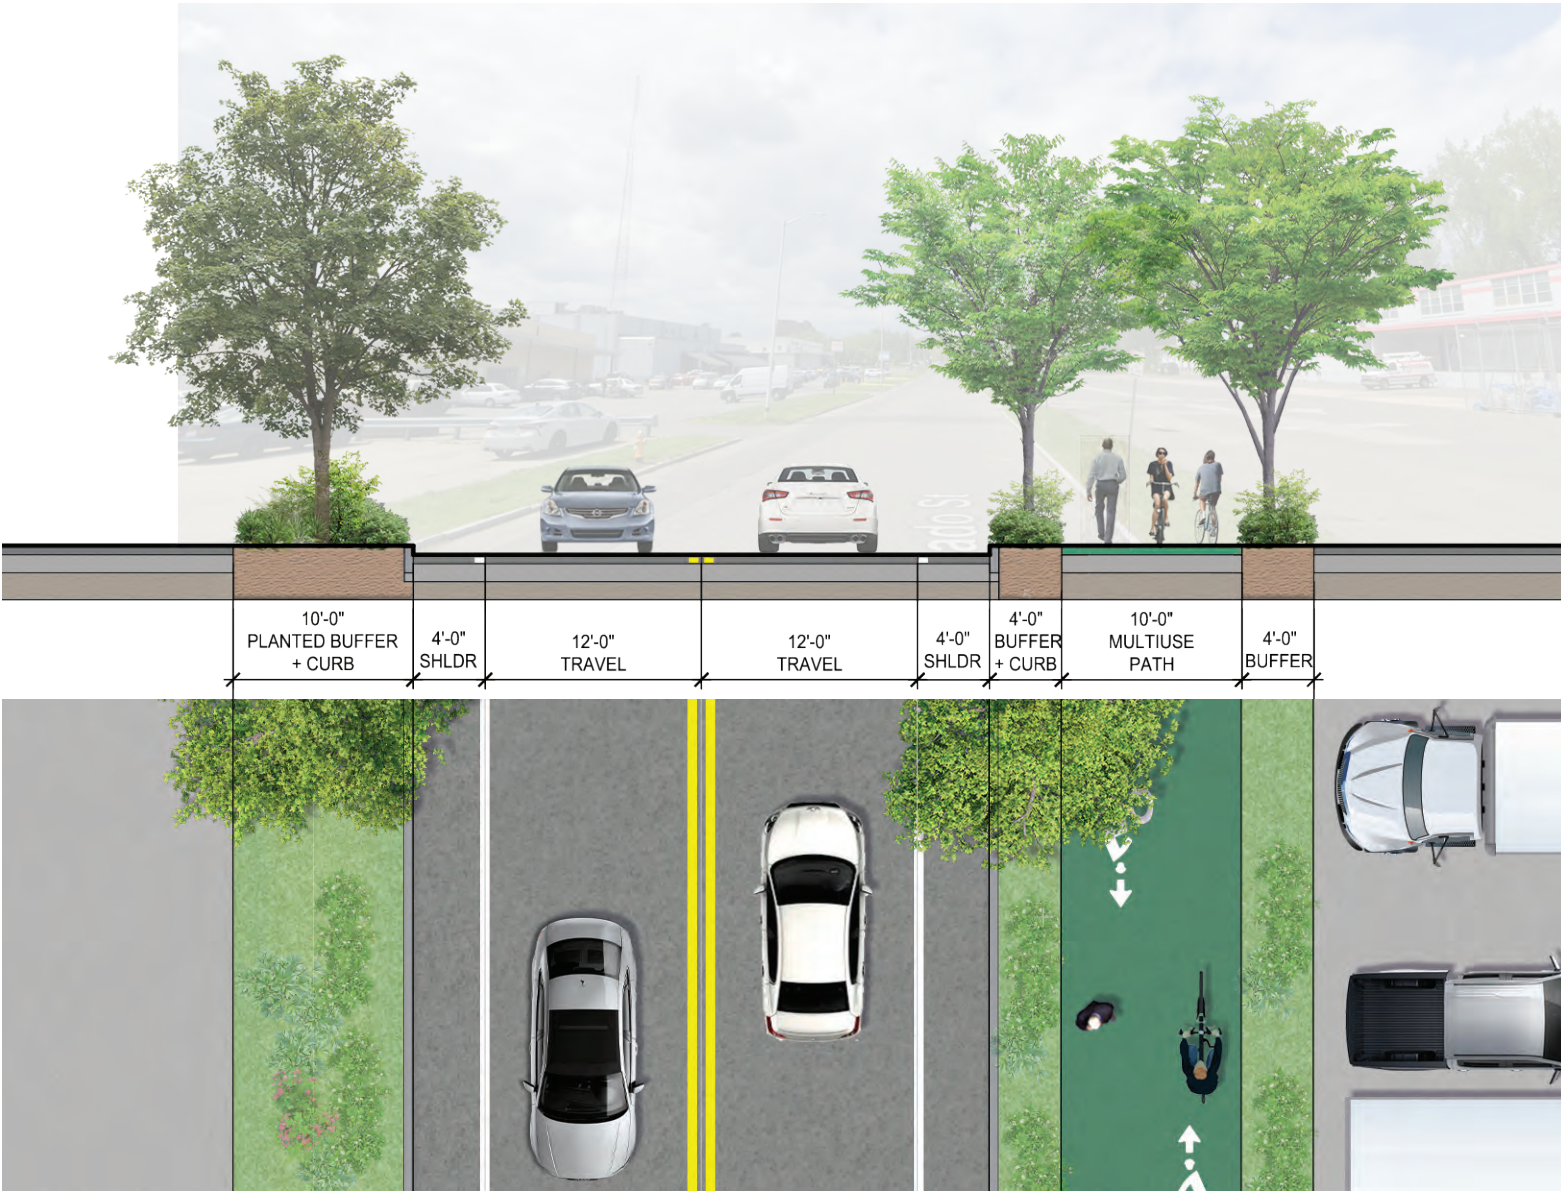

Street Section - Avocado Street | R1.19



Project Issue Date

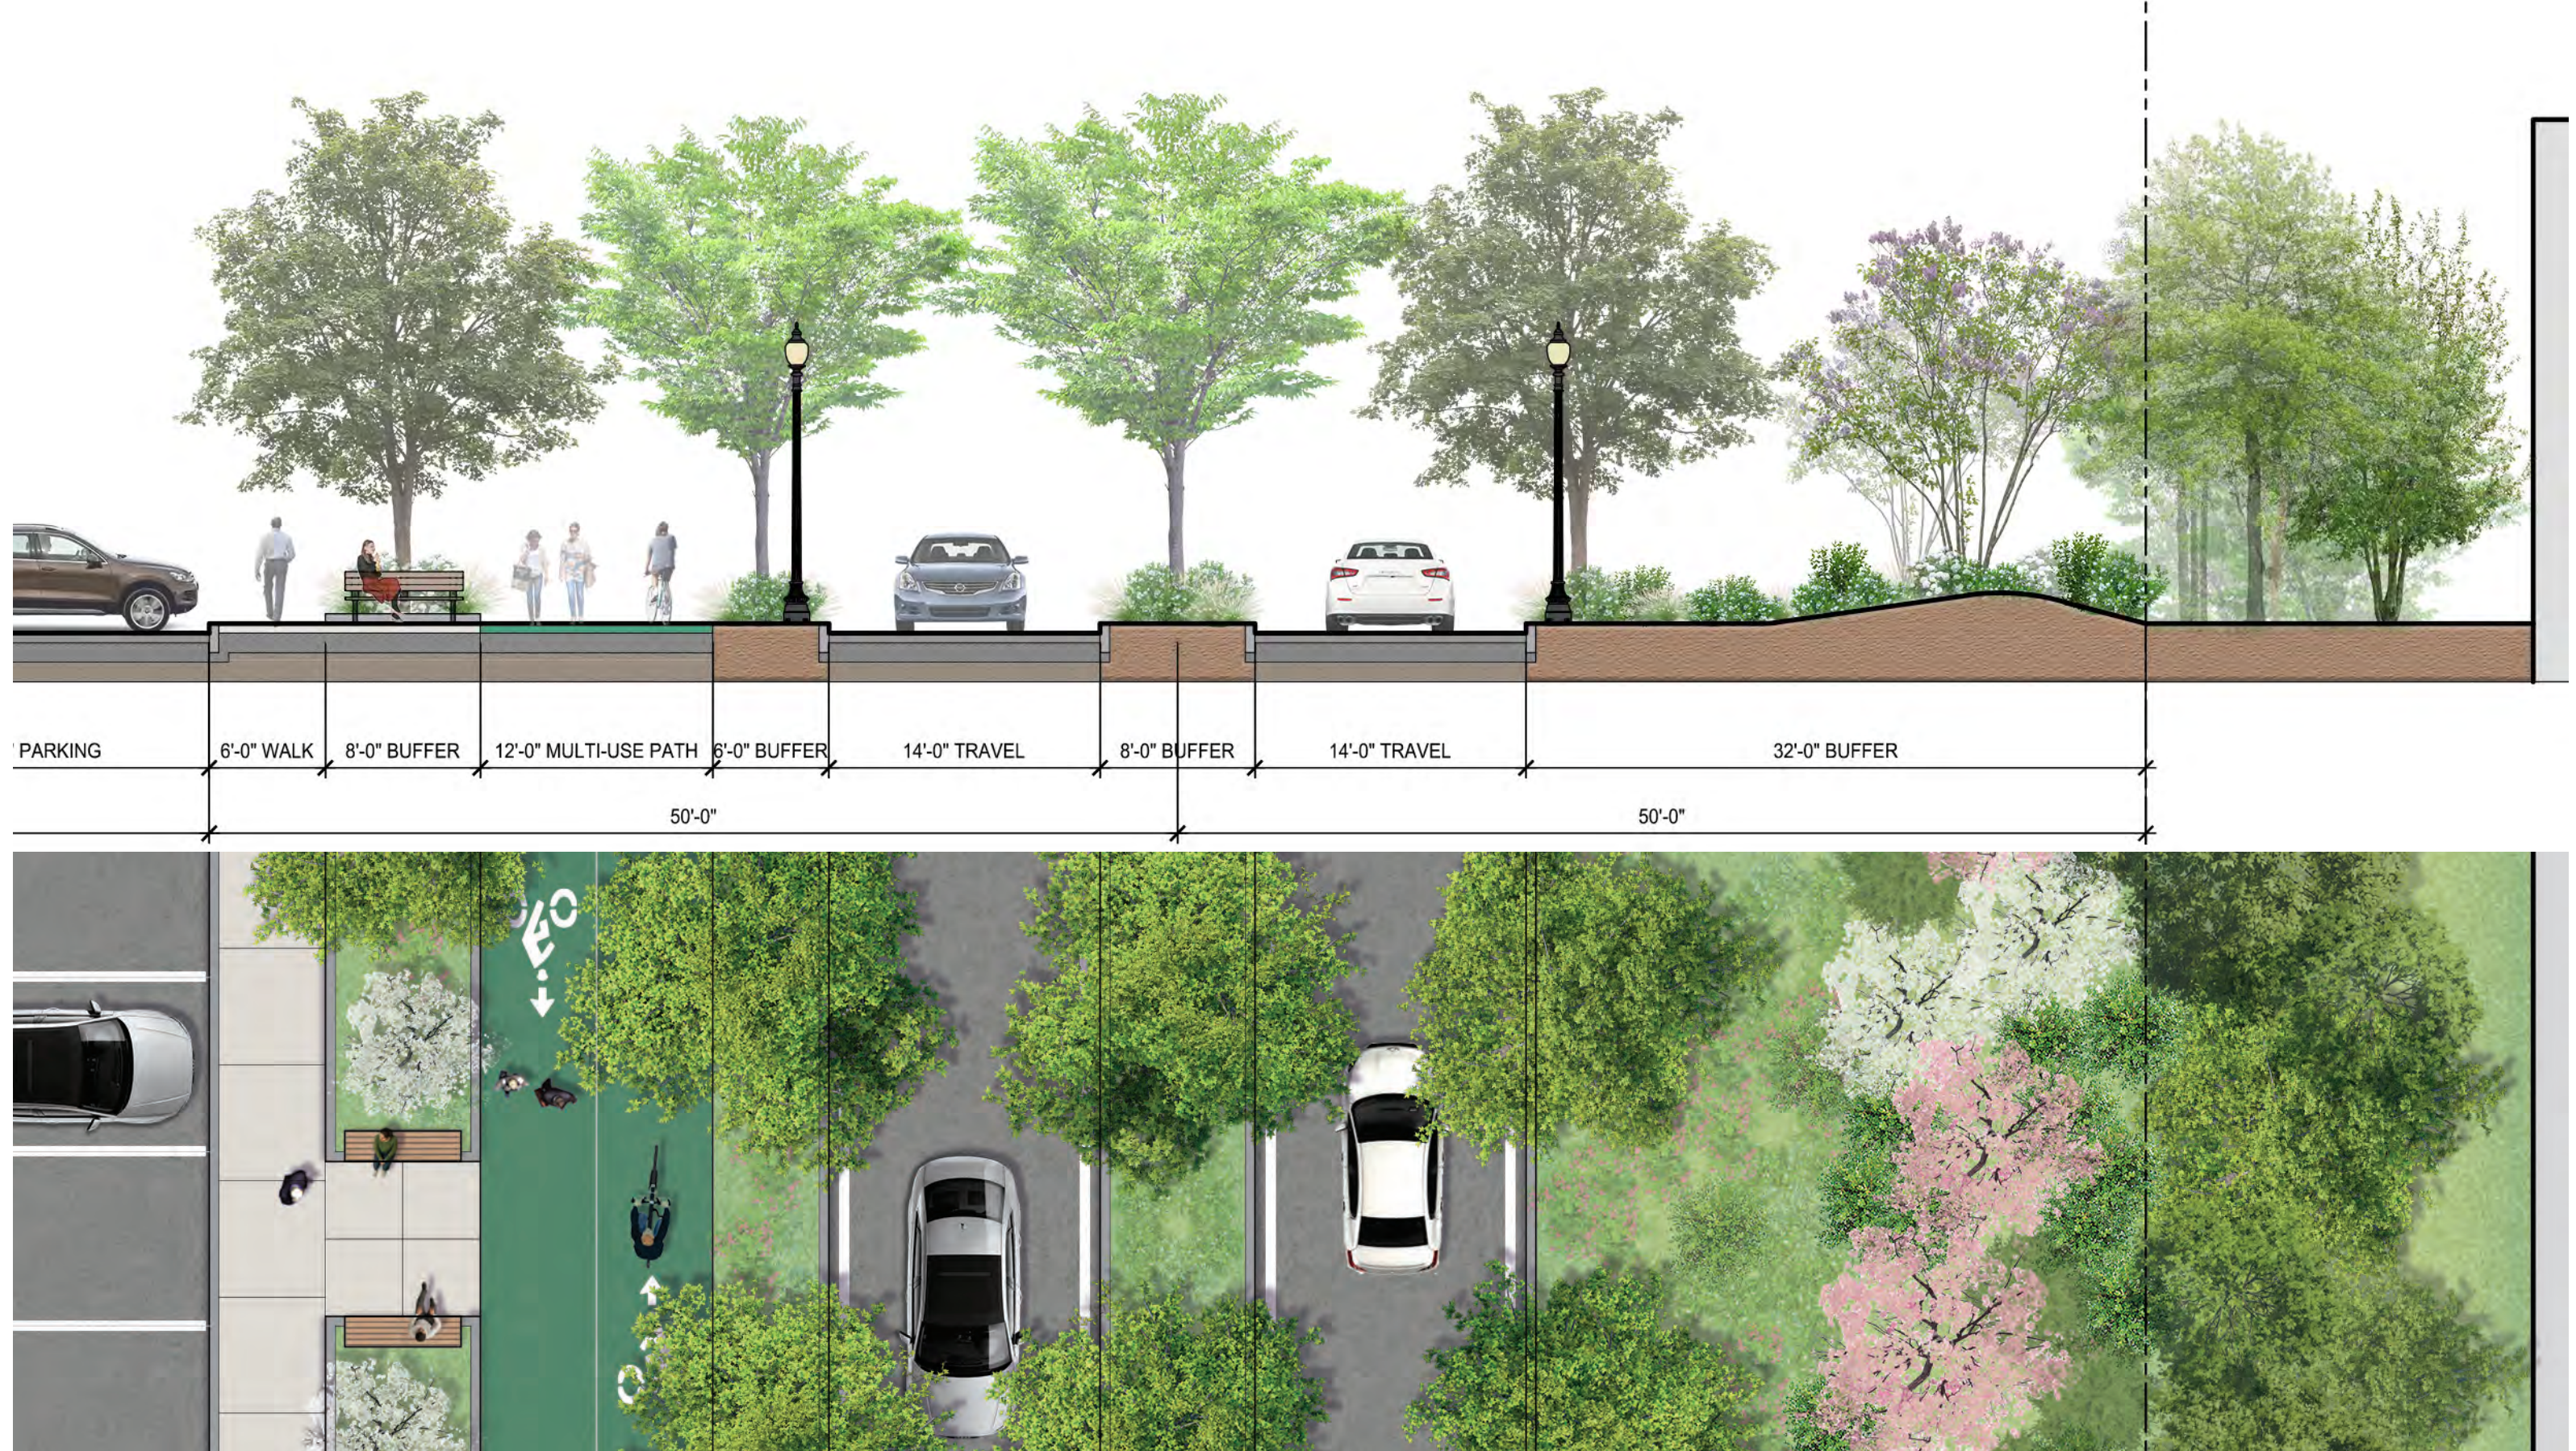

Street Section - Courthouse Dr. Proposed

R1.20



Project Issue Date

OPAL/Winn Multifamily Residential

**Justice Center Project's
Approximate Limit of
Improvements**

**Public Open Space Provided
with Justice Center Project**

**Springfield
Regional Justice
Center**

**Screening of Electrical
Sub-Station**

**Improved Clinton Street to
Include Separated Riverwalk**

**Re-Visioning of I-91
Underpass into Artful
Riverfront Gateway**


**Improved Liberty
Street Corridor
Including Two-Way
Vehicular Connection
to Riverfront and
Multi-Use Path**

Connecticut River


All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

**North End Riverfront
Masterplan Vision
Looking North**

R1.21



Project Issue Date

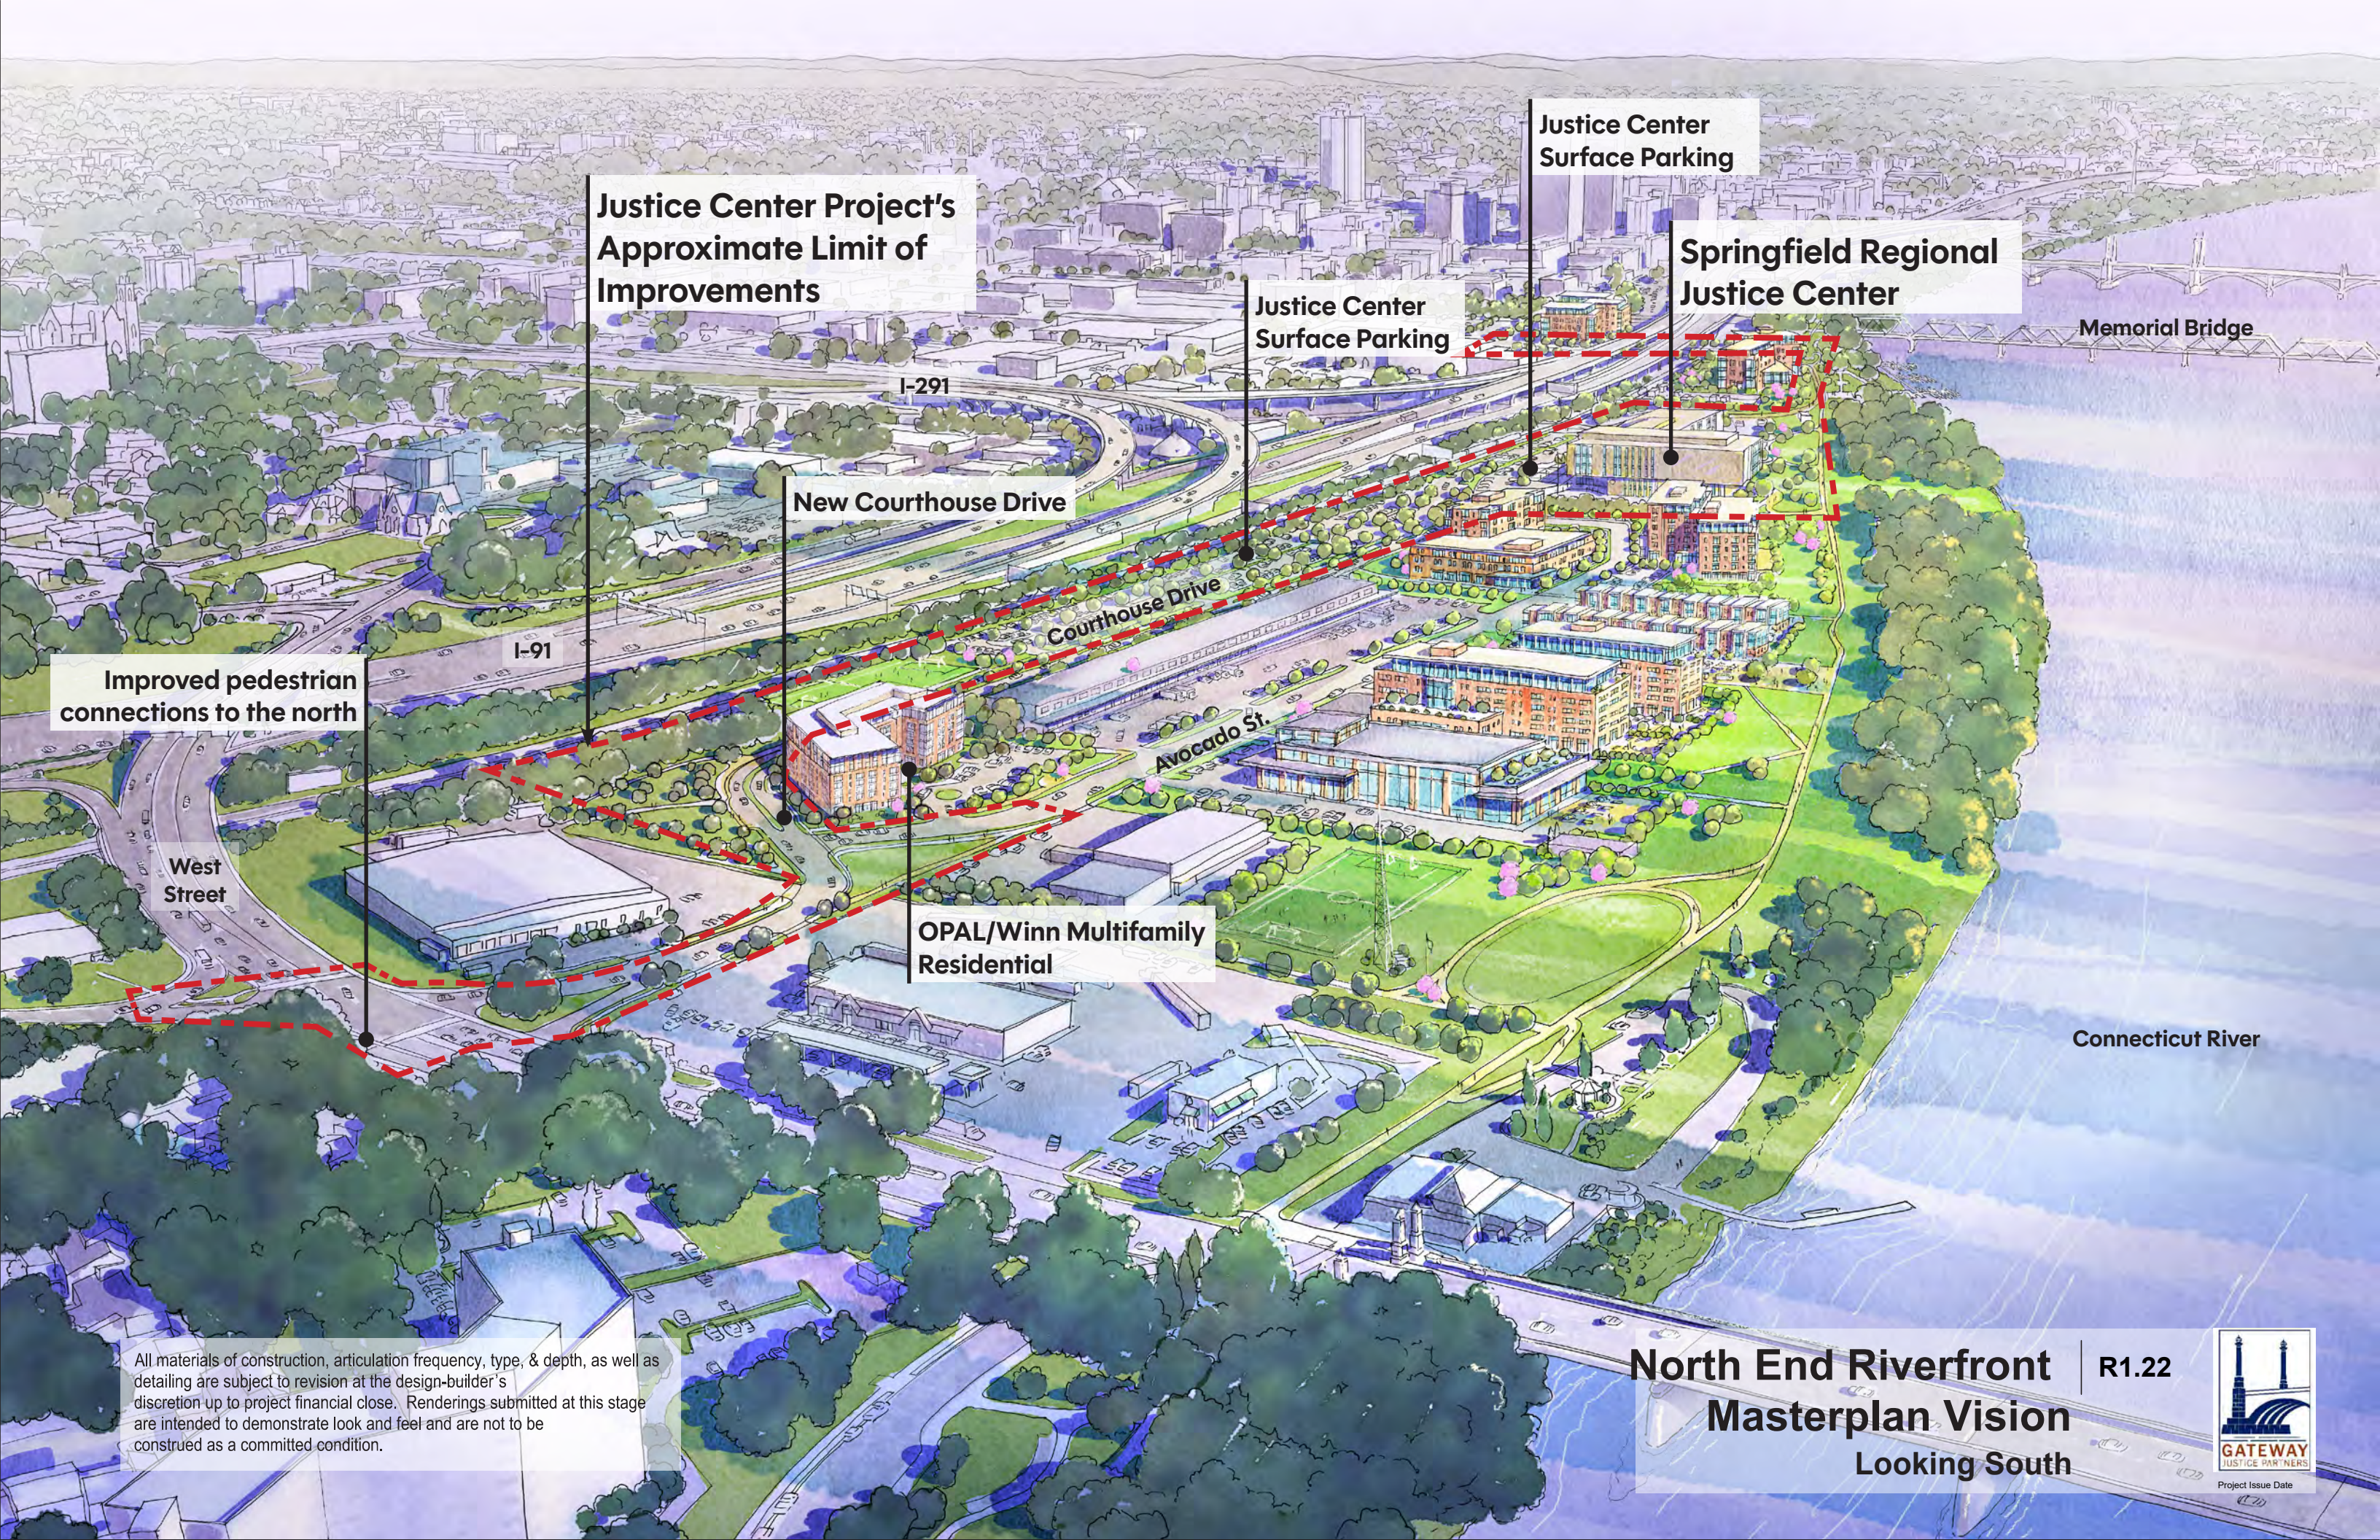

**Justice Center Project's
Approximate Limit of
Improvements**

**Justice Center
Surface Parking**

**Springfield Regional
Justice Center**

Memorial Bridge

**Justice Center
Surface Parking**

I-291

New Courthouse Drive

Courthouse Drive

I-91

**Improved pedestrian
connections to the north**

Avocado St.

**West
Street**

**OPAL/Winn Multifamily
Residential**


Connecticut River

All materials of construction, articulation frequency, type, & depth, as well as detailing are subject to revision at the design-builder's discretion up to project financial close. Renderings submitted at this stage are intended to demonstrate look and feel and are not to be construed as a committed condition.

**North End Riverfront
Masterplan Vision
Looking South**

R1.22



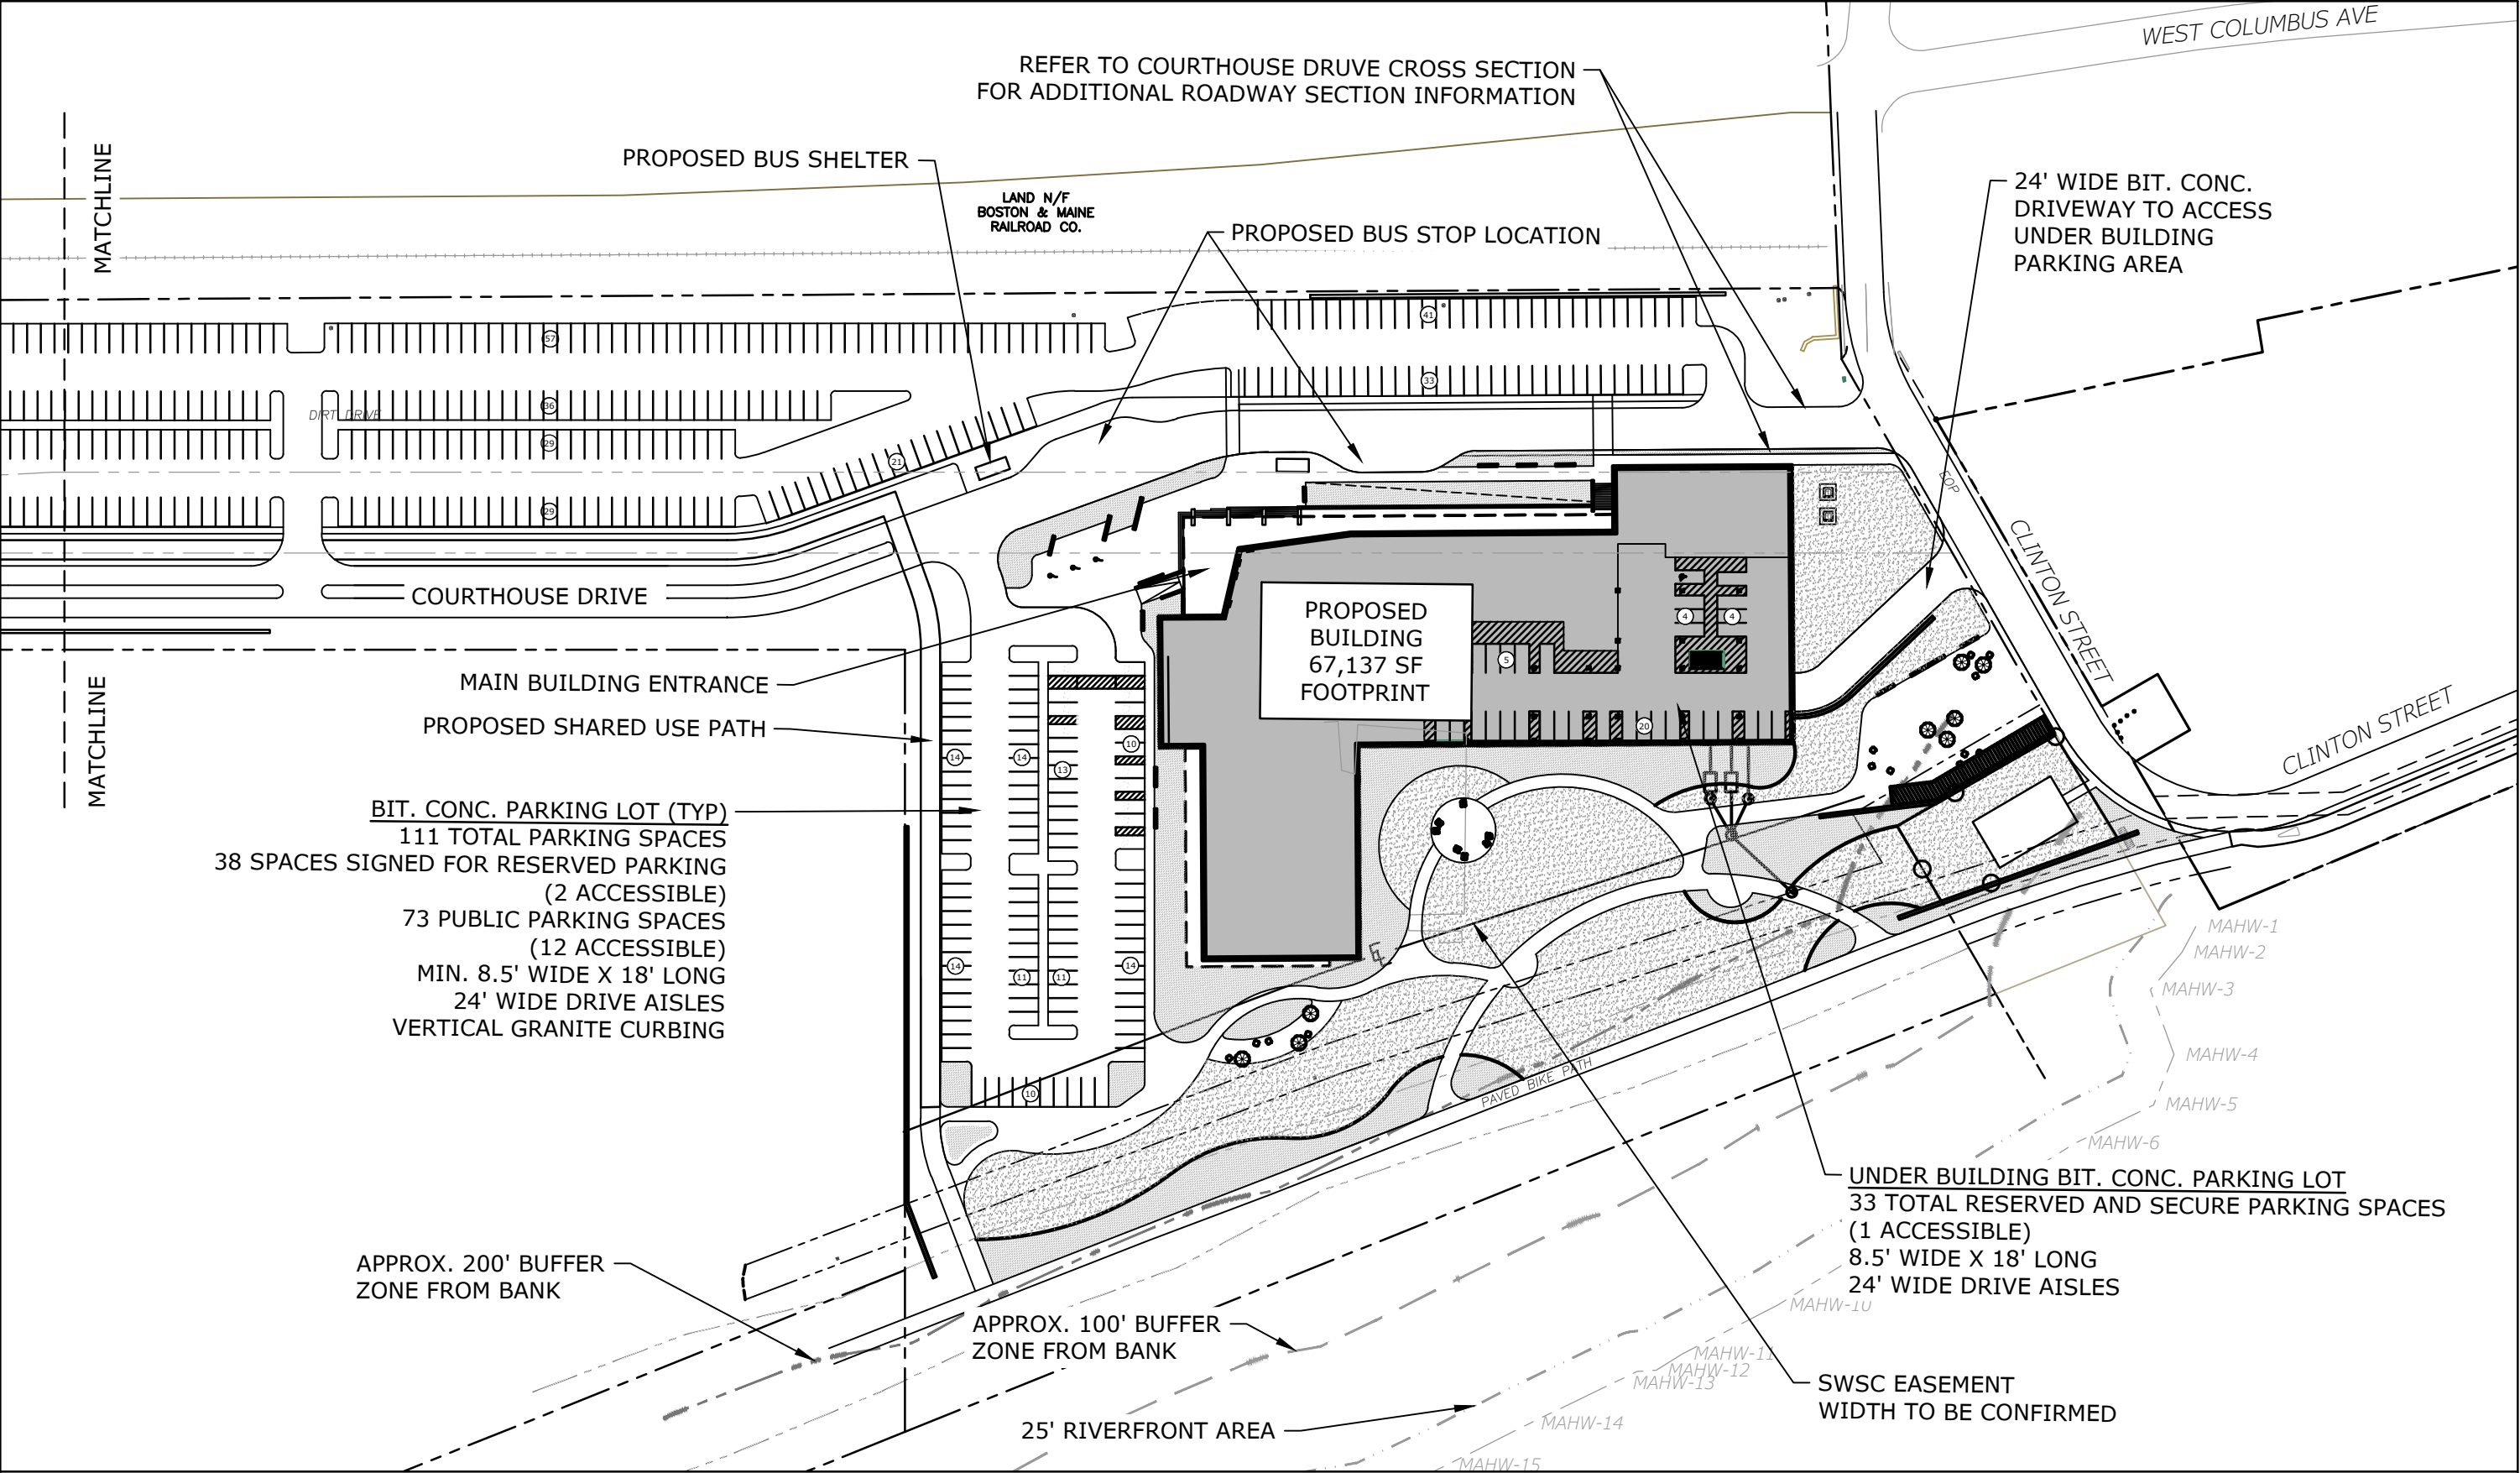

PARKING TYPE	LOCATION	STANDARD SPACES	ACCESSIBLE SPACES (VAN)	TOTAL SPACES	NOTES
PUBLIC PARKING	SURFACE LOTS (WITHIN 1/4 MILE RADIUS)	639	12 (3)	651	GENERAL PUBLIC, STAFF, JURORS
RESERVED, SECURED	BENEATH BUILDING	32	1 (1)	33	JUDGES AND DEPARTMENT HEADS, SECURE CIRCULATION
RESERVED	SURFACE LOT NORTH OF BUILDING	36	2 (1)	38	STAFF/OTHER RESERVED USES
TOTAL ON-SITE PARKING		707	15 (5)	722	

Proposed Site Plan

CP-101

BIT. CONC. PARKING LOT (TYP)
578 TOTAL PARKING SPACES
MIN. 8.5' WIDE X 18' LONG
24' WIDE DRIVE AISLES
VERTICAL GRANITE CURBING

MATCHLINE

PEDESTRIAN WALKWAY

SHARED-USE PATH

FUTURE DEVELOPMENT

BUS STOPS

FUTURE DEVELOPMENT

REFER TO COURTHOUSE DRIVE
CROSS SECTION FOR
ADDITIONAL LAYOUT AND
MATERIAL INFORMATION

COURTHOUSE DRIVE


MATCHLINE

AVOCADO STREET


PARKING TYPE	LOCATION	STANDARD SPACES	ACCESSIBLE SPACES (VAN)	TOTAL SPACES	NOTES
PUBLIC PARKING	SURFACE LOTS (WITHIN 1/4 MILE RADIUS)	639	12 (3)	651	GENERAL PUBLIC, STAFF, JURORS
RESERVED, SECURED	BENEATH BUILDING	32	1 (1)	33	JUDGES AND DEPARTMENT HEADS, SECURE CIRCULATION
RESERVED	SURFACE LOT NORTH OF BUILDING	36	2 (1)	38	STAFF/OTHER RESERVED USES
TOTAL ON-SITE PARKING		707	15 (5)	722	

Proposed Site Plan


CP-102






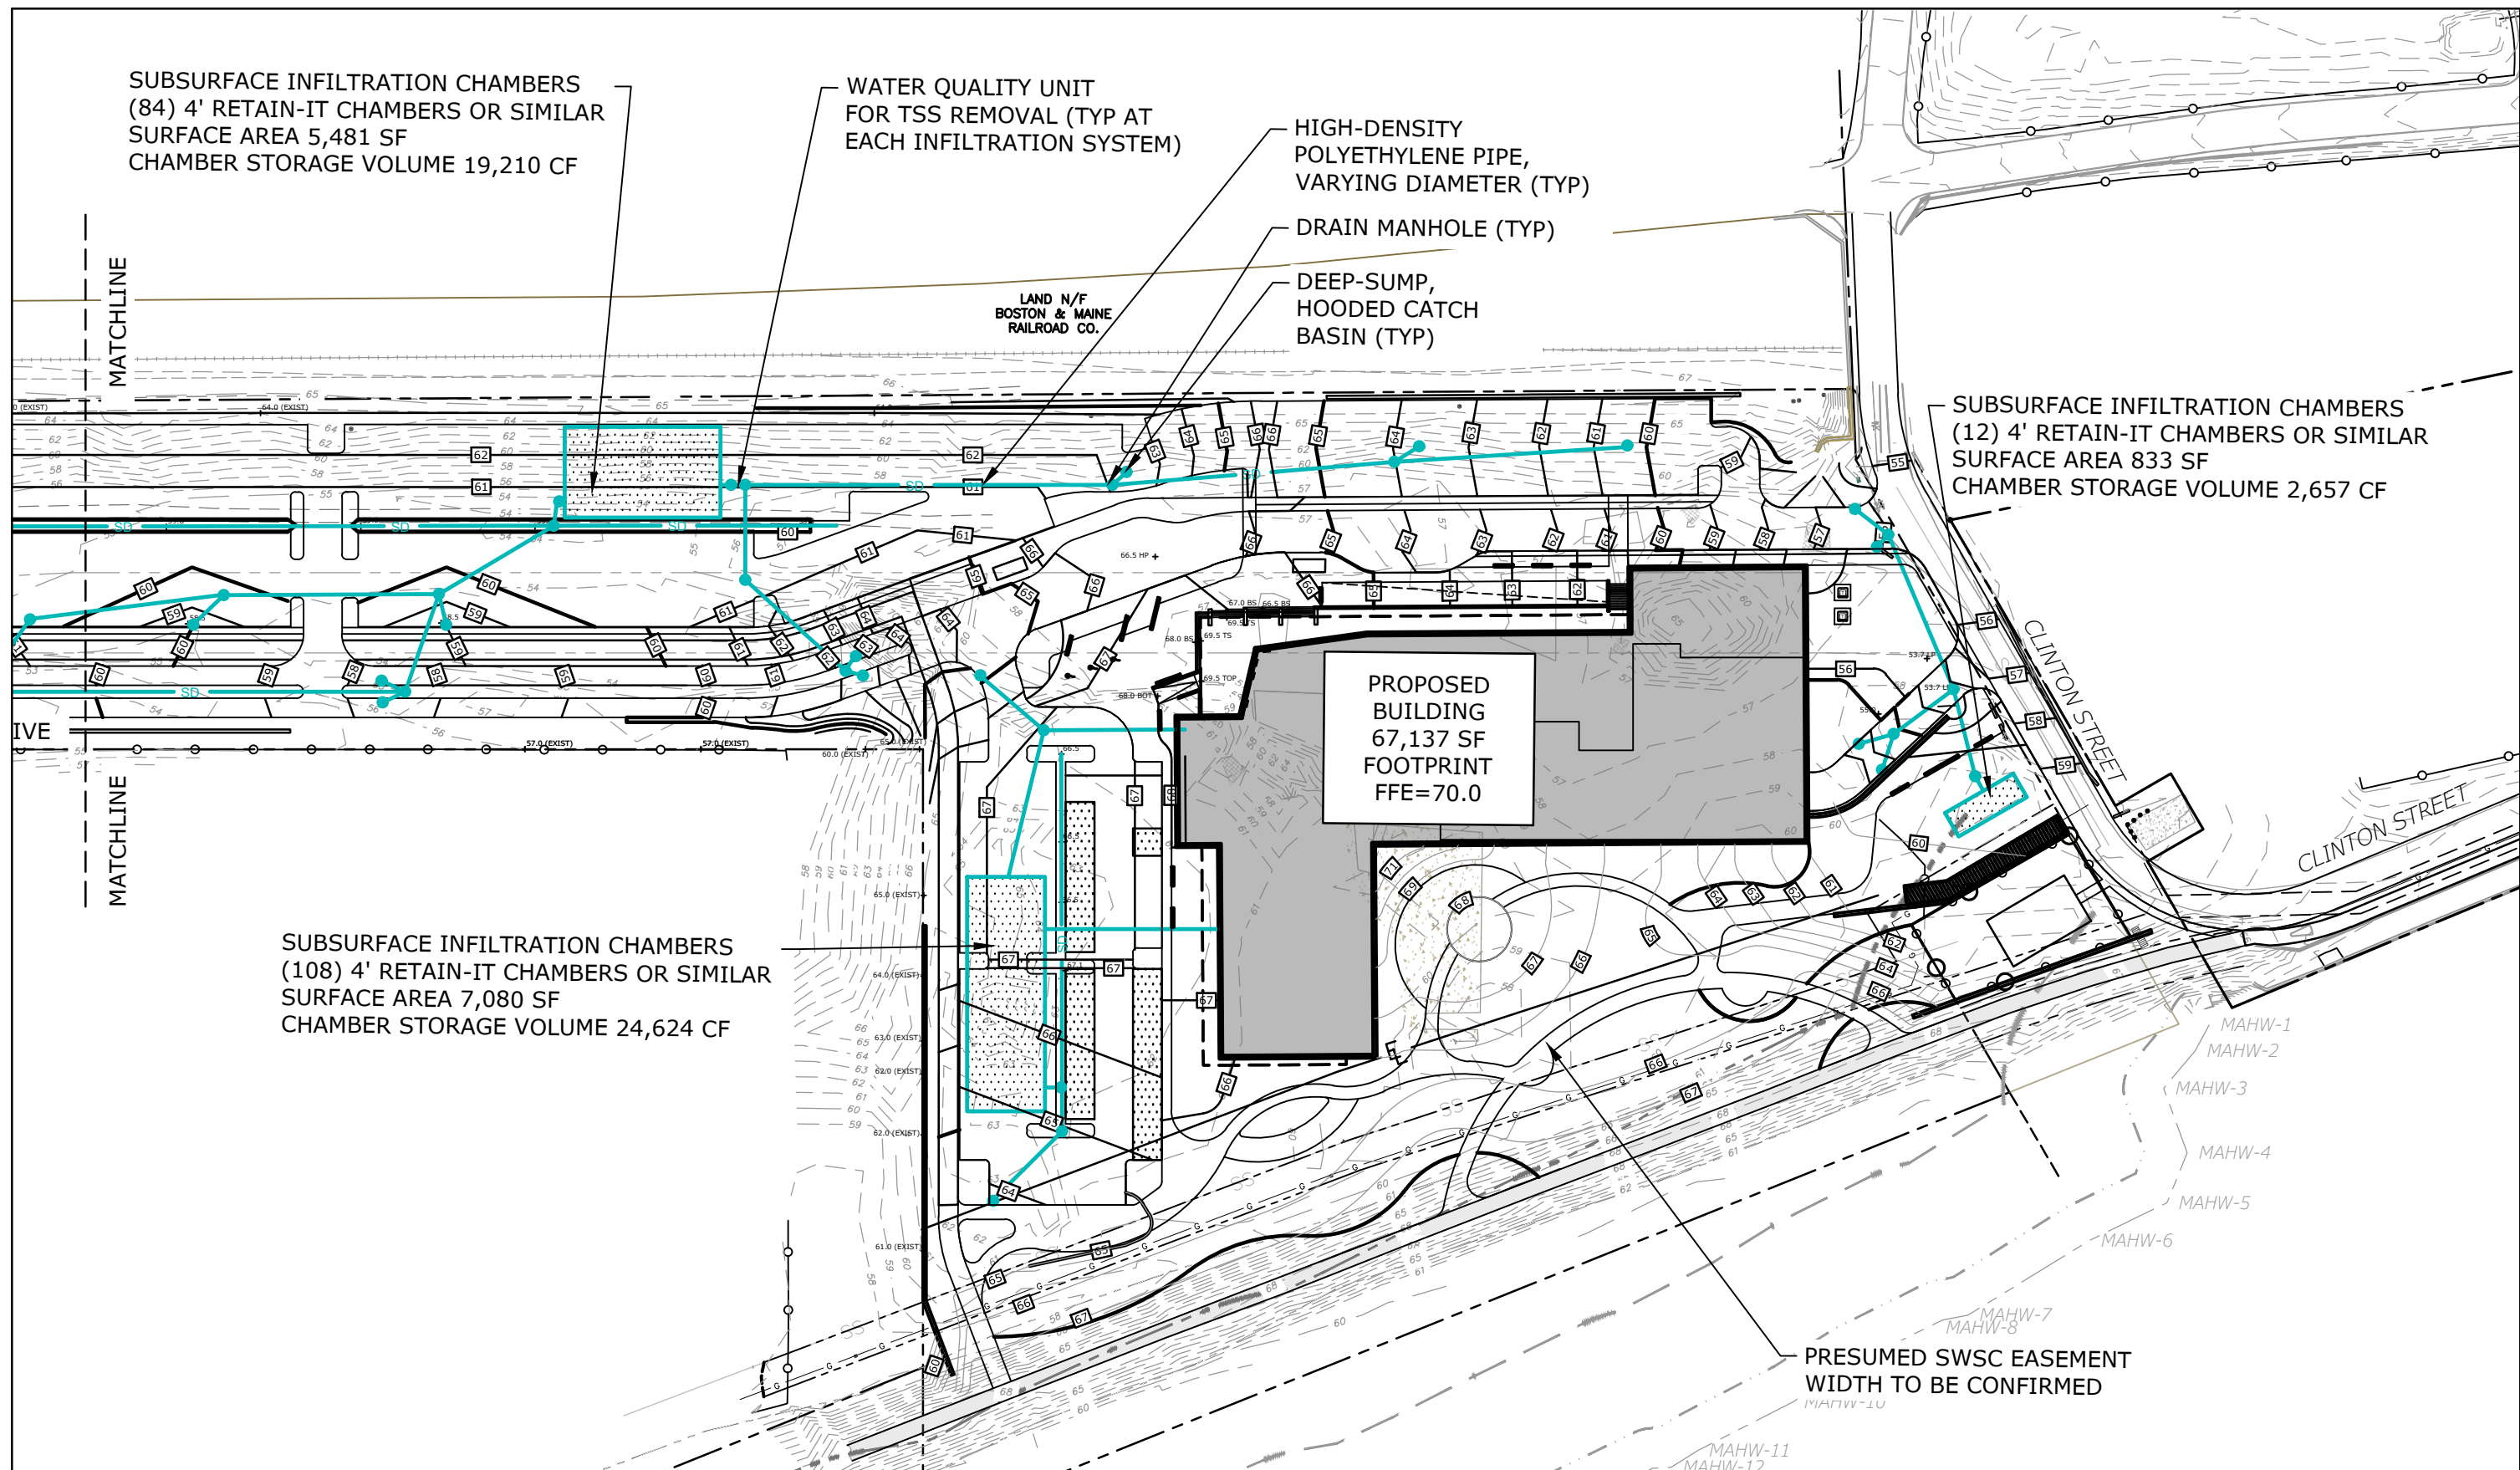



Grading & Drainage Plan | CP-201



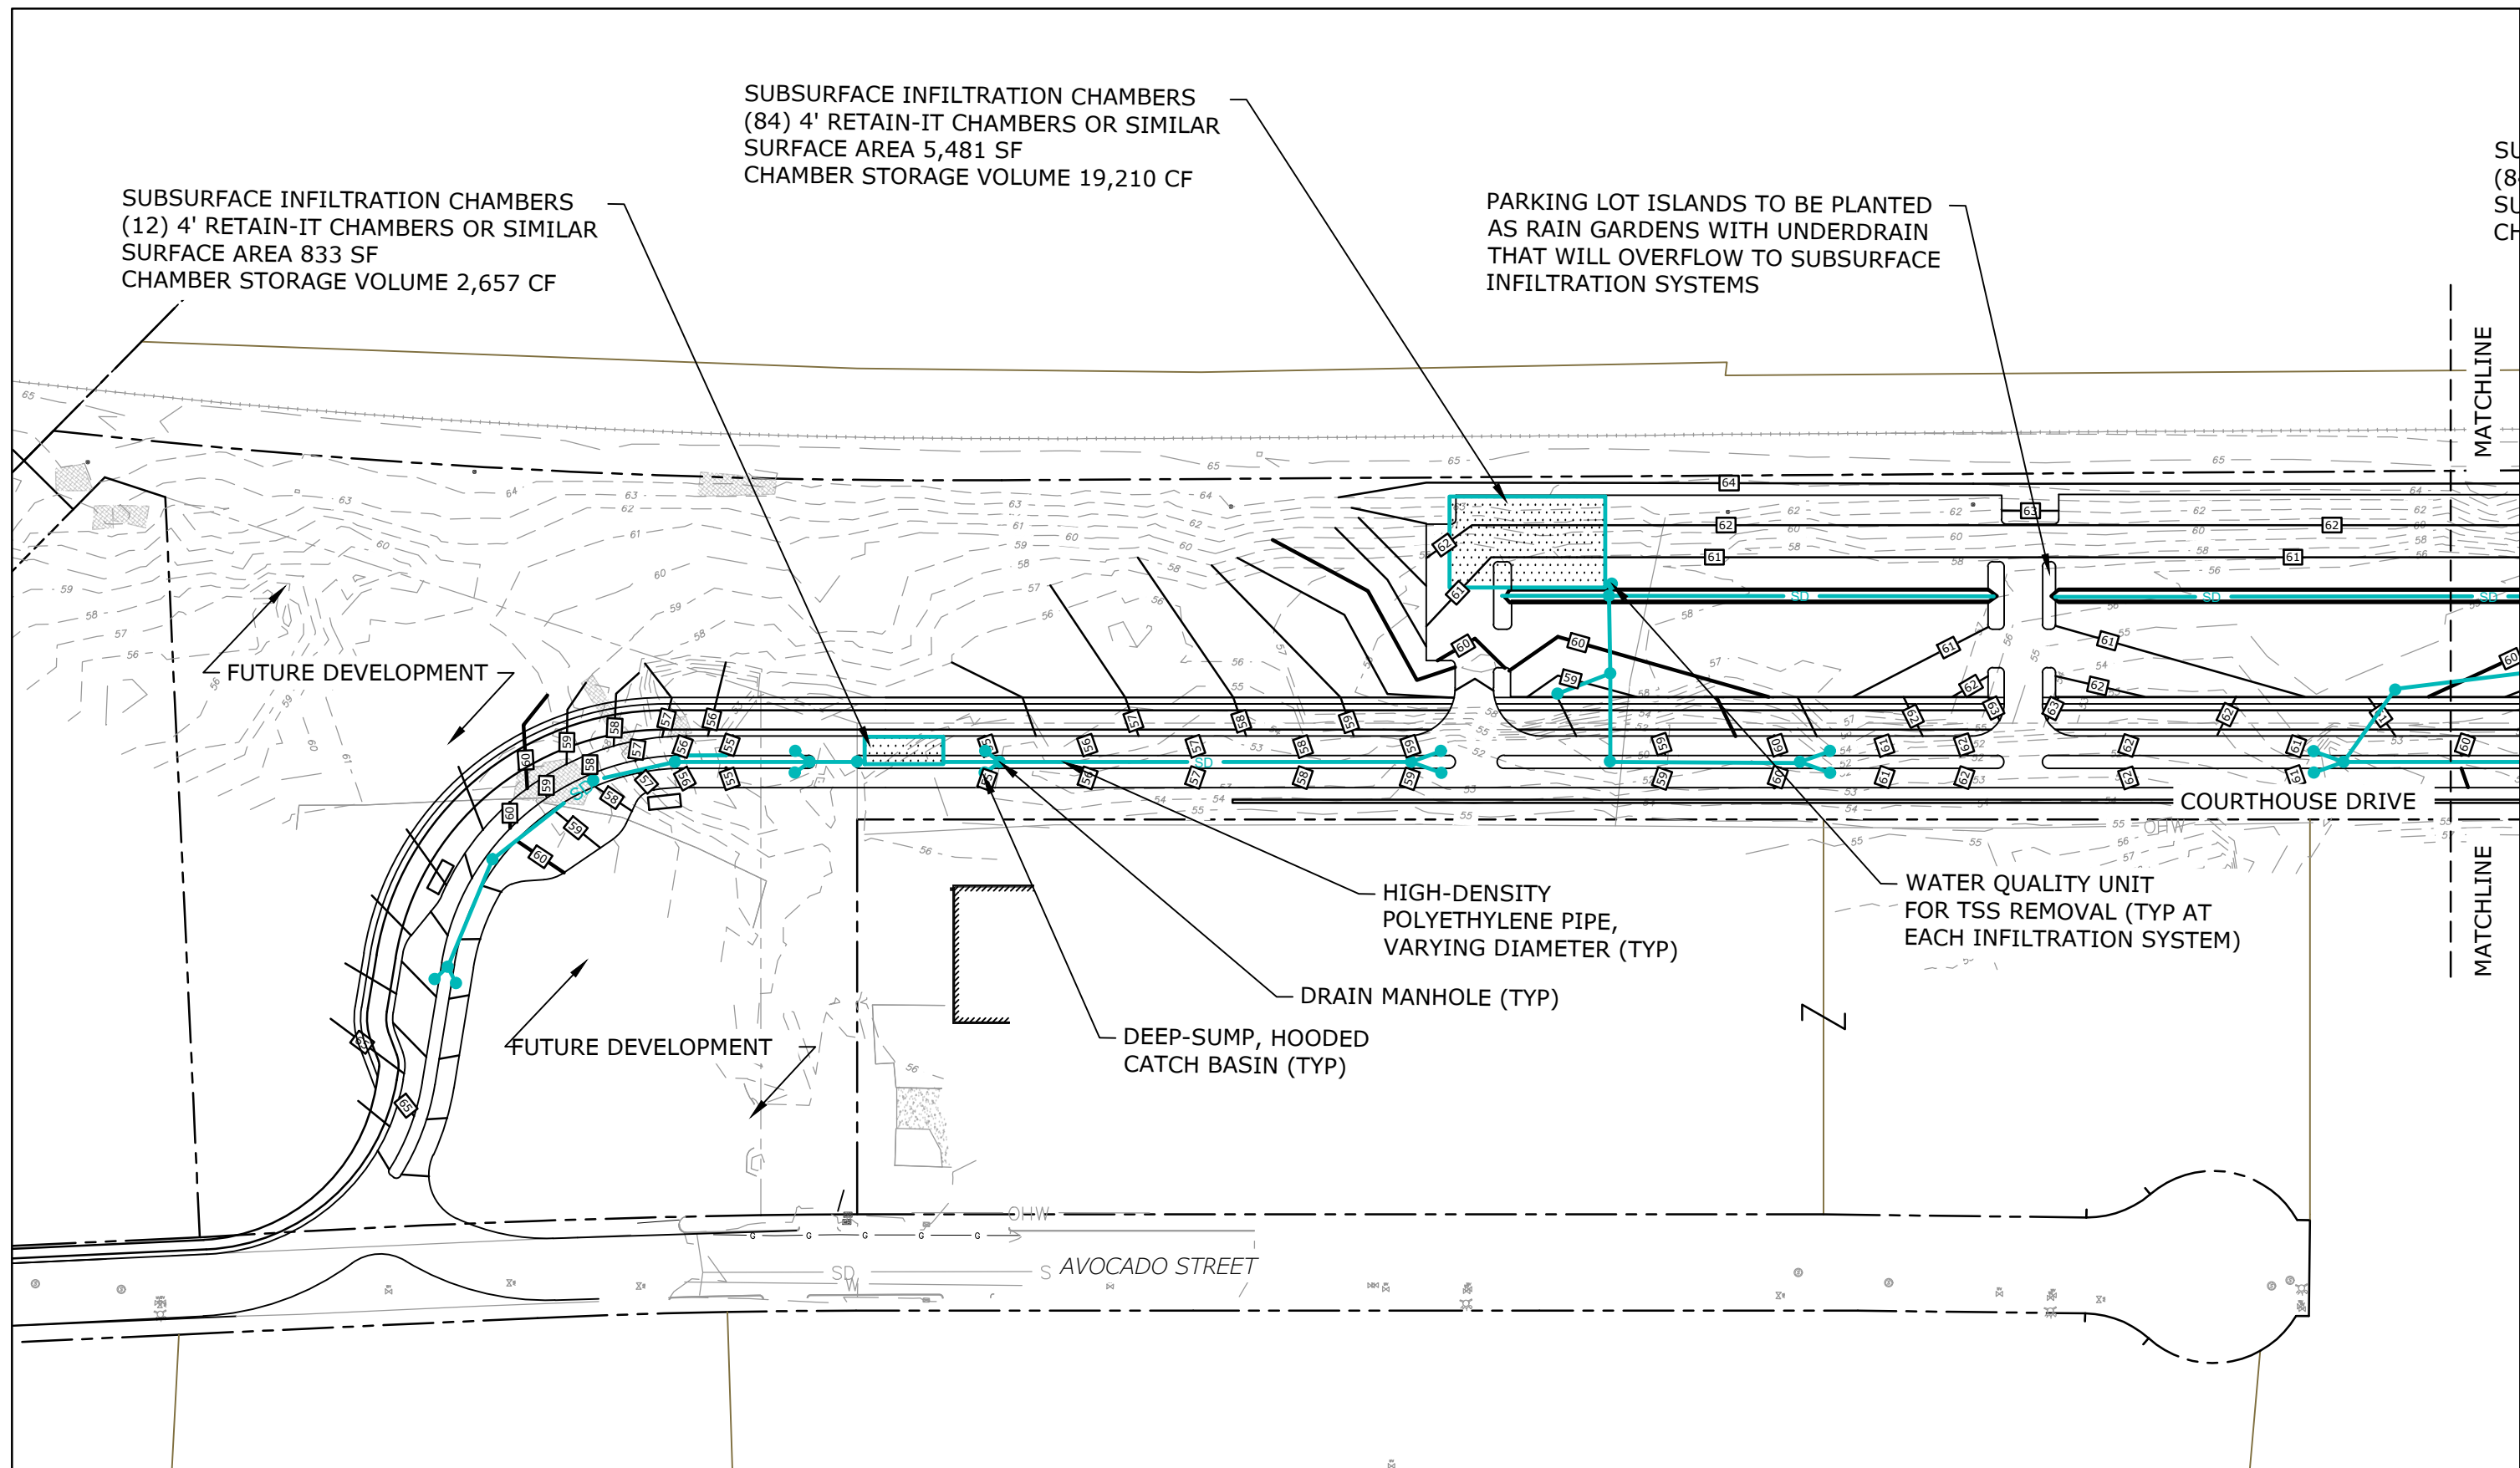


Grading & Drainage Plan | CP-202




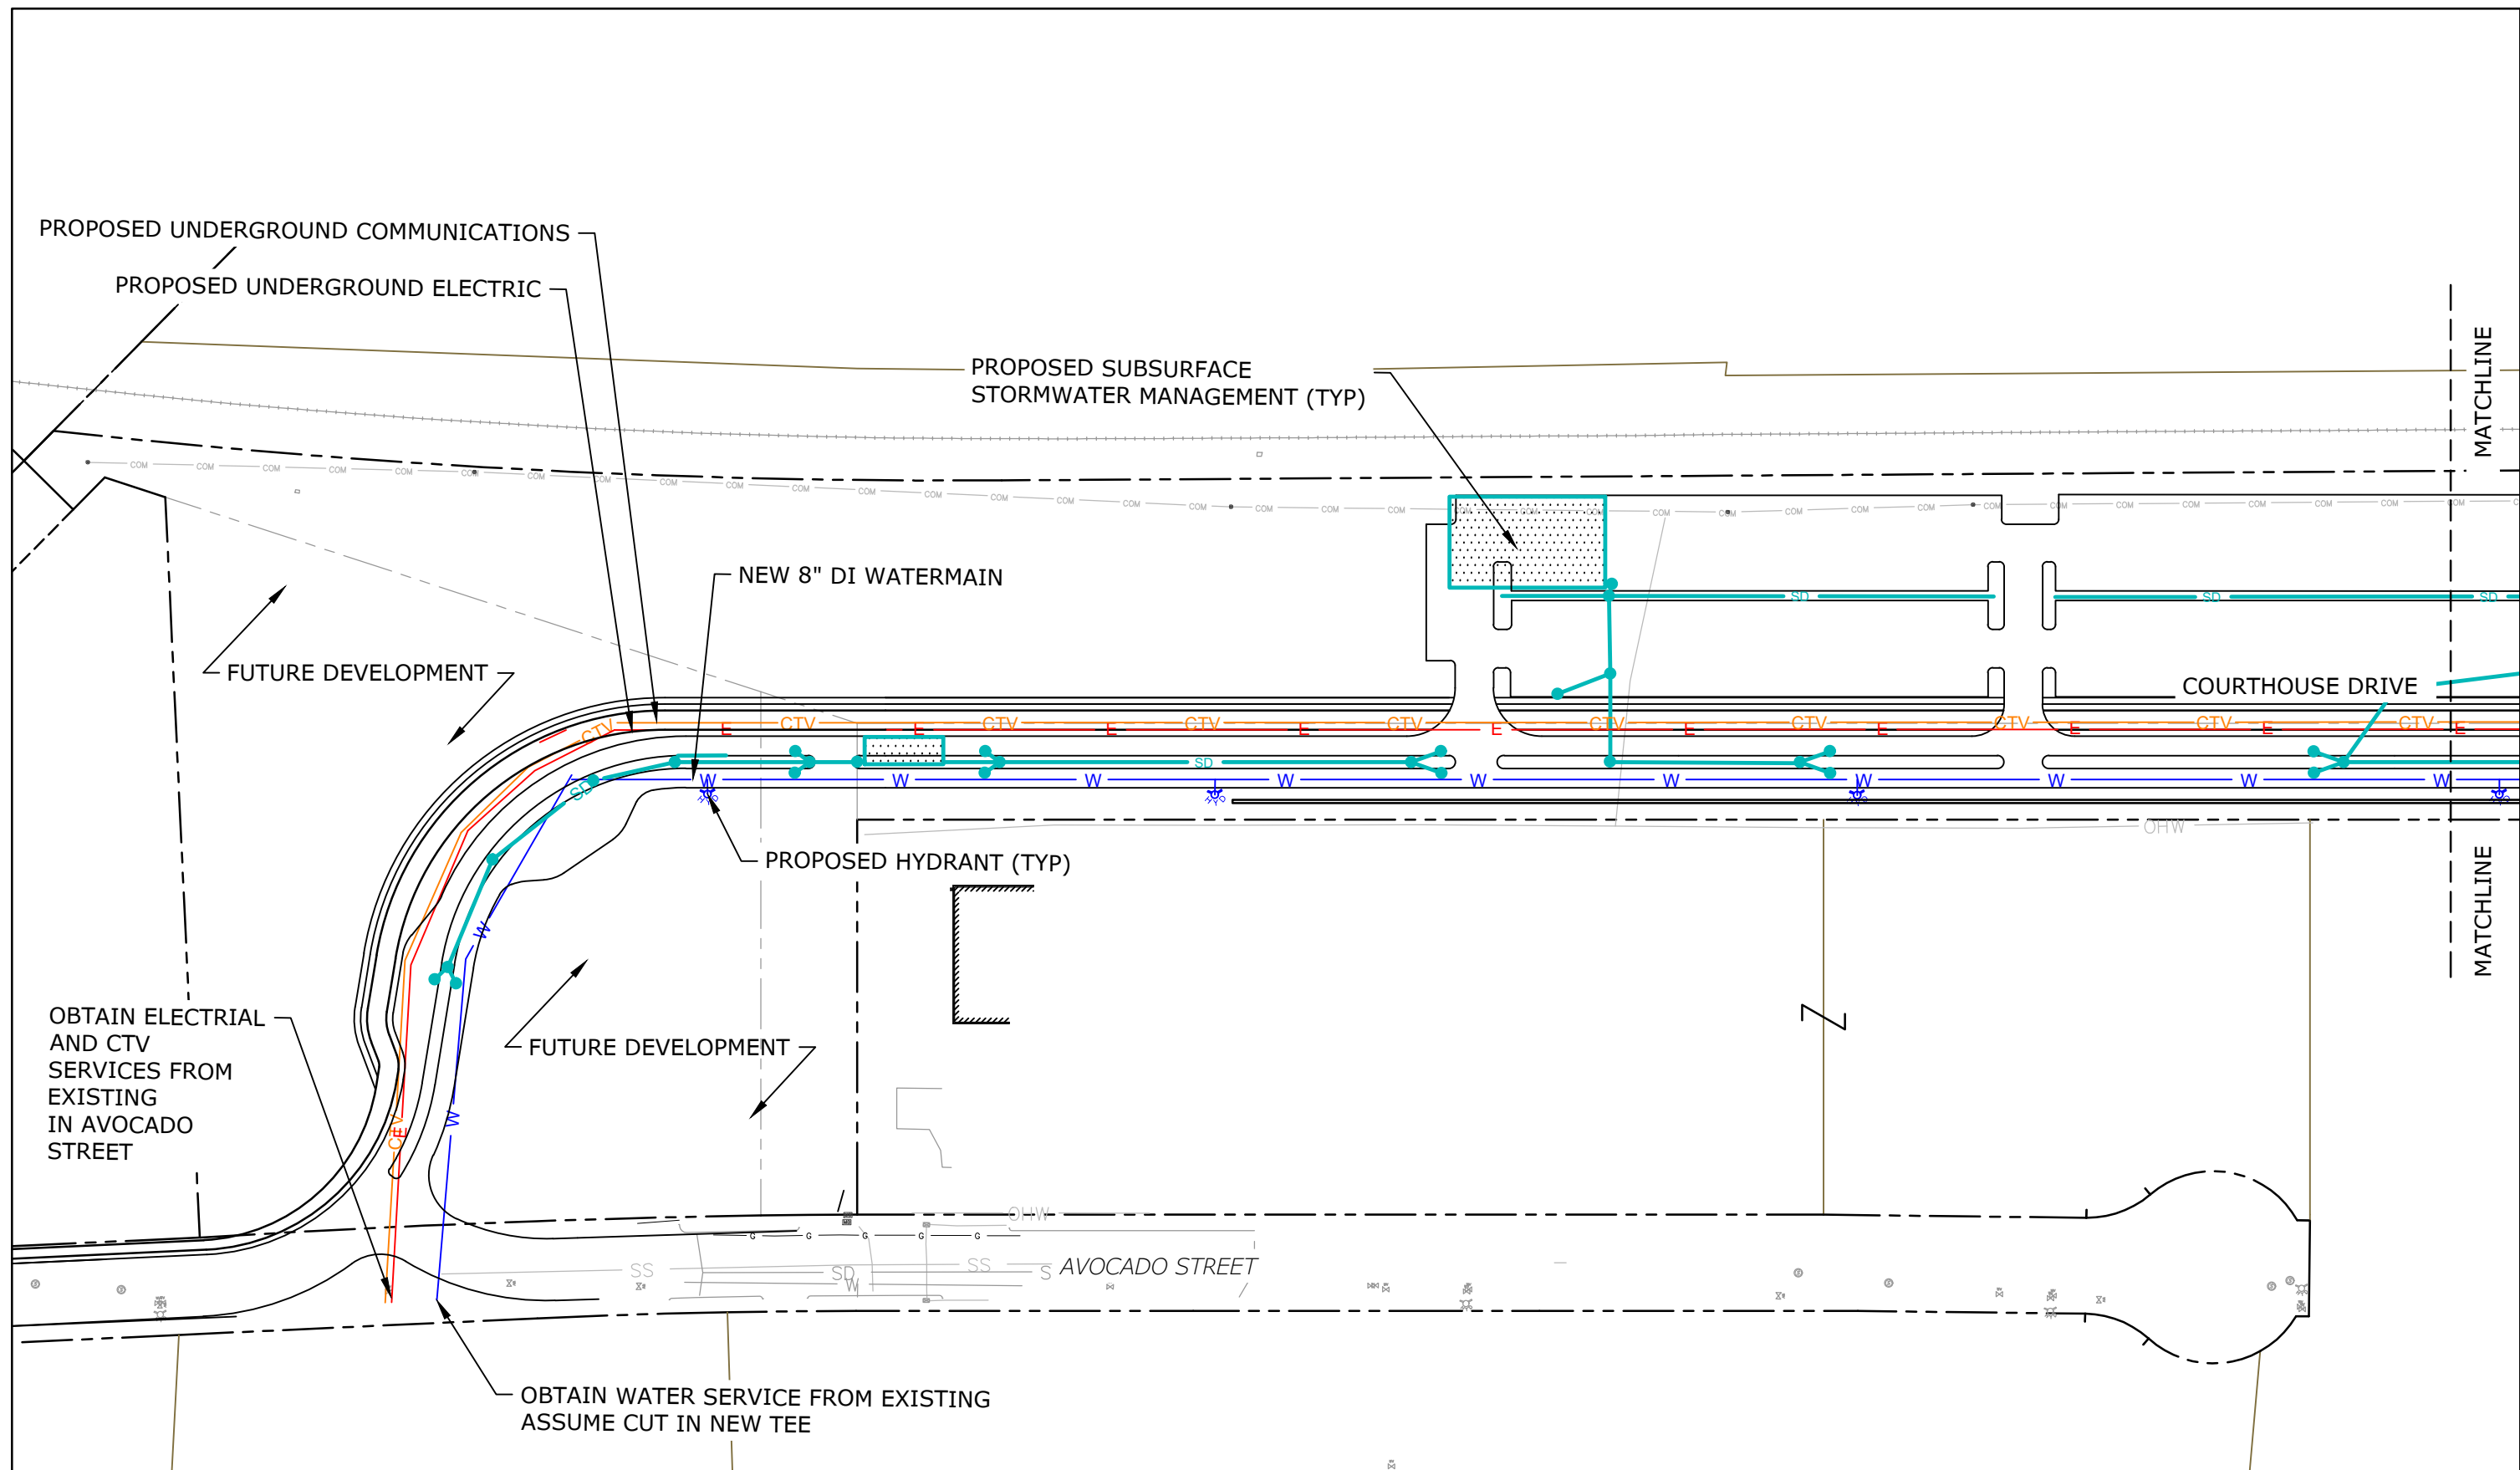


Utility Plan | CP-302



TOTAL GLAZING AREA: 32%

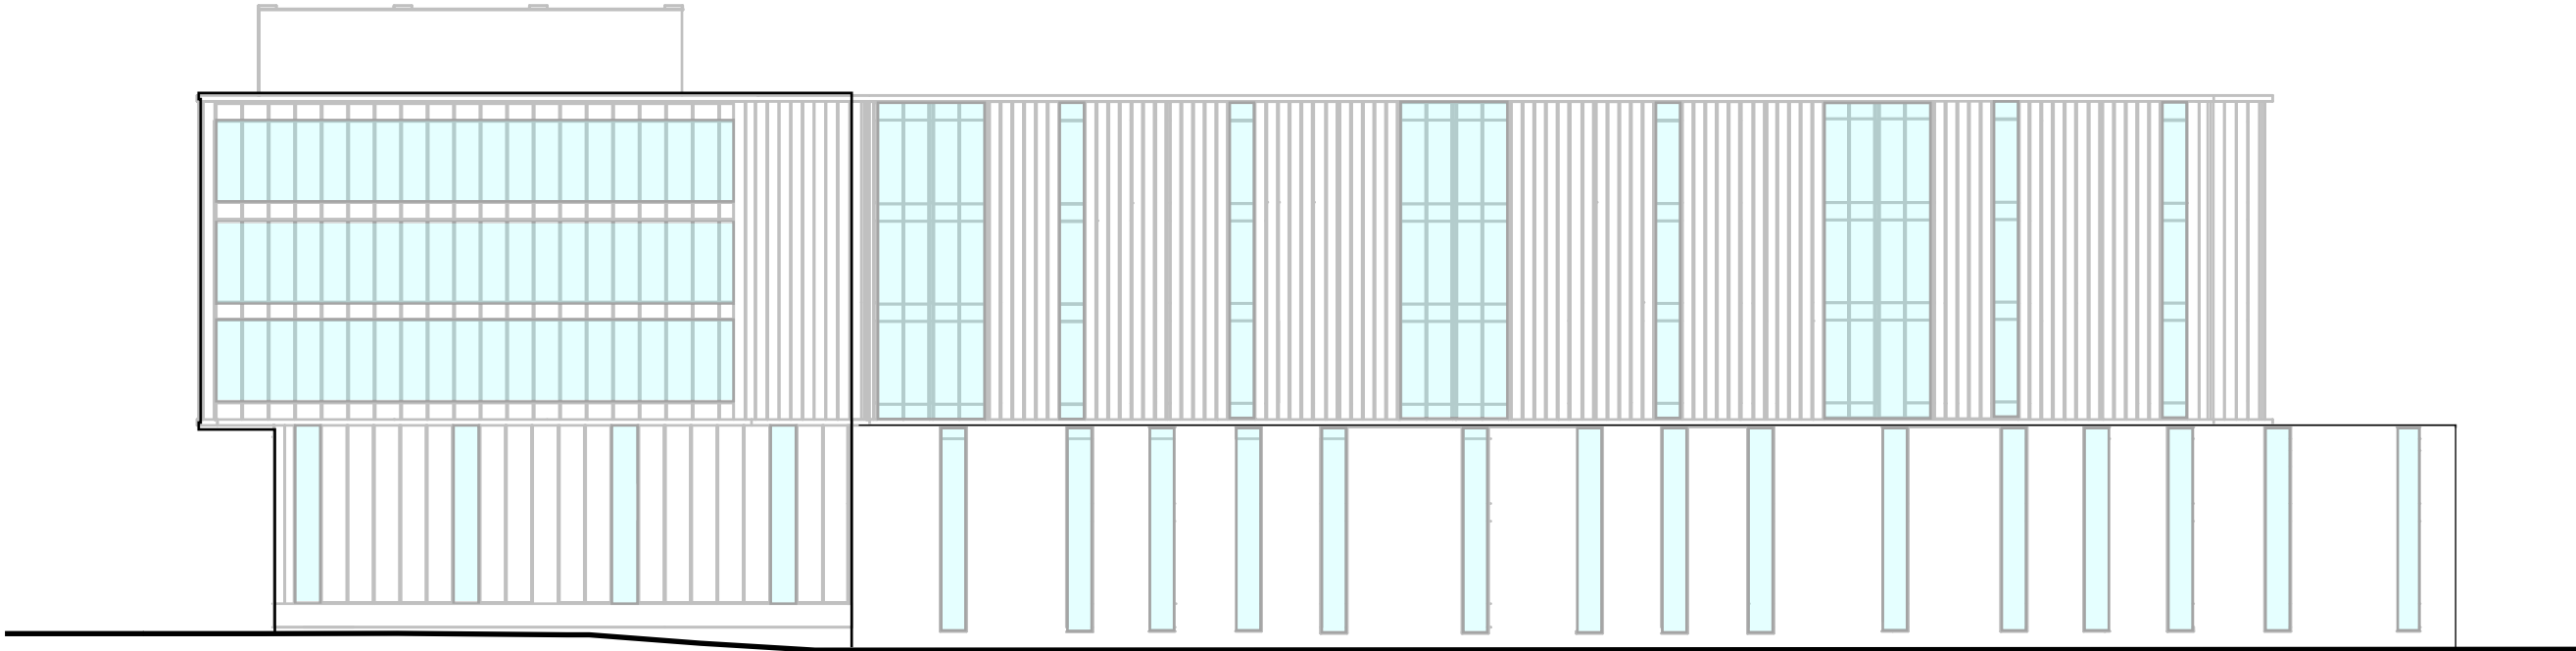

SOUTH WEST ELEVATION
GLAZING AREA: 34.5%

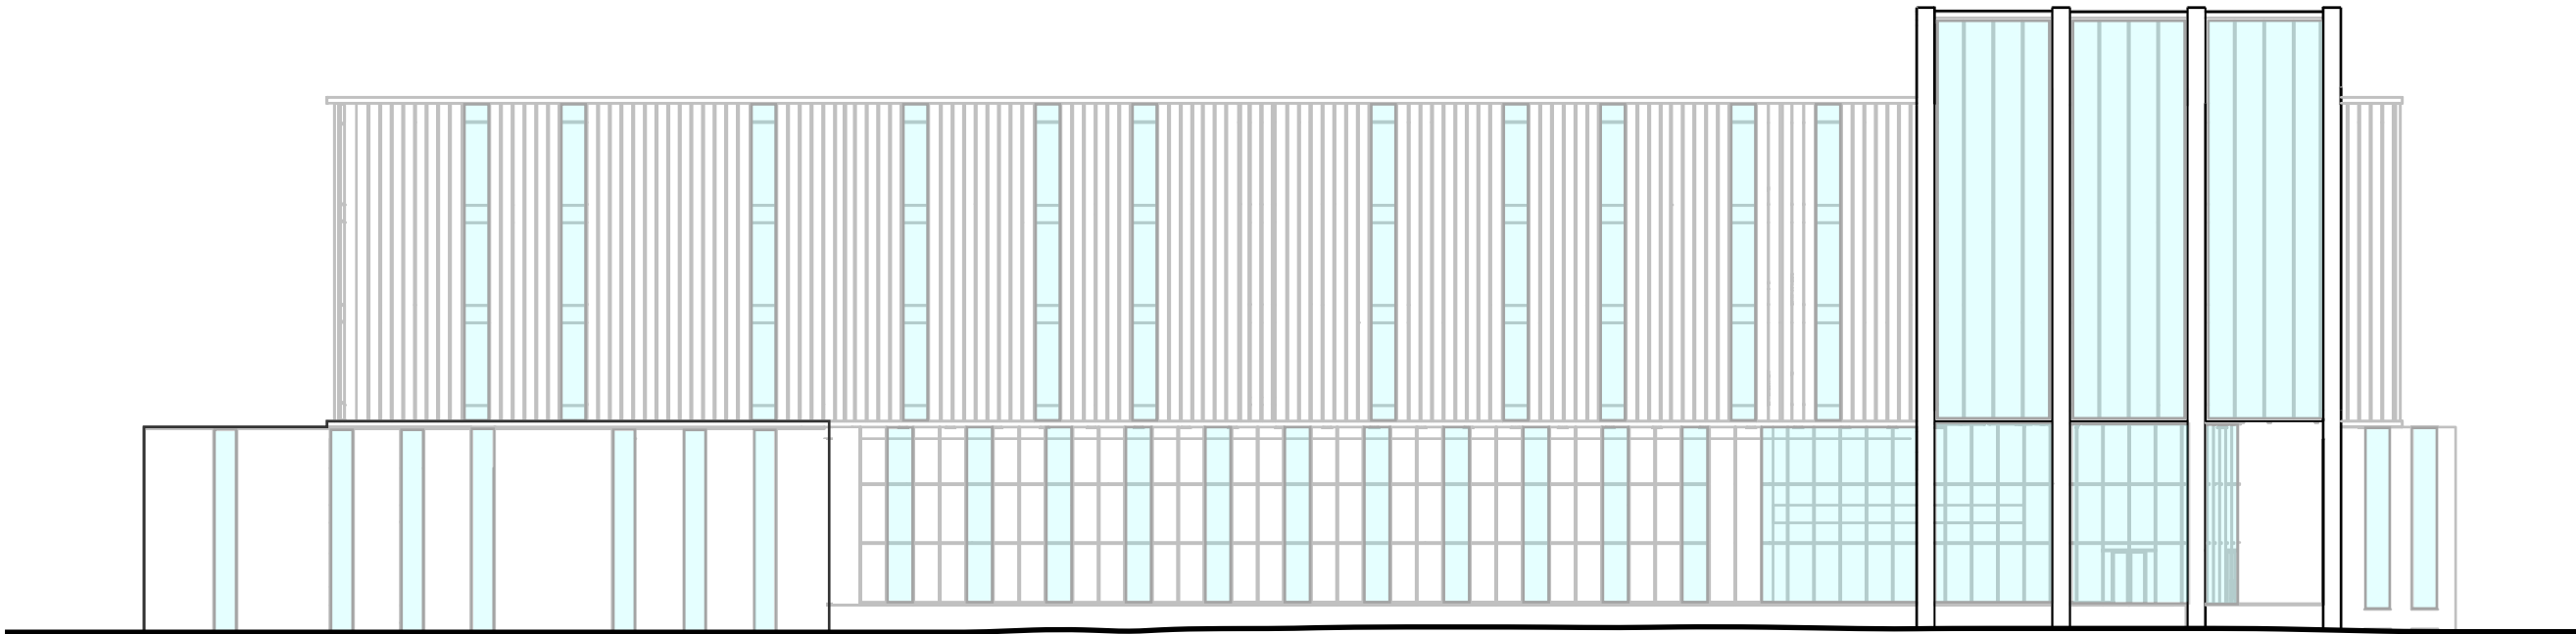


NORTH EAST ELEVATION
GLAZING AREA: 30.4%


BUILDING ELEVATIONS | AP2.08



TOTAL GLAZING AREA: 32%

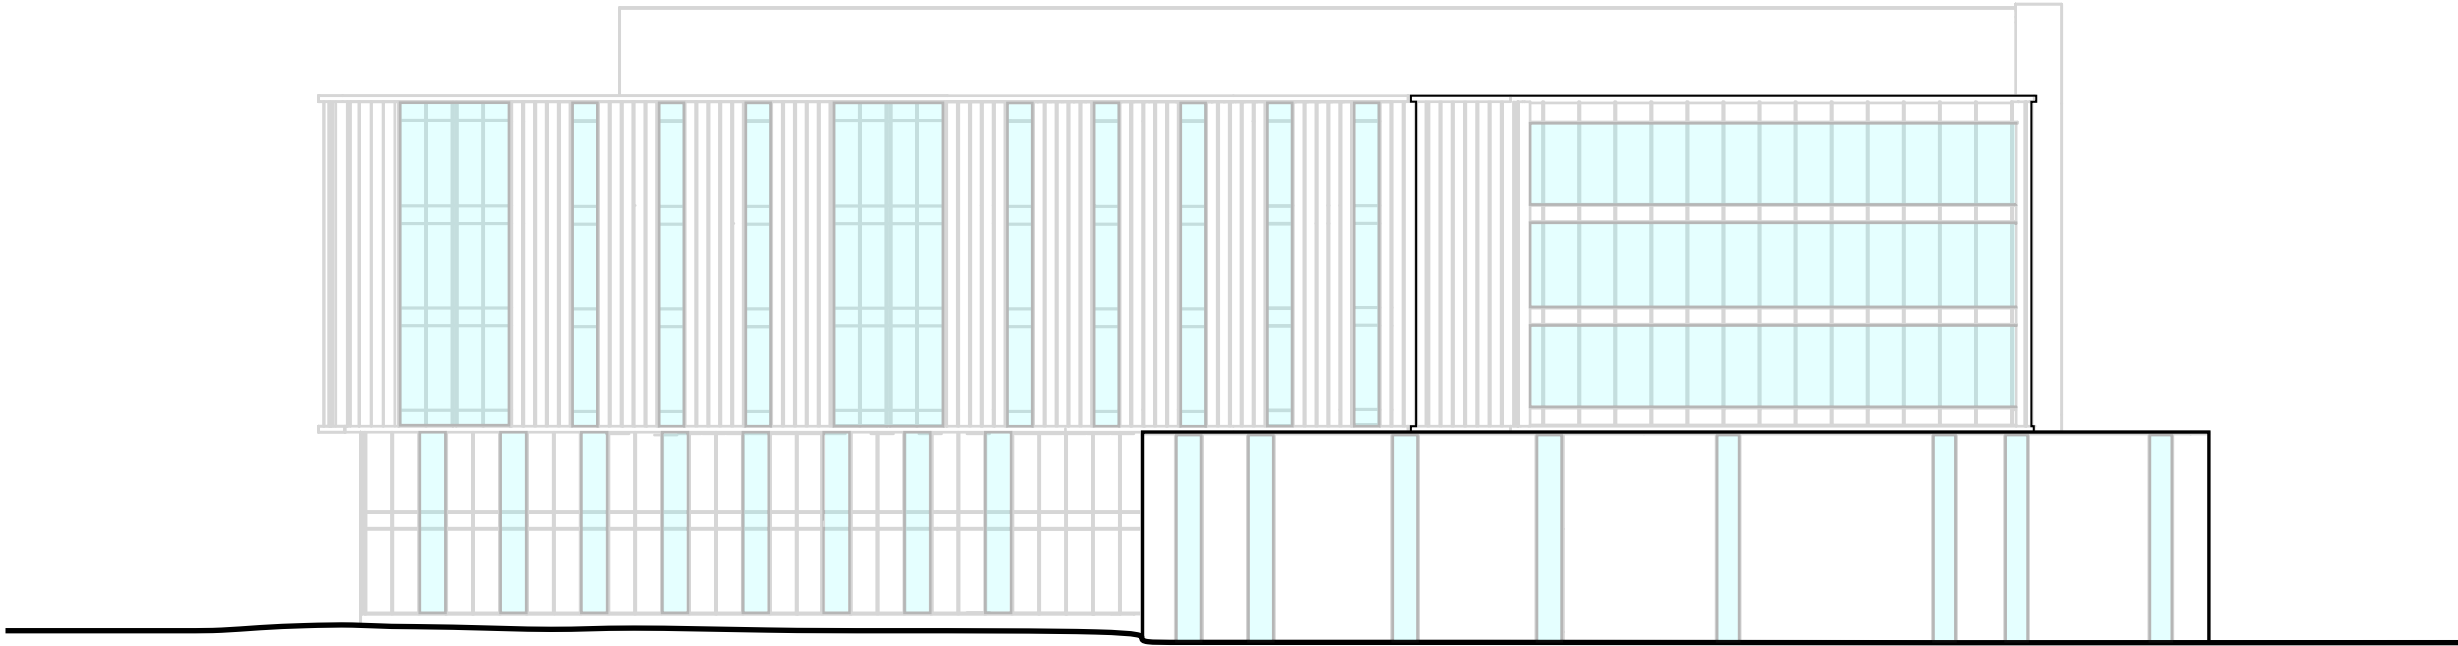

SOUTH EAST ELEVATION
GLAZING AREA: 36%

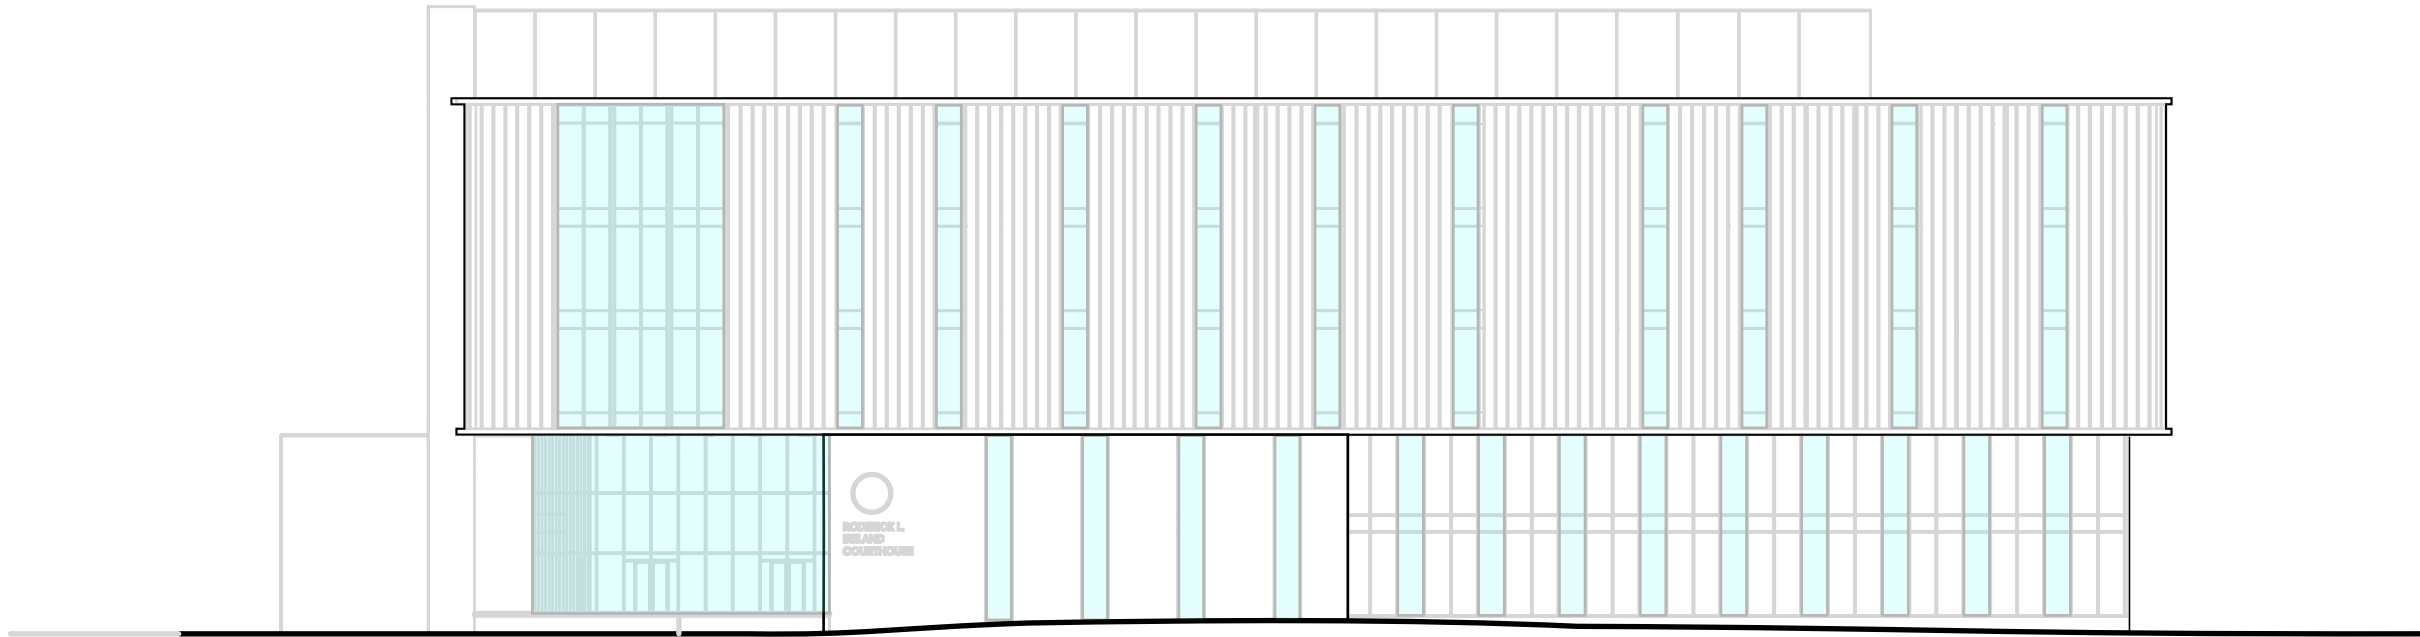

NORTH WEST ELEVATION
GLAZING AREA: 28.4%

BUILDING ELEVATIONS | AP2.09



Activity ID		Activity Name		Remaining Duration	Start	Finish	2025												2026												2027												2028												2029												2030												2031												2032																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
SPRINGFIELD REGIONAL JUSTICE CENTER							J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J												J											

Activity ID		Activity Name	Remaining Duration	Start	Finish	2025	2026	2027	2028	2029	2030	2031	2032
						JJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON
PRE-CONSTRUCTION			790	30-Jun-25	07-Jul-28								
PROGRAMMING AND PREDESIGN			165	30-Jun-25	13-Feb-26								
CM SELECTION			165	30-Jun-25	13-Feb-26								
PRE-1190	CM	Procurement - RFP Process	79	30-Jun-25	16-Oct-25								
PRE-1140	CM	Procurement - Issue RFP	0	30-Jun-25*									
PRE-1480	CM	Procurement - Proposals Due	0		16-Oct-25								
PRE-1500	DCAMM	Decision-Making Process	76	17-Oct-25	30-Jan-26								
PRE-1490	DCAMM	Notification to Winn/Fengate Team to Enter Contract Negotiation	10	02-Feb-26*	13-Feb-26								
SCHEMATIC DESIGN			280	14-Jul-25	07-Aug-26								
PRECONCEPT / CONCEPT			65	14-Jul-25	10-Oct-25								
PRE-1840	Preconcept	- Preconcept Design	20	14-Jul-25	08-Aug-25								
PRE-1850	Concept	- Concept Design / Massing	20	11-Aug-25	05-Sep-25								
PRE-1860	Concept	- Cost Estimate / Cost Model	25	08-Sep-25	10-Oct-25								
CONTINUED FINANCIAL DEVELOPMENT			125	16-Feb-26	07-Aug-26								
STIPULATED SUM			125	16-Feb-26	07-Aug-26								
PRE-1890	Stipulated Sum	- Prep and Submit Fixed Price + Negotiate Contract Terms	80	16-Feb-26	05-Jun-26								
PRE-1900	Stipulated Sum	- Approval and Financial Close	15	20-Jul-26	07-Aug-26								
PRE-2700	Stipulated Sum	- Lease Approval to Proceed with Drawings, Permitting et al.	15	20-Jul-26	07-Aug-26								
SCHEMATIC DESIGN DEVELOPMENT			108	16-Feb-26	17-Jul-26								
PRE-1141	SD	- Schematic Drawing Design Period	74	16-Feb-26	29-May-26								
PRE-1142	SD	- Fixed Price Update Estimate	34	01-Jun-26	17-Jul-26								
CONSTRUCTION DOCUMENTS			199	10-Aug-26	13-May-27								
DETAILED DESIGN			85	10-Aug-26	10-Dec-26								
PRE-1160	DD	- Design Period	85	10-Aug-26	10-Dec-26								
50% CONSTRUCTION DOCUMENTS PHASE			50	11-Dec-26	18-Feb-27								
PRE-1260	50% CD	- Design Period	50	11-Dec-26	18-Feb-27								
90% CONSTRUCTION DOCUMENTS PHASE			30	19-Feb-27	01-Apr-27								
PRE-1880	90% CD	- Design Period	30	19-Feb-27	01-Apr-27								
100% CONSTRUCTION DOCUMENTS PHASE			30	02-Apr-27	13-May-27								
PRE-1550	100% CD	- Design Period	30	02-Apr-27	13-May-27								
PERMITTING			625	16-Feb-26	07-Jul-28								
CONSTRUCTION PERMIT			30	19-Feb-27	01-Apr-27								
PRE-2690	Permit	- Final Construction Permit through GBCO (Remainder of Building)	30	19-Feb-27	01-Apr-27								
PRE-PERMITTING CONSULTATION			33	16-Feb-26	01-Apr-26								
PRE-1990	Permit	- Inter-Agency State and Federal Pre-Permitting Consultation	33	16-Feb-26	01-Apr-26								
PRE-2000	Permit	- City of Springfield Consultation	22	16-Feb-26	17-Mar-26								
ENHANCED COMMUNITY OUTREACH			500	10-Aug-26	07-Jul-28								
PRE-1910	Permit	- Enhanced Community Outreach	500	10-Aug-26	07-Jul-28								
MASSACHUSETTS ENVIRONMENTAL POLICY ACT (MEPA) REVIEW			318	16-Feb-26	05-May-27								
PRE-1920	Permit	- MEPA/ EEA Environmental Justice Pre-Filing Consultation	22	16-Feb-26	17-Mar-26								
PRE-2010	Permit	- Request EJ Reference List/ Update/ Re-Submit to MEPA	6	16-Feb-26	23-Feb-26								
PRE-2020	Permit	- Develop EJ Screening Form (English and Spanish)	22	24-Feb-26	25-Mar-26								
PRE-2040	Permit	- Prepare Expanded Environmental Notification Form (EENF)	75	18-Mar-26	30-Jun-26								
PRE-2030	Permit	- Circulate EJ Screening Form to Community Based Organizations	5	26-Mar-26	01-Apr-26								

Finish Date: 30-Nov-29
Data Date: 01-Jan-25
Run Date: 15-Oct-25 15:21
Page 2 of 11
MA-RFP-SR-JC



SPRINGFIELD REGIONAL JUSTICE CENTER

PROPOSAL SCHEDULE



Activity ID	Activity Name	Remaining Duration	Start	Finish	2025	2026	2027	2028	2029	2030	2031	2032
					JJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON
PRE-2050	Permit - Team Review of EENF	15	01-Jul-26	21-Jul-26			■ Permit - Team Review of EENF					
PRE-2060	Permit - Finalize/ Submit EENF	10	10-Aug-26	21-Aug-26			■ Permit - Finalize/ Submit EENF					
PRE-2070	Permit - MEPA Review	33	24-Aug-26	07-Oct-26			■ Permit - MEPA Review					
PRE-2080	Permit - Receive Certificate on EENF/ Scope for Single EIR	5	08-Oct-26	14-Oct-26			■ Permit - Receive Certificate on EENF/ Scope for Single EIR					
PRE-2090	Permit - Prepare Single EIR	50	15-Oct-26	23-Dec-26			■ Permit - Prepare Single EIR					
PRE-2640	Permit - Team Review EIR	17	24-Dec-26	15-Jan-27			■ Permit - Team Review EIR					
PRE-2650	Permit - Finalize/ Submit Single EIR	10	18-Jan-27	29-Jan-27			■ Permit - Finalize/ Submit Single EIR					
PRE-2660	Permit - MEPA Review	33	01-Feb-27	17-Mar-27			■ Permit - MEPA Review					
PRE-2720	Permit - MEPA Final Review	30	18-Mar-27	28-Apr-27			■ Permit - MEPA Final Review					
PRE-2670	Permit - Receive Certificate on Single EIR	5	29-Apr-27	05-May-27			■ Permit - Receive Certificate on Single EIR					
MASS DOT ACCESS PERMIT		381	16-Feb-26	05-Jul-27								
PRE-1930	Permit - Pre-Consultation Meeting with MassDOT District 2/ Confirm Study Area	33	16-Feb-26	01-Apr-26		■ Permit - Pre-Consultation Meeting with MassDOT District 2/ Confirm Study Area						
PRE-2100	Permit - Traffic Data Collection	20	02-Apr-26	29-Apr-26		■ Permit - Traffic Data Collection						
PRE-2110	Permit - Conduct Traffic Impact and Access Study (TIAS)	45	02-Apr-26	03-Jun-26		■ Permit - Conduct Traffic Impact and Access Study (TIAS)						
PRE-2120	Permit - Identify / Evaluate Mitigation Measures	31	05-May-26	16-Jun-26		■ Permit - Identify / Evaluate Mitigation Measures						
PRE-2130	Permit - Mobile Source Emissions Analysis	16	05-May-26	26-May-26		■ Permit - Mobile Source Emissions Analysis						
PRE-2140	Permit - Develop MassDOT Access Permit (25% Design/ Functional Design Report)	31	05-May-26	16-Jun-26		■ Permit - Develop MassDOT Access Permit (25% Design/ Functional Design Report)						
PRE-2150	Permit - Team Review Access Permit	15	17-Jun-26	07-Jul-26		■ Permit - Team Review Access Permit						
PRE-2160	Permit - Finalize/ Submit Access Permit	10	10-Aug-26	21-Aug-26		■ Permit - Finalize/ Submit Access Permit						
PRE-2170	Permit - MassDOT Review of Access Permit	51	24-Aug-26	02-Nov-26		■ Permit - MassDOT Review of Access Permit						
PRE-2180	Permit - Submit 75% Design	30	03-Nov-26	14-Dec-26		■ Permit - Submit 75% Design						
PRE-2190	Permit - MassDOT Review of 75% Design	43	15-Dec-26	11-Feb-27		■ Permit - MassDOT Review of 75% Design						
PRE-2200	Permit - Submit PS&E Design	30	12-Feb-27	25-Mar-27		■ Permit - Submit PS&E Design						
PRE-2210	Permit - MassDOT Review PS&E Design	22	26-Mar-27	26-Apr-27		■ Permit - MassDOT Review PS&E Design						
PRE-2730	Permit - MassDOT Final Review	45	27-Apr-27	28-Jun-27		■ Permit - MassDOT Final Review						
PRE-2220	Permit - Receive MassDOT Access Permit	5	29-Jun-27	05-Jul-27		■ Permit - Receive MassDOT Access Permit						
RAIL CROSSING MODIFICATION APPROVAL		385	16-Feb-26	06-Aug-27								
PRE-1940	Permit - Preliminary Engineering	42	16-Feb-26	14-Apr-26		■ Permit - Preliminary Engineering						
PRE-2790	Permit - Team Review	15	15-Apr-26	05-May-26		■ Permit - Team Review						
PRE-2810	Permit - Finalize / Submit	10	06-May-26	19-May-26		■ Permit - Finalize / Submit						
PRE-2230	Permit - CSX Review of Preliminary Engineering	52	20-May-26	30-Jul-26		■ Permit - CSX Review of Preliminary Engineering						
PRE-2240	Permit - Final Design	42	10-Aug-26	06-Oct-26		■ Permit - Final Design						
PRE-2800	Permit - Finalize / Submit	10	07-Oct-26	20-Oct-26		■ Permit - Finalize / Submit						
PRE-2250	Permit - CSX Review of Final Design	52	21-Oct-26	31-Dec-26		■ Permit - CSX Review of Final Design						
PRE-2260	Permit - Develop Railroad Agreements	53	01-Dec-26	11-Feb-27		■ Permit - Develop Railroad Agreements						
PRE-2740	Permit - Department of Public Utility / CSX Final Review	45	06-May-27	07-Jul-27		■ Permit - Department of Public Utility / CSX Final Review						
PRE-2270	Permit - Department of Public Utility Approval	22	08-Jul-27	06-Aug-27		■ Permit - Department of Public Utility Approval						
ARMY CORPS OF ENGINEERS SECTION 408 APPROVAL (LEVEE MODIFICATION)		310	16-Feb-26	23-Apr-27								
PRE-1950	Permit - Pre-Application Consultation with Army Corps and City of Springfield	43	16-Feb-26	15-Apr-26		■ Permit - Pre-Application Consultation with Army Corps and City of Springfield						
PRE-2350	Permit - Obtain Statement of Non-Objection from City of Springfield	23	01-Apr-26	01-May-26		■ Permit - Obtain Statement of Non-Objection from City of Springfield						
PRE-2360	Permit - Draft Application	52	01-Jun-26	11-Aug-26		■ Permit - Draft Application						
PRE-2370	Permit - Team Review	10	12-Aug-26	25-Aug-26		■ Permit - Team Review						
PRE-2380	Permit - Finalize/ Submit Application	5	26-Aug-26	01-Sep-26		■ Permit - Finalize/ Submit Application						
PRE-2390	Permit - Completeness Decision	21	02-Sep-26	30-Sep-26		■ Permit - Completeness Decision						

Finish Date: 30-Nov-29
Data Date: 01-Jan-25
Run Date: 15-Oct-25 15:21
Page 3 of 11
MA-RFP-SR-JC



SPRINGFIELD REGIONAL JUSTICE CENTER PROPOSAL SCHEDULE



Activity ID	Activity Name	Remaining Duration	Start	Finish	2025	2026	2027	2028	2029	2030	2031	2032
					JJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON
PRE-2400	Permit - Army Corps Review	52	01-Oct-26	11-Dec-26								
PRE-2710	Permit - Army Corps Final Review	90	14-Dec-26	16-Apr-27								
PRE-2410	Permit - Receive Section 408 Approval	5	19-Apr-27	23-Apr-27								
MASSACHUSETTS HISTORIC COMMISSION (MHC) REVIEW		105	16-Feb-26	10-Jul-26								
PRE-1960	Permit - Develop Project Notification Form	34	16-Feb-26	02-Apr-26								
PRE-2420	Permit - Team Review	10	03-Apr-26	16-Apr-26								
PRE-2430	Permit - Finalize/ Submit PNF	5	17-Apr-26	23-Apr-26								
PRE-2440	Permit - MHC Review	21	24-Apr-26	22-May-26								
PRE-2750	Permit - MHC Final Review	30	25-May-26	03-Jul-26								
PRE-2450	Permit - Receive MHC Determination	5	06-Jul-26	10-Jul-26								
JOINT MA WETLANDS PROTECTION ACT / MA ENDANGERED SPECIES ACT NOI		175	10-Aug-26	09-Apr-27								
PRE-2490	Permit - Develop Notice of Intent (NOI)	44	10-Aug-26	08-Oct-26								
PRE-2500	Permit - Team Review NOI	10	09-Oct-26	22-Oct-26								
PRE-2510	Permit - Finalize/ Submit NOI	10	23-Oct-26	05-Nov-26								
PRE-2520	Permit - Springfield Conservation Commission/ MassDEP/ NHESP Review	50	06-Nov-26	14-Jan-27								
PRE-2760	Permit - Springfield Conservation Commission/ MassDEP/ NHESP Final Review	45	15-Jan-27	18-Mar-27								
PRE-2530	Permit - Receive Order of Conditions	16	19-Mar-27	09-Apr-27								
CITY OF SPRINGFIELD LAND USE REVIEW		247	01-Jun-26	11-May-27								
PRE-1980	Permit - Building Commissioner Screening	24	01-Jun-26	02-Jul-26								
PRE-2560	Permit - Draft Tier 3 City Council Special Permit/ Site Plan Review Application	44	07-Jul-26	04-Sep-26								
PRE-2570	Permit - Team Review of Special Permit/ Site Plan Review Application	15	07-Sep-26	25-Sep-26								
PRE-2580	Permit - Finalize/ Submit Special Permit/ Site Plan Review Application	10	28-Sep-26	09-Oct-26								
PRE-2590	Permit - Springfield Riverfront Development Commission Review	21	12-Oct-26	09-Nov-26								
PRE-2600	Permit - City Council Review	80	10-Nov-26	01-Mar-27								
PRE-2770	Permit - Final Review	45	02-Mar-27	03-May-27								
PRE-2610	Permit - Receive City Council Approval	6	04-May-27	11-May-27								
PURCHASING - BID & AWARD		232	11-Dec-26	01-Nov-27								
WAVE 1 PACKAGES		61	11-Dec-26	05-Mar-27								
PUR-4060	Wave 1 Packages - Develop Bid Package	20	11-Dec-26	07-Jan-27								
PUR-4070	Wave 1 Packages - Bidding	15	08-Jan-27	28-Jan-27								
PUR-4080	Wave 1 Packages - De-Scopes	10	29-Jan-27	11-Feb-27								
PUR-4090	Wave 1 Packages - RTA to Client	1	12-Feb-27	12-Feb-27								
PUR-4100	Wave 1 Packages - Client Approval - RTA	5	15-Feb-27	19-Feb-27								
PUR-4110	Wave 1 Packages - Subcontract Execution	5	22-Feb-27	26-Feb-27								
PUR-4120	Wave 1 Packages - Certificate of Insurance/Compliance	5	01-Mar-27	05-Mar-27								
WAVE 2 PACKAGES		61	14-May-27	06-Aug-27								
PUR-1690	Wave 2 Packages - Develop Bid Package	20	14-May-27	10-Jun-27								
PUR-1800	Wave 2 Packages - Bidding	15	11-Jun-27	01-Jul-27								
PUR-2050	Wave 2 Packages - De-Scopes	10	02-Jul-27	15-Jul-27								
PUR-2160	Wave 2 Packages - RTA to Client	1	16-Jul-27	16-Jul-27								
PUR-2270	Wave 2 Packages - Client Approval - RTA	5	19-Jul-27	23-Jul-27								
PUR-2380	Wave 2 Packages - Subcontract Execution	5	26-Jul-27	30-Jul-27								
PUR-2490	Wave 2 Packages - Certificate of Insurance/Compliance	5	02-Aug-27	06-Aug-27								
WAVE 3 PACKAGES		61	09-Aug-27	01-Nov-27								

Finish Date: 30-Nov-29
Data Date: 01-Jan-25
Run Date: 15-Oct-25 15:21
Page 4 of 11
MA-RFP-SR-JC



SPRINGFIELD REGIONAL JUSTICE CENTER
PROPOSAL SCHEDULE



Activity ID	Activity Name	Remaining Duration	Start	Finish	2025	2026	2027	2028	2029	2030	2031	2032
					JJASON	DJFMAMJJASON	DJFMAMJJASON	DJFMAMJJASON	DJFMAMJJASON	DJFMAMJJASON	DJFMAMJJASON	DJFMAMJJASON
PUR-4130	Wave 3 Packages - Develop Bid Package	20	09-Aug-27	03-Sep-27				■ Wave 3 Packages - Develop Bid Package				
PUR-4140	Wave 3 Packages - Bidding	15	06-Sep-27	24-Sep-27				■ Wave 3 Packages - Bidding				
PUR-4150	Wave 3 Packages - De-Scopes	10	27-Sep-27	08-Oct-27				■ Wave 3 Packages - De-Scopes				
PUR-4160	Wave 3 Packages - RTA to Client	1	11-Oct-27	11-Oct-27				■ Wave 3 Packages - RTA to Client				
PUR-4170	Wave 3 Packages - Client Approval - RTA	5	12-Oct-27	18-Oct-27				■ Wave 3 Packages - Client Approval - RTA				
PUR-4190	Wave 3 Packages - Subcontract Execution	5	19-Oct-27	25-Oct-27				■ Wave 3 Packages - Subcontract Execution				
PUR-4180	Wave 3 Packages - Certificate of Insurance/Compliance	5	26-Oct-27	01-Nov-27				■ Wave 3 Packages - Certificate of Insurance/Compliance				
MATERIAL PROCUREMENT		640	01-Jun-26	10-Nov-28								
WAVE 1 PACKAGES		45	08-Mar-27	07-May-27								
PRO-1000	Wave 1 Packages - Submittals	20	08-Mar-27	02-Apr-27				■ Wave 1 Packages - Submittals				
PRO-1010	Wave 1 Packages - Submittals Approval	15	05-Apr-27	23-Apr-27				■ Wave 1 Packages - Submittals Approval				
PRO-1020	Wave 1 Packages - Materials Fab & Delvier	10	26-Apr-27	07-May-27				■ Wave 1 Packages - Materials Fab & Delvier				
LONG LEAD ITEMS		640	01-Jun-26	10-Nov-28								
PRO-2460	Long Lead Items - Load Letter by Design Team	40	01-Jun-26	24-Jul-26		■ Long Lead Items - Load Letter by Design Team						
PRO-2450	Long Lead Items - Utility Engineering	130	27-Jul-26	22-Jan-27		■ Long Lead Items - Utility Engineering						
PRO-1210	Long Lead Items - Submittals	20	08-Mar-27	02-Apr-27			■ Long Lead Items - Submittals					
PRO-2410	Long Lead Items - BIM Coordination	20	08-Mar-27	02-Apr-27			■ Long Lead Items - BIM Coordination					
PRO-1340	Long Lead Items - Submittals Approval	20	05-Apr-27	30-Apr-27			■ Long Lead Items - Submittals Approval					
PRO-2380	Long Lead Items - Fab & Deliver Switchboard / Switchgear	400	03-May-27	10-Nov-28				■ Long Lead Items - Fab & Deliver Switchboard / Switchgear				
PRO-2400	Long Lead Items - Fab & Deliver Utility Transformer	400	03-May-27	10-Nov-28				■ Long Lead Items - Fab & Deliver Utility Transformer				
PRO-5010	Long Lead Items - Fab & Deliver Long Lead Items	50	03-May-27	09-Jul-27				■ Long Lead Items - Fab & Deliver Long Lead Items				
MEGAPANEL PROCUREMENT AND DELIVERY		489	10-Aug-26	22-Jun-28								
PRO-2390	Long Lead Items - Envelope Design Assist	139	10-Aug-26	18-Feb-27		■ Long Lead Items - Envelope Design Assist						
PRO-5000	Long Lead Items - Envelope Fab and Deliver	350	18-Feb-27	22-Jun-28			■ Long Lead Items - Envelope Fab and Deliver					
WAVE 2 PACKAGES		80	09-Aug-27	26-Nov-27								
PRO-1520	Wave 2 Packages - Submittals	20	09-Aug-27	03-Sep-27				■ Wave 2 Packages - Submittals				
PRO-2000	Wave 2 Packages - Submittals Approval	15	06-Sep-27	24-Sep-27				■ Wave 2 Packages - Submittals Approval				
PRO-2370	Wave 2 Packages - Fab & Deliver	45	27-Sep-27	26-Nov-27				■ Wave 2 Packages - Fab & Deliver				
WAVE 3 PACKAGES		80	02-Nov-27	21-Feb-28								
PRO-2420	Wave 3 Packages - Submittals	20	02-Nov-27	29-Nov-27				■ Wave 3 Packages - Submittals				
PRO-2430	Wave 3 Packages - Submittals Approval	15	30-Nov-27	20-Dec-27				■ Wave 3 Packages - Submittals Approval				
PRO-2440	Wave 3 Packages - Fab & Deliver	45	21-Dec-27	21-Feb-28				■ Wave 3 Packages - Fab & Deliver				
CONSTRUCTION		668	12-May-27	30-Nov-29								
NEW BUILDING		668	12-May-27	30-Nov-29								
SITE ENABLING		442	12-May-27	18-Jan-29								
CON-1010	Site Enabling - Site Mobilization	10	12-May-27	25-May-27				■ Site Enabling - Site Mobilization				
CON-1020	Site Enabling - Temporary Fencing Installation / Erosion Control	12	26-May-27	10-Jun-27				■ Site Enabling - Temporary Fencing Installation / Erosion Control				
CON-1030	Site Enabling - Site Clearing	10	11-Jun-27	24-Jun-27				■ Site Enabling - Site Clearing				
CON-1050	Site Enabling - Clear Western Roadway and Fence + Install Gates	5	06-Jul-27	12-Jul-27				■ Site Enabling - Clear Western Roadway and Fence + Install Gates				
CON-6372	Site Enabling - Clear East Road, Fence + Install Gates & Railroad Crossing Upgrade	50	19-Aug-27	27-Oct-27				■ Site Enabling - Clear East Road, Fence + Install Gates & Railroad Crossing Upgrade				
CON-6912	Site Enabling - CSX Railroad Modifications	40	28-Oct-27	22-Dec-27				■ Site Enabling - CSX Railroad Modifications				
CON-1040	Site Enabling - Levee Modifications	80	29-Sep-28	18-Jan-29					■ Site Enabling - Levee Modifications			
FOUNDATIONS & STEEL STRUCTURE		410	25-Jun-27	18-Jan-29								
FOUNDATIONS		410	25-Jun-27	18-Jan-29								

Finish Date: 30-Nov-29
Data Date: 01-Jan-25
Run Date: 15-Oct-25 15:21
Page 5 of 11
MA-RFP-SR-JC



SPRINGFIELD REGIONAL JUSTICE CENTER PROPOSAL SCHEDULE

































Activity ID	Activity Name	Remaining Duration	Start	Finish	2025	2026	2027	2028	2029	2030	2031	2032
					JJAJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON
WHOLE BUILDING FOUNDATIONS												
CON-6602	Whole Building Foundations - Strip Fill Layer	15	25-Jun-27	15-Jul-27	■ Whole Building Foundations - Strip Fill Layer							
CON-1110	Whole Building Foundations - Excavate for Special Foundations	10	16-Jul-27	29-Jul-27	■ Whole Building Foundations - Excavate for Special Foundations							
CON-6592	Whole Building Foundations - Test, Stockpile, Treat, Export Unsuitables	150	16-Jul-27	10-Feb-28	■ Whole Building Foundations - Test, Stockpile, Treat, Export Unsuitables							
CON-6432	Whole Building Foundations - Create Access Ramp	5	30-Jul-27	05-Aug-27	■ Whole Building Foundations - Create Access Ramp							
CON-6292	Excavation and Backfill - Lightweight Backfill against Levee Contingent on Permit	80	29-Sep-28	18-Jan-29	■ Excavation and Backfill - Lightweight Backfill against Levee Contingent on Permit							
EAST FOUNDATIONS												
CON-6012	East Foundations - Special Foundations	35	06-Aug-27	23-Sep-27	■ East Foundations - Special Foundations							
CON-1120	East Foundations - F/R/P Pile Caps / Spread Footings	25	24-Sep-27	28-Oct-27	■ East Foundations - F/R/P Pile Caps / Spread Footings							
CON-7190	East Foundations - F/R/P Exterior Retaining Walls	30	24-Sep-27	04-Nov-27	■ East Foundations - F/R/P Exterior Retaining Walls							
CON-6212	East Foundations - Cast-In-Place Basement Walls (Minimum Two Crews)	30	05-Nov-27	16-Dec-27	■ East Foundations - Cast-In-Place Basement Walls (Minimum Two Crews)							
CON-1140	East Foundations - Below Grade Waterproofing	15	17-Dec-27	06-Jan-28	■ East Foundations - Below Grade Waterproofing							
CON-1210	East Foundations - Cast-In-Place Backfill	10	07-Jan-28	20-Jan-28	■ East Foundations - Cast-In-Place Backfill							
WEST FOUNDATIONS												
CON-7082	West Foundations - Special Foundations	25	21-Jan-28	24-Feb-28	■ West Foundations - Special Foundations							
CON-1130	West Foundations - F/R/P Exterior Retaining Walls	15	25-Feb-28	16-Mar-28	■ West Foundations - F/R/P Exterior Retaining Walls							
CON-7042	West Foundations - F/R/P Pile Caps / Spread Footings / Frost Wall	15	25-Feb-28	16-Mar-28	■ West Foundations - F/R/P Pile Caps / Spread Footings / Frost Wall							
CON-7180	West Foundations - Cast-In-Place Basement Walls (Minimum Two Crews)	20	17-Mar-28	13-Apr-28	■ West Foundations - Cast-In-Place Basement Walls (Minimum Two Crews)							
CON-7062	West Foundations - Below Grade Waterproofing	10	07-Apr-28	20-Apr-28	■ West Foundations - Below Grade Waterproofing							
CON-7072	West Foundations - Cast-In-Place Backfill	10	21-Jul-28	03-Aug-28	■ West Foundations - Cast-In-Place Backfill							
UNDERGROUND UTILITIES												
CON-6232	Underground Utilities - Install In-Road Utilities Along Ave of Justice and Backfill	25	28-Oct-27	01-Dec-27	■ Underground Utilities - Install In-Road Utilities Along Ave of Justice and Backfill							
CON-7200	Underground Utilities - Stormwater Management and Detention Systems	80	02-Dec-27	22-Mar-28	■ Underground Utilities - Stormwater Management and Detention Systems							
CON-1240	Underground Utilities - Install Exterior Underground Utilities and Backfill	25	21-Jul-28	24-Aug-28	■ Underground Utilities - Install Exterior Underground Utilities and Backfill							
STEEL ERECTION												
EAST STEEL												
CON-6472	East Steel Erection - Erect Main Columns and Diaphragm	25	17-Dec-27	20-Jan-28	■ East Steel Erection - Erect Main Columns and Diaphragm							
CON-6482	East Steel Erection - Level 1 Decking and Detailing	15	21-Jan-28	10-Feb-28	■ East Steel Erection - Level 1 Decking and Detailing							
CON-5742	East Steel Erection - Remaining East Wing Erect Structural Steel	35	17-Mar-28	04-May-28	■ East Steel Erection - Remaining East Wing Erect Structural Steel							
CON-5752	East Steel Erection - Remaining East Wing Detail Steel & Decking	20	05-May-28	01-Jun-28	■ East Steel Erection - Remaining East Wing Detail Steel & Decking							
WEST STEEL												
CON-7022	West Steel Erection - Erect Main Columns and Diaphragm	15	14-Apr-28	04-May-28	■ West Steel Erection - Erect Main Columns and Diaphragm							
CON-7032	West Steel Erection - Level 1 - Decking and Detailing	10	05-May-28	18-May-28	■ West Steel Erection - Level 1 - Decking and Detailing							
CON-6192	West Steel Erection - Remaining West Wing Erect Structural Steel	30	19-May-28	29-Jun-28	■ West Steel Erection - Remaining West Wing Erect Structural Steel							
CON-6202	West Steel Erection - Remaining West Wing Detail Steel & Decking	15	30-Jun-28	20-Jul-28	■ West Steel Erection - Remaining West Wing Detail Steel & Decking							
SLAB ON DECK												
CON-6222	Basement - FRP SOG and Building Footprint Underground Utilities	45	19-May-28	20-Jul-28	■ Basement - FRP SOG and Building Footprint Underground Utilities							
CON-6382	Roof - Roof Deck Protection Board and Temp Roof Membrane (AVB+)	20	23-Jun-28	20-Jul-28	■ Roof - Roof Deck Protection Board and Temp Roof Membrane (AVB+)							
CON-6182	Level 1 - FRP SOD	10	21-Jul-28	03-Aug-28	■ Level 1 - FRP SOD							
CON-1300	Level 2 - FRP SOD	10	04-Aug-28	17-Aug-28	■ Level 2 - FRP SOD							
CON-5762	Level 3 - FRP SOD	10	18-Aug-28	31-Aug-28	■ Level 3 - FRP SOD							
CON-5992	Level 4 - FRP SOD	10	01-Sep-28	14-Sep-28	■ Level 4 - FRP SOD							
CON-6732	Level 5 - FRP SOD	10	15-Sep-28	28-Sep-28	■ Level 5 - FRP SOD							
SPRAY FIREPROOFING												

Finish Date: 30-Nov-29
Data Date: 01-Jan-25
Run Date: 15-Oct-25 15:21
Page 6 of 11
MA-RFP-SR-JC



SPRINGFIELD REGIONAL JUSTICE CENTER
PROPOSAL SCHEDULE



Activity ID	Activity Name	Remaining Duration	Start	Finish	2025	2026	2027	2028	2029	2030	2031	2032
					JJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON	DJHVAMJJASON
CON-6492	Basement - Spray Fireproofing	10	21-Jul-28	03-Aug-28								
CON-5302	Level 1 - Spray Fireproofing	10	04-Aug-28	17-Aug-28								
CON-1410	Level 2 - Spray Fireproofing	10	18-Aug-28	31-Aug-28								
CON-1350	Level 3 - Spray Fireproofing	10	01-Sep-28	14-Sep-28								
CON-6002	Level 4 - Spray Fireproofing	10	15-Sep-28	28-Sep-28								
CON-6742	Level 5 - Spray Fireproofing	10	29-Sep-28	12-Oct-28								
GEOTHERMAL		210	23-Mar-28	16-Jan-29								
CON-5952	Geothermal - Drill Wells	130	23-Mar-28	20-Sep-28								
CON-5962	Geothermal - Horizontal Piping Installation	60	21-Sep-28	13-Dec-28								
CON-5972	Geothermal - Vault Install E&B	10	14-Dec-28	27-Dec-28								
CON-5982	Geothermal - Vault Mains to Building	10	28-Dec-28	10-Jan-29								
EXTERIOR ENVELOPE		175	26-May-28	25-Jan-29								
ROOF		30	26-May-28	14-Sep-28								
CON-1540	Roof + Mechanical Penthouse - Install Permanent Roofing Assembly	40	26-May-28	20-Jul-28								
CON-1660	Roof + Mechanical Penthouse - Install Flashing & Roof Accessories	10	21-Jul-28	03-Aug-28								
CON-6422	Roof + Mechanical Penthouse - Install Penthouse Screen	30	04-Aug-28	14-Sep-28								
ENVELOPE		115	18-Aug-28	28-Sep-28								
EAST WING		30	18-Aug-28	28-Sep-28								
CON-5312	East Wing Level 1 - Place Stick Envelope	30	18-Aug-28	28-Sep-28								
CON-6302	East Wing Level 2 - Place Unitized Envelope	20	01-Sep-28	28-Sep-28								
CON-6312	East Wing Level 3 - Place Unitized Envelope	20	29-Sep-28	26-Oct-28								
CON-6502	East Wing Level 1 - Final Seal on Stick Envelope	10	29-Sep-28	12-Oct-28								
CON-6512	East Wing Level 2 - Final Seal on Unitized Envelope	10	13-Oct-28	26-Oct-28								
CON-6322	East Wing Level 4 - Place Unitized Envelope	20	27-Oct-28	23-Nov-28								
CON-6522	East Wing Level 3 - Final Seal on Unitized Envelope	10	27-Oct-28	09-Nov-28								
CON-6532	East Wing Level 4 - Final Seal Unitized Envelope	10	24-Nov-28	07-Dec-28								
CON-6932	East Wing Level 5 - Place Unitized Envelope	20	24-Nov-28	21-Dec-28								
CON-6922	East Wing Level 5 - Final Seal Unitized Envelope	5	22-Dec-28	28-Dec-28								
WEST WING		75	13-Oct-28	25-Jan-29								
CON-6332	West Wing Level 1 - Place Stick Envelope	30	13-Oct-28	23-Nov-28								
CON-6342	West Wing Level 2 - Place Unitized Envelope	20	13-Oct-28	09-Nov-28								
CON-6352	West Wing Level 3 - Place Unitized Envelope	20	10-Nov-28	07-Dec-28								
CON-6552	West Wing Level 2 - Final Seal on Unitized Envelope	10	10-Nov-28	23-Nov-28								
CON-6542	West Wing Level 1 - Final Seal on Stick Envelope	5	24-Nov-28	30-Nov-28								
CON-6362	West Wing Level 4 - Place Unitized Envelope	15	08-Dec-28	28-Dec-28								
CON-6562	West Wing Level 3 - Final Seal on Unitized Envelope	5	08-Dec-28	14-Dec-28								
CON-6572	West Wing Level 4 - Final Seal on Unitized Envelope	5	29-Dec-28	04-Jan-29								
CON-6942	West Wing Level 5 - Place Unitized Envelope	15	29-Dec-28	18-Jan-29								
CON-6952	West Wing Level 5 - Final Seal on Unitized Envelope	5	19-Jan-29	25-Jan-29								
VERTICAL CIRCULATION		305	05-May-28	05-Jul-29								
STAIRS		215	05-May-28	01-Mar-29								
CON-6402	Vertical Circulation - Stair CMU Shafts	25	05-May-28	08-Jun-28								
CON-1610	Vertical Circulation - Stairs Installation	50	09-Jun-28	17-Aug-28								
CON-6712	Vertical Circulation - Stair Drywall Shafts	25	26-Jan-29	01-Mar-29								

Finish Date: 30-Nov-29
Data Date: 01-Jan-25
Run Date: 15-Oct-25 15:21
Page 7 of 11
MA-RFP-SR-JC



SPRINGFIELD REGIONAL JUSTICE CENTER PROPOSAL SCHEDULE



Activity ID	Activity Name	Remaining Duration	Start	Finish	2025	2026	2027	2028	2029	2030	2031	2032
					JJASON	DJFMAMJJASON	DJFMAMJJASON	DJFMAMJJASON	DJFMAMJJASON	DJFMAMJJASON	DJFMAMJJASON	DJFMAMJJASON
ELEVATOR		280	09-Jun-28	05-Jul-29								
CON-1640	Vertical Circulation - Elevator CMU Walls	25	09-Jun-28	13-Jul-28				■ Vertical Circulation - Elevator CMU Walls				
CON-6722	Vertical Circulation - Elevator Drywall Walls	25	02-Mar-29	05-Apr-29					■ Vertical Circulation - Elevator Drywall Walls			
CON-6682	Vertical Circulation - Elevator Railwork	20	06-Apr-29	03-May-29					■ Vertical Circulation - Elevator Railwork			
CON-2370	Vertical Circulation - Install Machine Room	20	04-May-29	31-May-29					■ Vertical Circulation - Install Machine Room			
CON-6692	Vertical Circulation - Install Elevator Car	20	01-Jun-29	28-Jun-29					■ Vertical Circulation - Install Elevator Car			
CON-6702	Vertical Circulation - Elevator Testing and Commissioning	5	29-Jun-29	05-Jul-29					■ Vertical Circulation - Elevator Testing and Commissioning			
INTERIOR ROUGH / FINISHES		306	04-Aug-28	05-Oct-29								
INTERIOR ROUGH / FINISHES - BASEMENT		210	04-Aug-28	04-May-29								
CON-6062	Basement - Rough in MEP's	35	04-Aug-28	21-Sep-28				■ Basement - Rough in MEP's				
CON-6162	Basement - Install Detention Equipment	25	25-Aug-28	28-Sep-28				■ Basement - Install Detention Equipment				
CON-6072	Basement - Layout & Framing/CMU Walls	30	08-Sep-28	19-Oct-28				■ Basement - Layout & Framing/CMU Walls				
CON-6082	Basement - In Wall Inspections	3	20-Oct-28	24-Oct-28				■ Basement - In Wall Inspections				
CON-6092	Basement - Install Drywall at LGMF Walls	15	25-Oct-28	14-Nov-28				■ Basement - Install Drywall at LGMF Walls				
CON-6122	Basement - Tape/Prime/1st Coat Walls	20	15-Nov-28	12-Dec-28				■ Basement - Tape/Prime/1st Coat Walls				
CON-6102	Basement - Install Ceiling Grid/Install Cuts	15	13-Dec-28	02-Jan-29				■ Basement - Install Ceiling Grid/Install Cuts				
CON-6112	Basement - Above Ceiling Inspections	3	03-Jan-29	05-Jan-29				■ Basement - Above Ceiling Inspections				
CON-6042	Basement - MEPF Finishes & Final Connections	15	08-Jan-29	26-Jan-29				■ Basement - MEPF Finishes & Final Connections				
CON-6132	Basement - Flood Ceilings	10	29-Jan-29	09-Feb-29				■ Basement - Flood Ceilings				
CON-6152	Basement - Finish Paint	15	12-Feb-29	02-Mar-29				■ Basement - Finish Paint				
CON-6052	Basement - Architectural Finishes (Millwork)	33	20-Feb-29	05-Apr-29				■ Basement - Architectural Finishes (Millwork)				
CON-6172	Basement - Install Flooring	25	20-Feb-29	26-Mar-29				■ Basement - Install Flooring				
CON-6142	Basement - Install Doors	5	13-Mar-29	19-Mar-29				■ Basement - Install Doors				
CON-6962	Basement - Final Finishes	30	06-Apr-29	17-May-29				■ Basement - Final Finishes				
CON-6032	Basement - Area Cleaning	5	18-May-29	24-May-29				■ Basement - Area Cleaning				
CON-6022	Basement - Area Complete	0		24-May-29				◆ Basement - Area Complete				
INTERIOR ROUGH / FINISHES - FIRST LEVEL		210	18-Aug-28	11-Jun-29								
CON-4812	First Floor - Rough in MEP's	55	18-Aug-28	02-Nov-28				■ First Floor - Rough in MEP's				
CON-4802	First Floor - Layout & Framing	30	29-Sep-28	09-Nov-28				■ First Floor - Layout & Framing				
CON-4822	First Floor - In Wall Inspections	3	10-Nov-28	14-Nov-28				■ First Floor - In Wall Inspections				
CON-4832	First Floor - Install Drywall at LGMF Walls	15	15-Nov-28	05-Dec-28				■ First Floor - Install Drywall at LGMF Walls				
CON-4842	First Floor - Tape/Prime/1st Coat Walls	20	06-Dec-28	02-Jan-29				■ First Floor - Tape/Prime/1st Coat Walls				
CON-4852	First Floor - Install Ceiling Grid/Install Cuts	15	03-Jan-29	23-Jan-29				■ First Floor - Install Ceiling Grid/Install Cuts				
CON-4862	First Floor - Above Ceiling Inspections	3	24-Jan-29	26-Jan-29				■ First Floor - Above Ceiling Inspections				
CON-4872	First Floor - MEPF Finishes & Final Connections	15	29-Jan-29	16-Feb-29				■ First Floor - MEPF Finishes & Final Connections				
CON-4882	First Floor - Flood Ceilings	10	19-Feb-29	02-Mar-29				■ First Floor - Flood Ceilings				
CON-4902	First Floor - Finish Paint	15	05-Mar-29	23-Mar-29				■ First Floor - Finish Paint				
CON-4922	First Floor - Architectural Finishes (Millwork)	30	13-Mar-29	23-Apr-29				■ First Floor - Architectural Finishes (Millwork)				
CON-4892	First Floor - Install Flooring	25	13-Mar-29	16-Apr-29				■ First Floor - Install Flooring				
CON-4912	First Floor - Install Doors	10	03-Apr-29	16-Apr-29				■ First Floor - Install Doors				
CON-6972	First Floor - Final Finishes	30	24-Apr-29	04-Jun-29				■ First Floor - Final Finishes				
CON-4942	First Floor - Area Cleaning	5	05-Jun-29	11-Jun-29				■ First Floor - Area Cleaning				
CON-4952	First Floor - Area Complete	0		11-Jun-29				◆ First Floor - Area Complete				
INTERIOR ROUGH / FINISHES - SECOND LEVEL		201	29-Sep-28	06-Jul-29								

Finish Date: 30-Nov-29
Data Date: 01-Jan-25
Run Date: 15-Oct-25 15:21
Page 8 of 11
MA-RFP-SR-JC



SPRINGFIELD REGIONAL JUSTICE CENTER PROPOSAL SCHEDULE



[illegible]

[illegible]

Finish Date: 30-Nov-29
Data Date: 01-Jan-25
Run Date: 15-Oct-25 15:21
Page 10 of 11
MA-RFP-SRJC



SPRINGFIELD REGIONAL JUSTICE CENTER PROPOSAL SCHEDULE



Activity ID	Activity Name	Remaining Duration	Start	Finish												
					2025		2026		2027		2028		2029		2030	
					J	J	J	J	J	J	J	J	J	J	J	J
CON-7080	Mechanical Systems - All Systems Complete + Ready for Testing and Balancing	0	03-Aug-29													
CON-7090	Mechanical Systems - All Systems Complete + Ready for Affidavits	0	03-Aug-29													
CON-7110	Mechanical Systems - Affidavits for All Equipment	20	03-Aug-29	30-Aug-29												
PERMANENT POWER		70	26-Jan-29	04-May-29												
CON-2700	Permanent Power - Switchboard / Switchgear Equipment Installation and Tie-In	60	26-Jan-29	19-Apr-29												
CON-6652	Permanent Power - Main Switchboard Energized	5	20-Apr-29	26-Apr-29												
CON-6662	Permanent Power - Panels Checked out, Ready, and Energized	5	27-Apr-29	03-May-29												
CON-6672	Permanent Power - Power Available for Distribution	0	04-May-29													
SITE IMPROVEMENTS		165	19-Jan-29	06-Sep-29												
CON-7140	Site Improvements - Curbing around all Paved Areas	30	19-Jan-29	01-Mar-29												
CON-7150	Site Improvements - Concrete Walks / Plaza Pavers	30	02-Mar-29	12-Apr-29												
CON-7160	Site Improvements - Pave Ramp to Sallyport	20	02-Mar-29	29-Mar-29												
CON-7170	Site Improvements - Landscaping and Plantings	35	30-Mar-29	17-May-29												
CON-6242	Site Improvements - Demolish Billboards	25	18-May-29	21-Jun-29												
ROAD / ENTRANCE WORK		135	26-Jan-29	02-Aug-29												
CON-6252	Road / Entrance Work - Repave Western Roadways and Multiuse Path	45	26-Jan-29	29-Mar-29												
CON-7210	Road / Entrance Work - Clinton St to West Columbus Ave Upgrades	45	30-Mar-29	31-May-29												
CON-7220	Road / Entrance Work - West Columbus Ave to Liberty St Upgrades	45	01-Jun-29	02-Aug-29												
SURFACE PARKING		110	06-Apr-29	06-Sep-29												
CON-6262	Surface Parking - Fence and Clear All Future Surface Parking	40	06-Apr-29	31-May-29												
CON-6582	Surface Parking - Final Stormwater Management	50	01-Jun-29	09-Aug-29												
CON-6272	Surface Parking - Compress + Pave Surface Parking	50	15-Jun-29	23-Aug-29												
CON-6282	Surface Parking - Line Stripe Parking Areas	10	24-Aug-29	06-Sep-29												
INSPECTIONS / BUILDING TURNOVER		120	18-Jun-29	30-Nov-29												
COM-1020	Inspections and Turnover - Commissioning of MEP Equipment	50	18-Jun-29	24-Aug-29												
COM-1030	Inspections and Turnover - Punchlist	50	30-Jul-29	05-Oct-29												
COM-1040	Inspections and Turnover - Final Elevator Testing	5	13-Aug-29	17-Aug-29												
COM-1000	Inspections and Turnover - Testing and Balancing	65	13-Aug-29	09-Nov-29												
COM-1090	Inspections and Turnover - Final Fire Alarm/Plumbing/Life-Safety/Electrical Inspections	15	09-Nov-29	30-Nov-29												
COM-1100	Inspections and Turnover - Test & Balance Complete	0		09-Nov-29												
COM-1080	Inspections and Turnover - Obtain Final Certificate of Occupancy / CO	0		30-Nov-29												
