


Activity ID	Activity Name	OD	Start	Finish	Calendar	2023				2024				2025		
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3

Design-Build CSTv1.0


Design-Build Contract Procurement

ContractNo	Activity Name	OD	Start	Finish	Calendar
ContractNo_Prelim	BTC Plans/Specs/Spec. Prov. accepted by MassDOT	0	03-Jan-23		Cal01-5d/8hr/12hol
ContractNo_Prelim10	FHWA Review BTC Plans/Specs/Spec. Provisions	30	03-Jan-23	01-Feb-23	Cal03A -7 d/8hr/No Holidays
ContractNo_LOI	Advertise Request for Letters-of-Interest (LOI)	0	07-Jan-23		Cal19 -5 aturday Only (Adv
ContractNo_LOIP	Letters-of-Interest (LOI) Procurement	40	07-Jan-23	15-Feb-23	Cal03A -7 d/8hr/No Holidays
ContractNo_RFP20	FHWA Concurrence to Advertise	0		01-Feb-23	Cal01-5d/8hr/12hol
ContractNo_LOID	Letters-of-Interest (LOI) Due	0		15-Feb-23	Cal01-5d/8hr/12hol
ContractNo_RFQ	Issue Request for Qualifications (RFQ)	0	16-Feb-23		Cal01-5d/8hr/12hol
ContractNo_RFQP	Statement of Qualifications Prepared	28	16-Feb-23	15-Mar-23	Cal03A -7 d/8hr/No Holidays
ContractNo_RFQD	Statement of Qualifications Due	0		15-Mar-23	Cal01-5d/8hr/12hol
ContractNo_ShList	Shortlist of Proposers Selected/Notified	20	16-Mar-23	04-Apr-23	Cal03A -7 d/8hr/No Holidays
ContractNo_RFP10	Advertise Request for Proposals	0	08-Apr-23		Cal19 -5 aturday Only (Adv
ContractNo_RFP	Release Request for Proposals (RFP)	0	10-Apr-23		Cal01-5d/8hr/12hol
ContractNo_RFPP20	Pre-Proposal Meeting	1	10-Apr-23	10-Apr-23	Cal01-5d/8hr/12hol
ContractNo_RFPP	Proposers Prepare Proposals	43	10-Apr-23	22-May-23	Cal03A -7 d/8hr/No Holidays
ContractNo_RFPP30	ATC Meetings	3	11-Apr-23	13-Apr-23	Cal01-5d/8hr/12hol
ContractNo_RFPP50	ATC Proposals Due	1	14-Apr-23	14-Apr-23	Cal01-5d/8hr/12hol
ContractNo_RFPP40	Final RFP Questions Due	1	15-May-23	15-May-23	Cal01-5d/8hr/12hol
ContractNo_RFPP10	Technical and Price Proposals Due	0		22-May-23	Cal01-5d/8hr/12hol
ContractNo_RFPD00	Oral Presentation of Design-Build Proposals	2	31-May-23	01-Jun-23	Cal01-5d/8hr/12hol
ContractNo_RFPD10	Scoring of Technical Proposals	2	02-Jun-23	05-Jun-23	Cal01-5d/8hr/12hol
ContractNo_BID	Public Price Bid Opening	0		06-Jun-23	Cal01-5d/8hr/12hol
ContractNo_NOA	Issue Notice of Award/Project Start	45	08-Jun-23	22-Jul-23	Cal03A -7 d/8hr/No Holidays

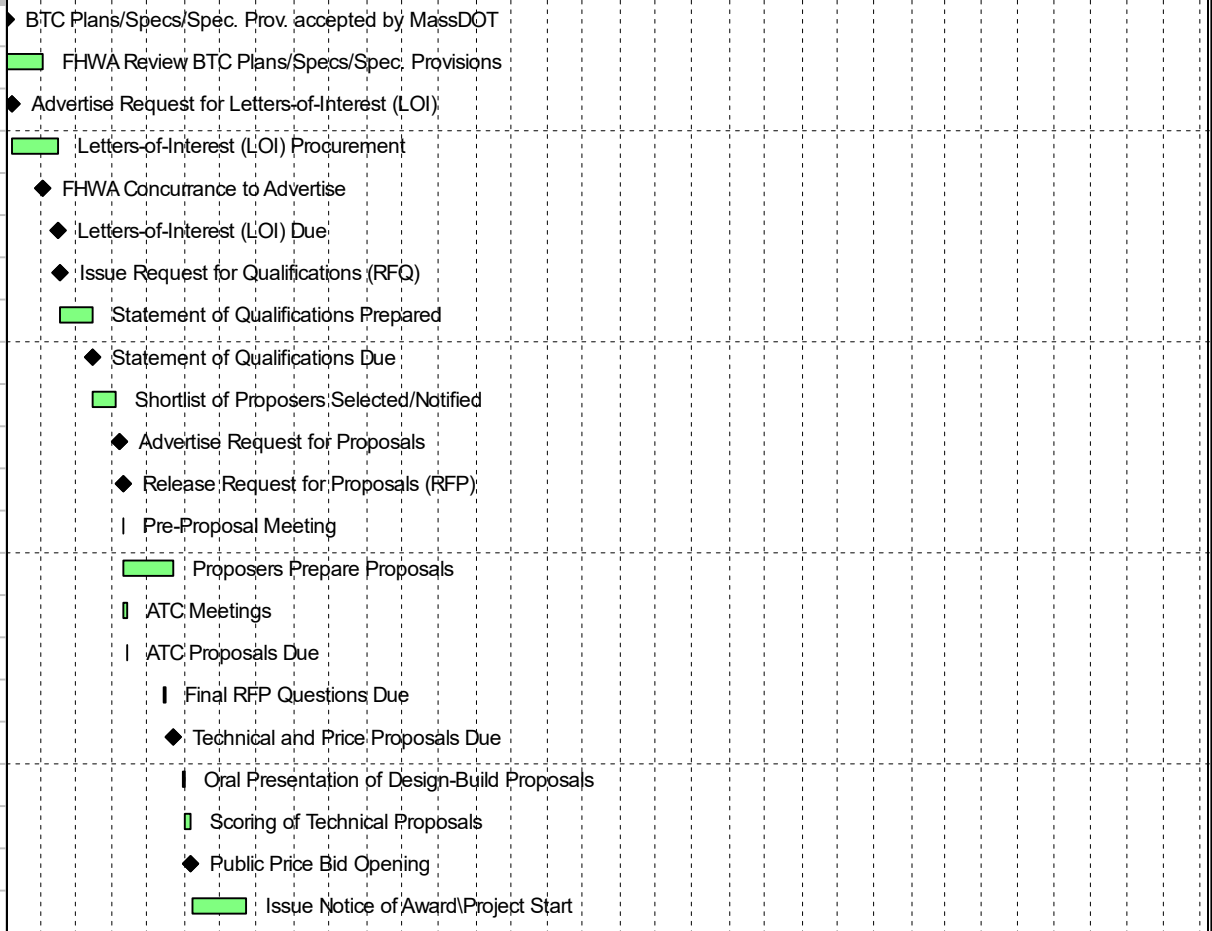


Milestones

General					
ContractNo	Activity Name	OD	Start	Finish	Calendar
ContractNo_NTP	Issue Design-Builder Notice-to-Proceed (NTP)	0	22-Jul-23		Cal04-7d/24Hr/No Hol (Mile
ContractNo_AR01	Access Restraint: Relocate Util before Bridge Demo	0	10-Apr-24		Cal04-7d/24Hr/No Hol (Mile
ContractNo_MS04	MS#04 -perform Final Traffic Move	0		23-Apr-25	Cal04-7d/24Hr/No Hol (Mile
ContractNo_MS03	MS#03 -Full Beneficial Use (FBU)	0		23-Apr-25*	Cal04-7d/24Hr/No Hol (Mile
ContractNo_MS02	MS#02 -Substantial Completion (SC)	0		22-May-25*	Cal04-7d/24Hr/No Hol (Mile
ContractNo_MS01	MS#01 -Field Completion (CFC)	0		08-Jul-25*	Cal04-7d/24Hr/No Hol (Mile

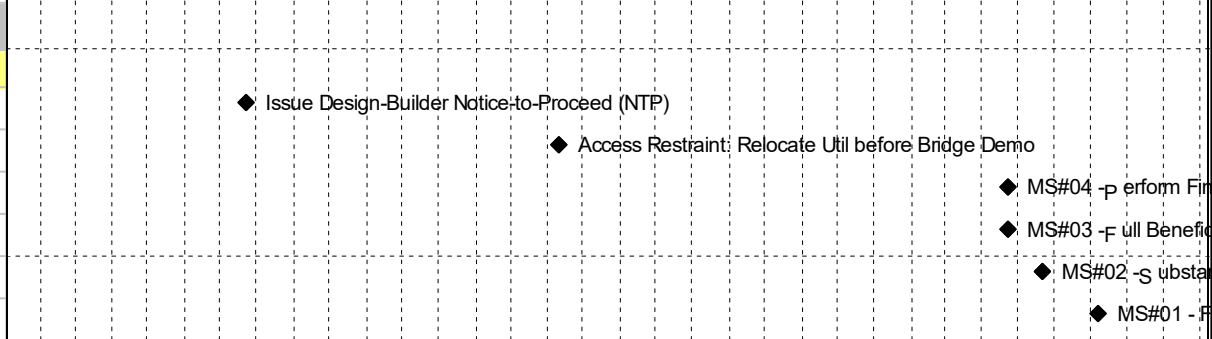

Durations

ContractNo	Activity Name	OD	Start	Finish	Calendar
ContractNo_1030	Construction Contract Duration (NTP to AR01)	263	22-Jul-23	10-Apr-24	Cal04-7d/24Hr/No Hol (Mile
ContractNo_1000	Construction Contract Duration (NTP to FBU)	641	22-Jul-23	23-Apr-25	Cal04-7d/24Hr/No Hol (Mile
ContractNo_1010	Construction Contract Duration (NTP to SC)	670	22-Jul-23	22-May-25	Cal04-7d/24Hr/No Hol (Mile



Legend:

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Layout = CST01-Baseline-All, Filter = TASK filter: All Activities
Data Date = 01-Jan-23, Run Date = 27-Jul-23, 09:50
Project Start = 01-Jan-23, Project Finish = 08-Jul-25

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	Start	Finish	Calendar	2023				2024				2025		
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
ContractNo_1020	Construction Contract Duration (NTP to CFC)	717	22-Jul-23	08-Jul-25	Cal04-7d/24Hr/No Hol (Mile											
Submittals & Procurements																
Early Release Design Packages																
Geotechnical Report																
ContractNo_2640	Prepare & Submit Subsurface Investigation Plan	10	24-Jul-23	04-Aug-23	Cal01-5d/8hr/12hol											
ContractNo_2660	Review & Approve Subsurface Investigation Plan	10	05-Aug-23	14-Aug-23	Cal03A -7 d/8hr/No Holiday:											
ContractNo_2650	Schedule/Perform Geotech Borings & Test Pits	30	15-Aug-23	26-Sep-23	Cal01-5d/8hr/12hol											
ContractNo_1680	Prepare Geotechnical Report	9	27-Sep-23	10-Oct-23	Cal01-5d/8hr/12hol											
ContractNo_1950	Schedule & Conduct OTS Review -G eotechnical Report	2	11-Oct-23	12-Oct-23	Cal01-5d/8hr/12hol											
ContractNo_1940	Submit Geotechnical Report	4	13-Oct-23	18-Oct-23	Cal01-5d/8hr/12hol											
ContractNo_2050	Review & Approve Geotechnical Report	30	19-Oct-23	17-Nov-23	Cal03A -7 d/8hr/No Holiday:											
Drilled Shafts																
ContractNo_1740	Prepare Drilled Shafts Design	10	19-Oct-23	01-Nov-23	Cal01-5d/8hr/12hol											
ContractNo_1990	Schedule & Conduct OTS Review -D rilled Shafts Design	1	02-Nov-23	02-Nov-23	Cal01-5d/8hr/12hol											
ContractNo_1980	Submit Drilled Shafts Design	3	03-Nov-23	07-Nov-23	Cal01-5d/8hr/12hol											
ContractNo_2060	Review & Approve Drilled Shafts Design	30	08-Nov-23	07-Dec-23	Cal03A -7 d/8hr/No Holiday:											
ContractNo_1750	Comment Resolution & Reissue Drilled Shafts Design	10	08-Dec-23	21-Dec-23	Cal01-5d/8hr/12hol											
ContractNo_1890	Procure Drilled Shaft Casings	30	22-Dec-23	20-Jan-24	Cal03A -7 d/8hr/No Holiday:											
Substructure Rebar																
ContractNo_1780	Prepare Early Release -S ubstructure Design	90	24-Jul-23	29-Nov-23	Cal01-5d/8hr/12hol											
ContractNo_2010	Schedule & Conduct OTS Review -E arly Release -S ubstructure Design	7	30-Nov-23	08-Dec-23	Cal01-5d/8hr/12hol											
ContractNo_2000	Submit Early Release -S ubstructure Design	4	11-Dec-23	14-Dec-23	Cal01-5d/8hr/12hol											
ContractNo_2070	Review & Approve Early Release -S ubstructure Design	30	15-Dec-23	13-Jan-24	Cal03A -7 d/8hr/No Holiday:											
ContractNo_1790	Comment Resolution & Reissue Early Release -S ubstructure Design	10	16-Jan-24	29-Jan-24	Cal01-5d/8hr/12hol											
Structural Steel																
ContractNo_1760	Prepare Early Release -S uperstructure Design	90	24-Jul-23	29-Nov-23	Cal01-5d/8hr/12hol											
ContractNo_1970	Schedule & Conduct OTS Review -E arly Release -S uperstructure Design	1	30-Nov-23	30-Nov-23	Cal01-5d/8hr/12hol											
ContractNo_1960	Submit Early Release -S uperstructure Design	1	01-Dec-23	01-Dec-23	Cal01-5d/8hr/12hol											
ContractNo_1770	Review & Approve Early Release -S uperstructure Design	30	02-Dec-23	31-Dec-23	Cal03A -7 d/8hr/No Holiday:											
ContractNo_2040	Comment Resolution & Reissue Early Release -S uperstructure Design	5	02-Jan-24	08-Jan-24	Cal01-5d/8hr/12hol											
ContractNo_1710	Prepare & Submit Structural Steel Shop Drawings	40	09-Jan-24	06-Mar-24	Cal01-5d/8hr/12hol											
ContractNo_1720	Review & Approve Structural Steel Shop Drawings	30	07-Mar-24	05-Apr-24	Cal03A -7 d/8hr/No Holiday:											
ContractNo_1730	Procure Structural Steel Stage 1	75	06-Apr-24	19-Jun-24	Cal03A -7 d/8hr/No Holiday:											
ContractNo_1800	Procure Structural Steel Stage 2	120	20-Jun-24	17-Oct-24	Cal03A -7 d/8hr/No Holiday:											
Bridge Bearings Design																
ContractNo_1830	Prepare & Submit Early Release Bridge Bearings	20	09-Jan-24	06-Feb-24	Cal01-5d/8hr/12hol											
ContractNo_1840	Review & Approve Early Release Bridge Bearings	30	07-Feb-24	07-Mar-24	Cal03A -7 d/8hr/No Holiday:											
Bridge Scuppers Design																

■ Remaining Level of Effort ◆ Milestone
■ Actual Level of Effort
■ Actual Work
■ Remaining Work
■ Critical Remaining Work

Layout = CST01-Baseline-All, Filter = TASK filter: All Activities
 Data Date = 01-Jan-23, Run Date = 27-Jul-23, 09:50
 Project Start = 01-Jan-23 Project Finish = 08-Jul-25

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	Start	Finish	Calendar	2023				2024				2025		
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
ContractNo_1850	Prepare & Submit Bridge Scupper Design	45	09-Jan-24	13-Mar-24	Cal01-5d/8hr/12hol						Prepare & Submit Bridge Scupper Design					
ContractNo_1860	Review & Approve Bridge Scupper Design	30	14-Mar-24	12-Apr-24	Cal03A -7 d/8hr/No Holiday:						Review & Approve Bridge Scupper Design					
Bridge Joint Design																
ContractNo_1870	Prepare & Submit Bridge Joint Design	45	09-Jan-24	13-Mar-24	Cal01-5d/8hr/12hol						Prepare & Submit Bridge Joint Design					
ContractNo_1880	Review & Approve Bridge Joint Design	30	14-Mar-24	12-Apr-24	Cal03A -7 d/8hr/No Holiday:						Review & Approve Bridge Joint Design					
Projectwide Submittals																
Project Schedule																
ContractNo_2080	Prepare & Submit Initial Baseline Project Schedule (Logic Only)	40	24-Jul-23	18-Sep-23	Cal01-5d/8hr/12hol						Prepare & Submit Initial Baseline Project Schedule (Logic Only)					
ContractNo_2090	Review & Comment on Initial Baseline Project Schedule (Logic Only)	30	19-Sep-23	18-Oct-23	Cal03A -7 d/8hr/No Holiday:						Review & Comment on Initial Baseline Project Schedule (Logic Only)					
ContractNo_2220	Prepare & Submit Baseline Schedule (Logic Only) (Rev 1)	15	19-Oct-23	08-Nov-23	Cal01-5d/8hr/12hol						Prepare & Submit Baseline Schedule (Logic Only) (Rev 1)					
ContractNo_2230	Review & Comment on Baseline Schedule (Logic Only) (Rev 1)	15	09-Nov-23	23-Nov-23	Cal03A -7 d/8hr/No Holiday:						Review & Comment on Baseline Schedule (Logic Only) (Rev 1)					
ContractNo_2620	Prepare & Submit Cost & Resource Loaded Baseline Schedule	15	24-Nov-23	14-Dec-23	Cal01-5d/8hr/12hol						Prepare & Submit Cost & Resource Loaded Baseline Schedule					
ContractNo_2630	Review & Approve Cost & Resource Loaded Baseline Schedule	21	15-Dec-23	04-Jan-24	Cal03A -7 d/8hr/No Holiday:						Review & Approve Cost & Resource Loaded Baseline Schedule					
Project Management Plan																
ContractNo_2100	Prepare & Submit Project Management Plan	30	24-Jul-23	01-Sep-23	Cal01-5d/8hr/12hol						Prepare & Submit Project Management Plan					
ContractNo_2110	Review & Approve Project Management Plan	30	02-Sep-23	01-Oct-23	Cal03A -7 d/8hr/No Holiday:						Review & Approve Project Management Plan					
Public Participation Plan																
ContractNo_2160	Setup Project Webpage	20	24-Jul-23	18-Aug-23	Cal01-5d/8hr/12hol						Setup Project Webpage					
ContractNo_2120	Prepare & Submit Public Participation Plan	30	24-Jul-23	01-Sep-23	Cal01-5d/8hr/12hol						Prepare & Submit Public Participation Plan					
ContractNo_2130	Review & Approve Public Participation Plan	30	02-Sep-23	01-Oct-23	Cal03A -7 d/8hr/No Holiday:						Review & Approve Public Participation Plan					
Health & Safety Plan																
ContractNo_2140	Prepare & Submit Health & Safety Plan	20	24-Jul-23	18-Aug-23	Cal01-5d/8hr/12hol						Prepare & Submit Health & Safety Plan					
ContractNo_2150	Review & Approve Health & Safety Plan	30	19-Aug-23	17-Sep-23	Cal03A -7 d/8hr/No Holiday:						Review & Approve Health & Safety Plan					
Environmental Submittals																
Groundwater & Soil Management Plan																
ContractNo_2520	Prepare & Submit Groundwater & Soil Management Plan	45	24-Jul-23	25-Sep-23	Cal01-5d/8hr/12hol						Prepare & Submit Groundwater & Soil Management Plan					
ContractNo_2530	Review & Approve Groundwater & Soil Management Plan	30	26-Sep-23	25-Oct-23	Cal03A -7 d/8hr/No Holiday:						Review & Approve Groundwater & Soil Management Plan					
Noise Control Plan																
ContractNo_2540	Prepare & Submit Noise Control Plan	30	24-Jul-23	01-Sep-23	Cal01-5d/8hr/12hol						Prepare & Submit Noise Control Plan					
ContractNo_2550	Review & Approve Noise Control Plan	30	02-Sep-23	01-Oct-23	Cal03A -7 d/8hr/No Holiday:						Review & Approve Noise Control Plan					
Dust Control Plan																
ContractNo_2560	Prepare & Submit Dust Control Plan	30	24-Jul-23	01-Sep-23	Cal01-5d/8hr/12hol						Prepare & Submit Dust Control Plan					
ContractNo_2570	Review & Approve Dust Control Plan	30	02-Sep-23	01-Oct-23	Cal03A -7 d/8hr/No Holiday:						Review & Approve Dust Control Plan					
Invasive Species Management Plan																
ContractNo_2600	Prepare & Submit Invasive Species Management Plan	40	24-Jul-23	18-Sep-23	Cal01-5d/8hr/12hol						Prepare & Submit Invasive Species Management Plan					
ContractNo_2610	Review & Approve Invasive Species Management Plan	30	19-Sep-23	18-Oct-23	Cal03A -7 d/8hr/No Holiday:						Review & Approve Invasive Species Management Plan					
Dredge Material Plan																
ContractNo_2580	Prepare & Submit Dredge Material Plan	90	24-Jul-23	29-Nov-23	Cal01-5d/8hr/12hol						Prepare & Submit Dredge Material Plan					
ContractNo_2590	Review & Approve Dredge Material Plan	30	30-Nov-23	29-Dec-23	Cal03A -7 d/8hr/No Holiday:						Review & Approve Dredge Material Plan					

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Layout = CST01-Baseline-All, Filter = TASK filter: All Activities
 Data Date = 01-Jan-23, Run Date = 27-Jul-23, 09:50
 Project Start = 01-Jan-23 Project Finish = 08-Jul-25

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	Start	Finish	Calendar	Gantt Chart											
						2023				2024				2025			
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Design Submittals																	
Formal Bridge Sketch Plan																	
ContractNo_1690	Prepare Formal Bridge Sketch Plan	35	24-Jul-23	11-Sep-23	Cal01-5d/8hr/12hol	■ Prepare Formal Bridge Sketch Plan											
ContractNo_1930	Schedule & Conduct OTS Review - Formal Bridge Sketch Plan	2	12-Sep-23	13-Sep-23	Cal01-5d/8hr/12hol	■ Schedule & Conduct OTS Review - Formal Bridge Sketch Plan											
ContractNo_1920	Submit Formal Bridge Sketch Plan	4	14-Sep-23	19-Sep-23	Cal01-5d/8hr/12hol	■ Submit Formal Bridge Sketch Plan											
ContractNo_2020	Review & Approve Formal Bridge Sketch Plan	30	20-Sep-23	19-Oct-23	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve Formal Bridge Sketch Plan											
ContractNo_1700	Comment Resolution & Reissue Formal Bridge Sketch Plan	10	20-Oct-23	02-Nov-23	Cal01-5d/8hr/12hol	■ Comment Resolution & Reissue Formal Bridge Sketch Plan											
First Structural Design - Bridge																	
ContractNo_2670	Prepare First Structural Bridge	37	20-Oct-23	12-Dec-23	Cal01-5d/8hr/12hol	■ Prepare First Structural Bridge											
ContractNo_2770	Schedule & Conduct OTS Review - First Structural Bridge	2	13-Dec-23	14-Dec-23	Cal01-5d/8hr/12hol	■ Schedule & Conduct OTS Review - First Structural Bridge											
ContractNo_2780	Finalize First Structural Bridge	2	15-Dec-23	18-Dec-23	Cal01-5d/8hr/12hol	■ Finalize First Structural Bridge											
ContractNo_2790	Formal QC Review First Structural Bridge	3	19-Dec-23	21-Dec-23	Cal01-5d/8hr/12hol	■ Formal QC Review First Structural Bridge											
ContractNo_2800	Submit First Structural Bridge	1	22-Dec-23	22-Dec-23	Cal01-5d/8hr/12hol	■ Submit First Structural Bridge											
ContractNo_2970	Review & Approve First Structural Bridge	30	23-Dec-23	21-Jan-24	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve First Structural Bridge											
ContractNo_2680	Comment Resolution & Reissue First Structural Bridge	10	22-Jan-24	02-Feb-24	Cal01-5d/8hr/12hol	■ Comment Resolution & Reissue First Structural Bridge											
Second Structural Design - Bridge																	
ContractNo_2710	Prepare Second Structural Bridge	5	05-Feb-24	09-Feb-24	Cal01-5d/8hr/12hol	■ Prepare Second Structural Bridge											
ContractNo_2850	Schedule & Conduct OTS Review - Second Structural Bridge	2	12-Feb-24	13-Feb-24	Cal01-5d/8hr/12hol	■ Schedule & Conduct OTS Review - Second Structural Bridge											
ContractNo_2860	Finalize Second Structural Bridge	2	14-Feb-24	15-Feb-24	Cal01-5d/8hr/12hol	■ Finalize Second Structural Bridge											
ContractNo_2870	Formal QC Review Second Structural Bridge	3	16-Feb-24	21-Feb-24	Cal01-5d/8hr/12hol	■ Formal QC Review Second Structural Bridge											
ContractNo_2880	Submit Second Structural Bridge	1	22-Feb-24	22-Feb-24	Cal01-5d/8hr/12hol	■ Submit Second Structural Bridge											
ContractNo_2990	Review & Approve Second Structural Bridge	30	23-Feb-24	23-Mar-24	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve Second Structural Bridge											
ContractNo_2720	Comment Resolution & Reissue Second Structural Bridge	10	25-Mar-24	05-Apr-24	Cal01-5d/8hr/12hol	■ Comment Resolution & Reissue Second Structural Bridge											
75% Design - Highway																	
ContractNo_2690	Prepare 75% Design - Highway	75	05-Feb-24	21-May-24	Cal01-5d/8hr/12hol	■ Prepare 75% Design - Highway											
ContractNo_2810	Schedule & Conduct OTS Review - 75% Design - Highway	2	22-May-24	23-May-24	Cal01-5d/8hr/12hol	■ Schedule & Conduct OTS Review - 75% Design - Highway											
ContractNo_2820	Finalize 75% Design - Highway	2	24-May-24	28-May-24	Cal01-5d/8hr/12hol	■ Finalize 75% Design - Highway											
ContractNo_2830	Formal QC Review 75% Design - Highway	3	29-May-24	31-May-24	Cal01-5d/8hr/12hol	■ Formal QC Review 75% Design - Highway											
ContractNo_2840	Submit 75% Design - Highway	1	03-Jun-24	03-Jun-24	Cal01-5d/8hr/12hol	■ Submit 75% Design - Highway											
ContractNo_2980	Review & Approve 75% Design - Highway	30	04-Jun-24	03-Jul-24	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve 75% Design - Highway											
ContractNo_2700	Comment Resolution & Reissue 75% Design - Highway	10	05-Jul-24	18-Jul-24	Cal01-5d/8hr/12hol	■ Comment Resolution & Reissue 75% Design - Highway											
ContractNo_3570	Submit 75% Design - Highway -R EV1 (15 Days if required)	0	19-Jul-24	19-Jul-24	Cal01-5d/8hr/12hol	■ Submit 75% Design - Highway -R EV1 (15 Days if required)											
ContractNo_3580	Review & Approve 75% Design - Highway -R EV-1 (30 Days if required)	0	19-Jul-24	19-Jul-24	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve 75% Design - Highway -R EV-1 (30 Days if required)											
100% Design - Highway																	
ContractNo_2750	Prepare 100% Design - Highway	20	19-Jul-24	15-Aug-24	Cal01-5d/8hr/12hol	■ Prepare 100% Design - Highway											
ContractNo_2890	Schedule & Conduct OTS Review - 100% Design - Highway	2	16-Aug-24	19-Aug-24	Cal01-5d/8hr/12hol	■ Schedule & Conduct OTS Review - 100% Design - Highway											
ContractNo_2900	Finalize 100% Design - Highway	2	20-Aug-24	21-Aug-24	Cal01-5d/8hr/12hol	■ Finalize 100% Design - Highway											

■ Remaining Level of Effort ◆ Milestone
■ Actual Level of Effort
■ Actual Work
■ Remaining Work
■ Critical Remaining Work

Layout = CST01-Baseline-All, Filter = TASK filter: All Activities
 Data Date = 01-Jan-23, Run Date = 27-Jul-23, 09:50
 Project Start = 01-Jan-23 Project Finish = 08-Jul-25

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	Start	Finish	Calendar	2023 2024 2025												
						2023				2024				2025				
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
ContractNo_2910	Formal QC Review 100% Design -H ighway	3	22-Aug-24	26-Aug-24	Cal01-5d/8hr/12hol													Formal QC Review:100% Design -H ighway
ContractNo_2920	Submit 100% Design -H ighway	1	27-Aug-24	27-Aug-24	Cal01-5d/8hr/12hol													Submit 100% Design -H ighway
ContractNo_3000	Review & Approve 100% Design -H ighway (MassDOT)	30	28-Aug-24	26-Sep-24	Cal03A -7 d/8hr/No Holiday:													Review & Approve:100% Design -H ighway (Mas
ContractNo_2760	Comment Resolution & Reissue 100% Design -H ighway	10	27-Sep-24	10-Oct-24	Cal01-5d/8hr/12hol													Comment Resolution & Reissue 100% Design
Final Design - Bridge & Highway																		
ContractNo_2730	Prepare "RFC" Final Design -B ridge & Highway	9	11-Oct-24	24-Oct-24	Cal01-5d/8hr/12hol													Prepare "RFC" Final Design -B ridge & Highw
ContractNo_2930	Schedule & Conduct OTS Review -R RFC" Final Design -B ridge & Highway	2	25-Oct-24	28-Oct-24	Cal01-5d/8hr/12hol													Schedule & Conduct OTS Review -R RFC" Fir
ContractNo_2940	Finalize "RFC" Final Design -B ridge & Highway	2	29-Oct-24	30-Oct-24	Cal01-5d/8hr/12hol													Finalize "RFC" Final Design -B ridge & Highw
ContractNo_2950	Formal QC Review "RFC" Final Design -B ridge & Highway	3	31-Oct-24	04-Nov-24	Cal01-5d/8hr/12hol													Formal QC Review "RFC" Final Design - Bric
ContractNo_2960	Submit "RFC" Final Design -B ridge & Highway	1	05-Nov-24	05-Nov-24	Cal01-5d/8hr/12hol													Submit "RFC" Final Design -B ridge & Highw
ContractNo_2740	Review & Approve "RFC" Final Design -B ridge & Highway (MassDOT)	30	06-Nov-24	05-Dec-24	Cal03A -7 d/8hr/No Holiday:													Review & Approve "RFC" Final Design -
Early Action Construction Submittals																		
RTTM																		
ContractNo_1470	Prepare & Submit RTTM System	20	24-Jul-23	18-Aug-23	Cal01-5d/8hr/12hol													Prepare & Submit RTTM System
ContractNo_1540	Review & Approve RTTM System	30	19-Aug-23	17-Sep-23	Cal03A -7 d/8hr/No Holiday:													Review & Approve RTTM System
ContractNo_1480	Comment Resolution & Reissue RTTM System	10	18-Sep-23	02-Oct-23	Cal01-5d/8hr/12hol													Comment Resolution & Reissue RTTM System
ContractNo_1490	Procure RTTM System	30	02-Oct-23	01-Nov-23	Cal03A -7 d/8hr/No Holiday:													Procure RTTM System
Quality Management Plan (QMP)																		
ContractNo_1040	Prepare & Submit Quality Management Plan	20	24-Jul-23	18-Aug-23	Cal01-5d/8hr/12hol													Prepare & Submit Quality Management Plan
ContractNo_1050	Review & Approve Quality Management Plan	30	19-Aug-23	17-Sep-23	Cal03A -7 d/8hr/No Holiday:													Review & Approve Quality Management Plan
Bathymetric Survey																		
ContractNo_1360	Schedule & Conduct Bathymetric Survey	7	24-Jul-23	01-Aug-23	Cal01-5d/8hr/12hol													Schedule & Conduct Bathymetric Survey
ContractNo_1370	Prepare & Submit Bathymetric Survey Report	10	02-Aug-23	15-Aug-23	Cal01-5d/8hr/12hol													Prepare & Submit Bathymetric Survey Report
Final Hydraulic & Scour Analysis Report																		
ContractNo_1380	Prepare & Submit Final Hydraulic & Scour Analysis Report	20	16-Aug-23	13-Sep-23	Cal01-5d/8hr/12hol													Prepare & Submit Final Hydraulic & Scour Analysis Report
Temporary Trestle Design																		
ContractNo_1390	Prepare & Submit Temporary Trestle Design	17	24-Jul-23	15-Aug-23	Cal01-5d/8hr/12hol													Prepare & Submit Temporary Trestle Design
ContractNo_1510	Review & Approve Temporary Trestle	30	16-Aug-23	14-Sep-23	Cal03A -7 d/8hr/No Holiday:													Review & Approve Temporary Trestle
ContractNo_1400	Comment Resolution & Reissue Temporary Trestle Design	10	15-Sep-23	29-Sep-23	Cal01-5d/8hr/12hol													Comment Resolution & Reissue Temporary Trestle Design
ContractNo_1410	Procure Temporary Trestle	20	29-Sep-23	19-Oct-23	Cal03A -7 d/8hr/No Holiday:													Procure Temporary Trestle
Support of Excavation Design																		
ContractNo_1610	Prepare & Submit Support of Excavation Design	30	24-Jul-23	01-Sep-23	Cal01-5d/8hr/12hol													Prepare & Submit Support of Excavation Design
ContractNo_1620	Review & Approve Support of Excavation Design	30	02-Sep-23	01-Oct-23	Cal03A -7 d/8hr/No Holiday:													Review & Approve Support of Excavation Design
ContractNo_1630	Comment Resolution & Reissue Support of Excavation Design	10	02-Oct-23	16-Oct-23	Cal01-5d/8hr/12hol													Comment Resolution & Reissue Support of Excavation Design
ContractNo_1500	Procure Support of Excavation	5	17-Oct-23	21-Oct-23	Cal03A -7 d/8hr/No Holiday:													Procure Support of Excavation
Existing Sewer Line Protection Plan																		
ContractNo_1420	Prepare & Submit Existing Sewer Line Protection Plan	19	24-Jul-23	17-Aug-23	Cal01-5d/8hr/12hol													Prepare & Submit Existing Sewer Line Protection Plan
ContractNo_1520	Review & Approve Existing Sewer Line Protection Plan	30	18-Aug-23	16-Sep-23	Cal03A -7 d/8hr/No Holiday:													Review & Approve Existing Sewer Line Protection Plan

■ Remaining Level of Effort
 ◆ Actual Level of Effort
 ■ Actual Work
 Remaining Work
 Critical Remaining Work
 ◆ Milestone

Layout = CST01-Baseline-All, Filter = TASK filter: All Activities
 Data Date = 01-Jan-23, Run Date = 27-Jul-23, 09:50
 Project Start = 01-Jan-23 Project Finish = 08-Jul-25
























Date	Revision	Checked	Approved






Activity ID	Activity Name	OD	Start	Finish	Calendar	Gantt Chart											
						2023				2024				2025			
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
ContractNo_1430	Comment Resolution & Reissue Existing Sewer Line Protection Plan	10	01-Sep-23	18-Sep-23	Cal01-5d/8hr/12hol	■ Comment Resolution & Reissue Existing Sewer Line Protection Plan											
ContractNo_1460	Conduct CCTV Inspection of Existing Sanitary Sewer & Submit Report	10	18-Sep-23	29-Sep-23	Cal01-5d/8hr/12hol	■ Conduct CCTV Inspection of Existing Sanitary Sewer & Submit Report											
Stormwater Management Plan																	
ContractNo_1440	Prepare & Submit Stormwater Management Plan	5	24-Jul-23	28-Jul-23	Cal01-5d/8hr/12hol	■ Prepare & Submit Stormwater Management Plan											
ContractNo_1560	Schedule & Conduct Over the Shoulder - Stormwater Management Plan	5	31-Jul-23	04-Aug-23	Cal01-5d/8hr/12hol	■ Schedule & Conduct Over the Shoulder - Stormwater Management Plan											
ContractNo_1530	Review & Approve Stormwater Management Plan	30	05-Aug-23	03-Sep-23	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve Stormwater Management Plan											
ContractNo_1450	Comment Resolution & Reissue Stormwater Management Plan	10	05-Sep-23	19-Sep-23	Cal01-5d/8hr/12hol	■ Comment Resolution & Reissue Stormwater Management Plan											
Geotechnical Instrumentation & Monitoring Plan																	
ContractNo_1580	Prepare & Submit Geotechnical Instrumentation & Monitoring Plan	20	24-Jul-23	18-Aug-23	Cal01-5d/8hr/12hol	■ Prepare & Submit Geotechnical Instrumentation & Monitoring Plan											
ContractNo_1590	Review & Approve Geotechnical Instrumentation & Monitoring Plan	30	19-Aug-23	17-Sep-23	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve Geotechnical Instrumentation & Monitoring Plan											
ContractNo_1600	Install Geotechnical & Monitoring Instrumentation	10	18-Sep-23	29-Sep-23	Cal01-5d/8hr/12hol	■ Install Geotechnical & Monitoring Instrumentation											
Quality Control Plans																	
Drilled Shaft Quality Control Plan																	
ContractNo_2400	Prepare & Submit Drilled Shaft Quality Control Plan	40	24-Jul-23	18-Sep-23	Cal01-5d/8hr/12hol	■ Prepare & Submit Drilled Shaft Quality Control Plan											
ContractNo_2410	Review & Approve Drilled Shaft Quality Control Plan	30	19-Sep-23	18-Oct-23	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve Drilled Shaft Quality Control Plan											
Deck Membrane Waterproofing																	
ContractNo_2420	Prepare & Submit Deck Membrane Waterproofing Quality Control Plan	40	24-Jul-23	18-Sep-23	Cal01-5d/8hr/12hol	■ Prepare & Submit Deck Membrane Waterproofing Quality Control Plan											
ContractNo_2430	Review & Approve Deck Membrane Waterproofing Quality Control Plan	30	19-Sep-23	18-Oct-23	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve Deck Membrane Waterproofing Quality Control Plan											
Earthwork																	
ContractNo_2440	Prepare & Submit Earthwork Quality Control Plan	40	24-Jul-23	18-Sep-23	Cal01-5d/8hr/12hol	■ Prepare & Submit Earthwork Quality Control Plan											
ContractNo_2450	Review & Approve Earthwork Quality Control Plan	30	19-Sep-23	18-Oct-23	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve Earthwork Quality Control Plan											
HMA Pavement																	
ContractNo_2460	Prepare & Submit HMA Pavement Quality Control Plan	40	24-Jul-23	18-Sep-23	Cal01-5d/8hr/12hol	■ Prepare & Submit HMA Pavement Quality Control Plan											
ContractNo_2470	Review & Approve HMA Pavement Quality Control Plan	30	19-Sep-23	18-Oct-23	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve HMA Pavement Quality Control Plan											
Portland Cement Concrete - Cast in Place Elements																	
ContractNo_2480	Prepare & Submit Portland Cement Concrete - Cast in Place Elements Quality Control Plan	40	24-Jul-23	18-Sep-23	Cal01-5d/8hr/12hol	■ Prepare & Submit Portland Cement Concrete - Cast in Place Elements Quality Control Plan											
ContractNo_2490	Review & Approve Portland Cement Concrete - Cast in Place Elements Quality Control Plan	30	19-Sep-23	18-Oct-23	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve Portland Cement Concrete - Cast in Place Elements Quality Control Plan											
Structural Steel Element																	
ContractNo_2500	Prepare & Submit Structural Steel Element Quality Control Plan	40	24-Jul-23	18-Sep-23	Cal01-5d/8hr/12hol	■ Prepare & Submit Structural Steel Element Quality Control Plan											
ContractNo_2510	Review & Approve Structural Steel Element Quality Control Plan	30	19-Sep-23	18-Oct-23	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve Structural Steel Element Quality Control Plan											
Construction Submittals																	
Traffic Management Plan (TTCP)																	
ContractNo_1900	Prepare Traffic Management Plan (Stage 1)	35	24-Jul-23	11-Sep-23	Cal01-5d/8hr/12hol	■ Prepare Traffic Management Plan (Stage 1)											
ContractNo_1910	Schedule & Conduct OTS Review - Traffic Management Plan (Stage 1)	2	12-Sep-23	13-Sep-23	Cal01-5d/8hr/12hol	■ Schedule & Conduct OTS Review - Traffic Management Plan (Stage 1)											
ContractNo_1810	Submit Traffic Management Plan (Stage 1)	4	14-Sep-23	19-Sep-23	Cal01-5d/8hr/12hol	■ Submit Traffic Management Plan (Stage 1)											
ContractNo_2030	Review & Approve Traffic Management Plan (Stage 1)	30	20-Sep-23	19-Oct-23	Cal03A -7 d/8hr/No Holiday:	■ Review & Approve Traffic Management Plan (Stage 1)											
ContractNo_1820	Comment Resolution & Reissue Traffic Management Plan	10	20-Oct-23	02-Nov-23	Cal01-5d/8hr/12hol	■ Comment Resolution & Reissue Traffic Management Plan											
Existing Bridge Monitoring Plan																	
ContractNo_2210	Prepare & Submit Existing Bridge Monitoring Plan	20	24-Jul-23	18-Aug-23	Cal01-5d/8hr/12hol	■ Prepare & Submit Existing Bridge Monitoring Plan											

■ Remaining Level of Effort ◆ Milestone
■ Actual Level of Effort
■ Actual Work
■ Remaining Work
■ Critical Remaining Work

Layout = CST01-Baseline-All, Filter = TASK filter: All Activities
 Data Date = 01-Jan-23, Run Date = 27-Jul-23, 09:50
 Project Start = 01-Jan-23 Project Finish = 08-Jul-25

Date	Revision	Checked	Approved






Activity ID	Activity Name	OD	Start	Finish	Calendar	Timeline											
						2023				2024				2025			
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
Dewatering Plan																	
ContractNo_2380	Prepare & Submit Dewatering Plan	50	24-Jul-23	02-Oct-23	Cal01-5d/8hr/12hol	 Prepare & Submit Dewatering Plan											
ContractNo_2390	Review & Approve Dewatering Plan	30	03-Oct-23	01-Nov-23	Cal03A -7 d/8hr/No Holiday:	 Review & Approve Dewatering Plan											
Demolition Plan - NB																	
ContractNo_2170	Prepare & Submit Demolition Plan	90	24-Jul-23	29-Nov-23	Cal01-5d/8hr/12hol	 Prepare & Submit Demolition Plan											
ContractNo_2180	Review & Approve Demolition Plan	30	30-Nov-23	29-Dec-23	Cal03A -7 d/8hr/No Holiday:	 Review & Approve Demolition Plan											
Drilled Shaft Installation/Testing Procedure																	
ContractNo_2240	Prepare & Submit Drilled Shaft Installation/Testing Procedure	70	24-Jul-23	31-Oct-23	Cal01-5d/8hr/12hol	 Prepare & Submit Drilled Shaft Installation/Testing Procedure											
ContractNo_2250	Review & Approve Drilled Shaft Installation/Testing Procedure	30	01-Nov-23	30-Nov-23	Cal03A -7 d/8hr/No Holiday:	 Review & Approve Drilled Shaft Installation/Testing Procedure											
Abutment Pile Installation Plan																	
ContractNo_2260	Prepare & Submit Abutment Pile Installation Plan	40	24-Jul-23	18-Sep-23	Cal01-5d/8hr/12hol	 Prepare & Submit Abutment Pile Installation Plan											
ContractNo_2270	Review & Approve Abutment Pile Installation Plan	30	19-Sep-23	18-Oct-23	Cal03A -7 d/8hr/No Holiday:	 Review & Approve Abutment Pile Installation Plan											
Erection Plan - Stage 1																	
ContractNo_2190	Prepare & Submit Erection Plan - Stage 1	60	24-Jul-23	17-Oct-23	Cal01-5d/8hr/12hol	 Prepare & Submit Erection Plan - Stage 1											
ContractNo_2200	Review & Approve Erection Plan - Stage 1	30	18-Oct-23	16-Nov-23	Cal03A -7 d/8hr/No Holiday:	 Review & Approve Erection Plan - Stage 1											
Erection Plan - Stage 2																	
ContractNo_2280	Prepare & Submit Erection Plan - Stage 2	60	17-Nov-23	14-Feb-24	Cal01-5d/8hr/12hol	 Prepare & Submit Erection Plan - Stage 2											
ContractNo_2290	Review & Approve Erection Plan - Stage 2	30	15-Feb-24	15-Mar-24	Cal03A -7 d/8hr/No Holiday:	 Review & Approve Erection Plan - Stage 2											
Erection Plan - Stage 3																	
ContractNo_2300	Prepare & Submit Erection Plan - Stage 3	60	24-Jul-23	17-Oct-23	Cal01-5d/8hr/12hol	 Prepare & Submit Erection Plan - Stage 3											
ContractNo_2310	Review & Approve Erection Plan - Stage 3	30	18-Oct-23	16-Nov-23	Cal03A -7 d/8hr/No Holiday:	 Review & Approve Erection Plan - Stage 3											
Deck Placement Plan																	
ContractNo_2320	Prepare & Submit Deck Placement Plan	90	24-Jul-23	29-Nov-23	Cal01-5d/8hr/12hol	 Prepare & Submit Deck Placement Plan											
ContractNo_2330	Review & Approve Deck Placement Plan	30	30-Nov-23	29-Dec-23	Cal03A -7 d/8hr/No Holiday:	 Review & Approve Deck Placement Plan											
Solid Pier Wall Construction Plan																	
ContractNo_2340	Prepare & Submit Solid Pier Wall Construction Plan	60	24-Jul-23	17-Oct-23	Cal01-5d/8hr/12hol	 Prepare & Submit Solid Pier Wall Construction Plan											
ContractNo_2350	Review & Approve Solid Pier Wall Construction Plan	30	18-Oct-23	16-Nov-23	Cal03A -7 d/8hr/No Holiday:	 Review & Approve Solid Pier Wall Construction Plan											
Formwork Plan																	
ContractNo_2360	Prepare & Submit Formwork Plan	60	24-Jul-23	17-Oct-23	Cal01-5d/8hr/12hol	 Prepare & Submit Formwork Plan											
ContractNo_2370	Review & Approve Formwork Plan	30	18-Oct-23	16-Nov-23	Cal03A -7 d/8hr/No Holiday:	 Review & Approve Formwork Plan											
Subcontractor Approvals																	
Licensed Site Professional																	
Structure Cleaning Subcontractor																	
Electrical Subcontractor																	
Bridge Demolition Subcontractor																	
Shop Drawings and Procurements																	
Superstructure Rebar Design																	
ContractNo_3040	Prepare & Submit Early Release Superstructure Rebar Design	45	24-Jul-23	25-Sep-23	Cal01-5d/8hr/12hol	 Prepare & Submit Early Release Superstructure Rebar Design											
ContractNo_3050	Review & Approve Early Release Superstructure Rebar Design	30	26-Sep-23	25-Oct-23	Cal03A -7 d/8hr/No Holiday:	 Review & Approve Early Release Superstructure Rebar Design											
Abutment Rebar																	
ContractNo_3010	Prepare & Submit Substructure Rebar Shop Drawings	20	24-Jul-23	18-Aug-23	Cal01-5d/8hr/12hol	 Prepare & Submit Substructure Rebar Shop Drawings											

 Remaining Level of Effort ◆ ◆ Milestone
 Actual Level of Effort
 Actual Work
 Remaining Work
 Critical Remaining Work

Layout = CST01-Baseline-All, Filter = TASK filter: All Activities
 Data Date = 01-Jan-23, Run Date = 27-Jul-23, 09:50
 Project Start = 01-Jan-23 Project Finish = 08-Jul-25

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	Start	Finish	Calendar	2023												2024				2025										
						Q1				Q2				Q3				Q4				Q1				Q2				Q3		
ContractNo_3020	Review & Approve Substructure Rebar Shop Drawings	30	19-Aug-23	17-Sep-23	Cal03A -7 d/8hr/No Holiday:																											
ContractNo_3030	Procure Substructure Rebar	30	18-Sep-23	17-Oct-23	Cal03A -7 d/8hr/No Holiday:																											
Drilled Shaft Rebar																																
ContractNo_3510	Prepare & Submit Drilled Shaft Rebar Shop Drawings	20	24-Jul-23	18-Aug-23	Cal01-5d/8hr/12hol																											
ContractNo_3520	Review & Approve Drilled Shaft Rebar Shop Drawings	30	19-Aug-23	17-Sep-23	Cal03A -7 d/8hr/No Holiday:																											
ContractNo_3530	Procure Drilled Shaft Rebar	30	18-Sep-23	17-Oct-23	Cal03A -7 d/8hr/No Holiday:																											
Pier Substructure Rebar																																
ContractNo_3540	Prepare & Submit Pier Substructure Rebar Shop Drawings	20	24-Jul-23	18-Aug-23	Cal01-5d/8hr/12hol																											
ContractNo_3550	Review & Approve Pier Substructure Rebar Shop Drawings	30	19-Aug-23	17-Sep-23	Cal03A -7 d/8hr/No Holiday:																											
ContractNo_3560	Procure Pier Substructure Rebar	45	18-Sep-23	01-Nov-23	Cal03A -7 d/8hr/No Holiday:																											
Stay in Place Formwork																																
ContractNo_3330	Prepare & Submit Stay in Place Formwork	20	24-Jul-23	18-Aug-23	Cal01-5d/8hr/12hol																											
ContractNo_3340	Review & Approve Stay in Place Formwork	30	19-Aug-23	17-Sep-23	Cal03A -7 d/8hr/No Holiday:																											
ContractNo_3350	Procure Stay in Place Formwork	60	18-Sep-23	16-Nov-23	Cal03A -7 d/8hr/No Holiday:																											
Solid Pier Wall (Pier Bases) Design & Shop Drawings																																
ContractNo_3130	Prepare & Submit Solid Pier Wall (Pier Bases) Design	60	24-Jul-23	17-Oct-23	Cal01-5d/8hr/12hol																											
ContractNo_3140	Review & Approve Solid Pier Wall (Pier Bases) Design	30	18-Oct-23	16-Nov-23	Cal03A -7 d/8hr/No Holiday:																											
ContractNo_3070	Prepare & Submit Solid Pier Wall (Pier Bases) Shop Drawings	20	17-Nov-23	15-Dec-23	Cal01-5d/8hr/12hol																											
ContractNo_3080	Review & Approve Solid Pier Wall Shop Drawings	30	16-Dec-23	14-Jan-24	Cal03A -7 d/8hr/No Holiday:																											
ContractNo_3090	Procure Solid Pier Wall Material	70	15-Jan-24	24-Mar-24	Cal03A -7 d/8hr/No Holiday:																											
Drainage Structures																																
ContractNo_3100	Prepare & Submit Drainage Structures	20	24-Jul-23	18-Aug-23	Cal01-5d/8hr/12hol																											
ContractNo_3110	Review & Approve Drainage Structures	30	19-Aug-23	17-Sep-23	Cal03A -7 d/8hr/No Holiday:																											
ContractNo_3120	Procure Drainage Structures	25	18-Sep-23	12-Oct-23	Cal03A -7 d/8hr/No Holiday:																											
TL-5 Pier Protection Barrier																																
ContractNo_3160	Prepare & Submit TL-5 Pier Protection Barrier	20	24-Jul-23	18-Aug-23	Cal01-5d/8hr/12hol																											
ContractNo_3170	Review & Approve TL-5 Pier Protection Barrier	30	19-Aug-23	17-Sep-23	Cal03A -7 d/8hr/No Holiday:																											
ContractNo_3180	Procure TL-5 Pier Protection Barrier	35	18-Sep-23	22-Oct-23	Cal03A -7 d/8hr/No Holiday:																											
Bridge Bearings																																
ContractNo_3220	Prepare & Submit Bridge Bearings Shop Drawings	30	24-Jul-23	01-Sep-23	Cal01-5d/8hr/12hol																											
ContractNo_3230	Review & Approve Bridge Bearings Shop Drawings	30	02-Sep-23	01-Oct-23	Cal03A -7 d/8hr/No Holiday:																											
ContractNo_3190	Procure Bridge Bearings	60	02-Oct-23	30-Nov-23	Cal03A -7 d/8hr/No Holiday:																											
Superstructure Rebar																																
ContractNo_3360	Prepare & Submit Superstructure Rebar Shop Drawings	30	26-Oct-23	07-Dec-23	Cal01-5d/8hr/12hol																											
ContractNo_3370	Review & Approve Superstructure Rebar Shop Drawings	30	08-Dec-23	06-Jan-24	Cal03A -7 d/8hr/No Holiday:																											
ContractNo_3060	Procure Superstructure Rebar	60	07-Jan-24	06-Mar-24	Cal03A -7 d/8hr/No Holiday:																											
Bridge Scuppers																																
ContractNo_3380	Prepare & Submit Bridge Scupper Shop Drawings	30	24-Jul-23	01-Sep-23	Cal01-5d/8hr/12hol																											

 Remaining Level of Effort ◆ ◆ Milestone
 Actual Level of Effort
 Actual Work
 Remaining Work
 Critical Remaining Work

Layout = CST01-Baseline-All, Filter = TASK filter: All Activities
 Data Date = 01-Jan-23, Run Date = 27-Jul-23, 09:50
 Project Start = 01-Jan-23 Project Finish = 08-Jul-25

Date	Revision	Checked	Approved

Prepared by MassDOT Highway

Activity ID	Activity Name	OD	Start	Finish	Calendar	Gantt Chart																	
						2023				2024				2025									
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4						
ContractNo_3390	Review & Approve Bridge Scupper Shop Drawings	30	02-Sep-23	01-Oct-23	Cal03A -7 d/8hr/No Holiday:																		
ContractNo_3200	Procure/Fabricate Bridge Scuppers	60	02-Oct-23	30-Nov-23	Cal03A -7 d/8hr/No Holiday:																		
Bridge Joint																							
ContractNo_3400	Prepare & Submit Bridge Shop Drawings	30	24-Jul-23	01-Sep-23	Cal01-5d/8hr/12hol																		
ContractNo_3410	Review & Approve Bridge Joint Design	30	02-Sep-23	01-Oct-23	Cal03A -7 d/8hr/No Holiday:																		
ContractNo_3210	Procure/Fabricate Bridge Joint	60	02-Oct-23	30-Nov-23	Cal03A -7 d/8hr/No Holiday:																		
Early Action Permit Plan Changes																							
National Marine Fishery Service (NMFS)																							
ContractNo_1300	Prepare & Submit Revised Section 7 Letter	25	24-Jul-23	25-Aug-23	Cal01-5d/8hr/12hol																		
ContractNo_1310	Review & Approve Revised Section 7 Letter	30	26-Aug-23	24-Sep-23	Cal03A -7 d/8hr/No Holiday:																		
ContractNo_1330	Comment Resolution & Reissue Revised Section 7 Letter	5	25-Sep-23	29-Sep-23	Cal01-5d/8hr/12hol																		
ContractNo_1320	NMFS -R eview & Approve Revised Section 7 Letter	30	30-Sep-23	29-Oct-23	Cal03A -7 d/8hr/No Holiday:																		
Water Quality Certification Permit Plan Changes																							
ContractNo_1220	Prepare & Submit WQC Permit Plan Changes	20	24-Jul-23	18-Aug-23	Cal01-5d/8hr/12hol																		
ContractNo_1240	Review & Approve WQC Permit Plan Changes	30	19-Aug-23	17-Sep-23	Cal03A -7 d/8hr/No Holiday:																		
ContractNo_1280	Comment Resolution & Reissue WQC Permit Plan Changes	5	18-Sep-23	22-Sep-23	Cal01-5d/8hr/12hol																		
ContractNo_1260	MassDEP -R eview & Approve WQC Permit Plan Changes	30	22-Sep-23	22-Oct-23	Cal04-7d/24Hr/No Hol (Mile																		
ContractNo_1340	MassDEP -is sue WQC Permit Plan Changes	1	30-Oct-23	30-Oct-23	Cal01-5d/8hr/12hol																		
Army Corp of Engineers Permit Plan Changes																							
ContractNo_1230	Prepare & Submit ACOE Permit Plan Changes	17	24-Jul-23	15-Aug-23	Cal01-5d/8hr/12hol																		
ContractNo_1250	Review & Approve ACOE Permit Plan Changes	30	16-Aug-23	14-Sep-23	Cal03A -7 d/8hr/No Holiday:																		
ContractNo_1290	Comment Resolution & Reissue ACOE Permit Plan Changes	5	15-Sep-23	21-Sep-23	Cal01-5d/8hr/12hol																		
ContractNo_1270	ACOE -R eview & Approve ACOE Permit Plan Changes	30	21-Sep-23	21-Oct-23	Cal04-7d/24Hr/No Hol (Mile																		
ContractNo_1350	ACOE -is sue ACOE Permit Plan Changes	1	30-Oct-23	30-Oct-23	Cal01-5d/8hr/12hol																		
Utility																							
Utility Relocation & Coordination Plan																							
ContractNo_P250	Prepare & Submit -E arly Utilitiy Relocation Request\Coordination Plan	14	02-Aug-23	15-Aug-23	Cal03A -7 d/8hr/No Holiday:																		
ContractNo_P260	Review & Approve -E arly Utilitiy Relocation Request\Coordination Plan	7	16-Aug-23	22-Aug-23	Cal03A -7 d/8hr/No Holiday:																		
Utility Notifications & Meetings																							
ContractNo_U100	Coordinate/Mobilization Period -R elocation w/ Utility Company -[i nsert Utility 1 Name]	30	23-Aug-23	21-Sep-23	Cal03A -7 d/8hr/No Holiday:																		
ContractNo_U350	Coordinate/Mobilization Period -R elocation w/ Utility Company -[i nsert Utility 2 Name]	30	23-Aug-23	21-Sep-23	Cal03A -7 d/8hr/No Holiday:																		
ContractNo_U360	Coordinate/Mobilization Period -R elocation w/ Utility Company -[i nsert Utility 3 Name]	30	23-Aug-23	21-Sep-23	Cal03A -7 d/8hr/No Holiday:																		
ContractNo_U370	Coordinate/Mobilization Period -R elocation w/ Utility Company -[i nsert Utility 4 Name]	30	23-Aug-23	21-Sep-23	Cal03A -7 d/8hr/No Holiday:																		
Utility Relocation																							
Utility 1 PUC Tasks																							
ContractNo_U340	Utility 1 Task 1: Copy Activity Name from PUC Form	20	15-Nov-23	14-Dec-23	Cal01-5d/8hr/12hol																		
ContractNo_U120	Utility 1 Task 2: Copy Activity Name from PUC Form	5	14-Dec-23	21-Dec-23	Cal01-5d/8hr/12hol																		
Utility 2 PUC Tasks																							

Remaining Level of Effort ◆ Milestone
 Actual Level of Effort
 Actual Work
 Remaining Work
 Critical Remaining Work

Layout = CST01-Baseline-All, Filter = TASK filter: All Activities
 Data Date = 01-Jan-23, Run Date = 27-Jul-23, 09:50
 Project Start = 01-Jan-23 Project Finish = 08-Jul-25

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	Start	Finish	Calendar	Timeline															
						2023				2024				2025							
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4				
ContractNo_CAL11	Cal11-Winter Shut 5D/8Hr, 12Hol	100	16-Mar-23	08-Aug-23	Cal11-Wntr Shut 5d/12hol																
ContractNo_CAL14	Cal14-Planting, 5D/12Hol - Deciduous	100	21-Mar-23	28-Nov-23	Cal14-Planting 5d/12hol - D																
ContractNo_CAL12	Cal12-Paving, 5D/12 Hol	100	03-Apr-23	24-Aug-23	Cal12-Paving 5d/12hol																
ContractNo_CAL17	Cal17 - Reclamation - 5d/12hol	100	18-Apr-23	08-Sep-23	Cal17 - Reclamation - 5d/1																
ContractNo_CAL13	Cal13-Planting, 5D/12Hol - Evergreen	100	18-Apr-23	23-May-24	Cal13-Planting 5d/12hol - E																
ContractNo_CAL15	Cal15-Water Access1, 5D/12Hol	100	01-Jun-23	25-Jun-24	Cal15-Wtr Acc 1-5d/12hol																
Deleted Activities																					

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Layout = CST01-Baseline-All, Filter = TASK filter: All Activities
 Data Date = 01-Jan-23, Run Date = 27-Jul-23, 09:50
 Project Start = 01-Jan-23 Project Finish = 08-Jul-25

Date	Revision	Checked	Approved

Prepared by MassDOT Highway
