


Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work

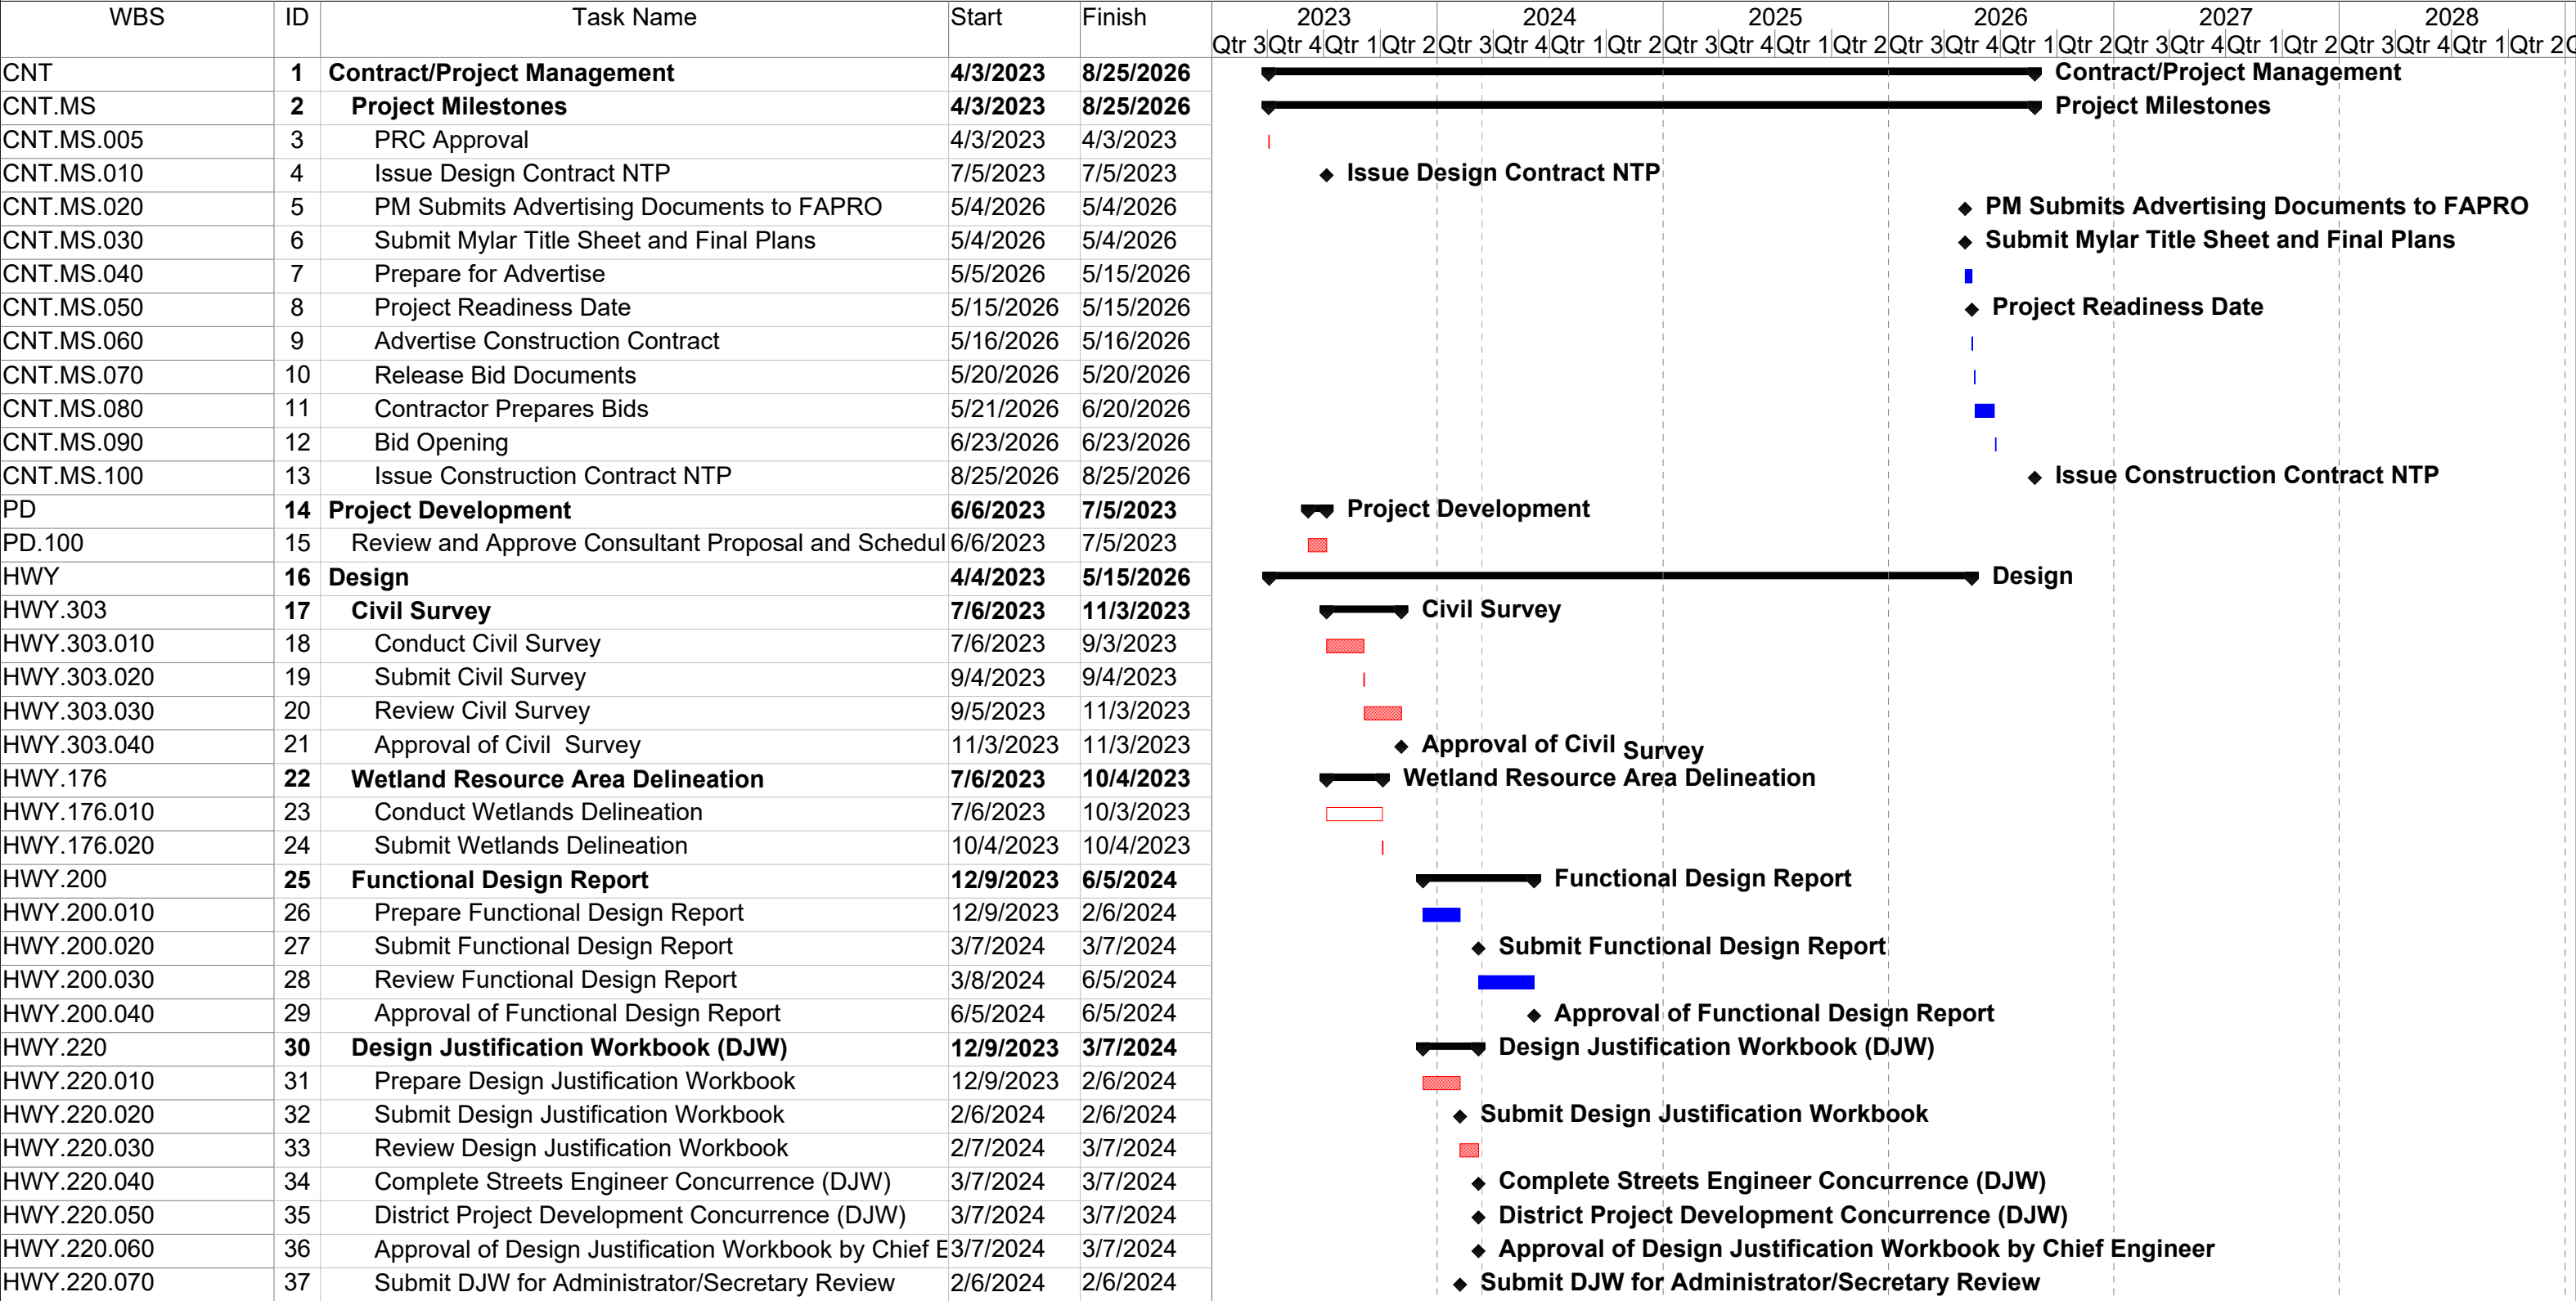

Task

Milestone

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

Massachusetts Department of Transportation

<MassDOT Project Info Number> <Short Project Description - City Names>

BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023				2024				2025				2026				2027				2028			
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2
HWY.220.080	38	Review of DJW by Administrator/Secretary	2/7/2024	3/7/2024																								
HWY.220.090	39	Approval of Design Justification Workbook by FHWA	3/7/2024	3/7/2024																								
HWY.220.100	40	Approval of Design Justification Workbook by Secretary	3/7/2024	3/7/2024																								
HWY.250	41	Pre-25% Design	4/4/2023	12/8/2023																								
HWY.250.010	42	Prepare and Submit Draft Project Scoping Checklist	4/4/2023	4/4/2023																								
HWY.250.020	43	Project Scoping Meeting	6/5/2023	6/5/2023																								
HWY.250.030	44	Prepare and Submit Final Project Scoping Checklist	6/6/2023	6/6/2023																								
HWY.250.040	45	Develop Reasonable Alternatives and Alternative Analysis	6/7/2023	7/6/2023																								
HWY.250.050	46	Prepare Pre-25% OTS Conceptual Design Package	7/7/2023	8/5/2023																								
HWY.250.060	47	Submit Pre-25% OTS Conceptual Design Package	10/5/2023	10/5/2023																								
HWY.250.070	48	Schedule Pre-25% OTS Review Meeting	10/6/2023	10/20/2023																								
HWY.250.080	49	Conduct Pre-25% OTS Review Meeting	10/23/2023	10/23/2023																								
HWY.250.090	50	Schedule Public Information Meeting	10/24/2023	12/7/2023																								
HWY.250.100	51	Conduct Public Information Meeting	12/8/2023	12/8/2023																								
HWY.275	52	Traffic and Safety	4/4/2023	8/7/2023																								
HWY.275.100	53	Intersection Control Evaluation (ICE)	4/4/2023	8/7/2023																								
HWY.275.100.44	54	Prepare ICE Stage 1	4/4/2023	4/5/2023																								
HWY.275.100.45	55	Submit ICE Stage 1	4/6/2023	4/6/2023																								
HWY.275.100.46	56	Review ICE Stage 1	4/7/2023	5/4/2023																								
HWY.275.100.47	57	Approve ICE Stage 1	5/5/2023	5/5/2023																								
HWY.275.100.48	58	Prepare ICE Stage 2	5/6/2023	6/4/2023																								
HWY.275.100.49	59	Submit ICE Stage 2	6/5/2023	6/5/2023																								
HWY.275.100.50	60	Review ICE Stage 2	6/6/2023	6/19/2023																								
HWY.275.100.51	61	Approve ICE Stage 2	6/20/2023	6/20/2023																								
HWY.275.100.52	62	Prepare ICE Stage 3	6/21/2023	7/20/2023																								
HWY.275.100.53	63	Submit ICE Stage 3	7/21/2023	7/21/2023																								
HWY.275.100.54	64	Review ICE Stage 3	7/22/2023	8/4/2023																								
HWY.275.100.55	65	Approve ICE Stage 3	8/7/2023	8/7/2023																								
HWY.275.200	66	Roadway Safety Audit (RSA)	4/4/2023	7/5/2023																								
HWY.275.200.56	67	Prepare RSA Background Materials	4/4/2023	6/2/2023																								
HWY.275.200.57	68	Conduct RSA	6/5/2023	6/5/2023																								
HWY.275.200.58	69	Prepare Draft RSA Report	6/6/2023	6/10/2023																								
HWY.275.200.59	70	Submit Draft RSA Report	6/12/2023	6/12/2023																								
HWY.275.200.60	71	Review Draft RSA Report	6/13/2023	6/17/2023																								
HWY.275.200.61	72	Prepare Final Draft RSA Report	6/18/2023	6/22/2023																								
HWY.275.200.62	73	Submit Final Draft RSA Report	6/23/2023	6/23/2023																								
HWY.275.200.63	74	Review Final Draft RSA Report	6/24/2023	6/28/2023																								

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

◆

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work



Task

Milestone

◆

Summary


Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work

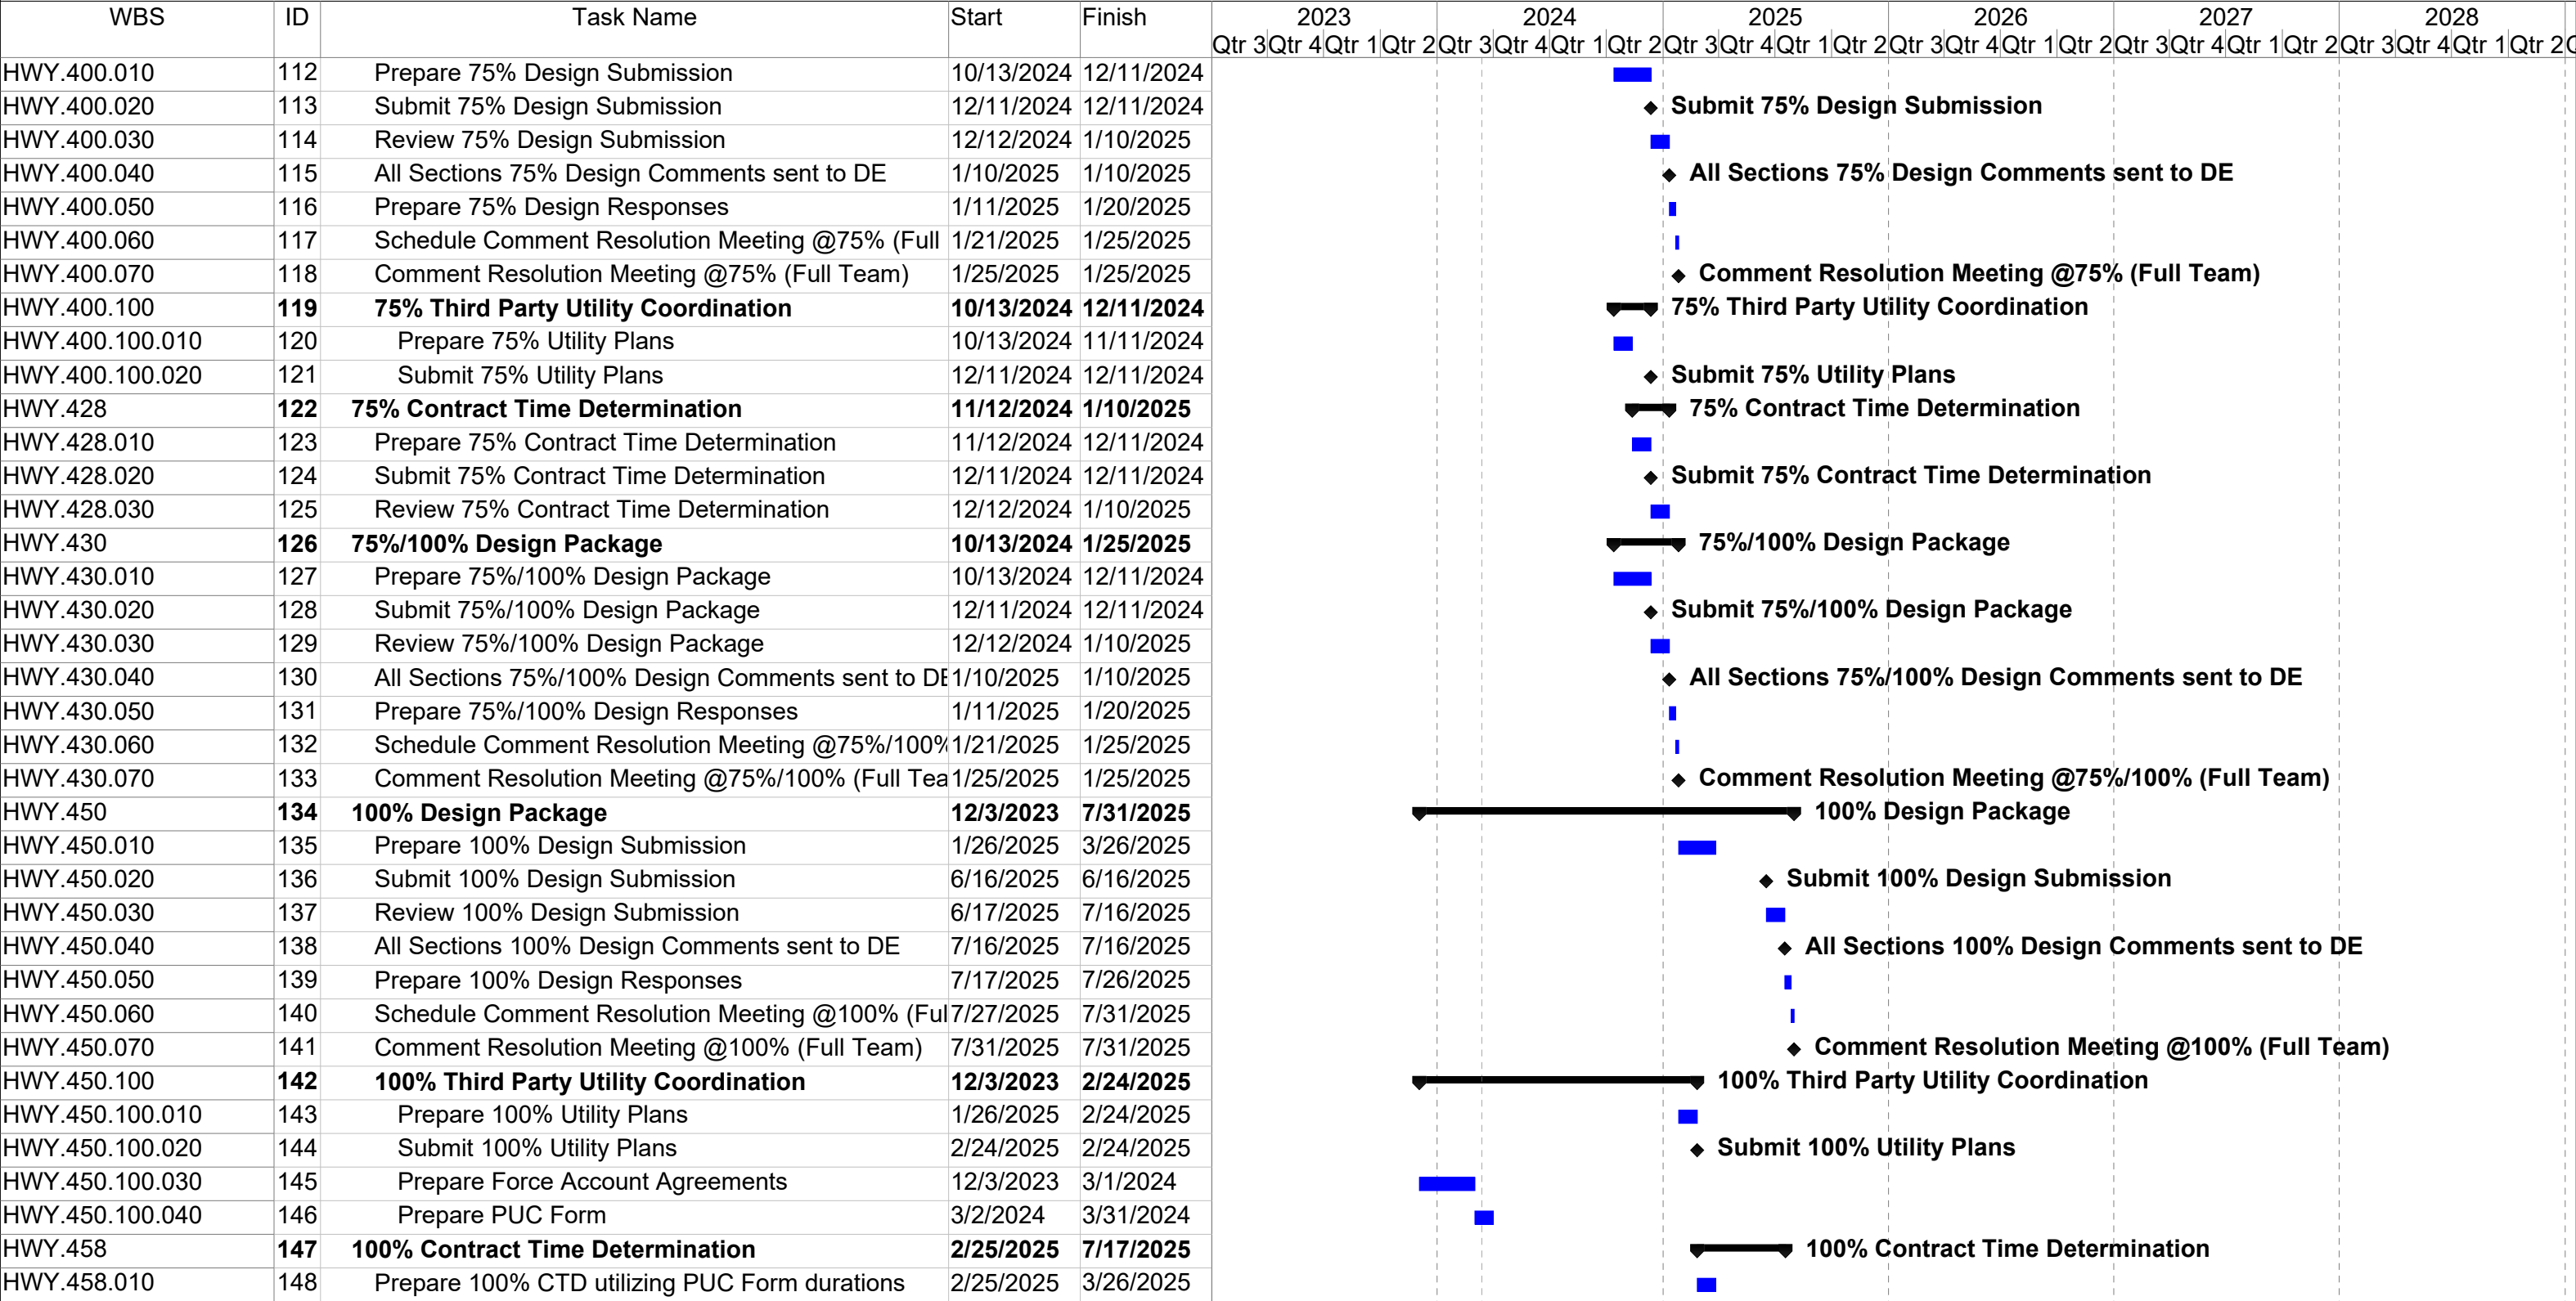

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

◆

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023				2024				2025				2026				2027				2028			
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2
HWY.458.020	149	Submit 100% Contract Time Determination	6/16/2025	6/16/2025																								
HWY.458.030	150	Review 100% Contract Time Determination	6/17/2025	7/16/2025																								
HWY.458.040	151	Request Construction Duration IOM from Area Engin	7/17/2025	7/17/2025																								
HWY.470	152	100%/PSE Design Package	1/26/2025	5/10/2025																								
HWY.470.010	153	Prepare 100%/PSE Design Package	1/26/2025	3/26/2025																								
HWY.470.020	154	Submit 100%/PSE Design Package	3/26/2025	3/26/2025																								
HWY.470.030	155	Review 100%/PSE Design Package	3/27/2025	4/25/2025																								
HWY.470.040	156	All Sections 100%/PSE Design Comments sent to DE	4/25/2025	4/25/2025																								
HWY.470.050	157	Prepare 100%/PSE Design Responses	4/26/2025	5/5/2025																								
HWY.470.060	158	Schedule Comment Resolution Meeting @100%/PSE	5/6/2025	5/10/2025																								
HWY.470.070	159	Comment Resolution Meeting @100%/PSE (Full Tea	5/10/2025	5/10/2025																								
HWY.800	160	PS&E Submittal	7/17/2025	5/15/2026																								
HWY.800.001	161	Request Federal Aid Number from FAPRO	7/17/2025	7/17/2025																								
HWY.800.002	162	FAPRO provides Federal Aid Number	7/18/2025	8/16/2025																								
HWY.800.010	163	Prepare PS&E Submission	8/1/2025	8/30/2025																								
HWY.800.020	164	Submit PS&E Submission	8/30/2025	8/30/2025																								
HWY.800.030	165	Review PS&E Submission	8/31/2025	9/14/2025																								
HWY.800.040	166	Send PS&E to FHWA (If Required)	9/1/2025	9/1/2025																								
HWY.800.050	167	FHWA Review PS&E Submission (If Required)	9/2/2025	10/1/2025																								
HWY.800.060	168	Approval of PS&E Submission	10/1/2025	10/1/2025																								
HWY.800.070	169	Prepare Advertising Documents for FAPRO	8/31/2025	9/10/2025																								
HWY.800.080	170	Review Advertising Documents by FAPRO	5/5/2026	5/15/2026																								
HWY.800.090	171	Prepare Draft Contract Documents for Specs	10/2/2025	10/15/2025																								
HWY.800.100	172	Submit Draft Contract Documents to Specs	10/22/2025	10/22/2025																								
HWY.800.110	173	Ready for Initial Review	10/23/2025	10/24/2025																								
HWY.800.120	174	Initial Review of Contract Documents By Specs	10/27/2025	11/5/2025																								
HWY.800.130	175	Prepare Bid Documents - Rev 1	11/6/2025	11/7/2025																								
HWY.800.140	176	Submit Bid Documents to Specs - Rev 1	11/7/2025	11/7/2025																								
HWY.800.150	177	Ready For Final Review	11/10/2025	11/11/2025																								
HWY.800.160	178	Final Review of Bid Documents	11/12/2025	11/14/2025																								
HWY.800.170	179	Prepare CDSP Bid Package	11/17/2025	11/21/2025																								
HWY.800.180	180	Prepare Final Plans for Plans and Records	10/2/2025	10/15/2025																								
HWY.800.190	181	Submit Final Plans for Plans and Records	10/16/2025	10/16/2025																								
HWY.800.200	182	Review Final Plans by Plans and Records	10/17/2025	10/30/2025																								
HWY.800.210	183	Approve Final Plans by Plans and Records	10/30/2025	10/30/2025																								
HWY.807	184	PS&E Contract Time Determination	8/1/2025	10/3/2025																								
HWY.807.010	185	Prepare PS&E CTD utilizing PUC Form durations	8/1/2025	8/15/2025																								

Task

Milestone

◆

Summary

Critical Path


Path Successor Normal Task

Path Successor Summary Task


Path Successor Milestone Task

◆

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work

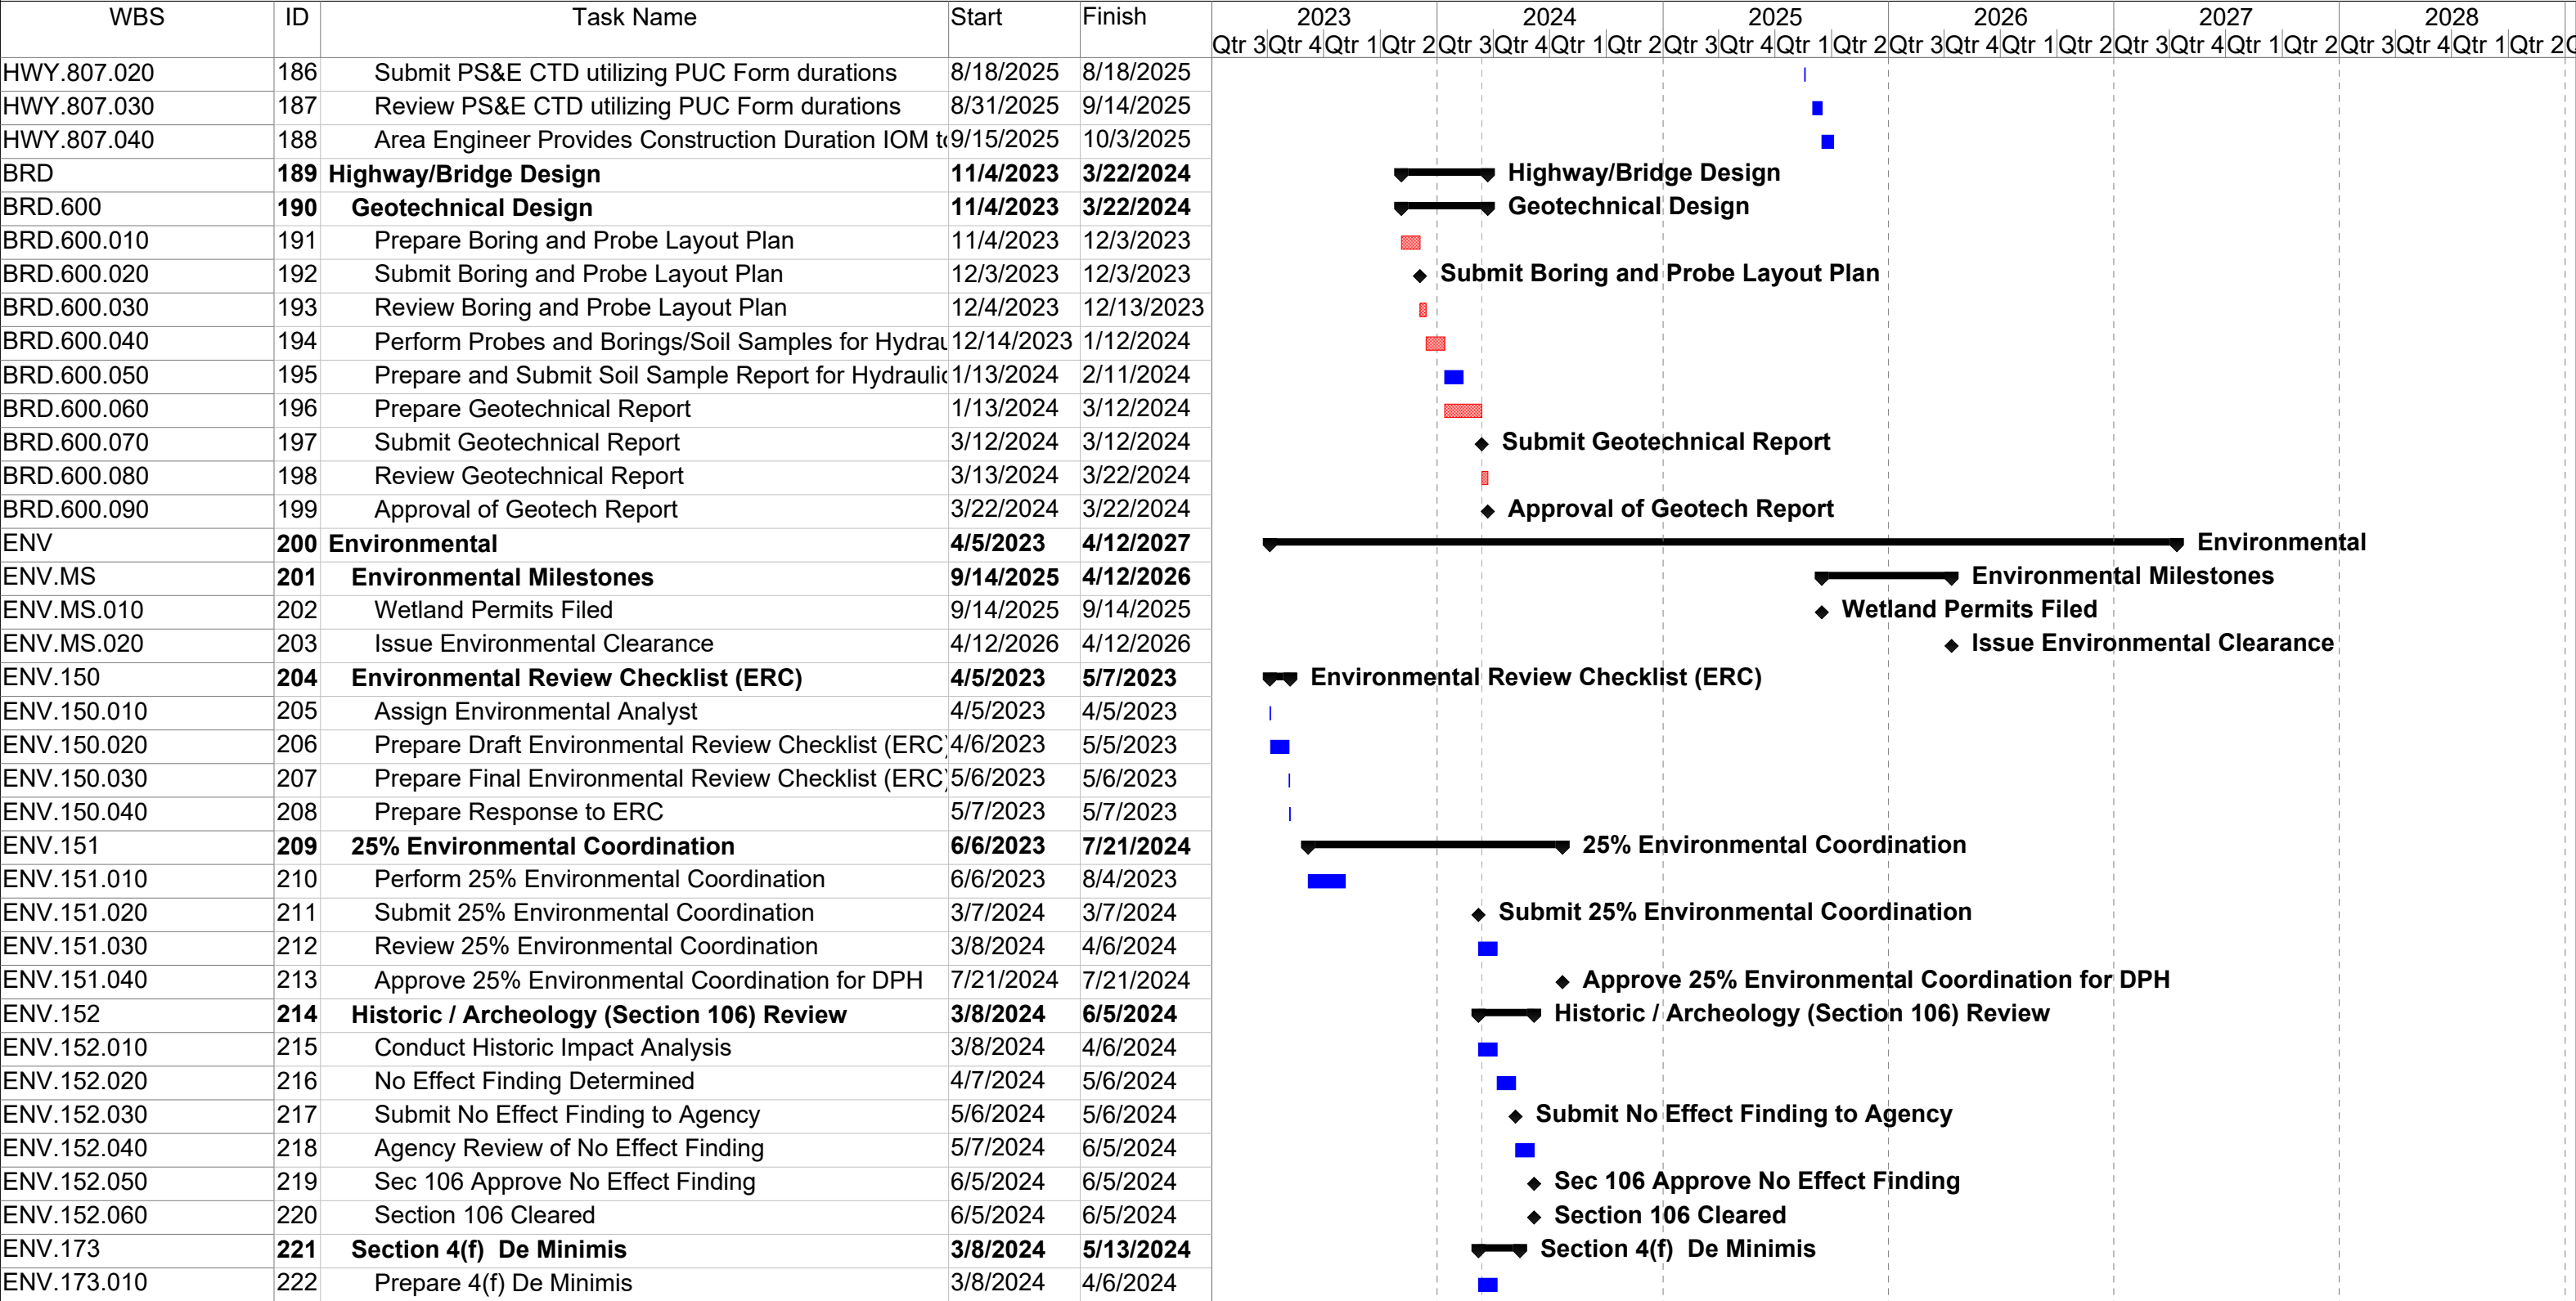

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work

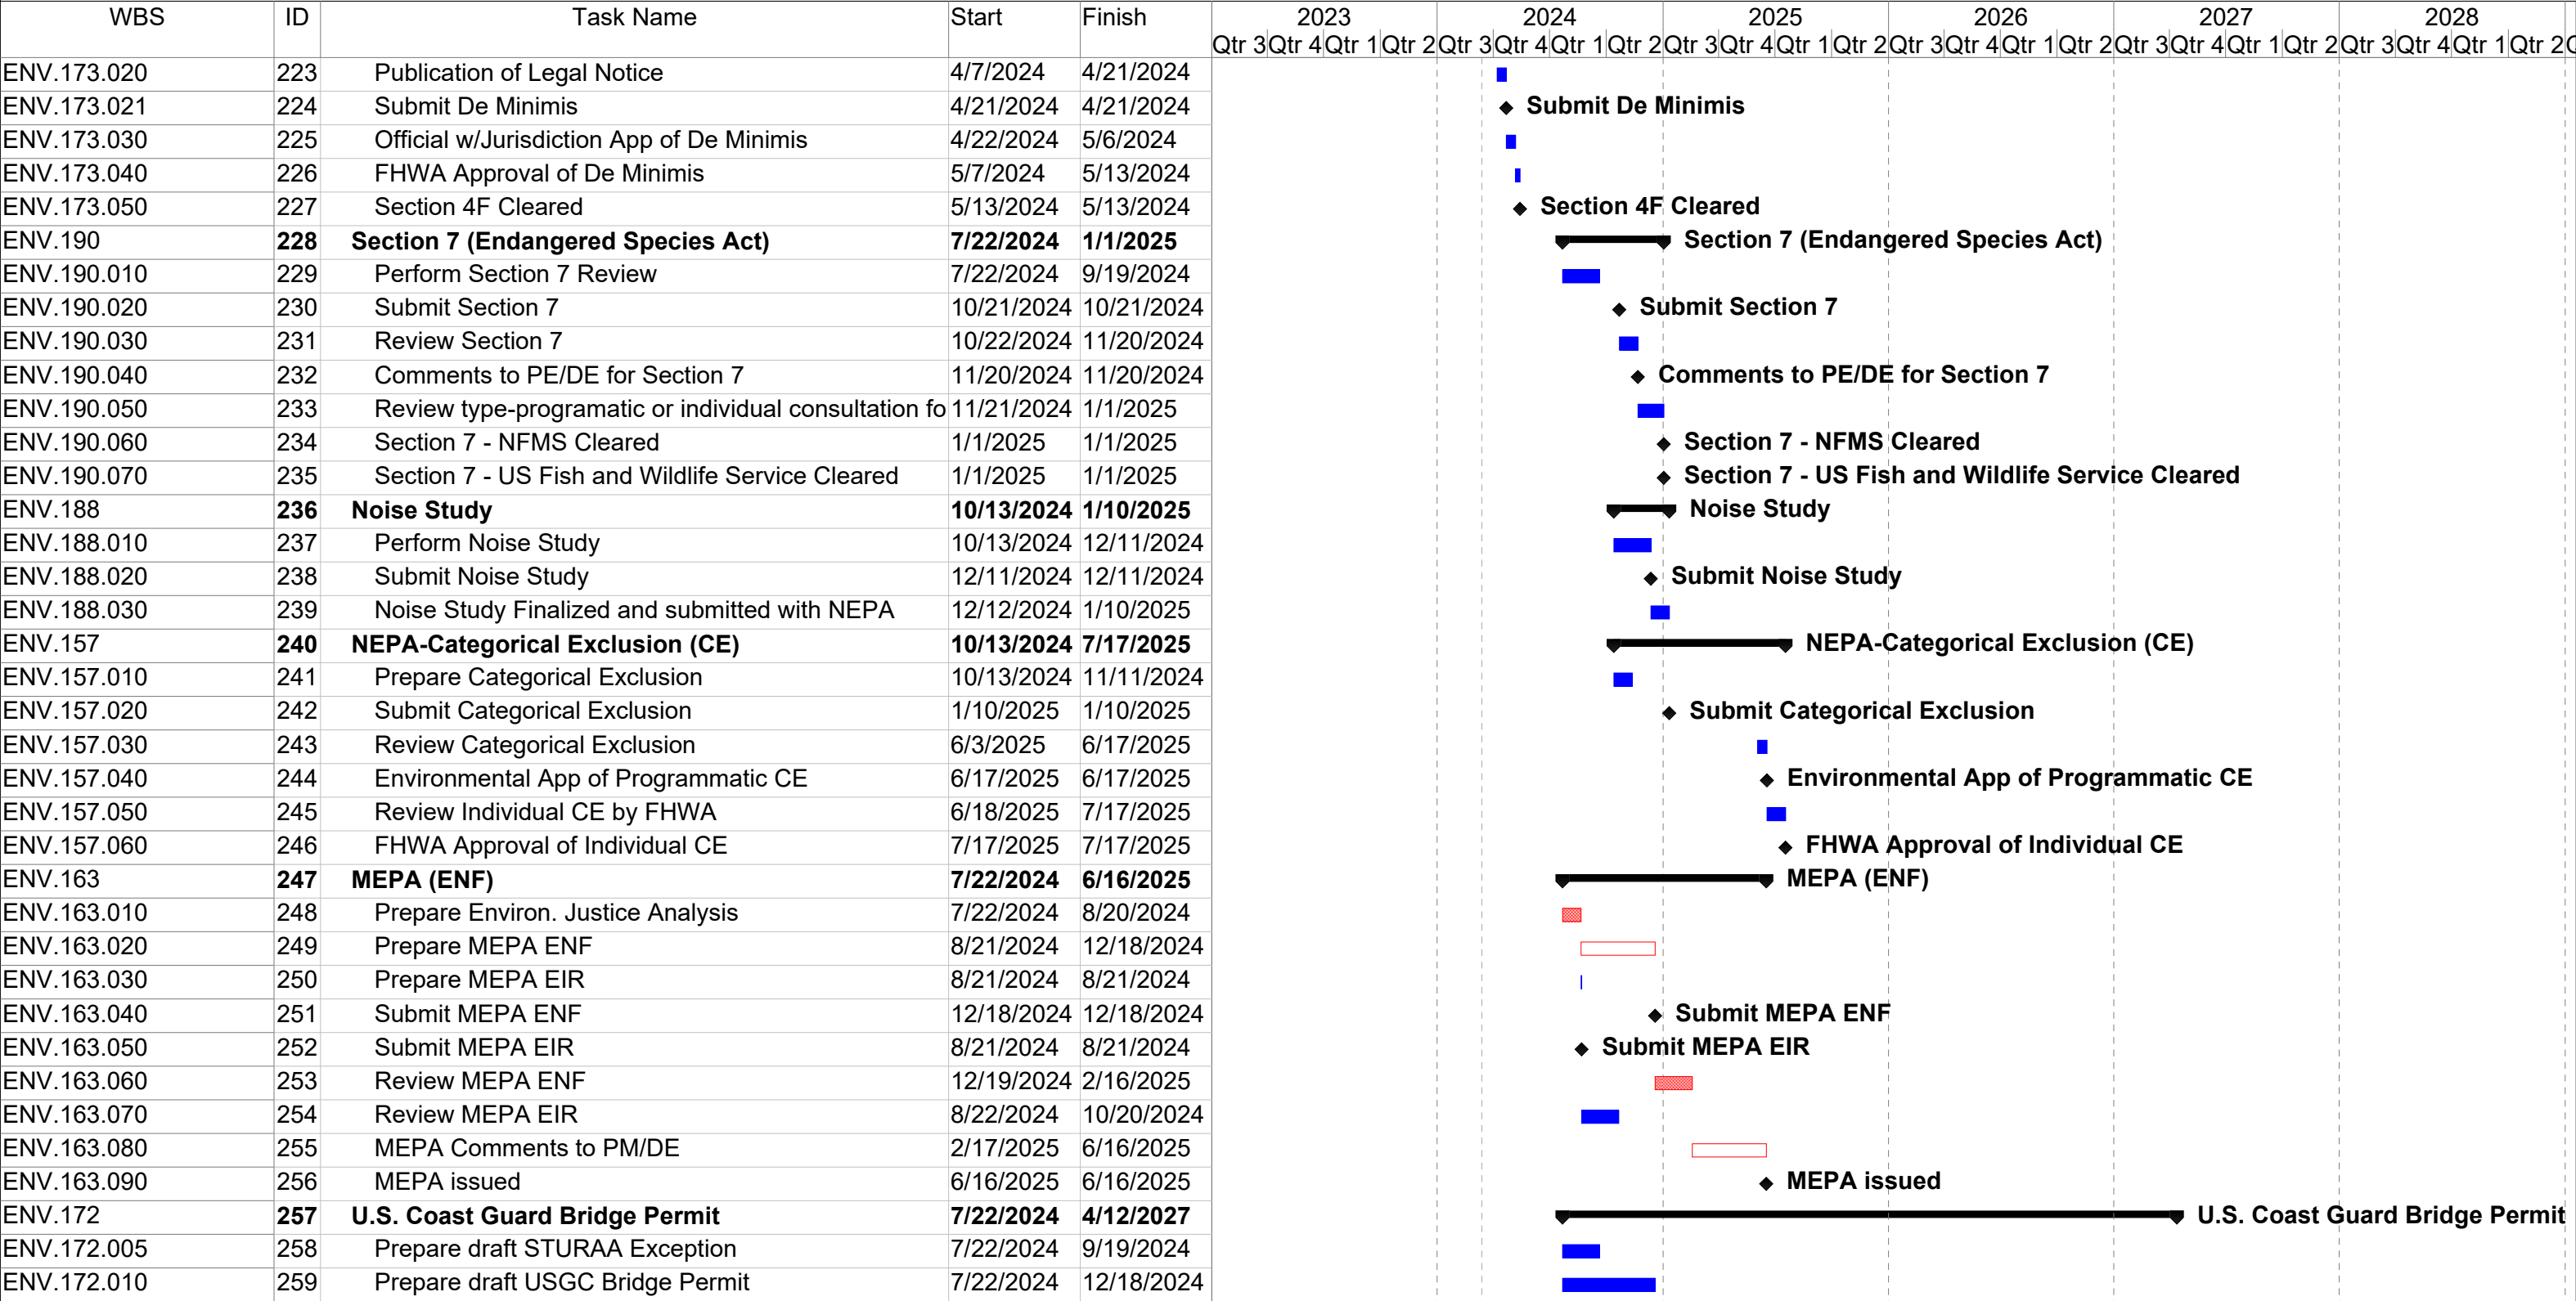

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023		2024		2025		2026		2027		2028	
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2
ENV.172.015	260	Submit draft STURAA	9/19/2024	9/19/2024						◆ Submit draft STURAA						
ENV.172.020	261	Submit draft USGC Bridge Permit	12/18/2024	12/18/2024						◆ Submit draft USGC Bridge Permit						
ENV.172.025	262	Review draft STURAA	9/20/2024	10/19/2024												
ENV.172.030	263	Review draft USGC Bridge Permit	1/2/2025	4/1/2025												
ENV.172.031	264	STURAA Comments to PE/DE	10/19/2024	10/19/2024						◆ STURAA Comments to PE/DE						
ENV.172.032	265	USCG Bridge Permit Comments to PE/DE	4/1/2025	4/1/2025						◆ USCG Bridge Permit Comments to PE/DE						
ENV.172.033	266	Revise STRAA	4/2/2025	4/15/2025												
ENV.172.034	267	Revise USCG Permit	4/2/2025	4/15/2025												
ENV.172.040	268	Submit final STURAA	4/15/2025	4/15/2025						◆ Submit final STURAA						
ENV.172.050	269	Submit final USCG Bridge Permit	7/17/2025	7/17/2025						◆ Submit final USCG Bridge Permit						
ENV.172.060	270	STURAA Exception	4/16/2025	4/29/2025												
ENV.172.070	271	USCG Bridge Permit Issued	1/13/2026	4/12/2026												
ENV.172.071	272	USCG Permit Duration	4/13/2026	4/12/2027												
ENV.172.072	273	USCG Permit Expired	4/12/2027	4/12/2027												
ENV.182	274	Water Quality Certification (401)	7/22/2024	9/14/2026												
ENV.182.005	275	Prepare Draft WQC	7/22/2024	8/20/2024												
ENV.182.010	276	Submit Draft WQC Application	12/11/2024	12/11/2024						◆ Submit Draft WQC Application						
ENV.182.015	277	Review Draft WQC	12/12/2024	1/10/2025												
ENV.182.020	278	WQC Comments to PM/DE	1/10/2025	1/10/2025						◆ WQC Comments to PM/DE						
ENV.182.021	279	Prepare Final WQC	1/11/2025	2/9/2025												
ENV.182.022	280	Submit Final WQC	2/9/2025	2/9/2025						◆ Submit Final WQC						
ENV.182.023	281	Review Final WQC	2/10/2025	3/11/2025												
ENV.182.021.1	282	Prepare Final WQC Rev 1	3/12/2025	3/14/2025												
ENV.182.022.1	283	Submit Final WQC Rev 1	3/14/2025	3/14/2025						◆ Submit Final WQC Rev 1						
ENV.182.023.1	284	Review Final WQC Rev 1	3/15/2025	3/16/2025												
ENV.182.030	285	WQC Permit Filed	3/16/2025	3/16/2025						◆ WQC Permit Filed						
ENV.182.040	286	WQC Permit Issued	6/17/2025	9/14/2025												
ENV.182.041	287	401 (WQC) Permit Duration	9/15/2025	9/14/2026												
ENV.182.042	288	401 (WQC) Permit Expired	9/14/2026	9/14/2026												
ENV.177	289	WPA (RDA/Notice of Intent)	7/22/2024	6/2/2026												
ENV.177.010	290	Perform Field Work and Prepare Draft Application	7/22/2024	8/20/2024												
ENV.177.020	291	Submit Draft WPA (RDA/NOI)	12/11/2024	12/11/2024						◆ Submit Draft WPA (RDA/NOI)						
ENV.177.021	292	Review Draft WPA (RDA/NOI)	12/12/2024	1/10/2025												
ENV.177.022	293	WPA Draft Comments to PM/DE	1/10/2025	1/10/2025						◆ WPA Draft Comments to PM/DE						
ENV.177.030	294	Prepare Final WPA (RDA/NOI)	1/11/2025	1/25/2025												
ENV.177.040	295	Submit Final WPA (RDA/NOI)	1/25/2025	1/25/2025						◆ Submit Final WPA (RDA/NOI)						
ENV.177.050	296	Review Final WPA (RDA/NOI)	1/26/2025	2/24/2025												

Task

Milestone

◆

Summary

Critical Path


Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

◆

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work

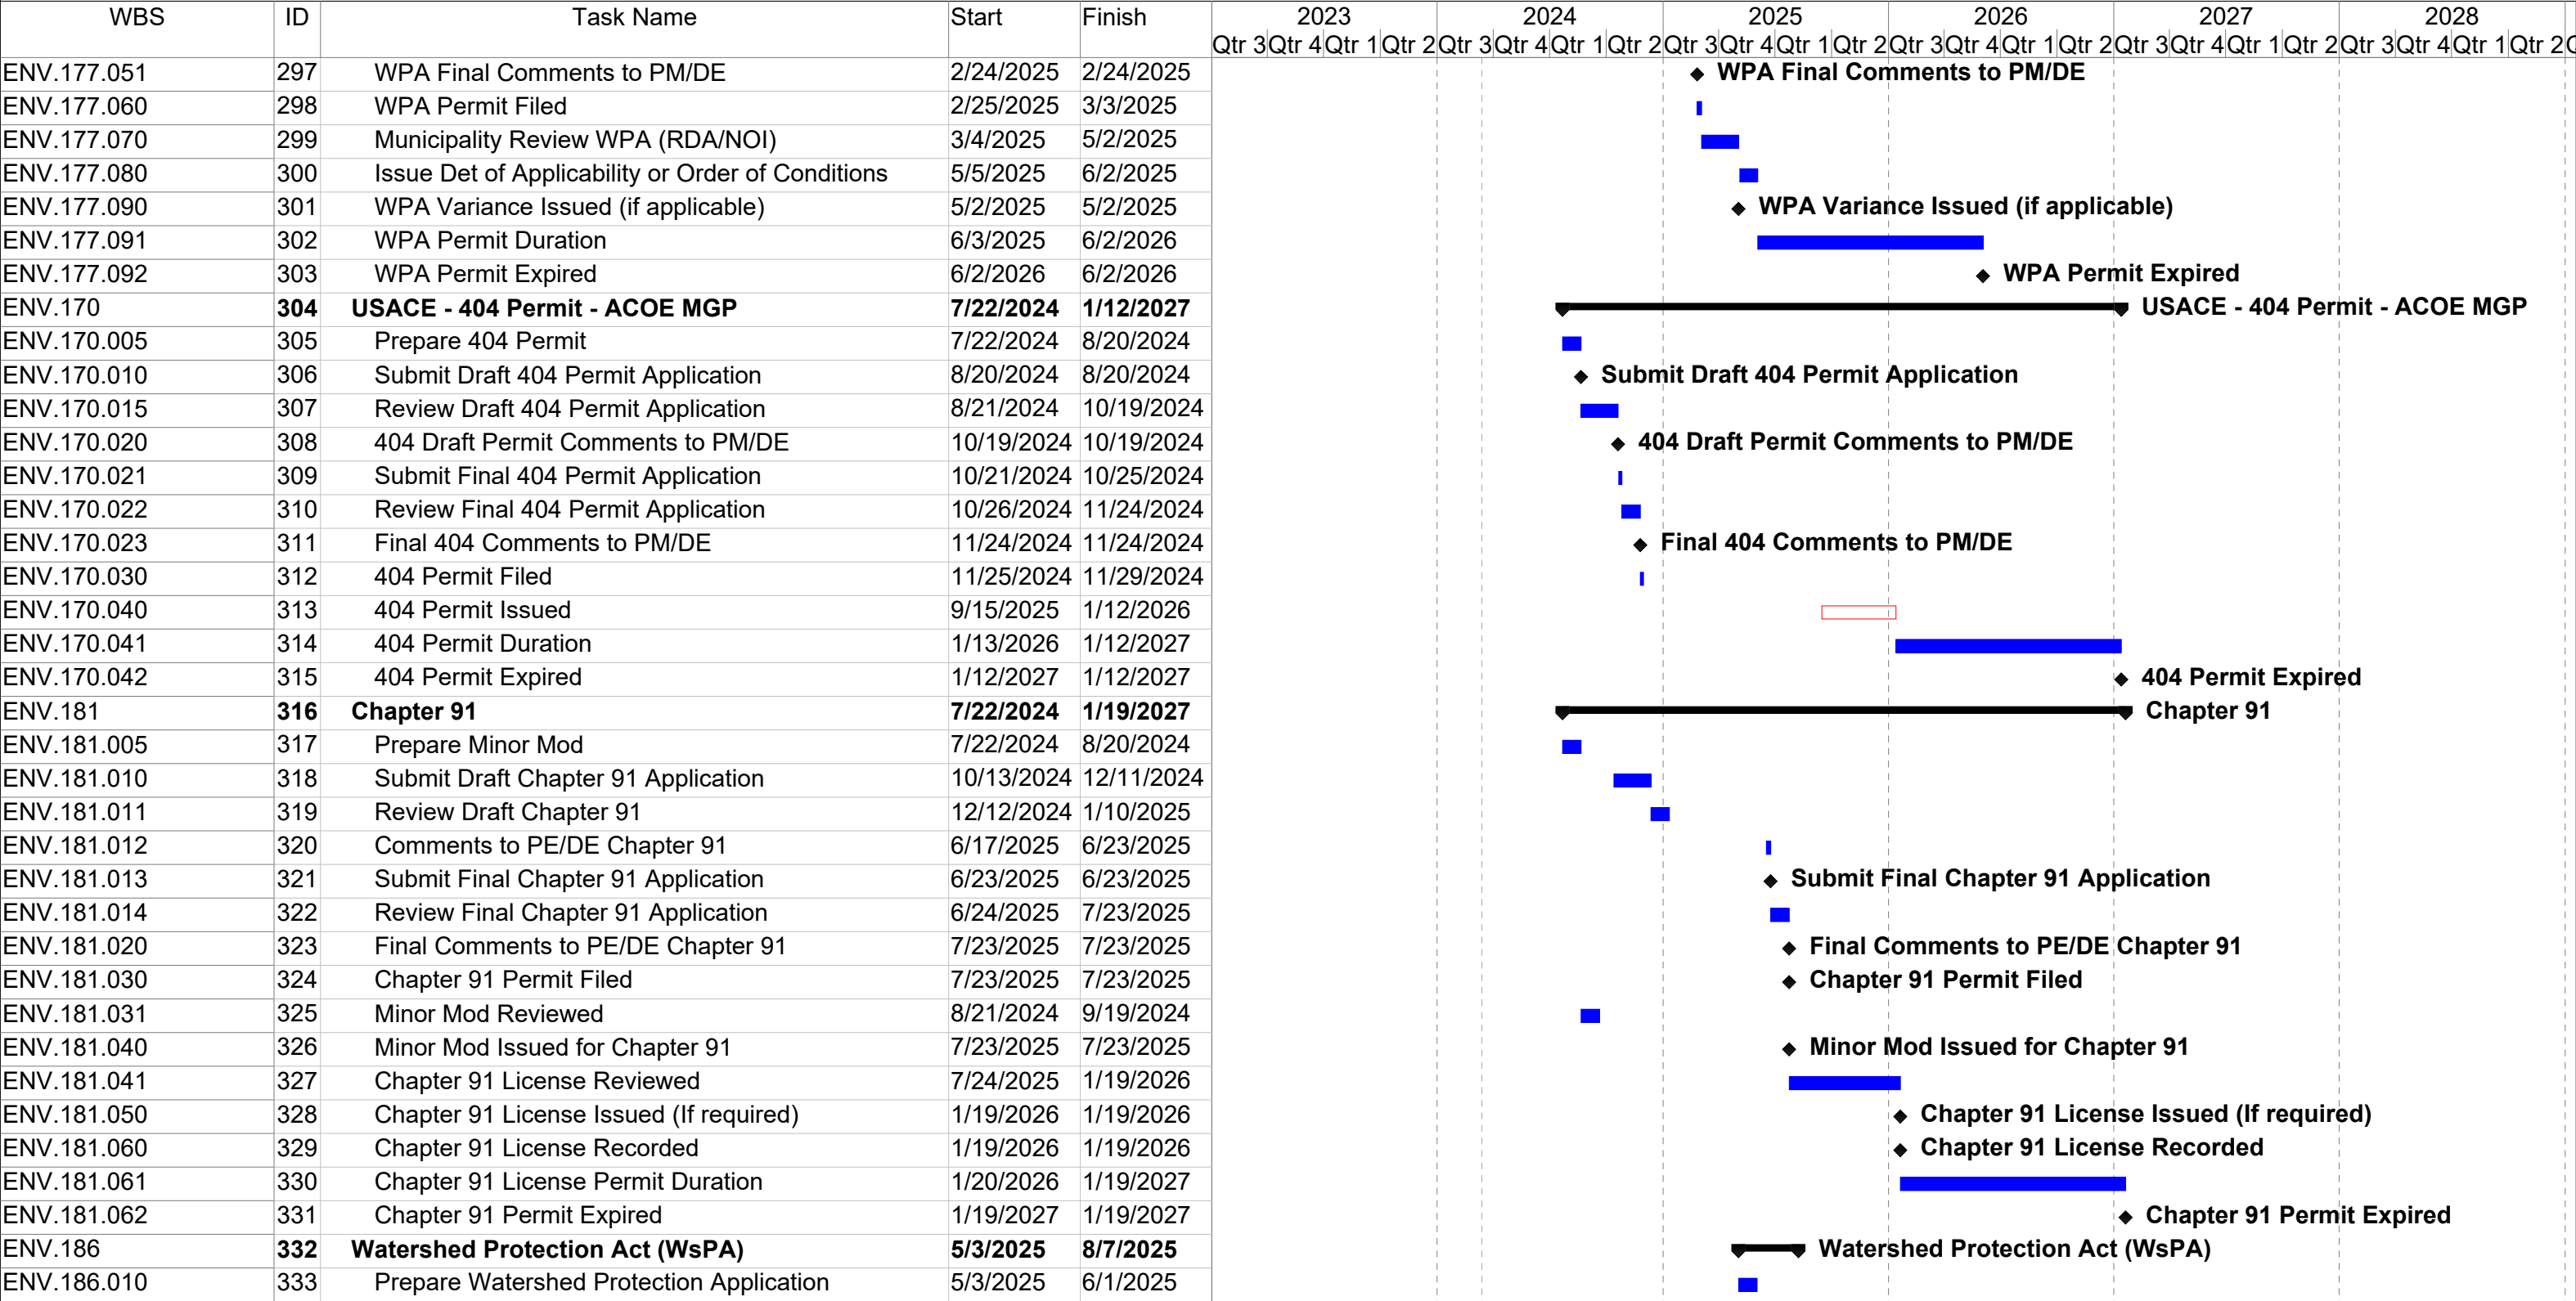

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

◆

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023		2024		2025		2026		2027		2028	
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2
ENV.186.011	334	Submit WsPA	6/1/2025	6/1/2025												
ENV.186.015	335	Review WsPA	6/2/2025	7/1/2025												
ENV.186.020	336	Watershed Protection Comments to PM/DE	7/1/2025	7/1/2025												
ENV.186.030	337	Watershed Protection Permit Filed	7/2/2025	7/8/2025												
ENV.186.040	338	Watershed Protection Permit Issued by DCR	7/9/2025	8/7/2025												
ENV.183	339	Coastal Zone Management	7/22/2024	11/26/2024												
ENV.183.010	340	Coordination Letter to CZM	7/22/2024	8/20/2024												
ENV.183.020	341	CZM Review through MEPA	8/21/2024	9/19/2024												
ENV.183.030	342	CZM Review through 404	8/21/2024	9/19/2024												
ENV.183.040	343	Draft CZM Invidual Federal Consistency Review	8/21/2024	8/21/2024												
ENV.183.050	344	Comments to PE/DE for CZM	8/22/2024	8/28/2024												
ENV.183.060	345	CZM Individual Federal Consistenceny Review Letter	8/29/2024	9/27/2024												
ENV.183.061	346	CZM Letter Reviewed	9/28/2024	11/26/2024												
ENV.183.070	347	CZM Concurrence Issued	11/26/2024	11/26/2024												
ENV.184	348	Wildlife/Rare Species Assessment	7/22/2024	10/21/2024												
ENV.184.010	349	Perform Wildlife Assessment	7/22/2024	9/19/2024												
ENV.184.020	350	Submit Wildlife Assessment	9/19/2024	9/19/2024												
ENV.184.030	351	Review Wildlife Assessment	9/20/2024	10/19/2024												
ENV.184.040	352	Comments to PE/DE Wildlife Assessment	10/21/2024	10/21/2024												
ENV.185	353	Essential Fish Habitat Assessment	7/22/2024	11/21/2024												
ENV.185.010	354	Prepare Fish Assessment	7/22/2024	8/20/2024												
ENV.185.020	355	Submit Fish Assessment	10/21/2024	10/21/2024												
ENV.185.030	356	Review Fish Assessment	10/22/2024	11/20/2024												
ENV.185.040	357	Comments to PE/DE Fish Assessment	11/21/2024	11/21/2024												
ENV.189	358	MESA (MA Endangered Species Act)	12/12/2024	7/16/2026												
ENV.189.010	359	Prepare MESA	12/12/2024	1/10/2025												
ENV.189.020	360	Submit MESA	1/10/2025	1/10/2025												
ENV.189.030	361	Review MESA type	1/11/2025	2/9/2025												
ENV.189.040	362	Comments to PE/DE MESA	2/9/2025	2/9/2025												
ENV.189.045	363	No Take or Conditional No Take	2/10/2025	2/27/2025												
ENV.189.050	364	Conservation and Management Permit	6/17/2025	7/16/2025												
ENV.189.051	365	MESA Permit Duration	7/17/2025	7/16/2026												
ENV.189.052	366	MESA Permit Expired	7/16/2026	7/16/2026												
ENV.154	367	Hazardous Materials	7/22/2024	11/18/2024												
ENV.154.010	368	Complete Env. Assessment / Initial Inclusion of Spec	7/22/2024	9/19/2024												
ENV.154.020	369	Submit for Hazmat Review	9/19/2024	9/19/2024												
ENV.154.030	370	Hazmat Review / Inclusion of SP Items	9/20/2024	10/19/2024												

Task

Milestone

◆

Summary


Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

Massachusetts Department of Transportation
<MassDOT Project Info Number> <Short Project Description - City Names>
BL PDS Schedule Grouped by Area of Work

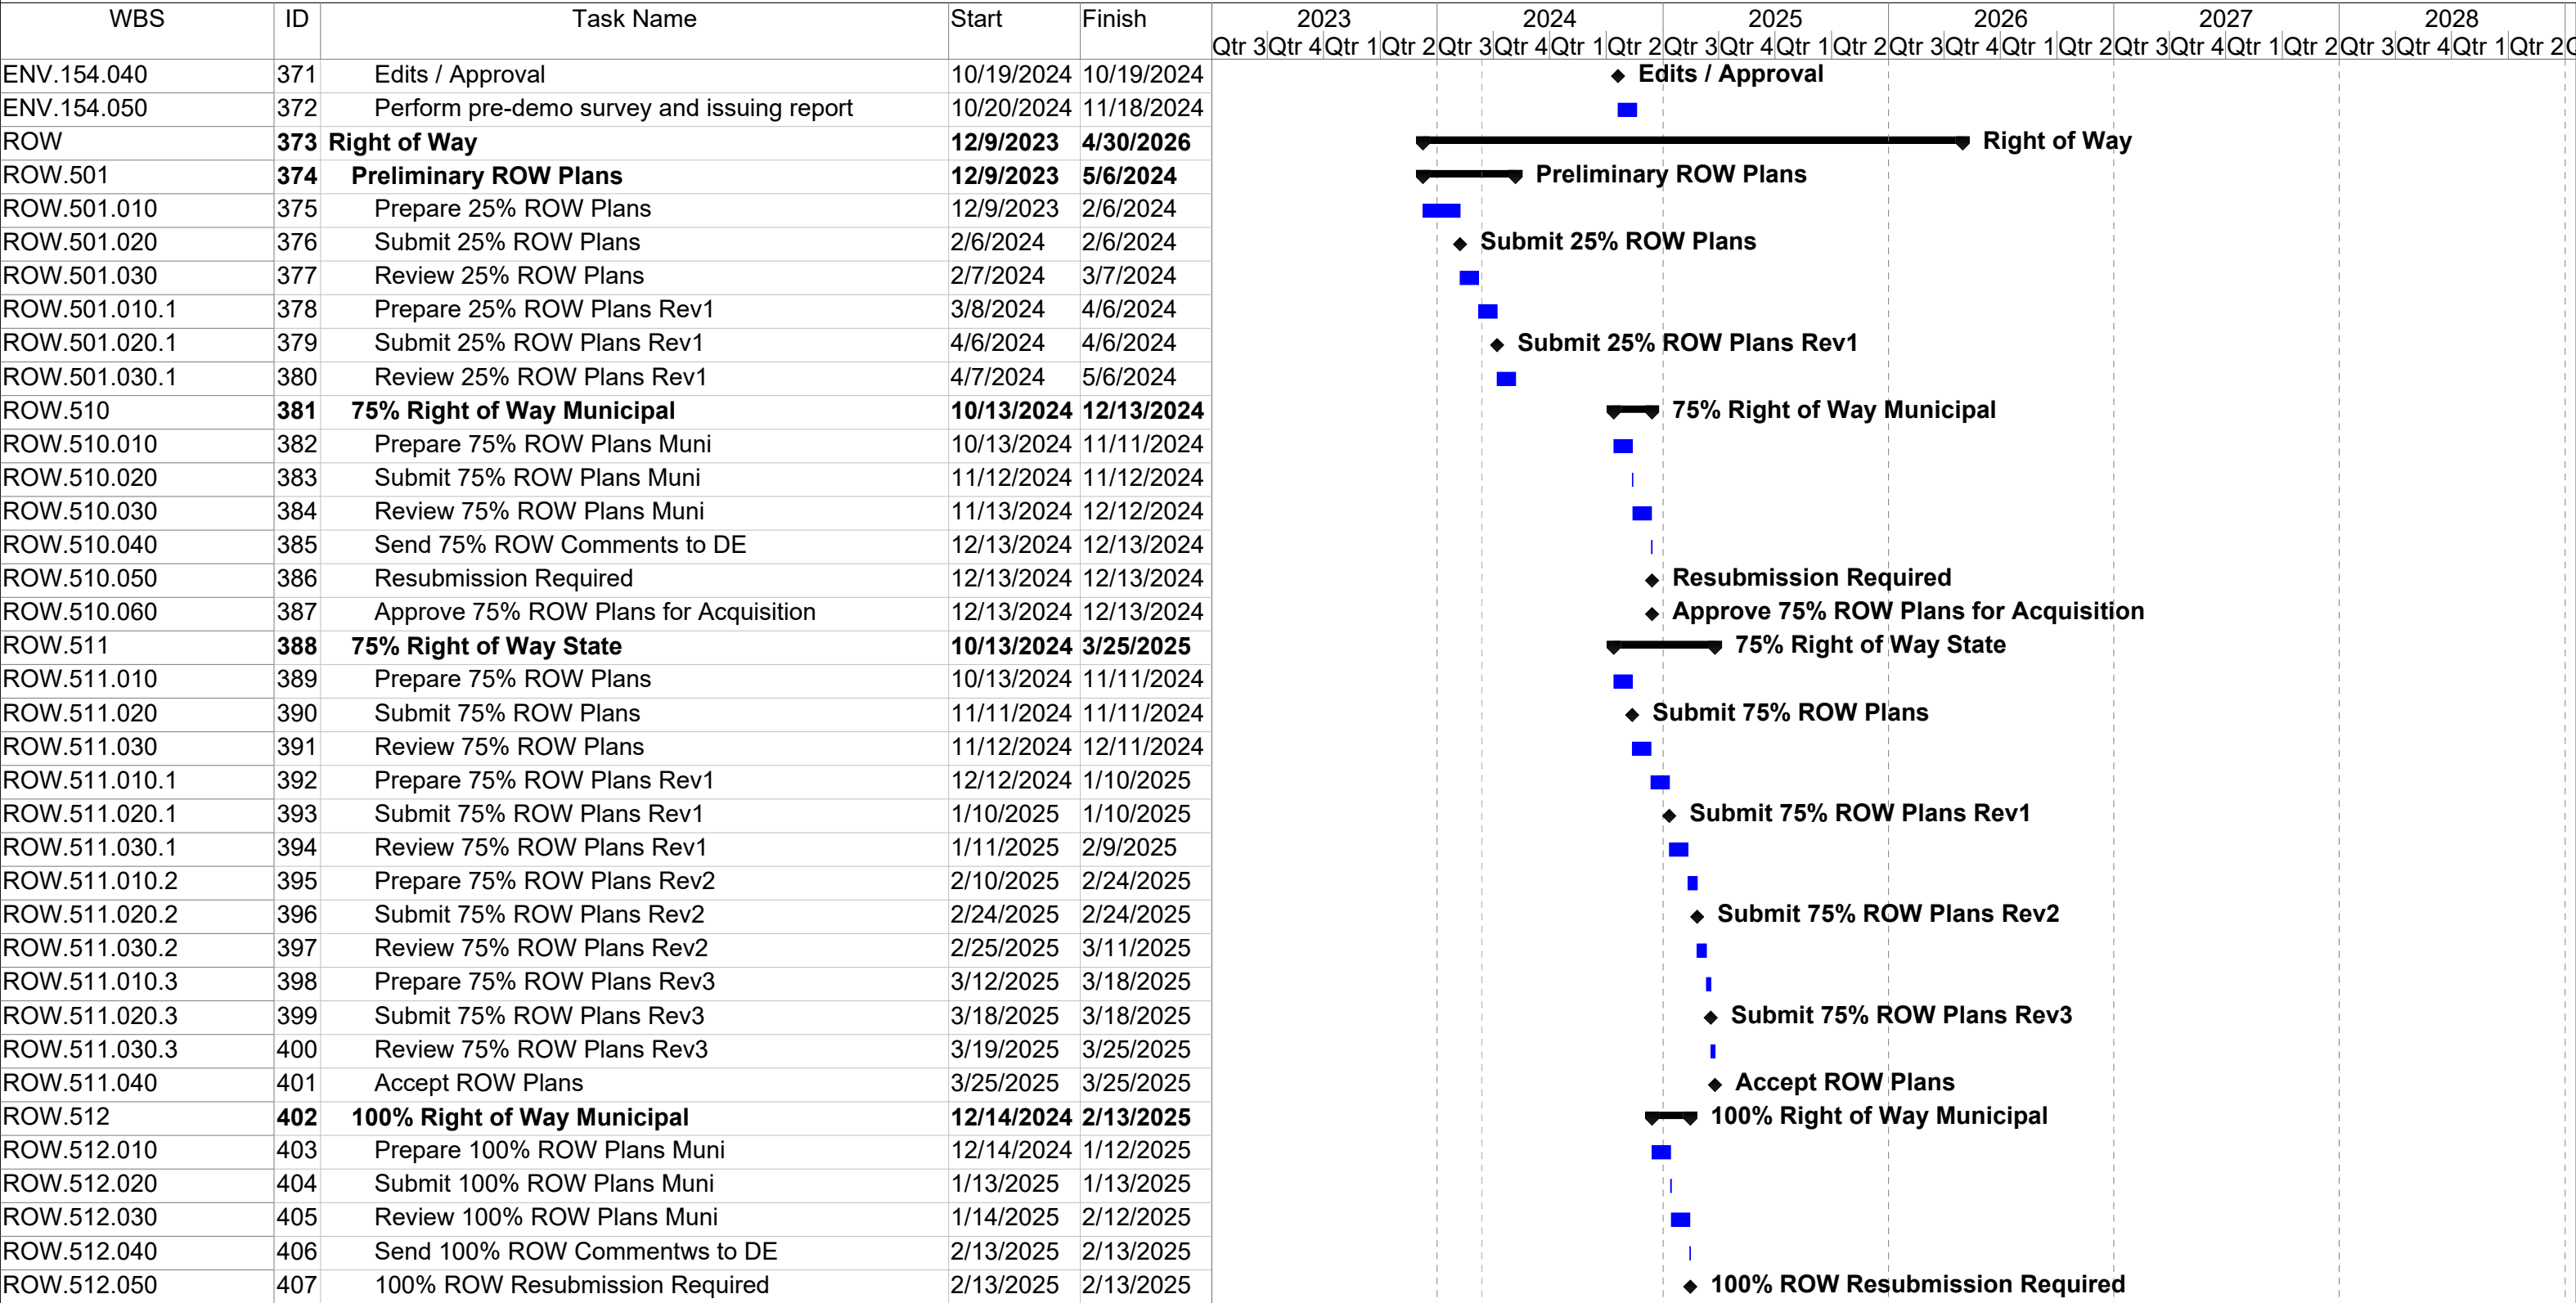

Task

Milestone

■

◆

Summary

Critical Path

◆

◆

Path Successor Normal Task

Path Successor Summary Task

◆

◆

Path Successor Milestone Task

Path Successor Milestone Task

Massachusetts Department of Transportation

<MassDOT Project Info Number> <Short Project Description - City Names>

BL PDS Schedule Grouped by Area of Work



WBS	ID	Task Name	Start	Finish	2023				2024				2025				2026				2027				2028			
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2
ROW.512.060	408	Approve 100% ROW Plans for Acquisition	2/13/2025	2/13/2025																								
ROW.502	409	Acquisition Process - 100% through PS&E	3/8/2024	4/30/2026																								
ROW.502.01	410	State ROW Acquisition Process	3/8/2024	4/30/2026																								
ROW.502.01.010	411	Perform Title Exams	3/26/2025	5/24/2025																								
ROW.502.01.020	412	Contact Property Owners	3/8/2024	3/27/2024																								
ROW.502.01.030	413	Property Interviews	5/25/2025	7/23/2025																								
ROW.502.01.040	414	Perform Appraisals	7/24/2025	10/21/2025																								
ROW.502.01.050	415	Prepare Draft Layout Taking Plans & Instrument (T	3/26/2025	6/23/2025																								
ROW.502.01.060	416	Submit Draft Layout TPIs	6/23/2025	6/23/2025																								
ROW.502.01.070	417	Review Draft Layout TPIs	6/24/2025	8/7/2025																								
ROW.502.01.080	418	Approve Layout Taking Plans	8/7/2025	8/7/2025																								
ROW.502.01.090	419	Offer, Negotiations, Record & File	10/22/2025	12/25/2025																								
ROW.502.01.100	420	Payment; Issue ROW Certificate	12/26/2025	4/30/2026																								
ROW.502.02	421	Municipal ROW Acquisition Process	3/8/2024	8/8/2025																								
ROW.502.02.010	422	Perform Title Exams (All TPI)	3/8/2024	11/11/2024																								
ROW.502.02.020	423	Hold Town Meeting (Verify Warrant Deadline)	5/7/2024	5/7/2024																								
ROW.502.02.030	424	Contact Property Owners	3/8/2024	3/27/2024																								
ROW.502.02.040	425	Perform Appraisals (All TPI)	12/14/2024	4/12/2025																								
ROW.502.02.050	426	Prepare Draft Layout Taking Plans & Instrument (T	11/13/2024	11/27/2024																								
ROW.502.02.060	427	Submit Draft Layout TPIs	11/27/2024	11/27/2024																								
ROW.502.02.070	428	Review Draft Layout TPIs	11/28/2024	12/27/2024																								
ROW.502.02.080	429	Approve Layout Taking Plans	12/28/2024	2/10/2025																								
ROW.502.02.090	430	Offer & Negotiations	4/13/2025	5/22/2025																								
ROW.502.02.100	431	Municipal Approval, Record & File	5/23/2025	6/11/2025																								
ROW.502.02.110	432	Submit Community Compliance Package	6/12/2025	6/18/2025																								
ROW.502.02.120	433	Review Community Compliance Package	6/19/2025	6/25/2025																								
ROW.502.02.130	434	Pay Award of Damages	6/26/2025	7/25/2025																								
ROW.502.02.140	435	Issue ROW Certificate	7/28/2025	8/8/2025																								
ROW.502.03	436	Article 97 Proceedings	3/25/2025	3/25/2025																								
ROW.502.03.010	437	Article 97 Proceedings	3/25/2025	3/25/2025																								

Task

Milestone

◆

Summary

Critical Path

Path Successor Normal Task

Path Successor Summary Task

Path Successor Milestone Task

◆
